



490th —————

Flash Report on

Central Sector Infrastructure

Projects —————



Scan the QR code to access
the PAIMANA Portal.

**(₹150 crore
& above)**

AUGUST 2026

<https://paimana.mospi.gov.in> @GoIStats /GoIStats GoIStats Ministry of Statistics & PI



CONTENTS

I. Overview*	2-4
II. North Eastern Region	5-6
III. As per Harmonized Master List (HML) 2022	7-13
IV. Major Infrastructure Central Ministries & Departments	14-19
V. Appendix : <i>List of Tables</i>	20 onwards
Table 1: Ministry-wise Ongoing Projects	
Table 2: State-wise Ongoing Projects	
Table 3: Completed Projects	
Table 4: Newly Added Projects	
Table 5: Ongoing Projects of North Eastern Region	
Table 6: All Ongoing Projects	

**Note: This report is web-generated from the PAIMANA portal (<https://paimana-proj.mospi.gov.in>) as of August 2026, based on the projects worth Rs. 150 crores and above reported by Central Line Ministries/ Departments/ Implementing Agencies on the CRIP portal (<https://paimana-crip.mospi.gov.in>) latest by 24th September 2026.*





Overview





Flash Report

Central Sector Infrastructure Projects Costing Rs. 150 crore & above

AUGUST 2026

1731 | 17

Ongoing Projects |
Line Ministries & Departments

₹ 30,71,947

Original Cost
(crores)

₹ 33,60,069

Revised Cost
(crores)

₹ 16,32,561

(48.59% of Revised Cost)
Cumulative Expenditure
(crores)

47


Commissioned during month

37

Newly Added during month


Sectoral Comparison : Major Sectors*

[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

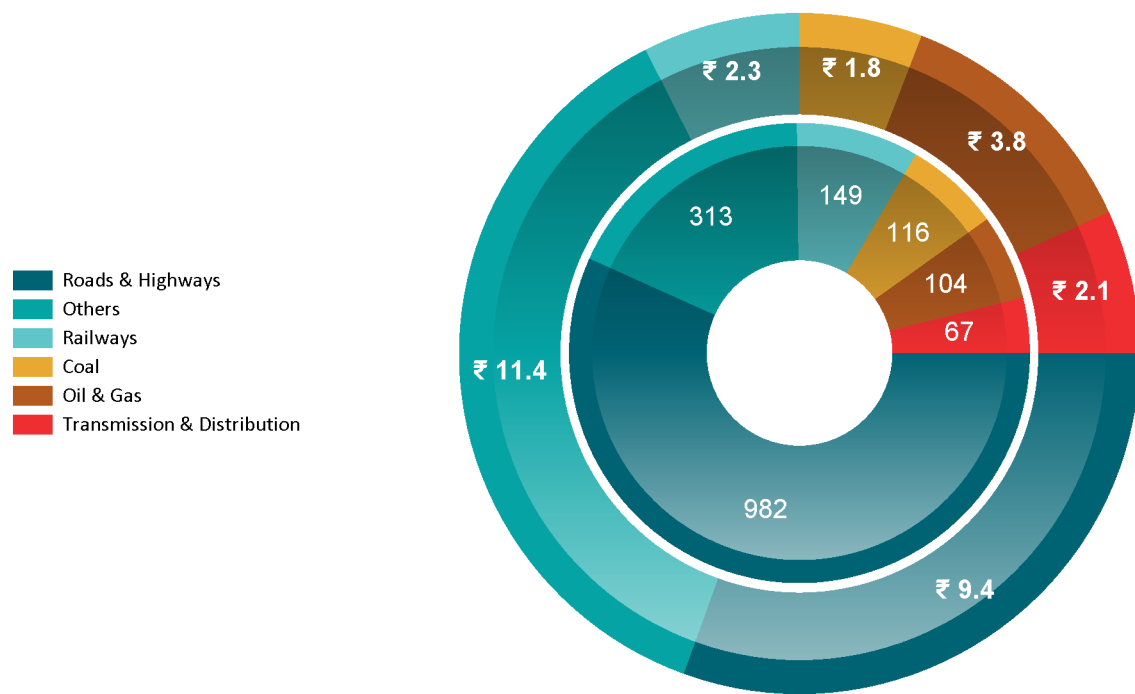


Ministry Comparison : Major Ministries*


[Outer Ring : Original Cost in ₹ lakh crore] & [Inner Ring : Project Count]

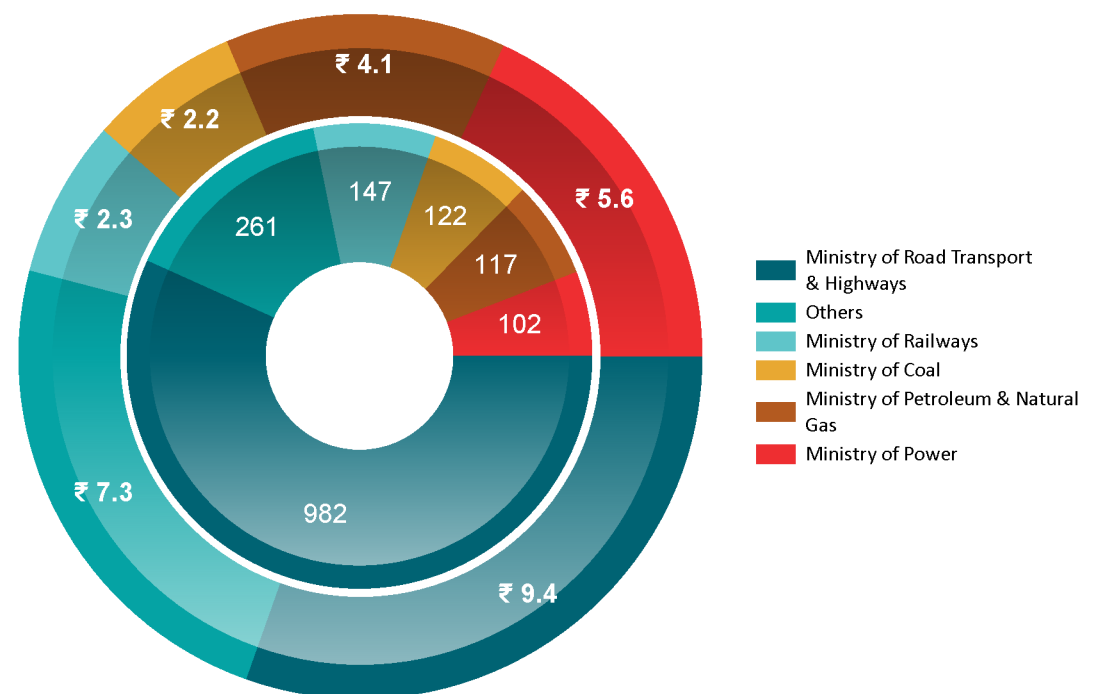

Cost Analytics : Major Sectors*

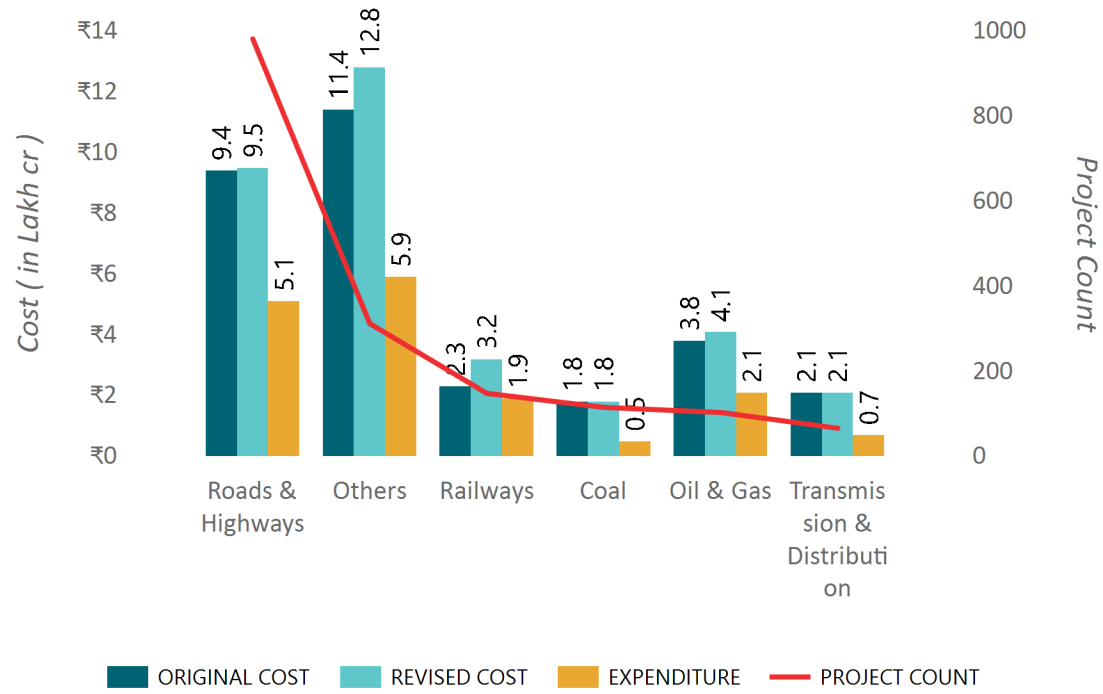


Cost Analytics : Major Ministries*

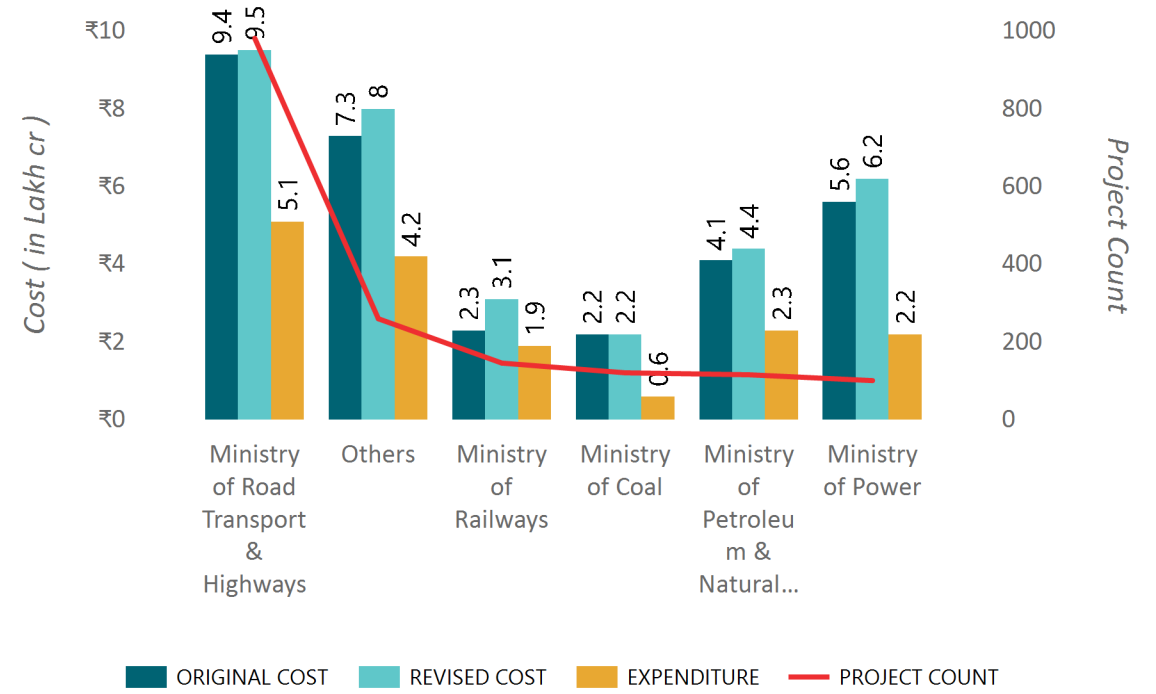


Note: * as per Project Count

Analytics: as per HML

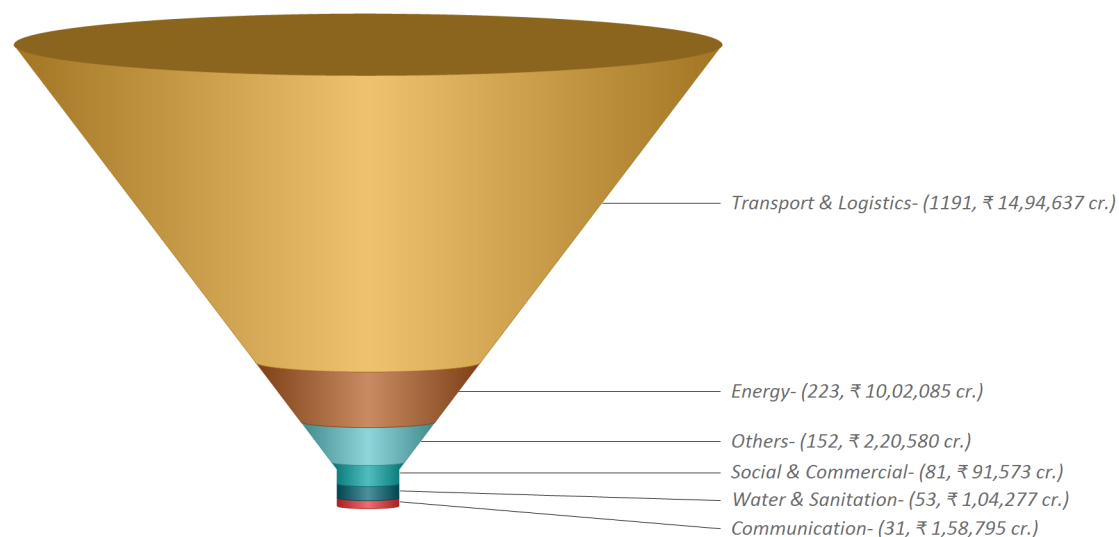


Note: all indicated legends are in format (Project count, Original Cost in crores)

Cumulative Physical & Financial progress (%) : Project count

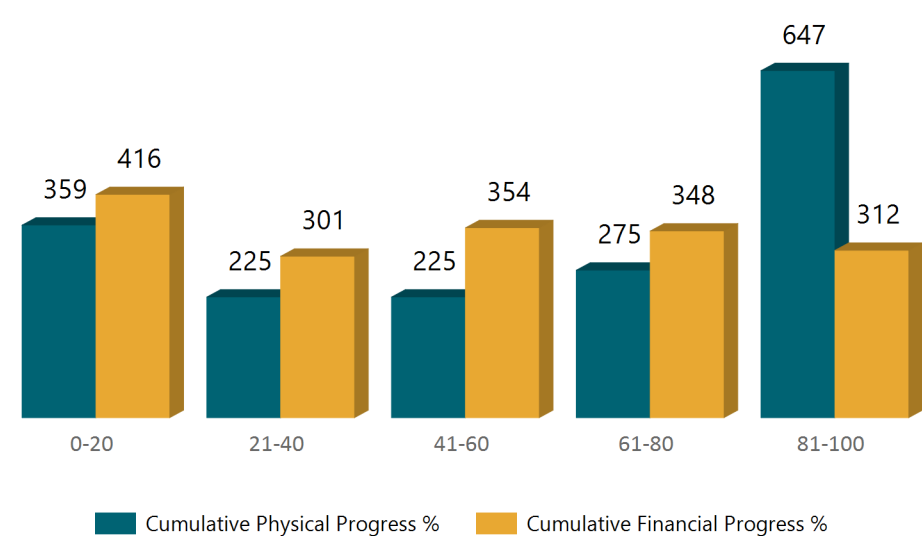




State Comparison : Major States*

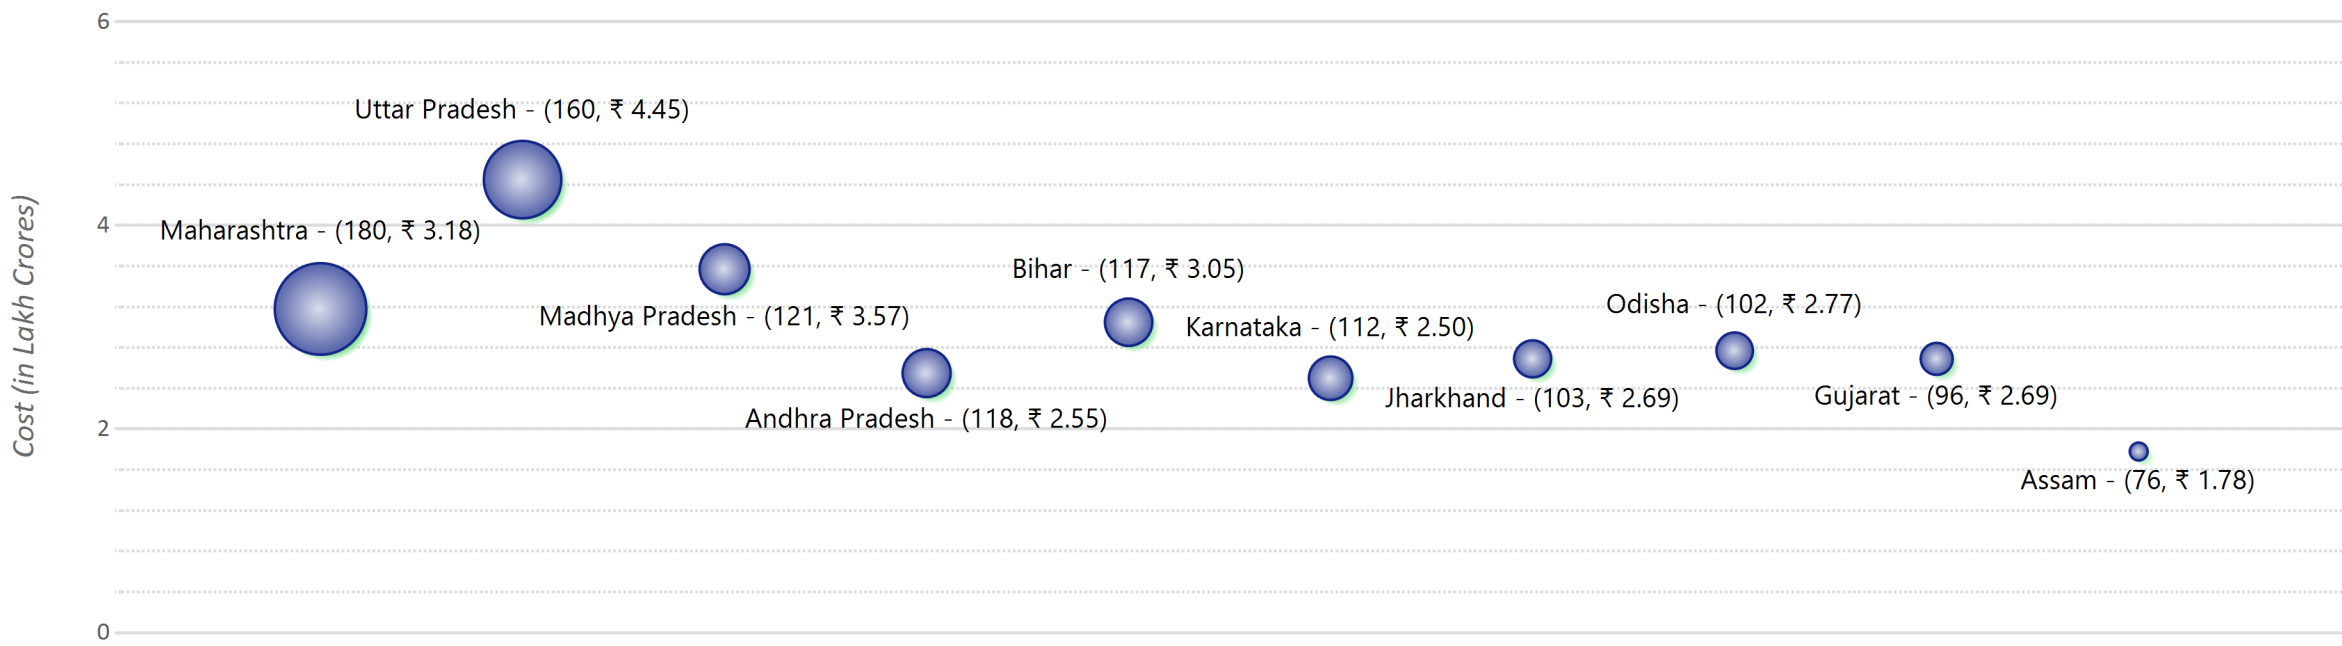

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
* as per project count


Ministry-wise Distribution of total 647 projects
with reported Physical Progress between 81-100%

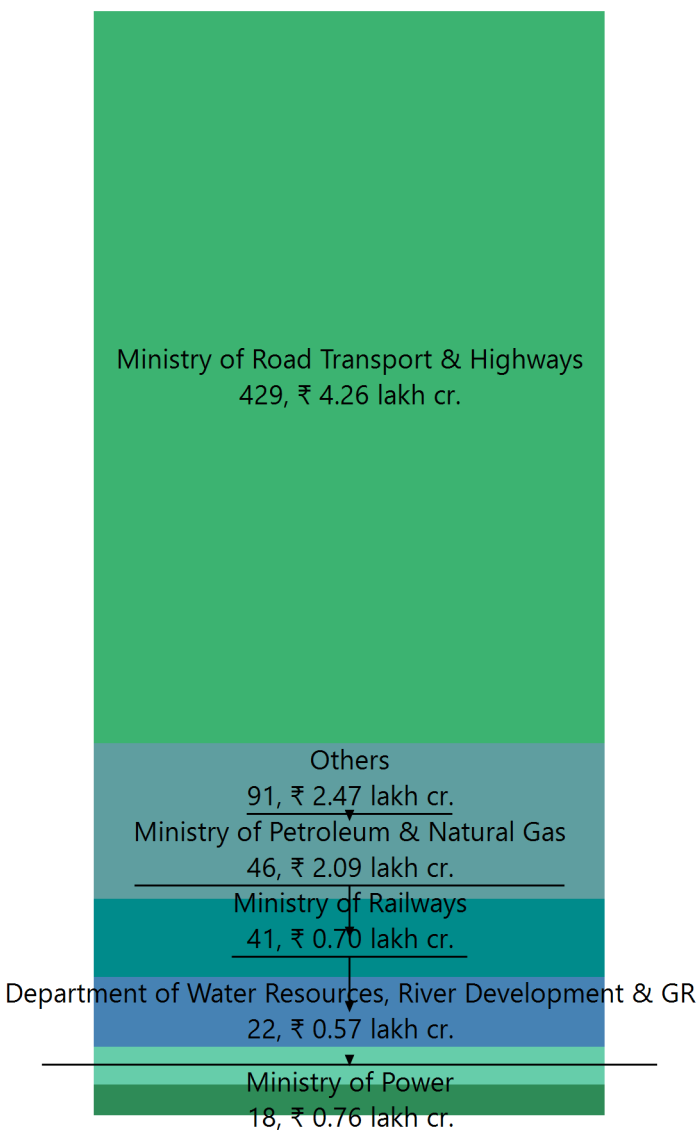

Total Ongoing Projects: Mega & Major




Total North East Region Ongoing Projects: Mega & Major




Note: all indicated legends are in format (Project count, Original Cost)
* Mega project if having original cost >= 1000 crore
* Major project if having original cost < 1000 crore

Project volume (nos.)

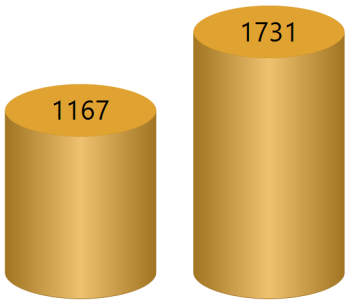


Change in Project Count : +48%

Total Project value (in lakh crore)

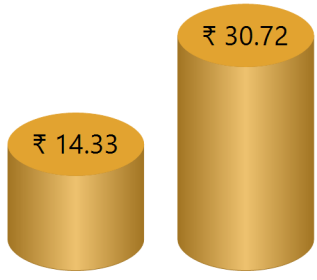

Change in Total Value : +117%

Cumulative Expenditure (in lakh crore)

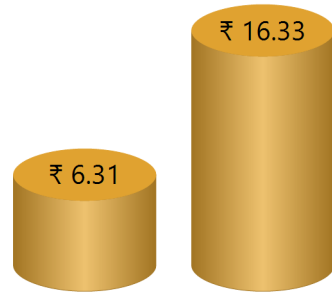

Change in Expenditure : +167%



North Eastern Region





Special Focus : North Eastern Region

AUGUST 2026

209 | 11

Ongoing Projects |
Line Ministries & Departments

₹ 3,35,218

Original Cost
(crores)

₹ 3,82,497

Revised Cost
(crores)

₹ 2,11,462

(55.28% of Revised Cost)
Cumulative Expenditure
(crores)

6


Commissioned during month

8


Newly Added during month

Ministry Comparison : Major Ministries*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

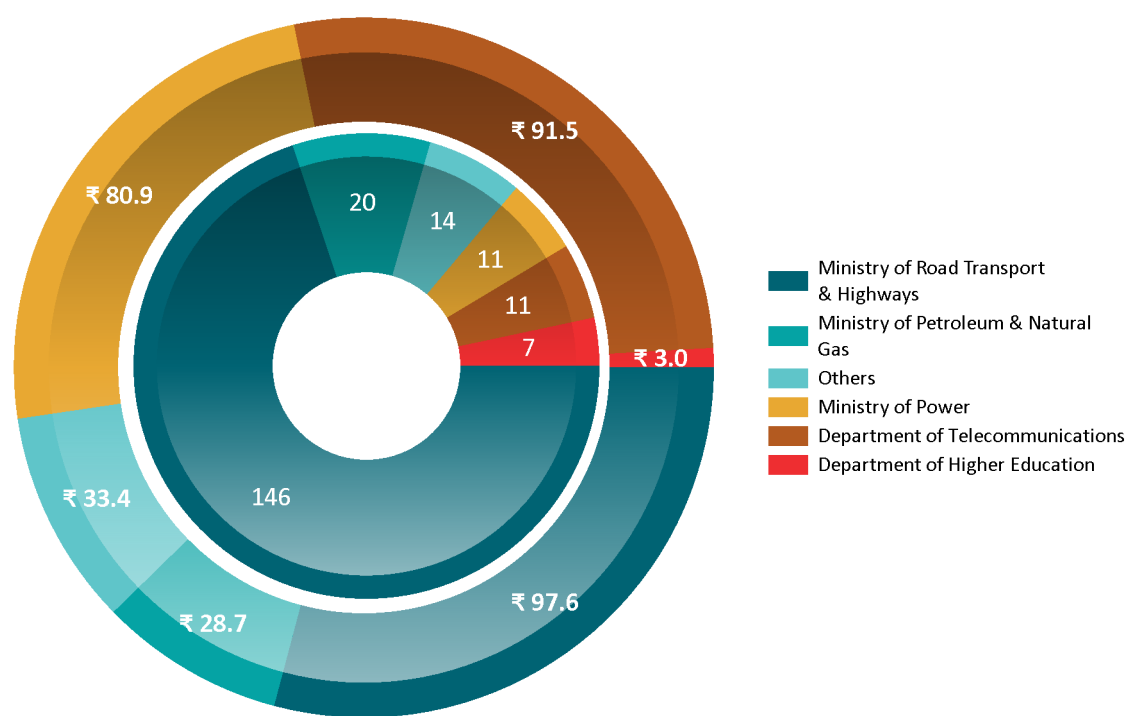


Cost Analytics : Major Ministries*

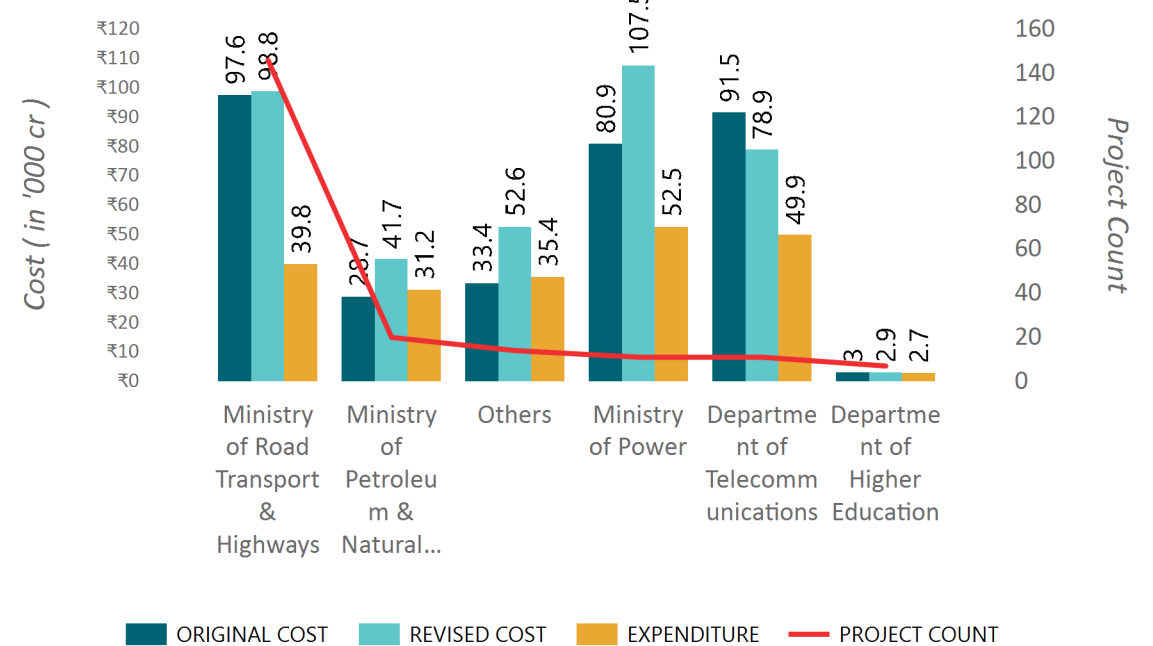


Note: * as per Project Count

Analytics: as per HML

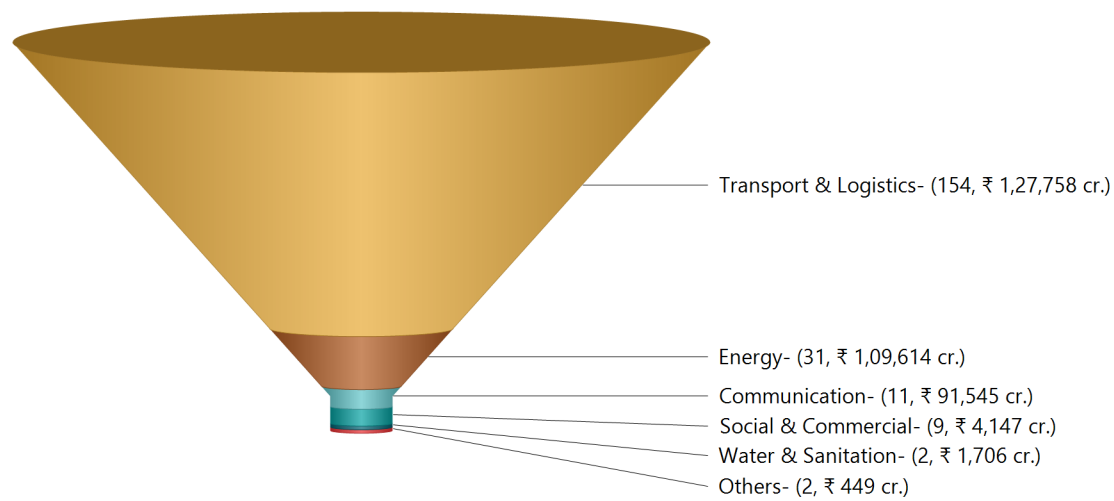


Note: all indicated legends are in format (Project count, Original Cost in crores)

Cumulative Physical & Financial progress (%) : Project count

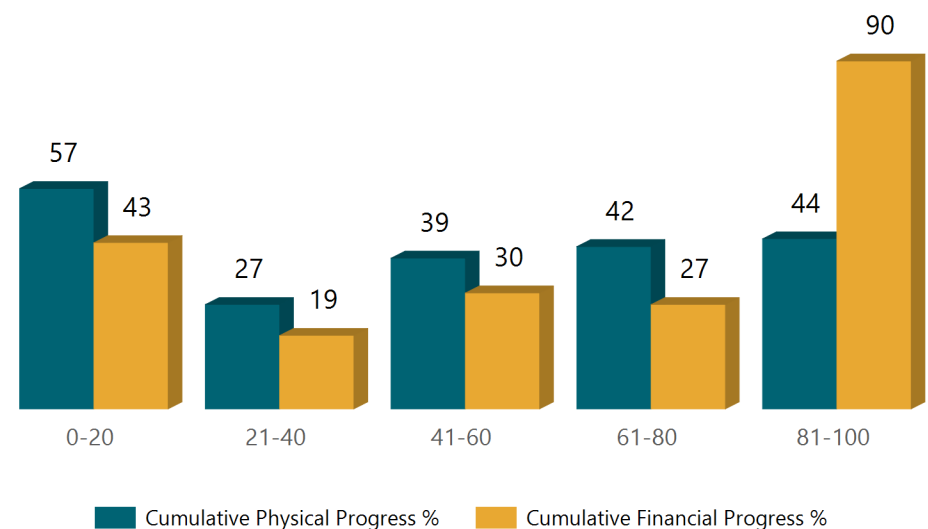

State Comparison : All States

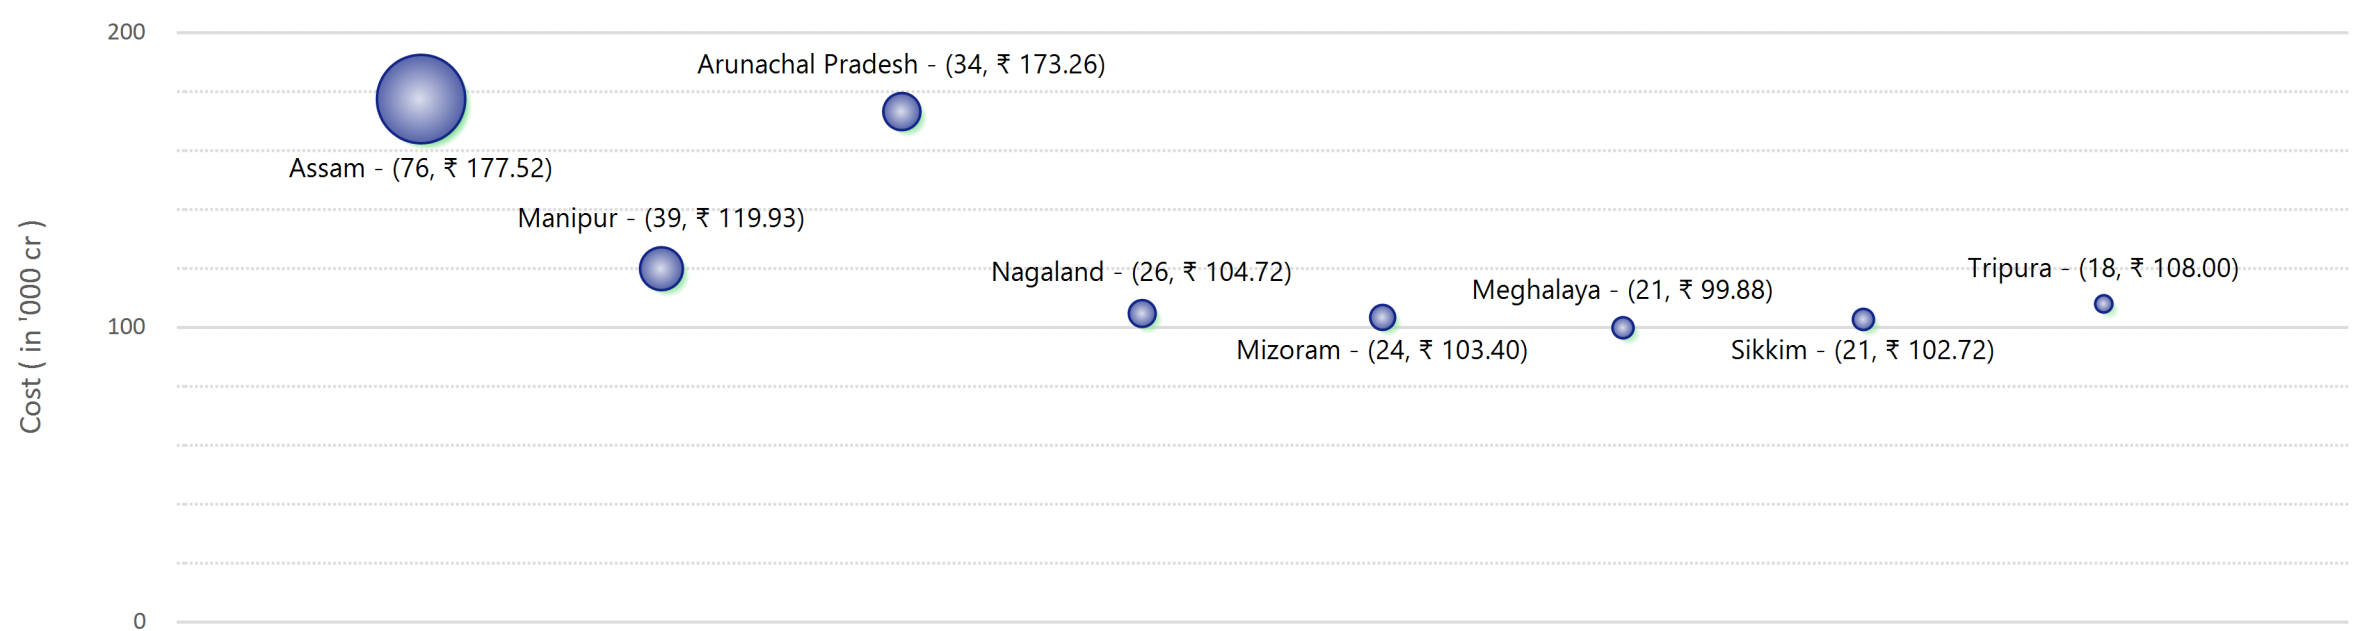

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in Thousand crores)



As per Harmonized Master List (HML)2022



HML Category 1 : Transport & Logistics

AUGUST 2026

1191
Ongoing Projects

₹ 14,94,637
Original Cost
(crores)


₹ 16,04,991
Revised Cost
(crores)

₹ 8,61,217
(53.66% of Revised Cost)
Cumulative Expenditure
(crores)


44
Commissioned during month

11
Newly Added during month

Cost Analytics : All Sectors

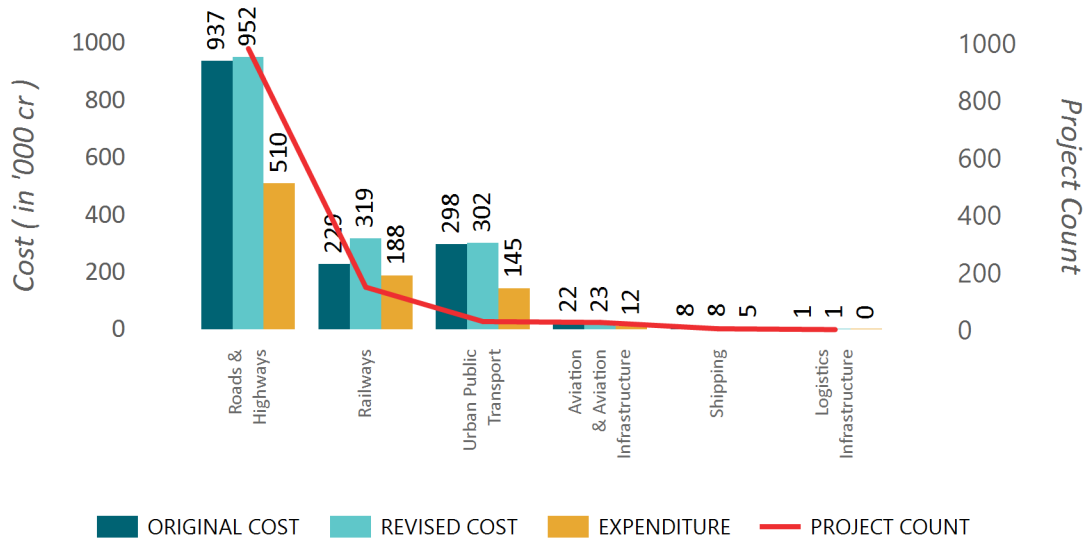

Cumulative Physical & Financial progress (%) : Project count

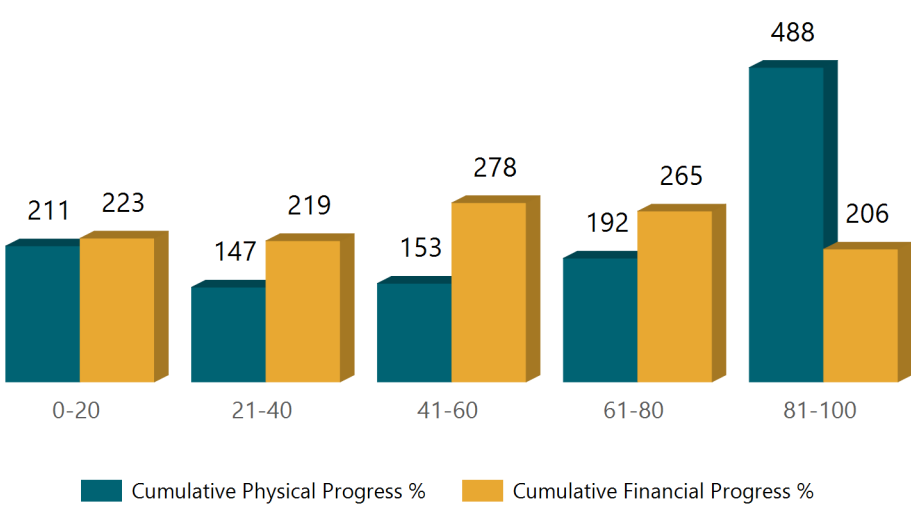

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Roads & Highways	982	937,452	951,926	510,396
2	Railways	149	229,288	319,238	188,418
3	Urban Public Transport	29	297,736	302,200	144,664
4	Aviation & Aviation Infrastructure	26	21,825	23,252	11,904
5	Shipping	4	7,573	7,613	5,405
6	Logistics Infrastructure	1	763	763	430

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	702668	CHENNAI METRO RAIL PHASE-II DEVELOPMENT PROJECT	63,246		35,228	56.53
2	702635	CONSTRUCTION OF BANGALORE METRO RAIL PROJECT PHASE 2.	26,405	30,695	29,845	96
3	702632	DMRTS PHASE - IV [3 PRIORITY CORRIDORS]	24,949		21,686	84.28
4	612878	BANGALORE METRO RAIL PROJECT - PHASE-3	15,611		0	3.9
5	702665	CONSTRUCTION BANGALORE METRO RAIL PROJECT PHASE-2A & 2B	14,788	14,788	11,079	68

HML Category 2 : Energy

AUGUST 2026

223
Ongoing Projects

₹ 10,02,085
Original Cost
(crores)


₹ 10,94,597
Revised Cost
(crores)

₹ 4,52,284
(41.32% of Revised Cost)
Cumulative Expenditure
(crores)


1
Commissioned during month

19
Newly Added during month

Cost Analytics : All Sectors

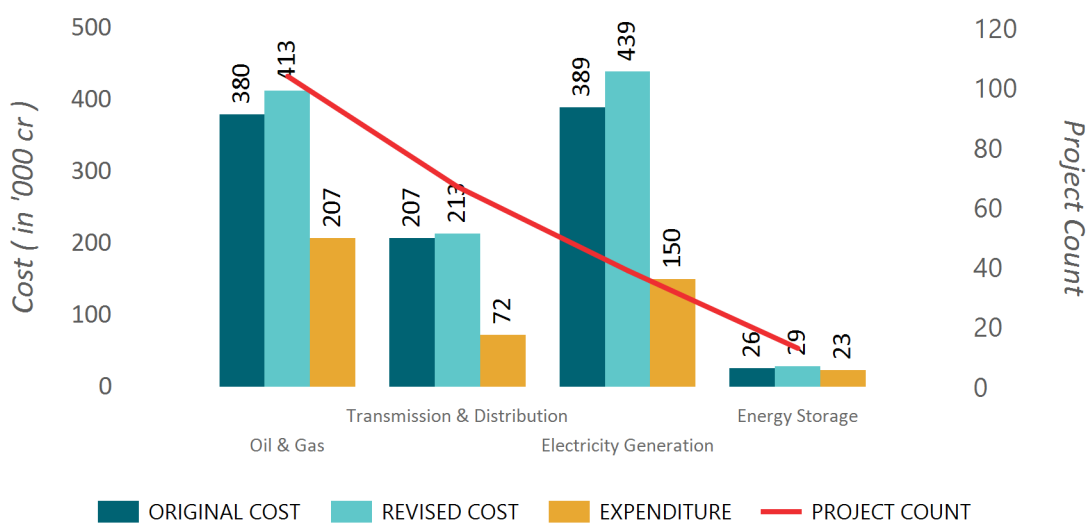

Cumulative Physical & Financial progress (%) : Project count

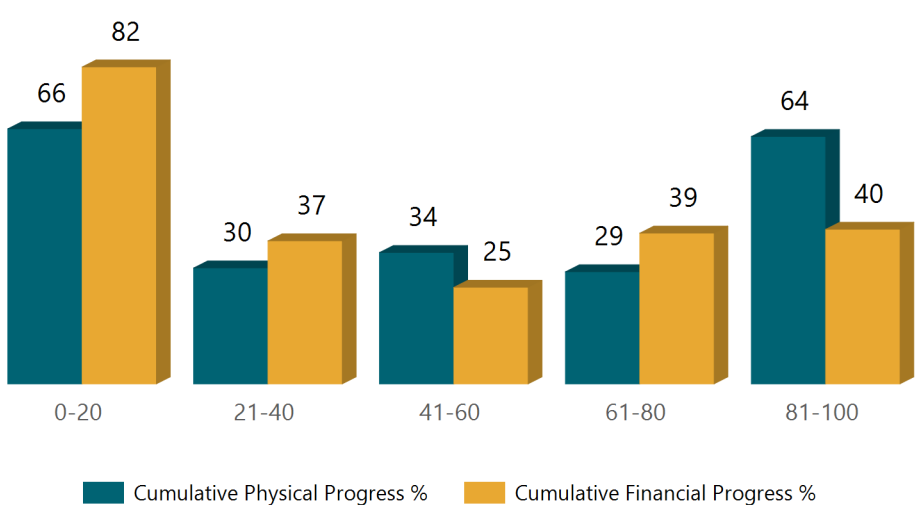

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Oil & Gas	104	379,840	412,878	206,955
2	Transmission & Distribution	67	207,446	213,410	72,153
3	Electricity Generation	39	389,214	439,436	149,819
4	Energy Storage	13	25,585	28,874	23,358

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	6,689	36.6
2	298178	MEJA THERMAL POWER PROJECT, STAGE-II , (3X800 MW)	38,358		1,028	0.11
3	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	28,279	94.7
4	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,199	97
5	602182	DIBANG MULTIPURPOSE PROJECT	31,876		5,119	18.12

HML Category 3 : Water & Sanitation

AUGUST 2026

53
Ongoing Projects



₹ 1,04,277
Original Cost
(crores)

₹ 2,03,701
Revised Cost
(crores)

₹ 1,45,681
(71.52% of Revised Cost)
Cumulative Expenditure
(crores)

0
Commissioned during month

0
Newly Added during month

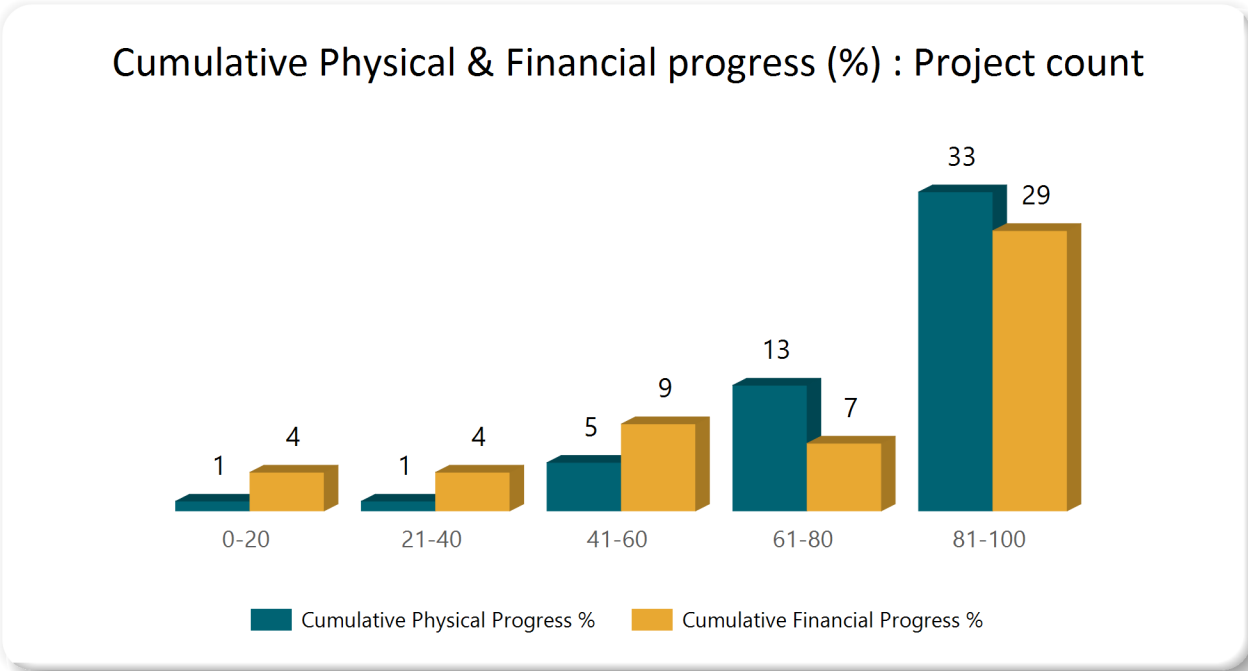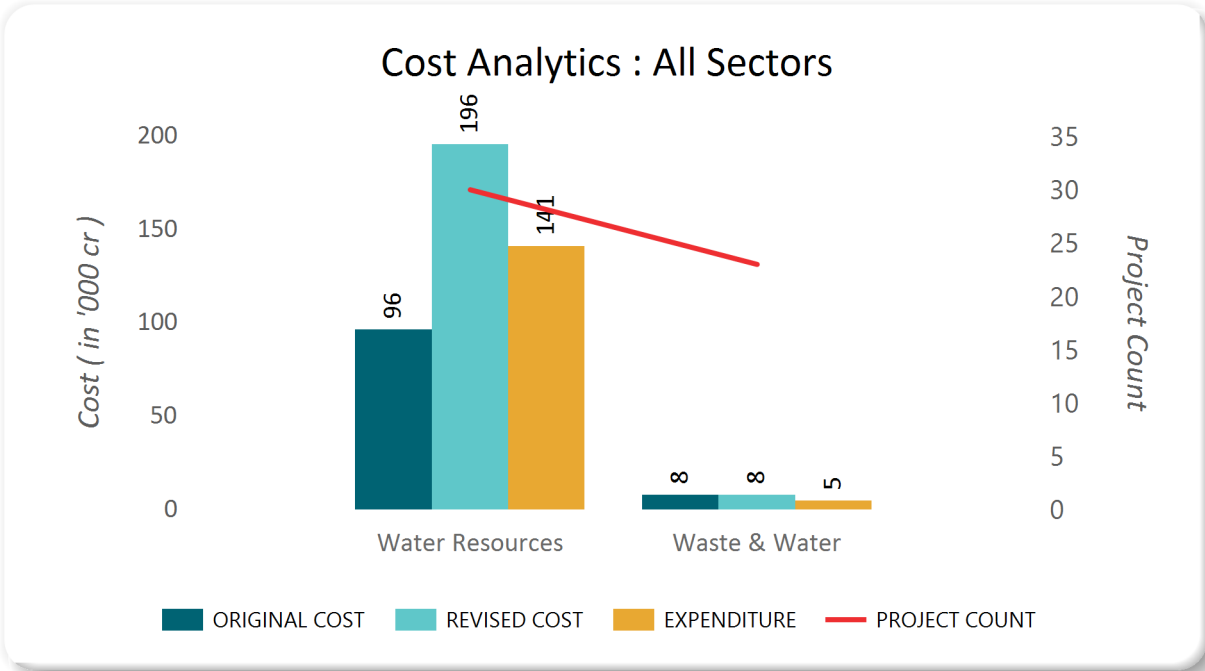

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Water Resources	30	96,487	195,812	140,895
2	Waste & Water	23	7,790	7,889	4,786

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701530	KEN-BETWA LINKING DEVELOPMENT PROJECT	21,030		8,531	0
2	701372	SARDAR SAROVAR PROJECT	20,718	33,413	31,987	93.7
3	701415	POLAVARAM IRRIGATION PROJECT	10,151	55,549	28,159	86.2
4	701405	J. CHOKKA RAO DEVADULA LIFT IRRIGATION SCHEME	8,201	13,445	4,841	87.7
5	701386	GOSIKHURD PROJECT	7,196	12,770	14,439	72.65



HML Category 4 : Communication

AUGUST 2026

31
Ongoing Projects

₹ 1,58,795
Original Cost
(crores)


₹ 1,33,825
Revised Cost
(crores)

₹ 64,410
(48.13% of Revised Cost)
Cumulative Expenditure
(crores)


0
Commissioned during month

0
Newly Added during month

Cost Analytics : All Sectors

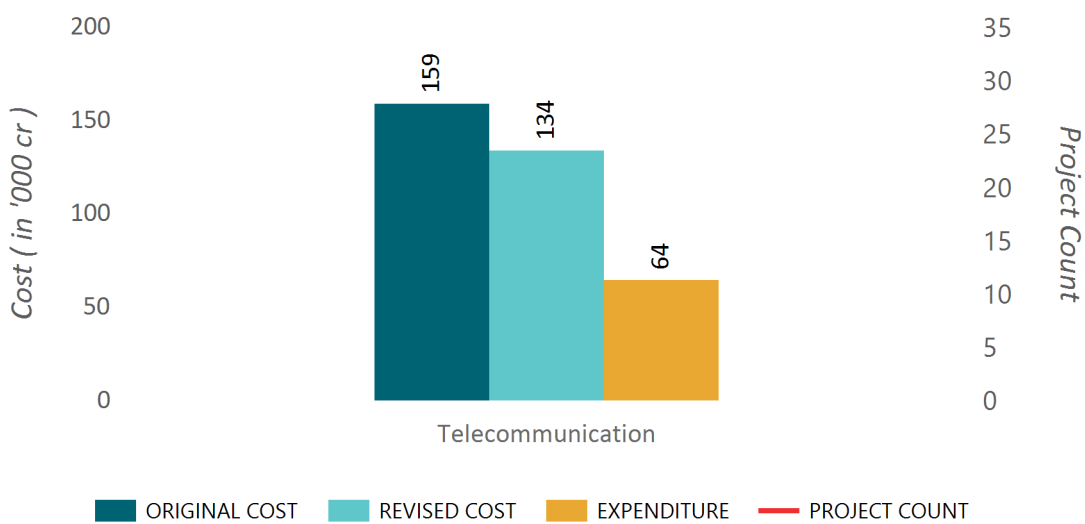

Cumulative Physical & Financial progress (%) : Project count

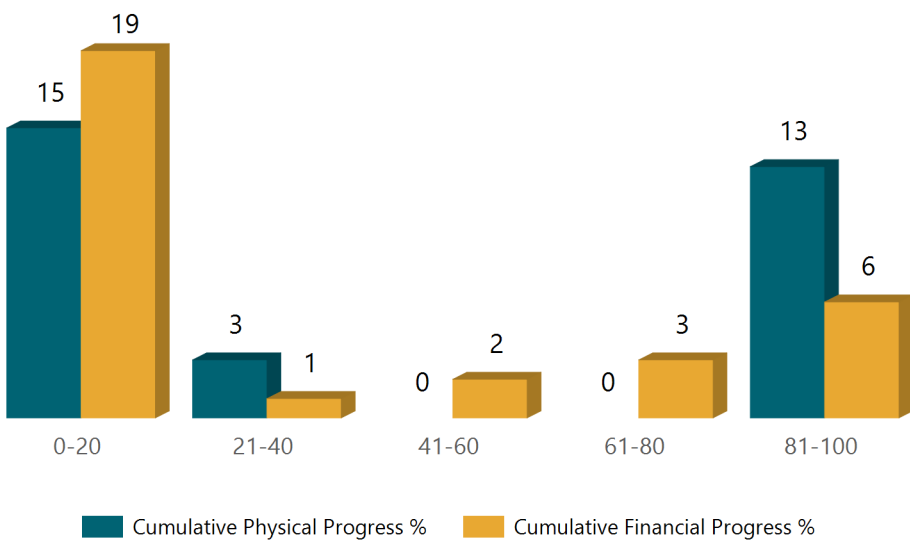

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Telecommunication	31	158,795	133,825	64,410

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	701593	4G SERVICES BY BSNL	28,466	19,592	9,173	98.63
2	400013	SATURATION 4G MOBILE COVERAGE OF UNCOVERED VILLAGES THROUGH USOF	26,316	15,393	8,723	89.4
3	709857	PLANNING, ENGINEERING, SUPPLY, INSTALLATION, TESTING, COMMISSIONING, INTEGRATION & ANNUAL MAINTENANCE OF 4G MOBILE NETWORK AT 1 LAKH SITES ON PAN INDIA BASIS INCLUDING MUMBAI & DELHI LSA ON TURNKEY BASIS UNDER PHASE IX.2 PROJECT.	24,545		9,174	98.63
4	547243	BHARATNET PHASE-II	22,175		20,692	93.33
5	706775	BHARATNET	12,709	12,709	10,320	99.98

HML Category 5 : Social & Commercial

AUGUST 2026

81

Ongoing Projects

₹ 91,573

Original Cost
(crores)

₹ 96,665

Revised Cost
(crores)

₹ 37,676



(38.98% of Revised Cost)
Cumulative Expenditure
(crores)

2

Commissioned during month

4

Newly Added during month

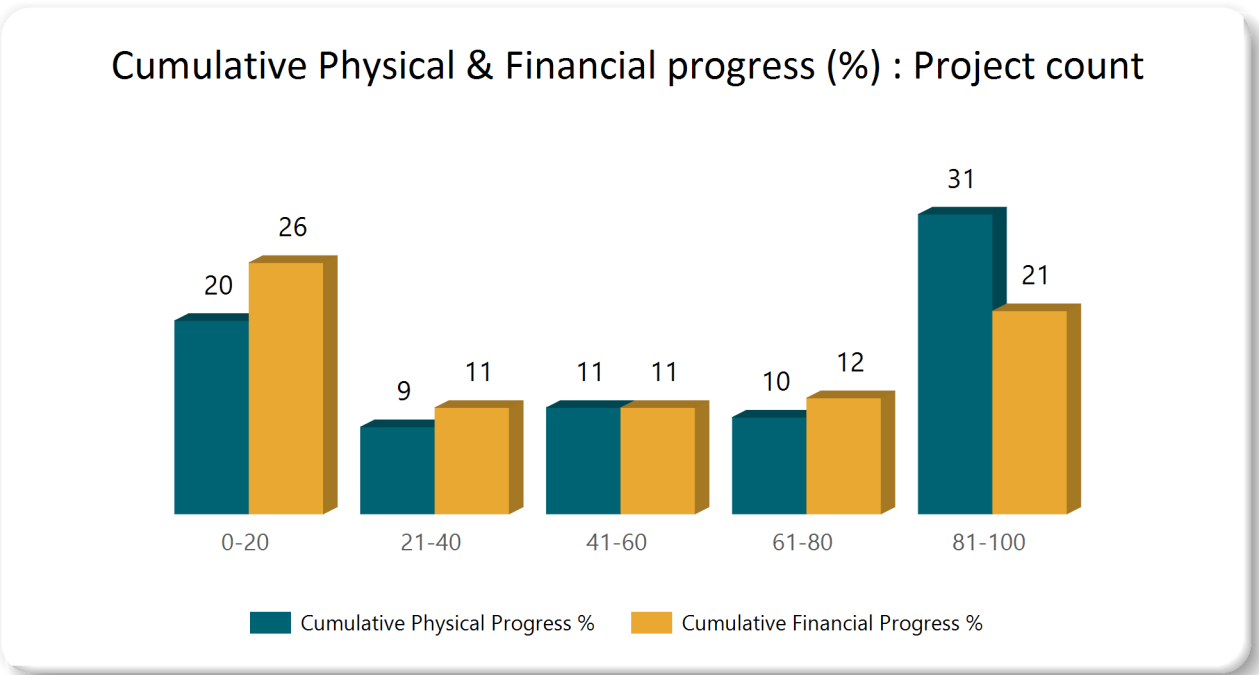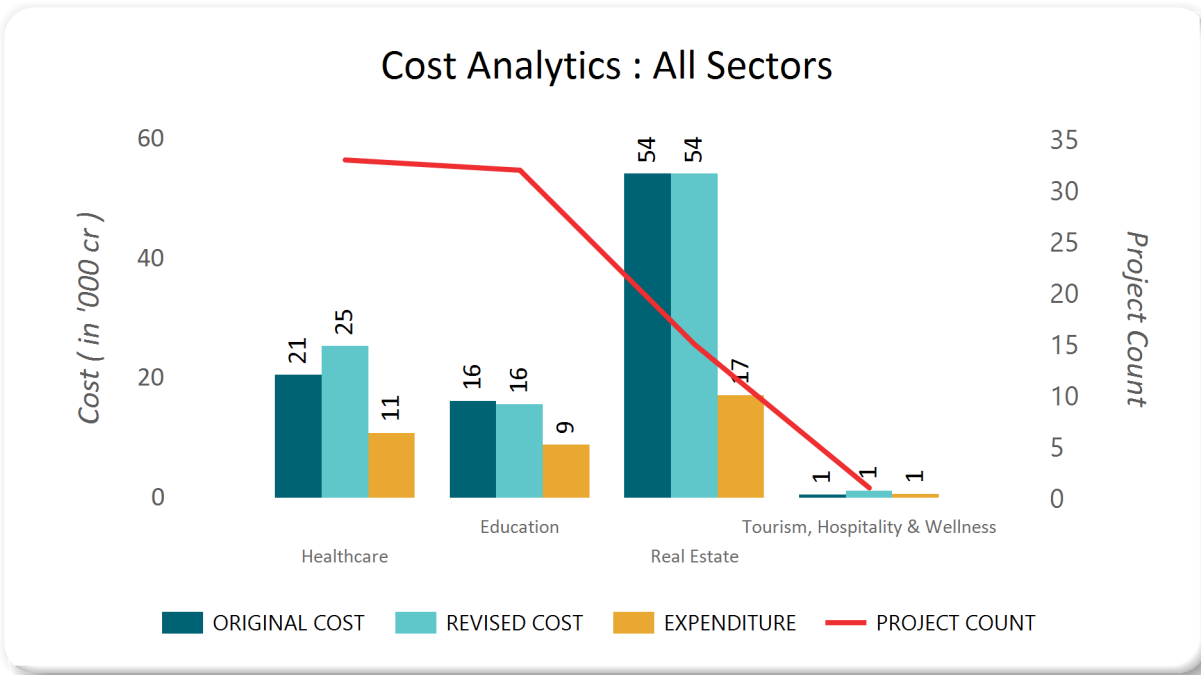

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Healthcare	33	20,619	25,444	10,887
2	Education	32	16,152	15,688	8,926
3	Real Estate	15	54,230	54,296	17,189
4	Tourism, Hospitality & Wellness	1	573	1,238	674

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400188	REDEVELOPMENT OF SEVEN GENERAL POOL RESIDENTIAL ACCOMMODATION [GPRA] COLONIES IN DELHI	32,850	32,841	14,370	46.7
2	617883	REDEVELOPMENT OF RESIDENTIAL COLONIES AT AYUR VIGYAN NAGAR AND WEST ANSARI NAGAR CAMPUSES OF AIIMS, NEW DELHI	4,441		44	57
3	701668	DEVELOPMENT OF PALAKKAD NODE UNDER EXTENSION OF CBIC TO KOCHI	3,805		59	5.37
4	617727	ORVAKAL INDUSTRIAL AREA	2,786		446	18.14
5	601812	DEVELOPMENT OF ZAHEERABAD NODE UNDER HYDERABAD NAGPUR INDUSTRIAL CORRIDOR	2,360		63	5.72

Other Sectors

AUGUST 2026

152
Ongoing Projects

₹ 2,20,580
Original Cost
(crores)


₹ 2,26,289
Revised Cost
(crores)

₹ 71,292
(31.5% of Revised Cost)
Cumulative Expenditure
(crores)

0
Commissioned during month

3
Newly Added during month

Cumulative Physical & Financial progress (%) : Project count

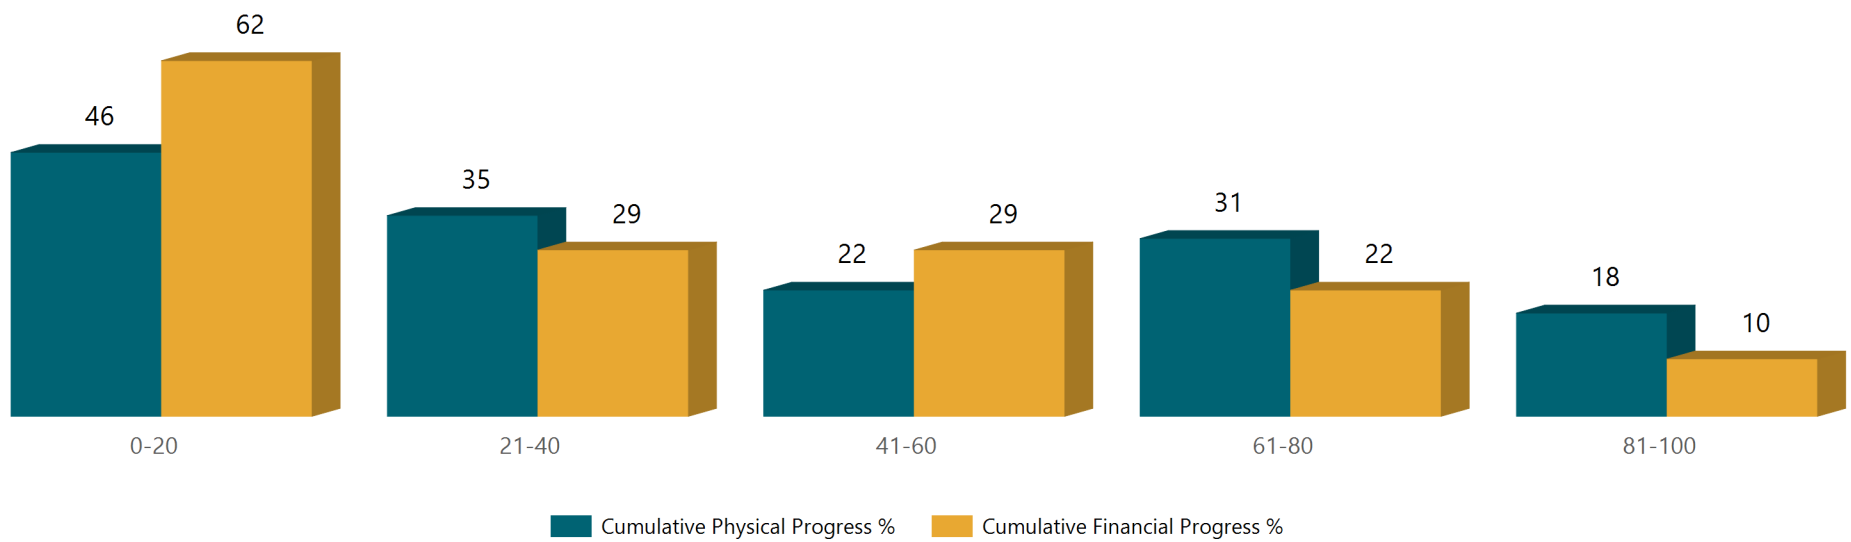

Sector - Overview

S.NO.	SECTOR NAME	PROJECT COUNT	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)
1	Coal	116	184,952	182,926	49,817
2	Steel	26	24,625	28,207	13,364
3	Metals & Mining	8	10,104	14,258	7,807
4	Construction	2	899	899	305

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	619032	JAYANT EXPN. [20 TO 38 MTPA]	25,560		425	2.63
2	400424	GEVRA OC [70 MTY]	11,816		6,985	78.48
3	400185	GOPALJI KANIHA OCP [10 TO 30 M	8,416	6,108	1,780	36.01
4	400150	RPR MAGADH EXP OCP	6,964		1,880	39.48
5	617416	REVISED JHARIA MASTER PLAN FOR DEALING WITH FIRE, SUBSIDENCE & REHABILITATION OF AFFECTED FAMILIES IN JHARIA COALFIELD- REG.	5,940		521	34



Major Infrastructure Central Ministries & Departments





Ministry of Road Transport & Highways

AUGUST 2026

982

Ongoing Projects

₹ 9,37,452

Original Cost
(crores)

₹ 9,51,926

Revised Cost
(crores)

₹ 5,10,396

(53.62% of Revised Cost)
Cumulative Expenditure
(crores)

376 | ₹ 638,341

Mega Projects
Count | Original Cost (crores)

606 | ₹ 299,112

Major Projects
Count | Original Cost

42


Commissioned during month

10

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

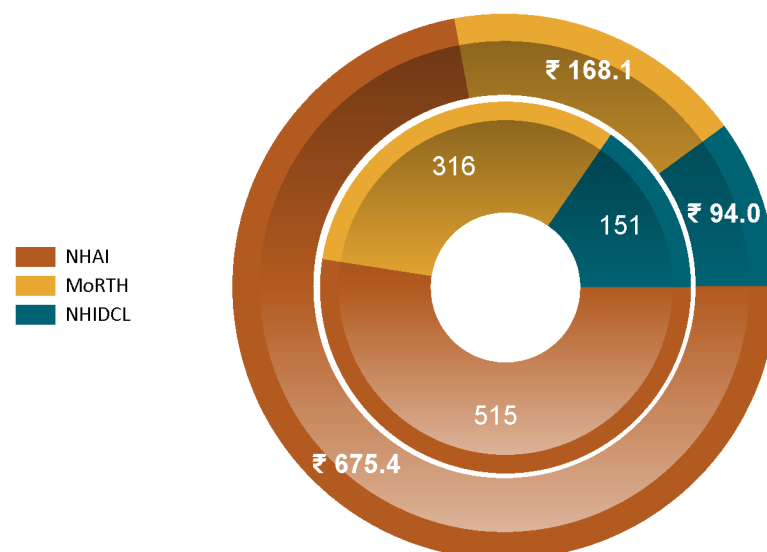


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Cumulative Physical & Financial progress (%) : Project count

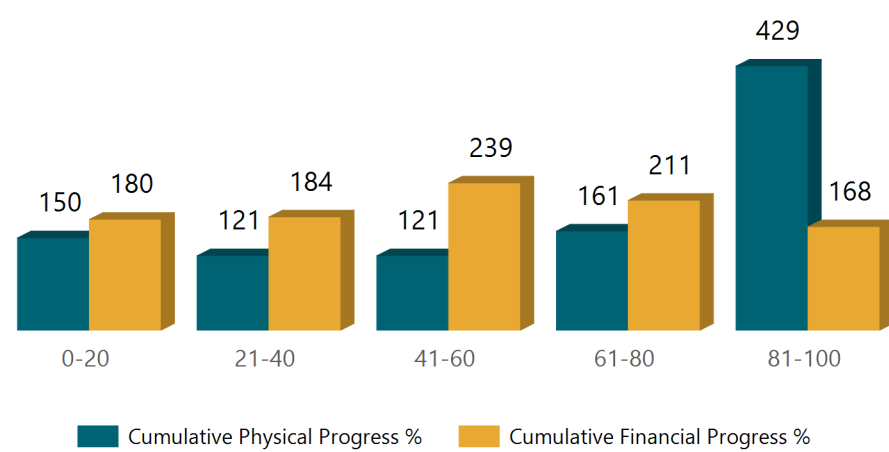

Cost Analytics : Major Sectors*

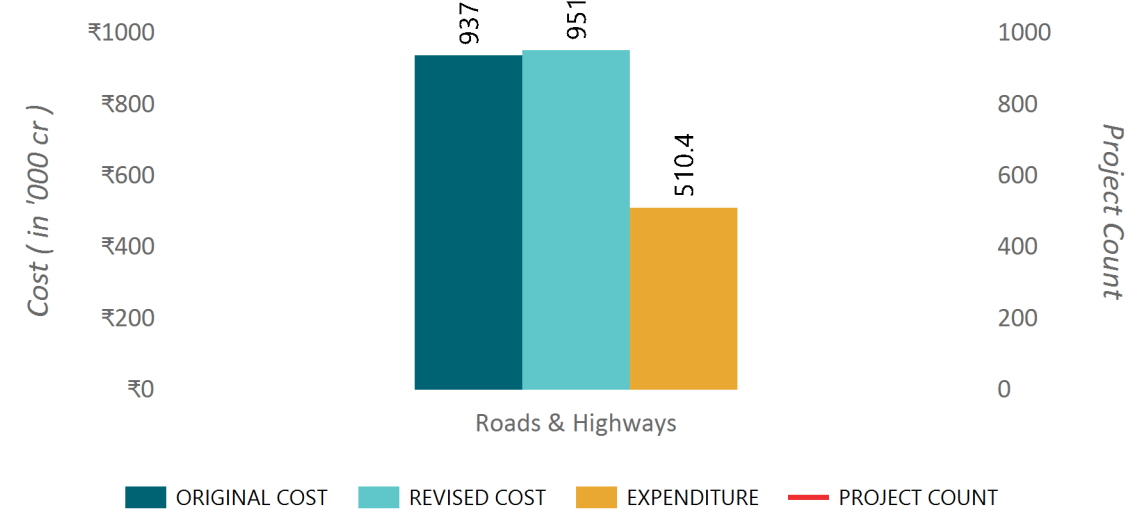

State Comparison : Major States*

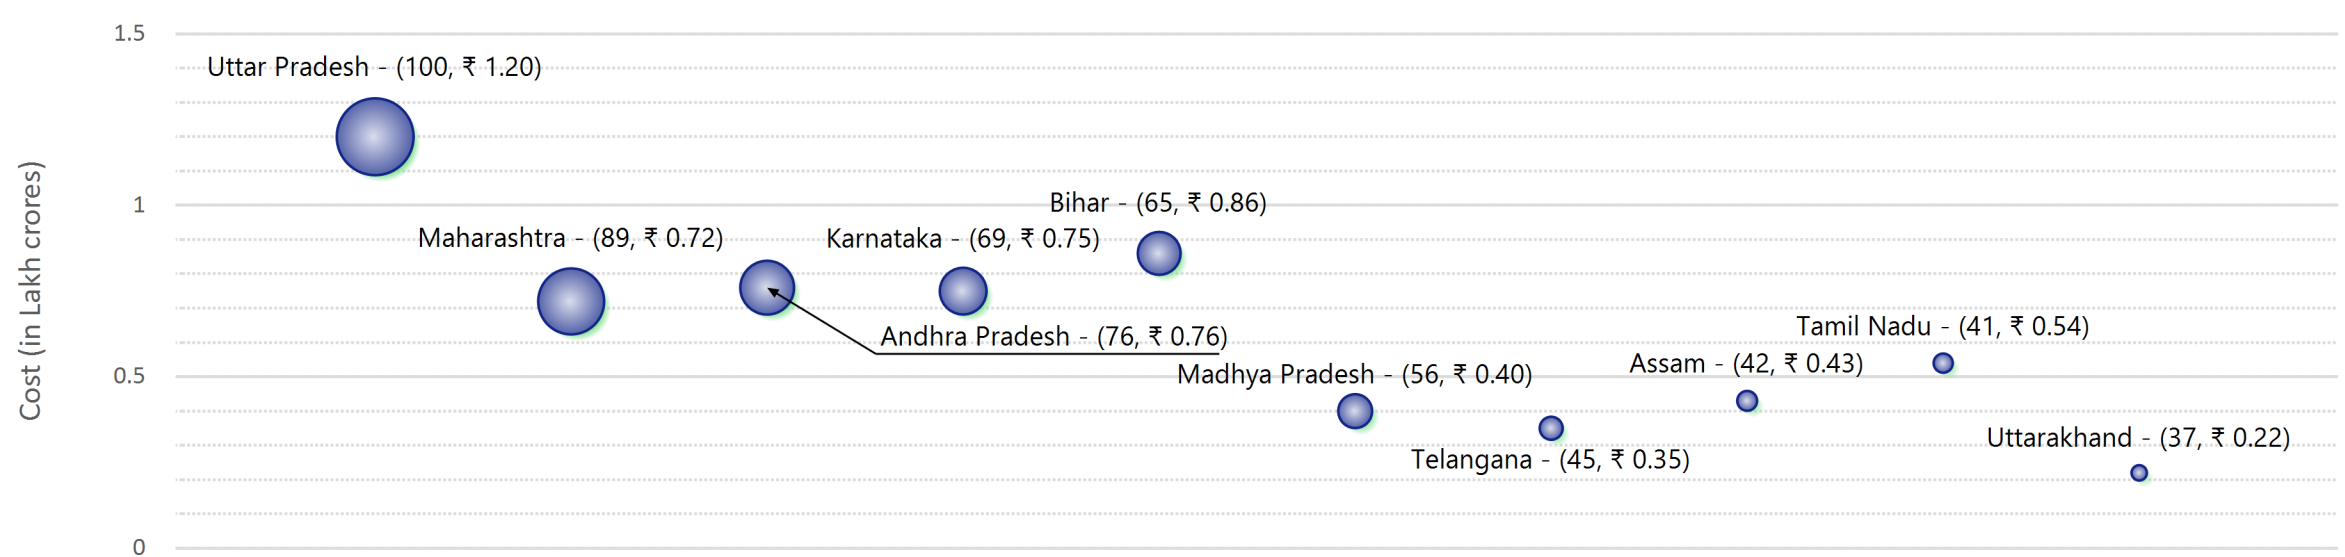

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	618412	CONSTRUCTION OF I CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL ROAD LENGTH 18.475KM AND II 14.150 KM LONG 2-L BI-DIRECTIONAL SINGLE TUBE ZOJI-LA TUNNEL ACROSS ZOJILA PASS ON SONAMARG - KARGIL SECTION FROM KM 82 TO KM 118 OF NH-01 UNDER PMDP	6,809	6,809	3,583	68.8
2	618738	6L BRIDGE AND ITS APPROACHES ACROSS RIVER GANGA AS PART OF PATNA RING ROAD NH-131G STARTING FROM KM 8.480 NEAR SHERPUR TO KM 23.000 NEAR DIGHWARA	6,292	3,352	769	22.05
3	618934	GUWAHATI RING ROAD IN THE STATE OF ASSAM	5,729	5,729	365	1.3
4	618373	CONSTRUCTION OF 4-LANE BRIDGE INCLUDING APPROACHES OVER RIVER BRAHMAPUTRA BETWEEN DHUBRI ON NORTH BANK,ASSAM AND PHULBARI ON SOUTH BANK,MEGHALAYA ON NH-127B UNDER JICA ODA LOAN ASSISTANCE PHASE-III	4,997	4,997	3,133	79.36
5	618599	6L OF RAMANATUKKARA JUNCTION TO START OF VALANCHERY BYPASS SECTION OF NH-66	4,919	4,919	3,764	100



Ministry of Railways

AUGUST 2026

147

Ongoing Projects

₹ 2,25,802

Original Cost
(crores)

₹ 3,14,235

Revised Cost
(crores)

₹ 1,85,840

(59.14% of Revised Cost)
Cumulative Expenditure
(crores)

71 | ₹ 187,522

Mega Projects
Count | Original Cost (crores)

76 | ₹ 38,280

Major Projects
Count | Original Cost

0


Commissioned during month

0

Newly Added during month

Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

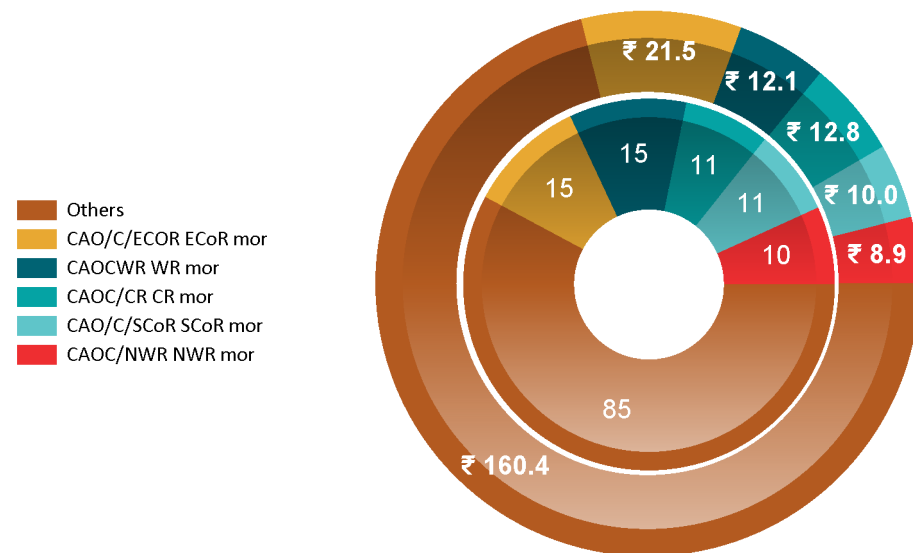


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]




Cumulative Physical & Financial progress (%) : Project count

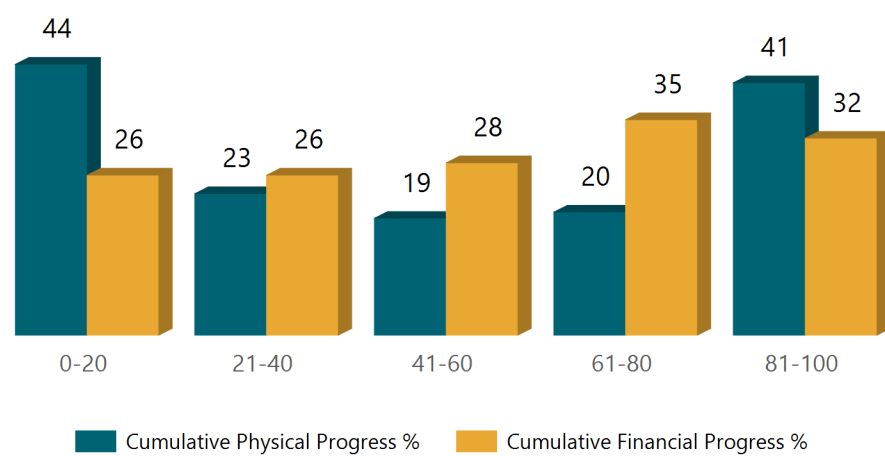

Cost Analytics : Major Sectors*

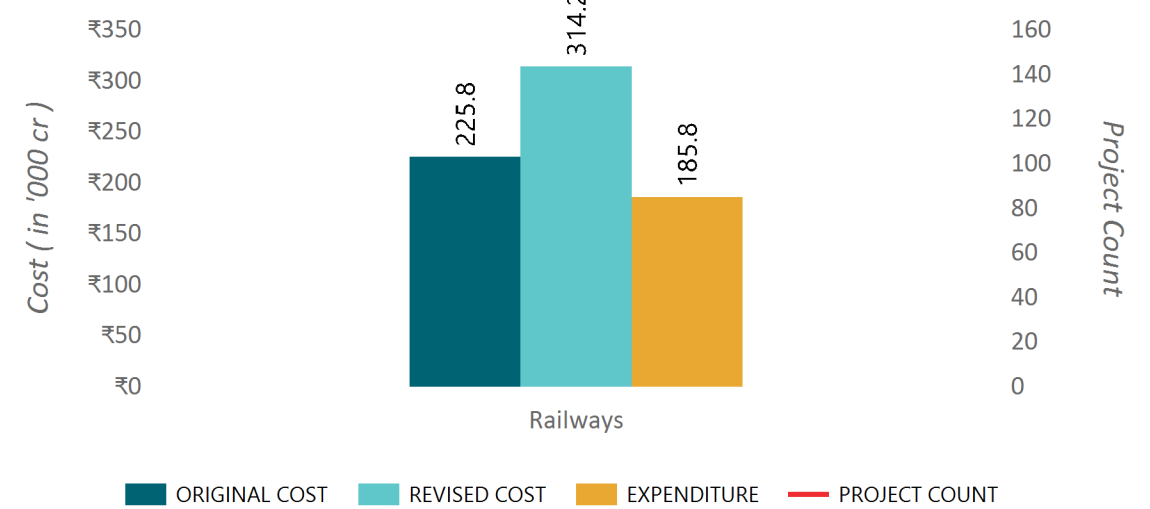

State Comparison : Major States*

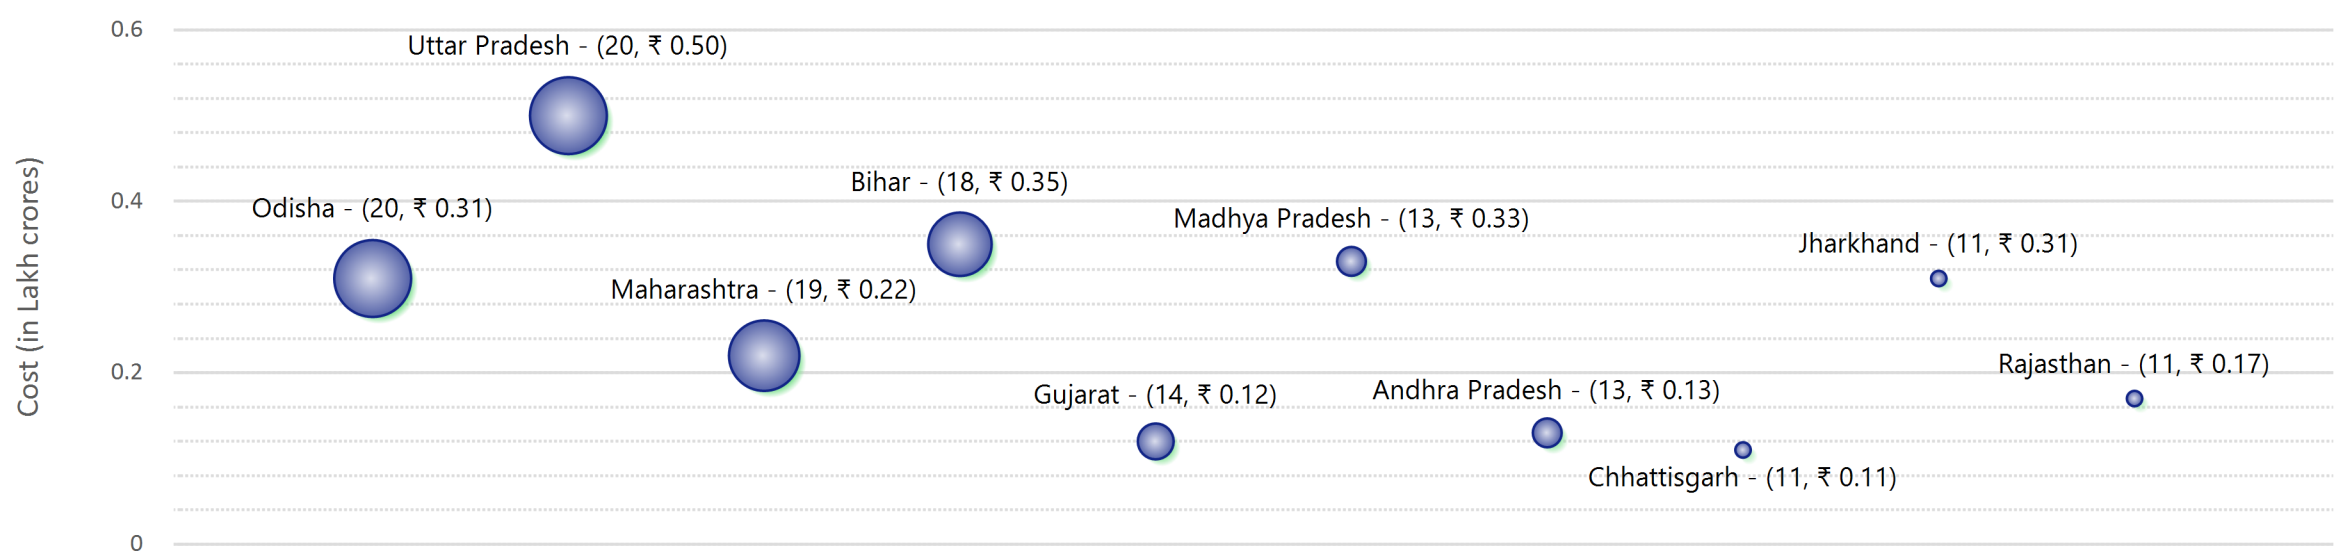

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	705391	JIRIBAM-IMPHAL 110 KM	14,323	21,886	16,932	78
2	616699	MULTI TRACKING OF SON NAGAR-ANDAL 374.53 RKM & 814.38 TKM PB34/ECOR/2023-24	12,334	12,334	1,351	3
3	705480	LALITPUR-SATNA, REWA-SINGRAULI & MAHOBA-KHAJURAHO 541 KM	8,914	8,914	6,695	73
4	705392	DIMAPUR-KOHIMA 88 KM	6,663	15,310	6,891	48
5	705667	MATHURA-JHANSI - 3RD LINE 273.80 KM	5,961	5,961	5,725	94



Ministry of Coal

AUGUST 2026

122

Ongoing Projects

₹ 2,23,137

Original Cost
(crores)

₹ 2,22,345

Revised Cost
(crores)

₹ 57,789

(25.99% of Revised Cost)
Cumulative Expenditure
(crores)

41 | ₹ 183,146

Mega Projects
Count | Original Cost (crores)

81 | ₹ 39,990

Major Projects
Count | Original Cost

0


Commissioned during month

1

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

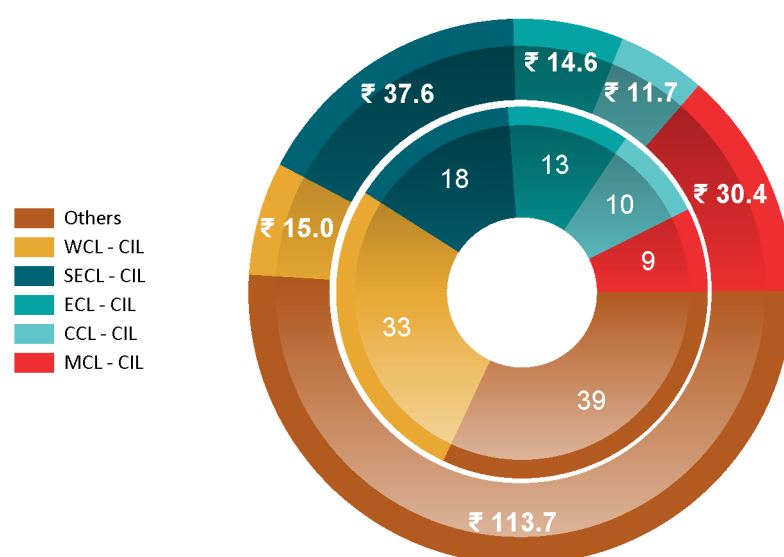


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

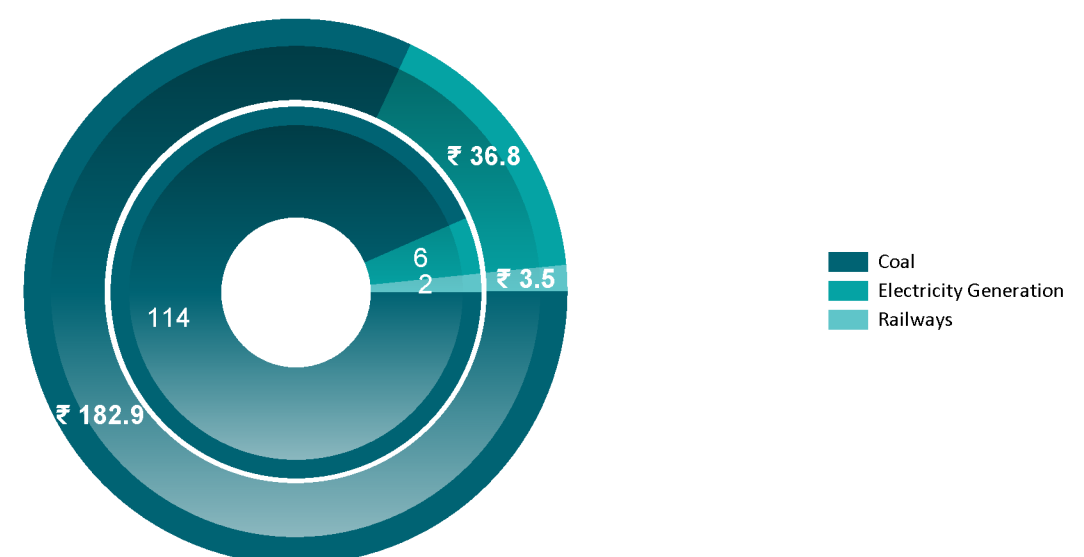


Cumulative Physical & Financial progress (%) : Project count

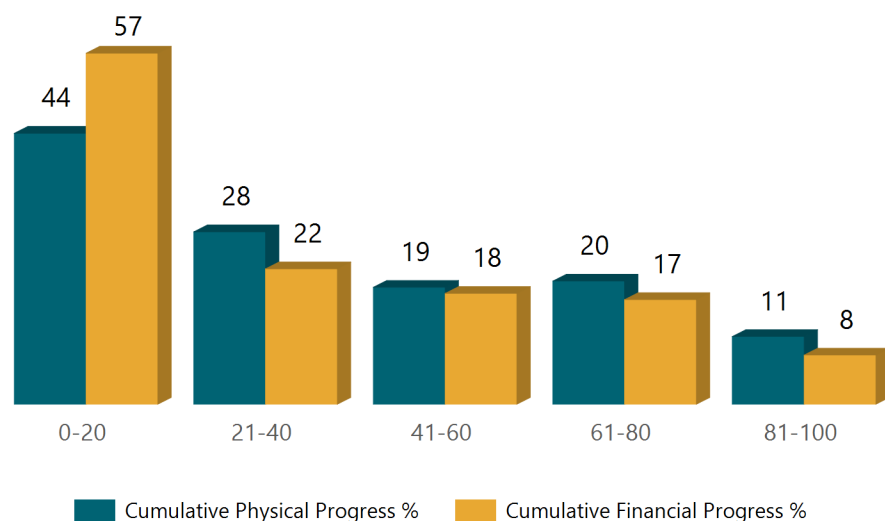

Cost Analytics : Major Sectors*

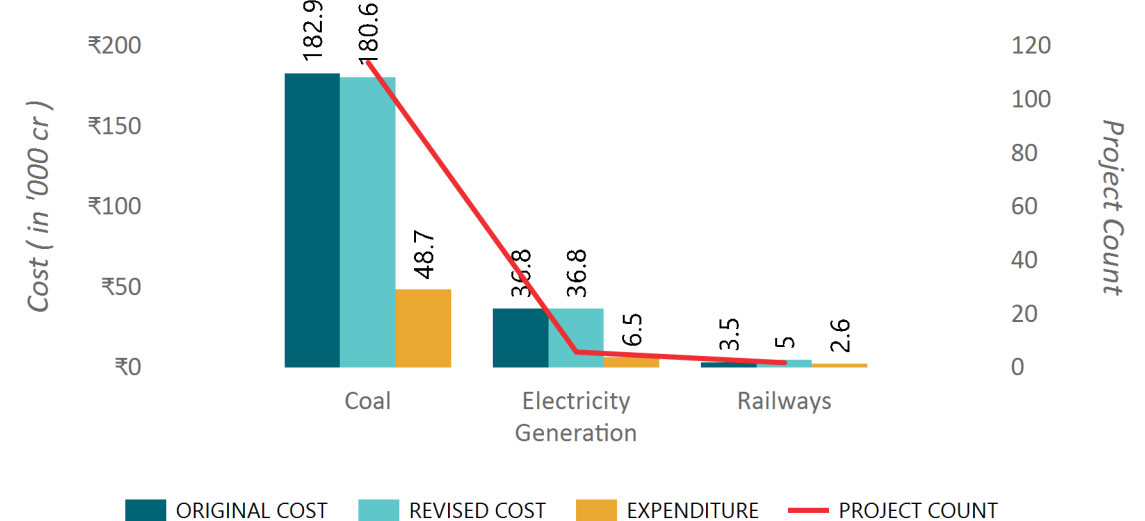

State Comparison : Major States*

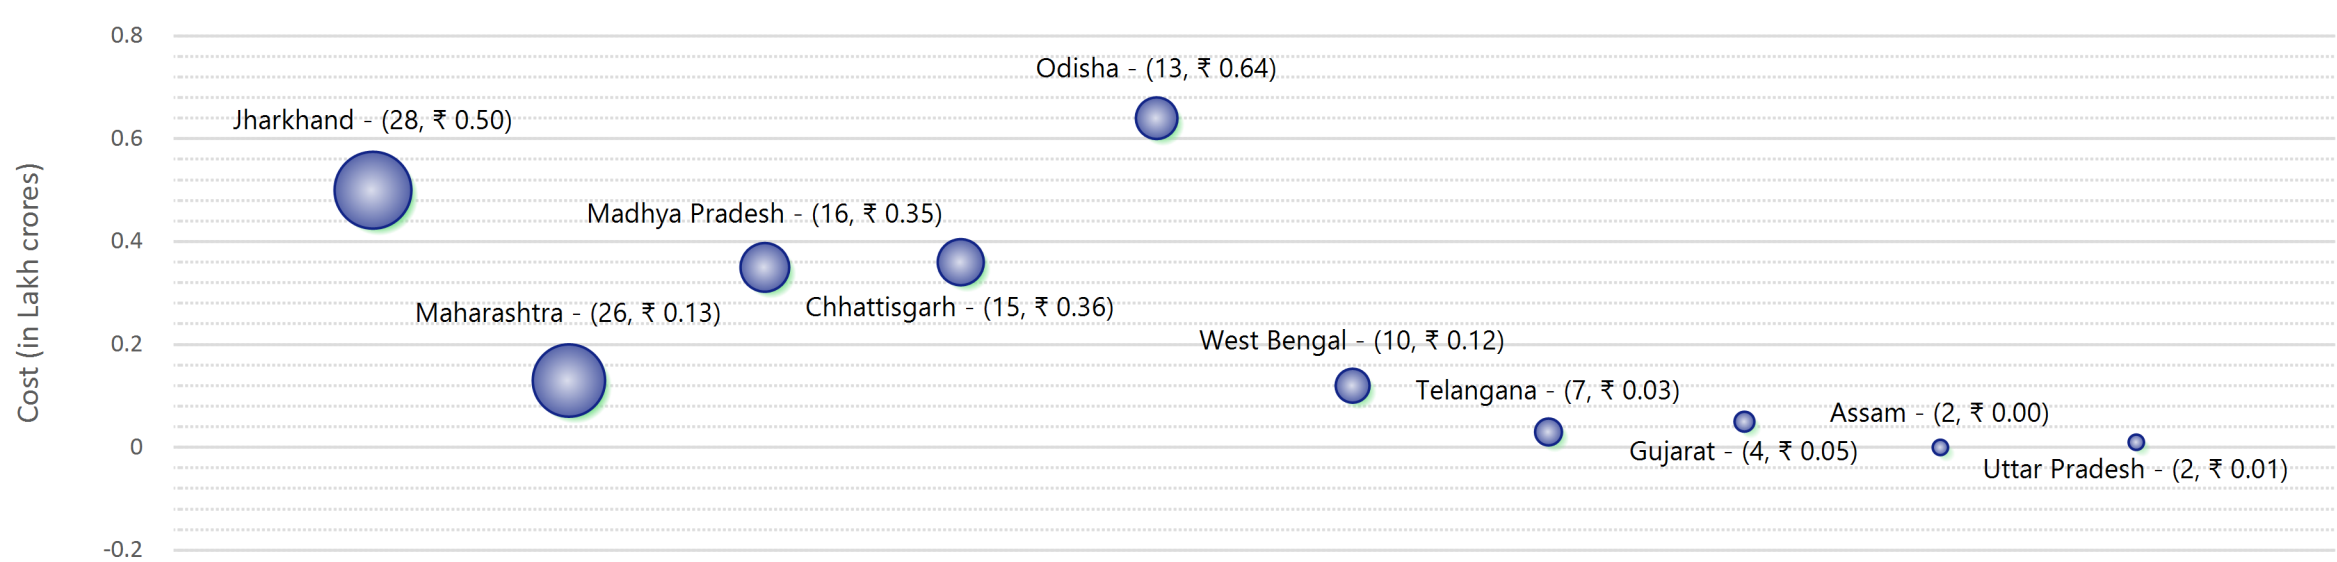

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	400231	NLC TALABIRA THERMAL POWER PROJECT	27,213	27,213	3,606	4.1
2	619032	JAYANT EXPN. [20 TO 38 MTPA]	25,560	25,560	425	2.63
3	400424	GEVRA OC [70 MTY]	11,816	11,816	6,985	78.48
4	400185	GOPALJI KANIHA OCP [10 TO 30 M]	8,416	6,108	1,780	36.01
5	400150	RPR MAGADH EXP OCP	6,964	6,964	1,880	39.48



Ministry of Petroleum & Natural Gas

AUGUST 2026

117

Ongoing Projects

₹ 4,05,425

Original Cost
(crores)

₹ 4,41,752

Revised Cost
(crores)

₹ 2,30,313

(52.14% of Revised Cost)
Cumulative Expenditure
(crores)

47 | ₹ 375,864

Mega Projects
Count | Original Cost (crores)

70 | ₹ 29,561

Major Projects
Count | Original Cost

1


Commissioned during month

15

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

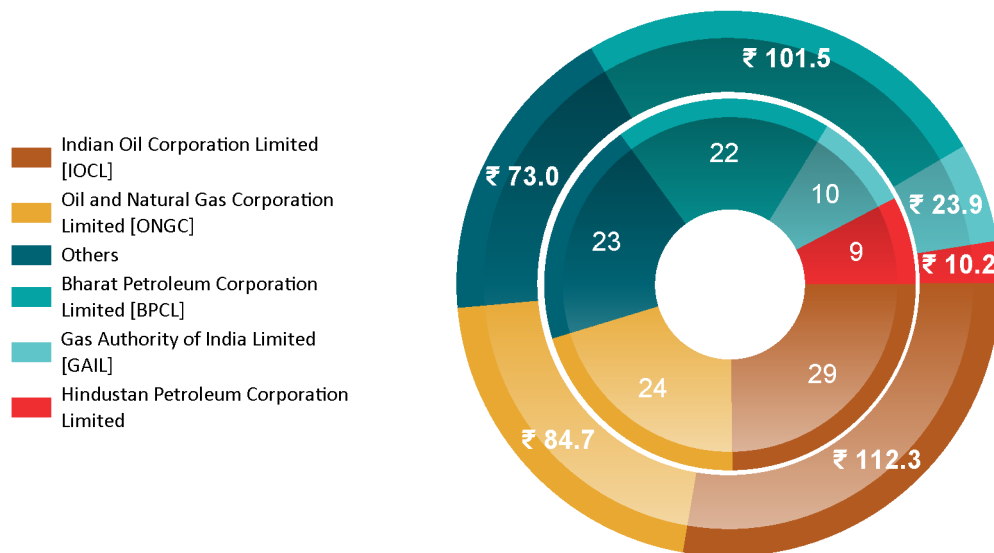


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

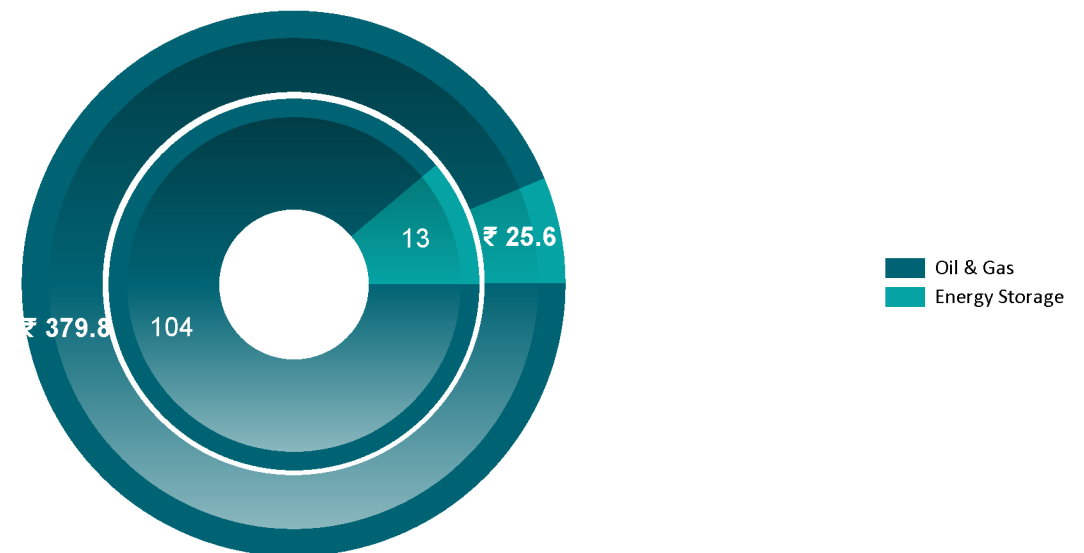


Cumulative Physical & Financial progress (%) : Project count

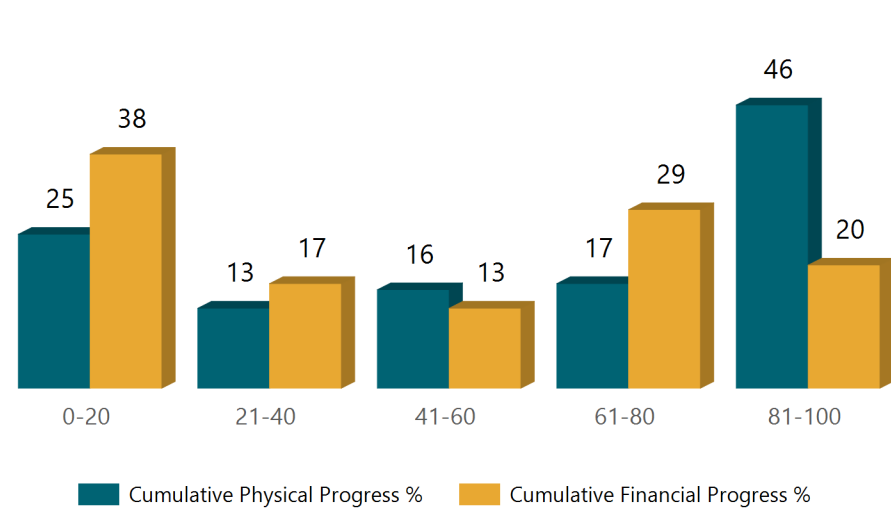

Cost Analytics : Major Sectors*

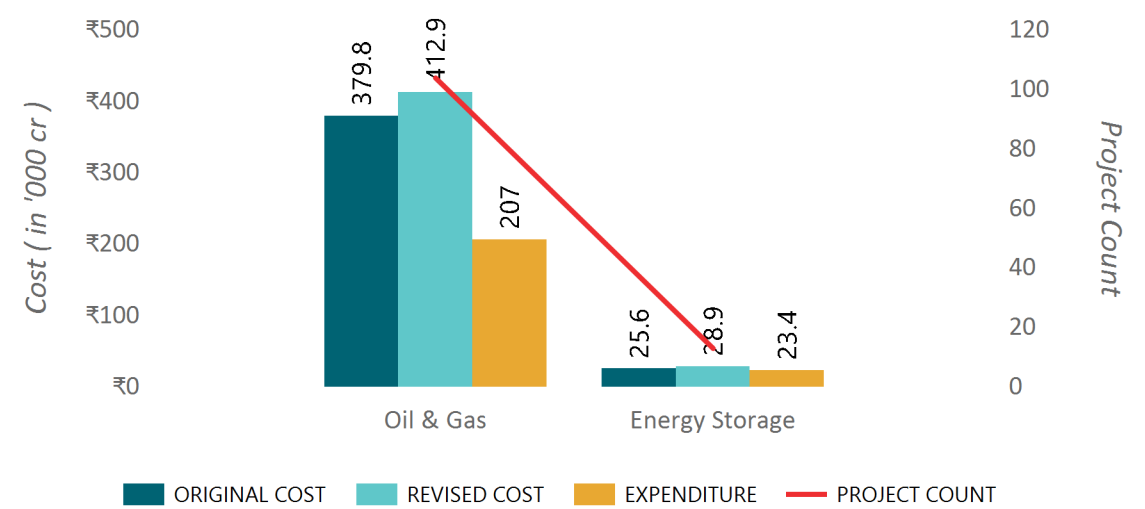

State Comparison : Major States*

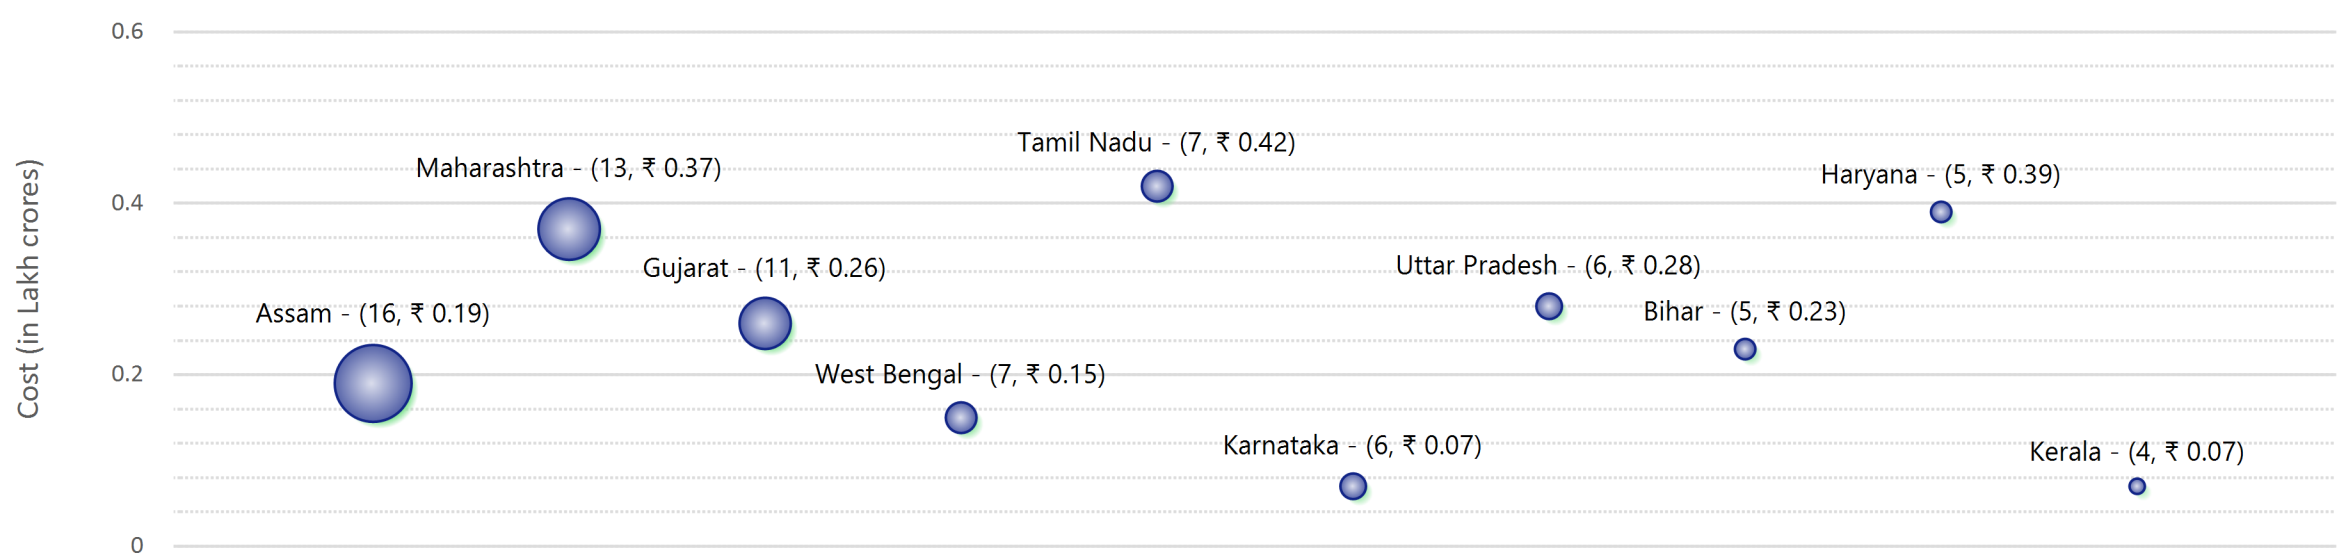

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRES (%)S
1	709798	ETHYLENE CRACKER PROJECT AT BINA REFINERY INCLUDING DOWNSTREAM PETROCHEMICAL PLANTS AND EXPANSION OF REFINERY	43,367	43,367	6,689	36.6
2	701289	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA	34,627	36,225	28,279	94.7
3	400120	KG-DWN-98/2 CLUSTER - II DEVELOPMENT PROJECT - NELP BLOCK	34,012	34,012	33,199	97
4	604795	CBR 9 MMTPA PROJECT	31,580	36,354	1,616	10.2
5	701329	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	18,936	17,825	13,954	89.9



Ministry of Power

AUGUST 2026

102

Ongoing Projects

₹ 5,61,962

Original Cost
(crores)

₹ 6,18,429

Revised Cost
(crores)

₹ 2,16,577

(35.02% of Revised Cost)
Cumulative Expenditure
(crores)

73 | ₹ 549,751

Mega Projects
Count | Original Cost (crores)

29 | ₹ 12,210

Major Projects
Count | Original Cost

0


Commissioned during month

4

Newly Added during month


Agency Comparison : Major Agencies*

[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

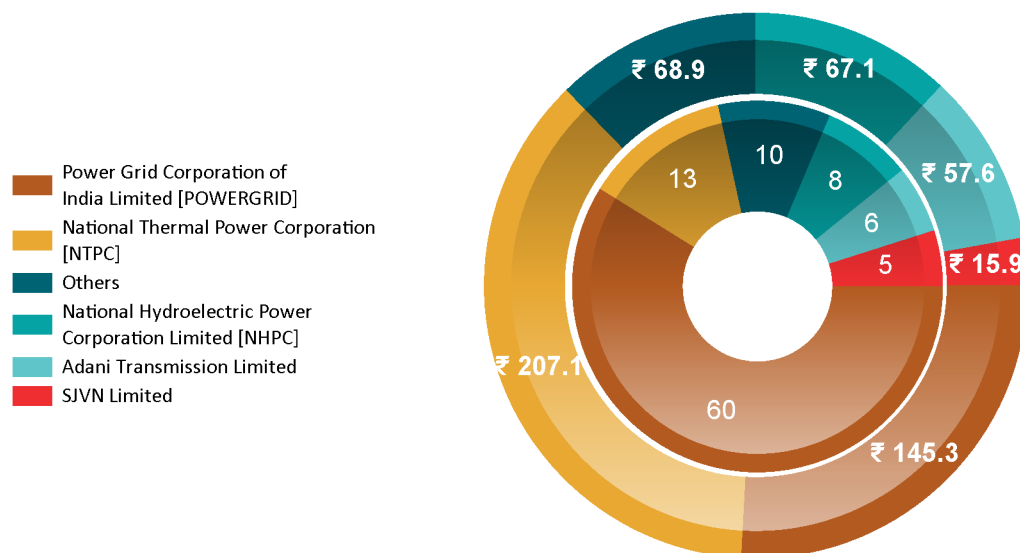


Sectoral Comparison : Major Sectors*


[Outer Ring : Original Cost in ₹ Thousand crore] & [Inner Ring : Project Count]

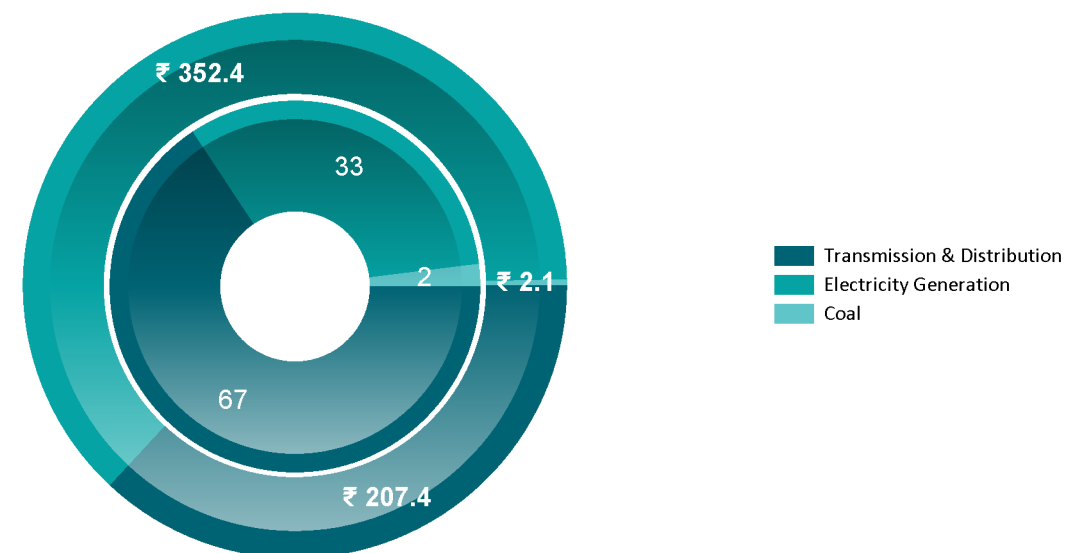


Cumulative Physical & Financial progress (%) : Project count

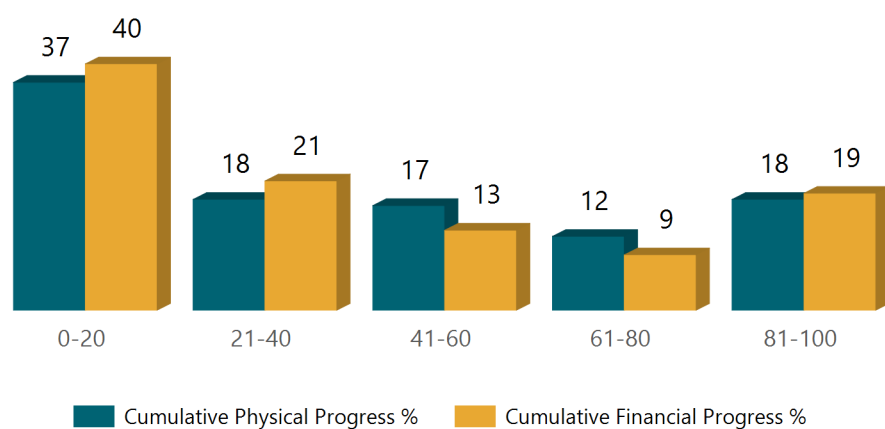

Cost Analytics : Major Sectors*

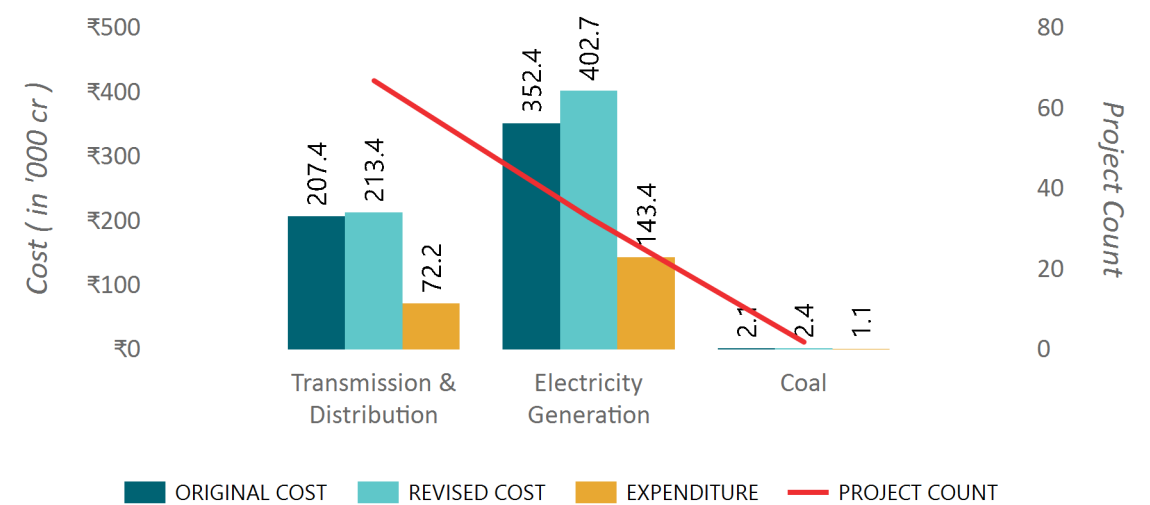

State Comparison : Major States*

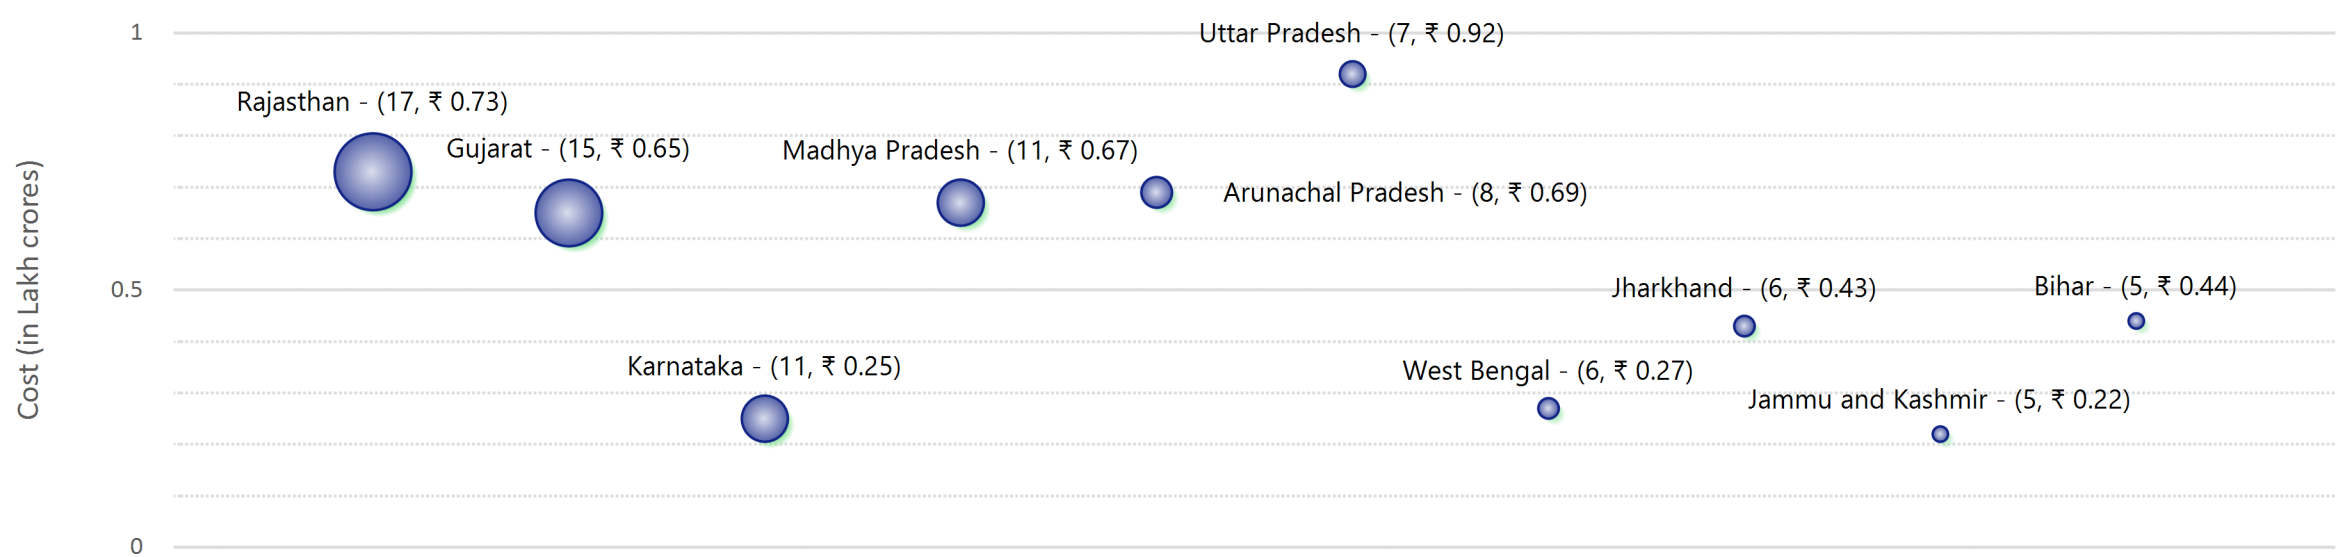

Note: all indicated legends are in format (Sector, Project count : bubble size, Original Cost in lakh crores)
Note: * as per Project Count

Major On-going Projects Monitored under PAIMANA

S.NO.	PROJECT ID	PROJECT NAME	ORIGINAL COST (₹ crores)	REVISED COST (₹ crores)	EXPENDITURE (₹ crores)	PHYSICAL PROGRESS (%)
1	298178	MEJA THERMAL POWER PROJECT, STAGE-II , (3X800 MW)	38,358	38,358	1,028	0.11
2	602182	DIBANG MULTIPURPOSE PROJECT	31,876	31,876	5,119	18.12
3	619051	NABINAGAR SUPER THERMAL POWER PROJECT, STAGE-II [3X800 MW]	29,948	29,948	3,677	16
4	619341	TELANGANA SUPER THERMAL POWER PROJECT , STAGE-II [3 X 800 MW]	29,345	29,345	734	1.04
5	619025	RAJASTHAN PART I POWER TRANSMISSION LIMITED	25,000	25,000	805	12



List of Tables




Table 1: Ministry-wise Ongoing Projects





Ministry-wise Ongoing Projects

AUGUST 2026

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Department for Promotion of Industry & Internal Trade	Logistics Infrastructure	1	763.00 (0.00)	430.00
		Real Estate	11	20,480.02 (0.00)	2,094.58
		Total	12	21,243.02 (0.00)	2,524.58
2	Department of Higher Education	Education	31	15,245.61 (0.00)	8,348.85
		Total	31	15,245.61 (0.00)	8,348.85
3	Department of Sports	Education	1	906.47 (0.00)	577.32
		Total	1	906.47 (0.00)	577.32
4	Department of Telecommunications	Telecommunication	31	158,794.71 (0.00)	64,410.07
		Total	31	158,794.71 (0.00)	64,410.07
5	Department of Water Resources, River Development & GR	Waste & Water	8	4,039.12 (0.00)	1,833.61
		Water Resources	30	96,487.38 (0.00)	140,895.38
		Total	38	100,526.50 (0.00)	142,728.99
6	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	26	21,825.13 (0.00)	11,903.84
		Total	26	21,825.13 (0.00)	11,903.84
7	Ministry of Coal	Coal	114	182,868.95 (0.00)	48,745.33
		Electricity Generation	6	36,781.81 (0.00)	6,466.16
		Railways	2	3,485.86 (0.00)	2,577.50
		Total	122	223,136.62 (0.00)	57,788.99
8	Ministry of Health & Family Welfare	Healthcare	24	18,319.26 (0.00)	9,637.14
		Total	24	18,319.26 (0.00)	9,637.14
9	Ministry of Housing & Urban Affairs	Construction	1	644.00 (0.00)	206.31
		Real Estate	4	33,749.85 (0.00)	15,093.97
		Urban Public Transport	29	297,736.37 (0.00)	144,664.19
		Waste & Water	15	3,750.55 (0.00)	2,952.39
		Total	49	335,880.77 (0.00)	162,916.86
10	Ministry of Labour and Employment	Healthcare	9	2,299.24 (0.00)	1,249.55
		Total	9	2,299.24 (0.00)	1,249.55
11	Ministry of Mines	Construction	1	255.37 (0.00)	98.96
		Metals & Mining	5	7,989.36 (0.00)	7,496.81
		Total	6	8,244.73 (0.00)	7,595.77
12	Ministry of Petroleum & Natural Gas	Energy Storage	13	25,585.08 (0.00)	23,358.06
		Oil & Gas	104	379,839.57 (0.00)	206,954.50
		Total	117	405,424.65 (0.00)	230,312.56
13	Ministry of Ports, Shipping and Waterways	Shipping	4	7,572.50 (0.00)	5,404.77
		Tourism, Hospitality & Wellness	1	573.00 (0.00)	674.35
		Total	5	8,145.50 (0.00)	6,079.12
14	Ministry of Power	Coal	2	2,083.00 (0.00)	1,071.32
		Electricity Generation	33	352,432.05 (0.00)	143,353.23
		Transmission & Distribution	67	207,446.47 (0.00)	72,152.52
		Total	102	561,961.52 (0.00)	216,577.07
15	Ministry of Railways	Railways	147	225,802.03 (0.00)	185,840.10
		Total	147	225,802.03 (0.00)	185,840.10



Ministry-wise Ongoing Projects

AUGUST 2026

Sl.No	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
16	Ministry of Road Transport & Highways	Roads & Highways	982	937,452.25 (0.00)	510,396.35
		Total	982	937,452.25 (0.00)	510,396.35
17	Ministry of Steel	Metals & Mining	3	2,114.35 (0.00)	309.80
		Steel	26	24,624.69 (0.00)	13,363.58
		Total	29	26,739.04 (0.00)	13,673.38
Total			1731	3,071,947.05 (0.00)	1,632,560.54




Table 2: State-wise Ongoing Projects





Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
1	Offshore	Ministry of Petroleum & Natural Gas	Oil & Gas	10	39,620.36 (42,894.50)	18,335.85
	PAN India	Department of Telecommunications	Telecommunication	1	28,466.00 (19,592.00)	9,173.00
	Total			11	68,086.36 (62,486.50)	27,508.85
2	Andaman & Nicobar	Ministry of Housing & Urban Affairs	Real Estate	1	209.88 (230.00)	37.35
		Ministry of Road Transport & Highways	Roads & Highways	3	653.97 (1,081.48)	275.78
	PAN India	Department of Telecommunications	Telecommunication	6	88,063.24 (77,140.10)	49,542.20
	Total			10	88,927.09 (78,451.58)	49,855.33
3	Andhra Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	3	7,061.44 (7,061.44)	1,506.57
		Department of Higher Education	Education	1	305.00 (305.00)	87.46
		Department of Telecommunications	Telecommunication	3	7,147.17 (3,937.81)	1,979.21
		Department of Water Resources, River Development & GR	Water Resources	3	10,901.50 (57,269.50)	29,663.15
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1,224.86 (1,437.34)	977.83
		Ministry of Housing & Urban Affairs	Waste & Water	1	172.22 (172.22)	88.86
		Ministry of Labour and Employment	Healthcare	1	384.27 (384.27)	286.38
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	34,879.34 (34,939.30)	33,394.86
		Ministry of Power	Transmission & Distribution	5	17,312.49 (17,312.50)	4,946.75
		Ministry of Railways	Railways	13	12,776.91 (18,385.70)	7,079.72
		Ministry of Road Transport & Highways	Roads & Highways	76	76,366.38 (73,961.60)	35,834.58
	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79
	Total			118	254,920.82 (290,632.78)	165,164.16
4	Arunachal Pradesh	Department of Higher Education	Education	1	592.61 (592.61)	551.30
		Department of Telecommunications	Telecommunication	1	1,255.49 (276.62)	237.98
		Ministry of Power	Electricity Generation	6	64,102.68 (83,892.90)	32,327.16
			Transmission & Distribution	2	4,963.80 (9,338.70)	8,177.67
		Ministry of Railways	Railways	1	435.00 (1,334.45)	1,057.21
		Ministry of Road Transport & Highways	Roads & Highways	17	14,356.93 (14,356.90)	3,834.10
	PAN India	Department of Telecommunications	Telecommunication	6	87,557.24 (76,634.10)	49,442.07
	Total			34	173,263.75 (186,426.28)	95,627.49
5	Assam	Department of Higher Education	Education	1	153.71 (153.71)	798.42
		Department of Telecommunications	Telecommunication	1	1,255.49 (276.62)	237.98
		Department of Water Resources, River Development & GR	Water Resources	1	256.16 (256.16)	44.70
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	1,712.00 (2,520.00)	2,670.23
		Ministry of Coal	Coal	2	449.23 (449.23)	218.45
		Ministry of Petroleum & Natural Gas	Energy Storage	3	973.52 (973.52)	448.22
			Oil & Gas	13	17,848.76 (30,857.90)	23,628.84
		Ministry of Power	Electricity Generation	1	6,285.33 (26,075.50)	26,575.24
			Transmission & Distribution	1	5,111.33 (6,700.00)	5,577.75
		Ministry of Railways	Railways	4	13,281.70 (23,752.30)	12,024.35
		Ministry of Road Transport & Highways	Roads & Highways	42	42,966.75 (43,643.10)	17,224.34
	PAN India	Department of Telecommunications	Telecommunication	6	87,221.24 (76,298.10)	49,401.95
	Total			76	177,515.22 (211,956.14)	138,850.47
6	Bihar	Department for Promotion of Industry & Internal Trade	Real Estate	1	1,339.02 (1,339.02)	0.00
		Department of Higher Education	Education	1	499.21 (499.21)	449.96
		Department of Telecommunications	Telecommunication	3	3,883.82 (2,718.14)	1,023.24
		Department of Water Resources, River Development & GR	Waste & Water	5	2,351.43 (2,351.43)	1,486.90

Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
6	Bihar	Department of Water Resources, River Development & GR	Water Resources	1	1,622.27 (2,430.76)	345.94
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3,541.56 (3,541.56)	1,689.02
		Ministry of Health & Family Welfare	Healthcare	2	2,256.07 (2,506.07)	143.74
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	13,365.77 (13,365.80)	5,198.09
			Waste & Water	1	158.78 (158.78)	135.72
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	23,096.50 (25,031.50)	14,583.45
		Ministry of Power	Electricity Generation	2	40,387.09 (43,704.60)	17,490.99
			Transmission & Distribution	3	3,119.63 (3,119.63)	322.81
		Ministry of Railways	Railways	18	34,866.24 (42,475.70)	20,678.59
		Ministry of Road Transport & Highways	Roads & Highways	65	86,301.42 (86,653.90)	45,559.11
	PAN India	Department of Telecommunications	Telecommunication	6	87,939.24 (77,016.10)	49,541.56
Total				117	304,728.05 (306,912.20)	158,649.12
7	PAN India	Department of Telecommunications	Telecommunication	4	64,214.68 (53,291.50)	28,627.07
	Total			4	64,214.68 (53,291.50)	28,627.07
8	Chhattisgarh	Department of Higher Education	Education	1	1,188.97 (1,188.97)	1.92
		Department of Telecommunications	Telecommunication	3	7,147.17 (3,937.81)	1,979.21
		Department of Water Resources, River Development & GR	Water Resources	2	842.26 (1,109.33)	869.21
		Ministry of Coal	Coal	14	34,428.39 (34,428.40)	12,920.62
			Railways	1	1,686.22 (2,438.53)	792.73
		Ministry of Health & Family Welfare	Healthcare	3	975.00 (972.85)	538.39
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	2,769.04 (2,769.04)	587.63
		Ministry of Power	Electricity Generation	2	25,321.00 (25,897.00)	7,754.14
			Transmission & Distribution	1	6,444.00 (6,444.00)	12.88
		Ministry of Railways	Railways	11	11,386.90 (12,635.50)	9,237.59
		Ministry of Road Transport & Highways	Roads & Highways	22	21,163.16 (22,402.40)	10,517.33
		Ministry of Steel	Metals & Mining	1	1,700.00 (1,756.20)	303.01
			Steel	7	7,640.96 (10,504.50)	6,631.45
	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79
Total				75	209,082.31 (201,950.63)	101,464.90
9	Dadra & Nagar Haveli and Daman & Diu	Ministry of Road Transport & Highways	Roads & Highways	2	2,107.80 (2,891.81)	1,272.20
	PAN India	Department of Telecommunications	Telecommunication	5	69,157.68 (58,234.50)	29,189.20
	Total			7	71,265.48 (61,126.31)	30,461.40
10	Delhi	Department of Higher Education	Education	1	373.00 (373.00)	33.03
		Department of Telecommunications	Telecommunication	1	248.20 (248.20)	237.43
		Ministry of Health & Family Welfare	Healthcare	2	4,799.19 (4,799.19)	98.17
		Ministry of Housing & Urban Affairs	Real Estate	1	32,850.00 (32,841.00)	14,370.45
			Urban Public Transport	4	51,594.36 (51,594.40)	23,029.43
		Ministry of Power	Transmission & Distribution	3	3,038.00 (3,038.00)	2,601.04
		Ministry of Railways	Railways	1	667.00 (701.88)	400.84
		Ministry of Road Transport & Highways	Roads & Highways	2	4,234.61 (6,132.95)	5,396.50
	PAN India	Department of Telecommunications	Telecommunication	2	25,189.68 (25,189.70)	9,584.25
Total				17	122,994.04 (124,918.32)	55,751.14
11	Goa	Ministry of Railways	Railways	1	1,892.00 (1,892.00)	0.00
		Ministry of Road Transport & Highways	Roads & Highways	5	2,476.30 (2,252.18)	780.23



Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
11	PAN India	Department of Telecommunications	Telecommunication	4	55,247.68 (44,324.50)	18,742.38
		Total		10	59,615.98 (48,468.68)	19,522.61
12	Gujarat	Department of Higher Education	Education	3	809.63 (809.63)	517.84
		Department of Water Resources, River Development & GR	Water Resources	1	20,718.17 (33,412.50)	31,986.52
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1,668.10 (1,914.10)	1,096.83
		Ministry of Coal	Electricity Generation	4	5,421.78 (5,421.78)	2,609.83
		Ministry of Health & Family Welfare	Healthcare	3	1,845.00 (2,477.48)	2,213.48
		Ministry of Housing & Urban Affairs	Real Estate	1	539.00 (539.00)	623.44
			Urban Public Transport	1	12,020.32 (12,020.30)	9,535.85
		Ministry of Labour and Employment	Healthcare	2	763.99 (763.99)	161.10
		Ministry of Petroleum & Natural Gas	Energy Storage	1	356.86 (304.40)	169.74
			Oil & Gas	10	25,312.12 (25,290.50)	19,228.84
		Ministry of Ports, Shipping and Waterways	Shipping	2	4,414.64 (4,455.25)	3,028.20
			Tourism, Hospitality & Wellness	1	573.00 (1,238.05)	674.35
		Ministry of Power	Electricity Generation	1	339.35 (339.35)	376.64
			Transmission & Distribution	14	64,870.45 (64,870.50)	13,208.20
		Ministry of Railways	Railways	14	12,108.86 (22,857.90)	13,324.57
		Ministry of Road Transport & Highways	Roads & Highways	31	30,403.64 (30,547.30)	15,643.37
	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79
	Total			96	268,554.15 (282,728.13)	163,717.59
13	Haryana	Department for Promotion of Industry & Internal Trade	Logistics Infrastructure	1	763.00 (763.00)	430.00
		Ministry of Health & Family Welfare	Healthcare	1	1,299.00 (1,646.43)	772.62
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	11,683.71 (11,683.70)	1,024.52
			Waste & Water	1	278.01 (278.01)	228.49
		Ministry of Petroleum & Natural Gas	Oil & Gas	5	38,892.07 (42,563.10)	32,027.40
		Ministry of Power	Transmission & Distribution	3	13,749.00 (13,749.00)	6,557.27
		Ministry of Railways	Railways	2	2,011.00 (2,413.17)	1,453.98
		Ministry of Road Transport & Highways	Roads & Highways	19	25,551.69 (28,133.70)	16,796.44
	PAN India	Department of Telecommunications	Telecommunication	5	65,051.68 (54,128.50)	28,710.75
	Total			39	159,279.16 (155,358.61)	88,001.47
14	Himachal Pradesh	Department of Higher Education	Education	2	559.17 (621.44)	478.37
		Ministry of Power	Electricity Generation	3	5,113.04 (10,664.10)	4,439.30
		Ministry of Railways	Railways	2	3,558.00 (6,018.32)	4,101.84
		Ministry of Road Transport & Highways	Roads & Highways	24	22,820.53 (26,827.40)	15,589.05
	PAN India	Department of Telecommunications	Telecommunication	6	87,681.24 (76,758.10)	49,467.72
	Total			37	119,731.98 (120,889.36)	74,076.28
15	Jammu and Kashmir	Department of Higher Education	Education	1	424.93 (500.91)	484.52
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	861.37 (861.37)	388.13
		Ministry of Health & Family Welfare	Healthcare	2	2,153.00 (2,895.19)	1,850.38
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	538.00 (538.00)	4.47
		Ministry of Power	Electricity Generation	4	22,207.77 (27,945.10)	17,730.86
			Transmission & Distribution	1	218.60 (218.60)	3.72
		Ministry of Road Transport & Highways	Roads & Highways	36	33,854.13 (33,955.00)	18,363.85



Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
15	PAN India	Department of Telecommunications	Telecommunication	6	88,010.24 (77,087.10)	49,488.84
		Total		52	148,268.04 (144,001.27)	88,314.77
16	Jharkhand	Department of Telecommunications	Telecommunication	3	7,147.17 (3,937.81)	1,979.21
		Department of Water Resources, River Development & GR	Water Resources	2	5,430.04 (12,010.30)	6,435.06
		Ministry of Coal	Coal	27	48,328.18 (48,328.20)	10,630.00
			Railways	1	1,799.64 (2,564.34)	1,784.77
		Ministry of Health & Family Welfare	Healthcare	2	500.00 (958.90)	604.10
		Ministry of Housing & Urban Affairs	Waste & Water	3	654.14 (654.14)	403.16
		Ministry of Petroleum & Natural Gas	Oil & Gas	2	633.07 (633.07)	335.42
		Ministry of Power	Coal	2	2,083.00 (2,365.00)	1,071.32
			Electricity Generation	2	33,026.00 (34,660.00)	21,822.08
			Transmission & Distribution	2	8,286.25 (8,286.25)	1,660.93
		Ministry of Railways	Railways	11	30,580.04 (31,732.20)	12,486.87
		Ministry of Road Transport & Highways	Roads & Highways	36	41,529.98 (41,172.20)	19,675.56
		Ministry of Steel	Steel	5	2,340.76 (3,059.05)	1,825.93
	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79
	Total			103	268,727.51 (265,827.56)	130,033.20
17	Karnataka	Department for Promotion of Industry & Internal Trade	Real Estate	1	1,701.81 (1,701.81)	375.68
		Department of Water Resources, River Development & GR	Water Resources	1	770.16 (1,592.32)	1,517.10
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	1,143.40 (1,143.40)	811.04
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	56,804.24 (61,094.20)	40,924.27
			Waste & Water	1	162.73 (162.73)	79.50
		Ministry of Labour and Employment	Healthcare	2	428.92 (428.92)	111.57
		Ministry of Petroleum & Natural Gas	Oil & Gas	6	7,187.24 (7,224.86)	5,245.31
		Ministry of Ports, Shipping and Waterways	Shipping	1	153.23 (153.23)	97.45
		Ministry of Power	Transmission & Distribution	11	24,711.99 (24,712.00)	10,472.19
		Ministry of Railways	Railways	8	12,961.70 (9,790.61)	5,534.46
		Ministry of Road Transport & Highways	Roads & Highways	69	74,996.53 (79,232.90)	66,754.46
		Ministry of Steel	Steel	1	1,043.63 (1,043.63)	658.17
	PAN India	Department of Telecommunications	Telecommunication	5	67,956.68 (57,033.50)	29,062.38
	Total			112	250,022.26 (245,314.11)	161,643.58
18	Kerala	Department for Promotion of Industry & Internal Trade	Real Estate	1	3,805.00 (3,805.00)	58.62
		Department of Higher Education	Education	2	2,533.45 (2,744.40)	716.83
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	484.57 (484.57)	246.96
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	1,957.05 (1,957.05)	816.80
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	6,587.52 (6,977.52)	1,417.89
		Ministry of Power	Transmission & Distribution	1	173.14 (173.14)	2.08
		Ministry of Railways	Railways	3	2,846.00 (6,520.10)	4,013.14
		Ministry of Road Transport & Highways	Roads & Highways	21	55,625.30 (61,868.60)	42,717.02
	PAN India	Department of Telecommunications	Telecommunication	6	87,154.24 (76,231.10)	49,413.74
	Total			40	161,166.27 (160,761.48)	99,403.08
19	Ladakh	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	480.00 (640.00)	524.37
		Ministry of Road Transport & Highways	Roads & Highways	3	1,184.27 (1,184.27)	1,038.43



Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
19	PAN India	Department of Telecommunications	Telecommunication	5	75,301.24 (64,378.10)	39,168.84
		Total		9	76,965.51 (66,202.37)	40,731.64
20	PAN India	Department of Telecommunications	Telecommunication	3	47,364.24 (47,364.20)	30,275.97
		Total		3	47,364.24 (47,364.20)	30,275.97
21	Madhya Pradesh	Department of Higher Education	Education	1	496.28 (496.28)	97.35
		Department of Telecommunications	Telecommunication	3	3,883.82 (2,718.14)	1,023.24
		Department of Water Resources, River Development & GR	Water Resources	3	23,010.18 (23,323.00)	11,616.85
		Ministry of Coal	Coal	16	34,924.44 (34,924.40)	3,874.45
		Ministry of Health & Family Welfare	Healthcare	2	650.00 (650.00)	268.91
		Ministry of Housing & Urban Affairs	Urban Public Transport	2	14,442.20 (14,442.20)	9,761.83
			Waste & Water	3	880.74 (941.16)	840.57
		Ministry of Mines	Metals & Mining	1	1,856.36 (3,800.00)	1,059.82
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	46,091.18 (46,091.20)	7,423.93
		Ministry of Power	Electricity Generation	1	20,446.00 (20,446.00)	2,434.64
			Transmission & Distribution	10	46,260.32 (46,260.30)	10,206.82
		Ministry of Railways	Railways	13	32,517.11 (58,545.00)	40,400.38
		Ministry of Road Transport & Highways	Roads & Highways	56	40,168.59 (37,899.30)	17,867.54
	PAN India	Department of Telecommunications	Telecommunication	6	91,332.24 (80,409.10)	49,880.92
	Total			121	356,959.46 (370,946.08)	156,757.25
22	Maharashtra	Department of Higher Education	Education	1	441.85 (441.85)	0.00
		Department of Telecommunications	Telecommunication	3	7,147.17 (3,937.81)	1,979.21
		Department of Water Resources, River Development & GR	Water Resources	6	10,857.15 (20,187.10)	22,101.62
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 (500.48)	399.77
		Ministry of Coal	Coal	26	12,900.30 (12,900.30)	3,337.60
		Ministry of Housing & Urban Affairs	Urban Public Transport	8	37,119.66 (37,293.40)	3,819.68
			Waste & Water	1	194.20 (194.20)	136.56
		Ministry of Labour and Employment	Healthcare	2	455.06 (456.83)	332.68
		Ministry of Petroleum & Natural Gas	Energy Storage	2	764.49 (872.81)	676.18
			Oil & Gas	11	36,605.84 (40,683.10)	13,840.62
		Ministry of Power	Transmission & Distribution	4	29,246.00 (29,246.00)	3,319.93
		Ministry of Railways	Railways	19	22,103.80 (44,830.40)	28,400.04
		Ministry of Road Transport & Highways	Roads & Highways	89	72,484.62 (75,034.10)	36,843.46
		Ministry of Steel	Metals & Mining	2	414.35 (414.35)	6.79
	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79
	Total			180	317,624.21 (342,458.83)	164,512.93
23	Manipur	Department of Sports	Education	1	906.47 (611.74)	577.32
		Department of Water Resources, River Development & GR	Water Resources	1	1,449.44 (1,822.24)	1,848.17
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	499.00 (499.00)	215.10
		Ministry of Power	Transmission & Distribution	1	5,111.33 (6,700.00)	5,577.75
		Ministry of Railways	Railways	1	14,323.00 (21,886.00)	16,931.50
		Ministry of Road Transport & Highways	Roads & Highways	28	10,082.46 (10,082.50)	6,817.09
	PAN India	Department of Telecommunications	Telecommunication	6	87,557.24 (76,634.10)	49,442.07
	Total			39	119,928.94 (118,235.58)	81,409.00

Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
24	Meghalaya	Department of Higher Education	Education	1	494.52 (429.70)	385.32
		Department of Telecommunications	Telecommunication	1	971.96 (180.46)	167.23
		Ministry of Power	Transmission & Distribution	1	5,111.33 (6,700.00)	5,577.75
		Ministry of Road Transport & Highways	Roads & Highways	12	6,148.96 (5,995.63)	2,295.53
	PAN India	Department of Telecommunications	Telecommunication	6	87,157.24 (76,234.10)	49,318.79
Total				21	99,884.01 (89,539.89)	57,744.62
25	Mizoram	Department of Higher Education	Education	1	474.23 (474.23)	167.55
		Ministry of Petroleum & Natural Gas	Energy Storage	1	225.71 (225.71)	33.36
		Ministry of Power	Transmission & Distribution	1	5,111.33 (6,700.00)	5,577.75
		Ministry of Road Transport & Highways	Roads & Highways	15	10,428.13 (10,428.10)	3,726.85
	PAN India	Department of Telecommunications	Telecommunication	6	87,157.24 (76,234.10)	49,318.79
Total				24	103,396.64 (94,062.14)	58,824.30
26	Nagaland	Department of Higher Education	Education	1	275.63 (275.63)	263.25
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	227.62 (227.62)	28.65
		Ministry of Power	Transmission & Distribution	1	5,111.33 (6,700.00)	5,577.75
		Ministry of Railways	Railways	1	6,663.00 (15,310.20)	6,891.03
		Ministry of Road Transport & Highways	Roads & Highways	16	4,881.46 (5,435.51)	2,108.56
	PAN India	Department of Telecommunications	Telecommunication	6	87,557.24 (76,634.10)	49,442.07
Total				26	104,716.28 (104,583.06)	64,311.31
27	Odisha	Department of Higher Education	Education	3	1,882.56 (1,496.33)	1,034.14
		Department of Telecommunications	Telecommunication	3	7,147.17 (3,937.81)	1,979.21
		Department of Water Resources, River Development & GR	Water Resources	3	4,612.34 (12,314.50)	13,971.29
		Ministry of Coal	Coal	12	36,569.58 (34,261.30)	13,977.10
			Electricity Generation	1	27,212.96 (27,213.00)	3,606.38
		Ministry of Labour and Employment	Healthcare	1	164.60 (164.60)	17.52
		Ministry of Mines	Metals & Mining	3	5,967.00 (8,121.17)	6,301.99
		Ministry of Petroleum & Natural Gas	Oil & Gas	4	16,925.45 (14,903.50)	9,834.07
		Ministry of Ports, Shipping and Waterways	Shipping	1	3,004.63 (3,004.63)	2,279.12
		Ministry of Power	Electricity Generation	2	22,974.75 (23,674.00)	7,729.59
			Transmission & Distribution	2	3,065.19 (3,065.19)	349.66
		Ministry of Railways	Railways	20	31,436.42 (41,706.80)	26,002.49
		Ministry of Road Transport & Highways	Roads & Highways	36	22,415.44 (24,630.40)	14,511.74
		Ministry of Steel	Steel	5	5,160.31 (5,160.31)	1,752.35
	PAN India	Department of Telecommunications	Telecommunication	6	88,102.24 (77,179.10)	49,318.79
Total				102	276,640.64 (280,832.64)	152,665.44
28	PAN India	Department of Telecommunications	Telecommunication	4	41,640.68 (41,640.70)	20,339.56
	Puducherry	Ministry of Railways	Railways	1	713.00 (1,748.55)	1,271.33
		Ministry of Road Transport & Highways	Roads & Highways	4	7,027.60 (7,051.29)	4,118.22
	Total			9	49,381.28 (50,440.54)	25,729.11
29	PAN India	Department of Telecommunications	Telecommunication	6	87,634.24 (76,711.10)	49,318.79
	Punjab	Department for Promotion of Industry & Internal Trade	Real Estate	1	1,367.72 (1,367.72)	0.00
		Department of Higher Education	Education	2	559.30 (597.85)	402.44
		Department of Water Resources, River Development & GR	Water Resources	2	3,727.07 (5,177.86)	4,582.82
		Ministry of Health & Family Welfare	Healthcare	2	650.00 (924.75)	52.04
		Ministry of Housing & Urban Affairs	Waste & Water	2	545.53 (553.64)	380.36



Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
29	Punjab	Ministry of Petroleum & Natural Gas	Oil & Gas	3	2,094.36 (2,094.36)	1,656.11
		Ministry of Power	Transmission & Distribution	1	5,969.00 (5,969.00)	2,268.22
		Ministry of Railways	Railways	2	2,255.64 (4,336.48)	3,108.35
		Ministry of Road Transport & Highways	Roads & Highways	32	41,876.31 (46,755.20)	28,176.70
	Total			53	146,679.17 (144,487.96)	89,945.83
30	PAN India	Department of Telecommunications	Telecommunication	6	89,228.24 (78,305.10)	49,602.72
	Rajasthan	Department for Promotion of Industry & Internal Trade	Real Estate	1	921.66 (921.66)	0.00
		Department of Higher Education	Education	1	522.89 (522.89)	29.47
		Department of Telecommunications	Telecommunication	1	421.65 (228.94)	152.96
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	2,874.00 (2,874.00)	1,036.49
		Ministry of Coal	Electricity Generation	1	4,147.07 (4,147.07)	249.95
		Ministry of Housing & Urban Affairs	Urban Public Transport	3	14,222.55 (14,222.50)	128.16
		Ministry of Petroleum & Natural Gas	Energy Storage	1	461.05 (461.05)	256.76
			Oil & Gas	2	10,599.00 (10,599.00)	6,796.89
		Ministry of Power	Transmission & Distribution	17	72,773.00 (72,773.00)	26,509.86
		Ministry of Railways	Railways	11	17,468.46 (20,353.30)	15,710.09
		Ministry of Road Transport & Highways	Roads & Highways	22	16,241.58 (14,357.50)	8,570.26
	Total			69	229,881.15 (219,766.01)	109,043.61
31	PAN India	Department of Telecommunications	Telecommunication	6	86,549.24 (75,626.10)	49,318.79
	Sikkim	Department of Higher Education	Education	2	999.82 (951.31)	575.56
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	323.26 (323.26)	87.61
		Ministry of Health & Family Welfare	Healthcare	1	250.00 (635.21)	667.21
		Ministry of Power	Electricity Generation	2	6,686.33 (7,576.15)	6,403.12
			Transmission & Distribution	1	4,754.42 (9,129.32)	8,173.48
		Ministry of Road Transport & Highways	Roads & Highways	8	3,158.89 (3,287.17)	2,070.76
	Total			21	102,721.96 (97,528.52)	67,296.53
32	PAN India	Department of Telecommunications	Telecommunication	4	73,680.24 (62,757.10)	38,998.79
	Tamil Nadu	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1,687.06 (1,687.06)	377.78
		Ministry of Health & Family Welfare	Healthcare	1	1,264.00 (2,021.51)	567.36
		Ministry of Housing & Urban Affairs	Urban Public Transport	1	63,246.00 (63,246.00)	35,228.00
		Ministry of Mines	Metals & Mining	1	166.00 (166.00)	135.00
		Ministry of Petroleum & Natural Gas	Energy Storage	2	1,507.00 (2,561.00)	1,626.63
			Oil & Gas	5	40,005.00 (47,773.00)	7,031.77
		Ministry of Power	Transmission & Distribution	2	1,320.65 (1,320.65)	219.20
		Ministry of Railways	Railways	6	4,762.69 (11,918.00)	6,039.52
		Ministry of Road Transport & Highways	Roads & Highways	41	54,094.87 (51,067.60)	24,801.32
	Total			65	241,733.51 (244,517.92)	115,025.37
33	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79
	Telangana	Department for Promotion of Industry & Internal Trade	Real Estate	1	2,360.00 (2,360.00)	63.19
		Department of Higher Education	Education	1	262.00 (262.00)	225.58
		Department of Telecommunications	Telecommunication	2	3,462.17 (2,489.20)	870.28
		Department of Water Resources, River Development & GR	Water Resources	3	10,268.14 (20,335.40)	10,303.64
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	1	500.48 (500.48)	399.77
		Ministry of Coal	Coal	7	2,986.57 (2,986.57)	1,811.09



Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore	
33	Telangana	Ministry of Health & Family Welfare	Healthcare	1	1,028.00 (1,365.95)	1,037.55	
		Ministry of Housing & Urban Affairs	Construction	1	644.00 (644.00)	206.31	
		Ministry of Petroleum & Natural Gas	Oil & Gas	1	215.00 (215.00)	47.50	
		Ministry of Power	Electricity Generation	1	29,344.85 (29,344.80)	733.63	
			Transmission & Distribution	1	1,368.00 (1,368.00)	1,299.60	
		Ministry of Railways	Railways	3	4,289.95 (4,470.41)	1,193.70	
		Ministry of Road Transport & Highways	Roads & Highways	45	34,782.65 (37,550.20)	15,874.87	
	Total			73	177,901.05 (179,358.11)	83,385.50	
34	PAN India	Department of Telecommunications	Telecommunication	6	87,157.24 (76,234.10)	49,318.79	
	Tripura	Ministry of Petroleum & Natural Gas	Oil & Gas	2	9,474.33 (9,396.51)	7,093.06	
		Ministry of Power	Transmission & Distribution	1	5,111.33 (6,700.00)	5,577.75	
		Ministry of Road Transport & Highways	Roads & Highways	9	6,260.76 (6,260.76)	2,091.07	
	Total			18	108,003.66 (98,591.37)	64,080.67	
35	PAN India	Department of Telecommunications	Telecommunication	5	86,389.24 (75,466.10)	49,318.79	
	Uttar Pradesh	Department for Promotion of Industry & Internal Trade	Real Estate	1	658.00 (658.00)	75.63	
		Department of Higher Education	Education	1	246.00 (246.00)	214.03	
		Department of Telecommunications	Telecommunication	5	10,808.82 (9,643.14)	1,525.24	
		Department of Water Resources, River Development & GR	Waste & Water	2	1,532.96 (1,532.96)	243.43	
			Water Resources	2	22,090.67 (25,447.20)	13,106.60	
		Ministry of Civil Aviation	Aviation & Aviation Infrastructure	3	3,949.13 (3,949.13)	1,457.72	
		Ministry of Coal	Coal	2	1,328.09 (1,328.09)	1,116.55	
		Ministry of Housing & Urban Affairs	Urban Public Transport	4	27,511.50 (27,511.50)	16,015.98	
			Waste & Water	2	704.20 (734.95)	659.17	
		Ministry of Petroleum & Natural Gas	Energy Storage	2	11,068.45 (11,068.50)	8,910.71	
			Oil & Gas	4	17,302.12 (17,302.10)	1,030.32	
		Ministry of Power	Electricity Generation	2	55,553.00 (55,553.00)	5,074.41	
			Transmission & Distribution	5	36,697.81 (36,697.80)	5,814.47	
		Ministry of Railways	Railways	20	49,695.71 (51,902.90)	28,329.57	
		Ministry of Road Transport & Highways	Roads & Highways	100	119,618.79 (113,245.00)	55,591.43	
		Total			160	445,154.49 (432,286.37)	188,484.05
		36	PAN India	Department of Telecommunications	Telecommunication	6	88,210.24 (77,287.10)
	Uttarakhand		Department for Promotion of Industry & Internal Trade	Real Estate	1	1,265.37 (1,265.37)	14.89
Department of Higher Education			Education	1	650.85 (650.85)	414.41	
Department of Water Resources, River Development & GR			Water Resources	1	2,584.10 (2,584.10)	1,379.51	
Ministry of Health & Family Welfare			Healthcare	2	650.00 (1,093.89)	823.19	
Ministry of Housing & Urban Affairs			Real Estate	1	150.97 (206.00)	62.73	
Ministry of Labour and Employment			Healthcare	1	102.40 (297.63)	340.30	
Ministry of Power			Electricity Generation	2	6,838.35 (17,312.40)	13,793.36	
Ministry of Road Transport & Highways			Roads & Highways	37	21,654.88 (20,370.80)	10,438.10	
Total			52	122,107.16 (121,068.14)	76,795.15		
37	PAN India	Department of Telecommunications	Telecommunication	6	88,063.24 (77,140.10)	49,542.20	
	West Bengal	Department of Higher Education	Education	1	500.00 (442.00)	420.10	
		Department of Telecommunications	Telecommunication	2	3,462.17 (2,489.20)	870.28	
		Department of Water Resources, River Development & GR	Waste & Water	1	154.73 (154.73)	103.28	

Ongoing Projects State-Wise

AUGUST 2026

Sl.No	STATE NAME	Allocated To	Sector	Project Count	Original Cost (Latest Revised Cost) in Rs. Crore	Cumulative Expenditure in Rs. Crore
37	West Bengal	Ministry of Civil Aviation	Aviation & Aviation Infrastructure	2	1,877.30 (1,877.30)	724.50
		Ministry of Coal	Coal	10	12,282.26 (12,282.20)	1,976.02
		Ministry of Mines	Construction	1	255.37 (255.37)	98.96
		Ministry of Petroleum & Natural Gas	Energy Storage	1	10,228.00 (12,407.00)	11,236.46
			Oil & Gas	6	5,147.65 (6,085.00)	3,957.62
		Ministry of Power	Electricity Generation	3	20,091.84 (21,644.60)	5,243.31
			Transmission & Distribution	3	7,195.63 (7,195.63)	169.93
		Ministry of Railways	Railways	9	26,048.48 (29,782.40)	9,694.13
		Ministry of Road Transport & Highways	Roads & Highways	22	14,834.57 (14,244.70)	8,423.15
		Ministry of Steel	Steel	8	8,439.03 (8,439.03)	2,495.68
Total				75	198,580.27 (194,439.26)	94,955.62




Table 3: Completed Projects

Completed Projects During Month						AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
	Department of Higher Education					
	Education					
1	Phase 1B - Construction of Academic Block, Hostel, Residential Tower, Directors Residence and External Development works at National Institute of Technology, Delhi Campus on Engineering, Procurement and Construction basis <i>(National Institute of Technology Delhi)</i> 612851	Delhi	09/2009 (11/2022)	06/2026 (09/2025) (01/2026)	333.49 (336.42)	336.42
2	Establishment of NIT Puducherry Permanent Campus [Phase-I and Phase-II] <i>(National Institute of Technology, Puducherry)</i> 612877	Puducherry	09/2009 (07/2013)	08/2026 (12/2024) (08/2026)	618.34 (544.34)	543.74
	Total (2)				951.83 (880.76)	880.16
	Ministry of Housing & Urban Affairs					
	Urban Public Transport					
3	Mumbai Metro Line 3 <i>(Mumbai Metro Rail Corporation Limited [MMRC])</i> 702637	Maharashtra	07/2013 (06/2016)	10/2025 (03/2023) (08/2025)	23,136.00 (37,276.00)	36,139.24
	Total (1)				23,136.00 (37,276.00)	36,139.24
	Ministry of Petroleum & Natural Gas					
	Oil & Gas					
4	Haldia Panagarh Pipeline Project <i>(Hindustan Petroleum Corporation Limited)</i> 709753	West Bengal	11/2022 (11/2022)	08/2026 (11/2025) (08/2026)	1,010.00 (1,107.00)	895.30
	Total (1)				1,010.00 (1,107.00)	895.30
	Ministry of Ports, Shipping and Waterways					
	Inland Waterways					
5	Jal Marg Vikas Project <i>(Inland Waterways Authority of India [IWAI])</i> 701565	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	01/2018 (02/2018)	06/2026 (12/2023) (06/2026)	5,369.18 (5,061.15)	4,220.81
	Total (1)				5,369.18 (5,061.15)	4,220.81
	Ministry of Road Transport & Highways					
	Roads & Highways					
6	Dornala to Kunta Junction from Design Chainage Km 244000 to 267990 section of NH-765 Package-2 <i>(MoRTH)</i> 618062	Andhra Pradesh	12/2022 (03/2024)	02/2026 (09/2025) (02/2026)	244.83 (0.00)	143.94
7	Duttalur at NH-565 Junction to Kavali Joining on NH-16 Chainage Km. 36/400 to Km. 107/224 excluding the stretch from Km 101.880 to 105.300 67.404 Km of NH-167BG from in the State of Andhra Pradesh on EPC mode <i>(MoRTH)</i> 618192	Andhra Pradesh	03/2021 (07/2022)	03/2026 (07/2024) (03/2026)	423.67 (0.00)	300.76
8	Sheohar-Sitamarhi Section km 40.000 to 79.400 km Lot-I <i>(MoRTH)</i> 618005	Bihar	02/2016 (05/2016)	09/2024 (05/2018) (09/2024)	178.85 (278.53)	232.61
9	Sitamarhi-Jaynagar Section km 79.400 to km 156.500 Lot-II <i>(MoRTH)</i> 618006	Bihar	02/2016 (06/2016)	06/2026 (12/2018) (06/2026)	369.77 (503.28)	459.61
10	Jaynagar-Narahia Section km 156.500 to km 219.945 Lot-III <i>(MoRTH)</i> 618007	Bihar	02/2016 (05/2016)	06/2026 (11/2018) (06/2026)	553.30 (706.39)	661.96
11	Development of Chiloda - Gandhinagar- Sarkhej ofNH-147 Package -II <i>(MoRTH)</i> 617977	Gujarat	04/2018 (11/2018)	09/2024 (11/2020) (09/2024)	211.28 (234.44)	234.39
12	Reconstruction and widening to 2 lane with paved shoulder from existing chainage km 102000 to km 134950 Design chainage km 90150 to km 116980 including construction of Naushera Tunnel Total length of tunnel 0.700 km under 31 TF on Akhnoor-Poonch road NH-144A in the UT of Jammu & Kashmir under Project Sampark BRO on EPC mode Package-V Job no NH-144A-J&K-2020-21-104 <i>(MoRTH)</i> 618220	Jammu and Kashmir	03/2021 (07/2022)	11/2025 (07/2024) (11/2025)	642.24 (572.51)	524.46
13	Widening to 2-Lane with Paved Shoulders from Km 116.800 to 149.070Design Changes on Hosadurga - Holalkere Section of NH-173 in the State of Karnataka on EPC mode under Annual Plan 2021-22 Job no. NH-173-KNT-2021-22-946 <i>(MoRTH)</i> 618000	Karnataka	03/2022 (10/2022)	05/2026 (02/2024) (05/2026)	170.34 (147.39)	125.98
14	Construction of Major Bridge Across Sharavathi Backwaters and approaches between Ambargodu and Kalasavalli Near Sigandhur in Sagar Taluk on NH 369E in the State of Karnataka on EPC mode.Job No. NH-369E-KNT-2018-19-895 dated 06.03.2019. <i>(MoRTH)</i> 618144	Karnataka	03/2019 (12/2019)	08/2025 (12/2022) (08/2025)	423.15 (0.00)	462.70
15	Construction of 4 Lane Flyover at Nagpur RTO Chowk To Nagpur University Campus from Ch 2/250 to 5/100 and 4 lane flyover at wadi/midc junction from km 8/360 to km, 10/300 on NH 53 in state of Maharashtra. <i>(MoRTH)</i> 617917	Maharashtra	03/2021 (03/2022)	07/2025 (03/2024) (07/2025)	478.83 (490.52)	436.95
16	Up-gradation to four lane/ Two lane with paved shoulders configuration of Kalyan - Murbad - Malshej Ghat - Nirmal Road NH- 61 km 15/200 to Km 38/00 and from Km. 58/00 to Km 84/00 Design length 48.58 km of NH-61 on EPC Mode in Thane District in the state of Maharashtra <i>(MoRTH)</i> 617933	Maharashtra	02/2023 (03/2024)	02/2026 (08/2026) (02/2026)	984.07 (0.00)	549.37
17	Kashedi ghat tunnel NH-66 [Bhogaon Khurd - Kashedi section] 4 lanes under NHDP on EPC mode <i>(MoRTH)</i> 617944	Maharashtra	09/2018 (10/2018)	02/2026 (04/2021) (02/2026)	680.43 (701.46)	675.72

Completed Projects During Month						AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
18	Rehabilitation & Up-gradation of Sabalkhed to Ashti Section from Km 37900 to Km 55100 & Chinchpur to Jamkhed Section from km 70000 to km 72922 of NH-561 to Two lane with Paved shoulder/ Four lane configuration in the State of Maharashtra on EPC Mode Length20.122km. (MoRTH) 618046	Maharashtra	03/2022 (04/2023)	09/2025 (09/2024) (09/2025)	213.33 (0.00)	108.78
19	Sarsam - Kothari of NH-161A - 2L PS from Km.33/00 to 90/00 (MoRTH) 618090	Maharashtra	02/2017 (06/2017)	01/2024 (06/2019) (01/2024)	545.64 (0.00)	350.38
20	Rehabilitation and Upgradation of Shewali phata to Kalambhir section i.e. Km 0443 to Km 4500 & Nizampur to Chadwel section i.e. Km 13485 to Km 26265 Length16.317 Km excluding 2 Major Bridges with approaches Km 13735 to Km 14095 & Km 19660 to Km 20030 of NH 753B to 2LPS Configuration in the State of Maharashtra on EPC Mode. (MoRTH) 618179	Maharashtra	03/2024 (08/2024)	08/2025 (02/2026) (08/2025)	181.58 (0.00)	125.04
21	Rehabilitation / Upgradation to 4 Lane with Paved shoulder of Existing Section in Sillod Town with Design Ch. Km54500 to Km 60679 [Length6.179 km] section of NH 753F Aurangabad-Jalgaon road on EPC Mode in the State of Maharashtra (MoRTH) 618181	Maharashtra	03/2023 (01/2024)	12/2025 (07/2025) (12/2025)	153.79 (0.00)	73.82
22	Rehabilitation and Up-gradation to 2 lane with paved shoulder configuration of Mahud Sangola road NH 965 G 159400 to 161900and 162400 to 183960 Design Chainage from km. 32/300 to km. 34/800 and km. 35/800 to km. 56/860 Rigid Pavement on EPC mode in the State of Maharashtra. (MoRTH) 618188	Maharashtra	02/2023 (11/2023)	01/2026 (05/2025) (01/2026)	253.78 (0.00)	127.54
23	Widening to Existing single lane /intermediate lane to 2 lane from Km185.00 to Km 220.00 of NH-61 New NH-02 in the state of Nagaland. (MoRTH) 618072	Nagaland	03/2021 (07/2022)	02/2026 (07/2024) (02/2026)	297.25 (0.00)	175.31
24	Work of Widening/upgradation of 2-Lane with paved shoulder of Sri Muktsar Sahib to Malout road from Km 279.400 to Km 307.060 section of NH-354 in the State of Punjab on EPC mode. Job No. NH-354-PB-2021-22-555 (MoRTH) 618023	Punjab	03/2022 (10/2023)	03/2026 (04/2025) (03/2026)	152.58 (0.00)	118.99
25	Widening to Two Lane with Paved Shoulders from Km 67.000 to Km 114.425 of Kalwakurthy- Mallapally Section of NH 167 Erstwhile section of SH 18 in the State of Telangana on EPC mode under NH O Annual Plan 2016-17 (MoRTH) 617995	Telangana	01/2017 (05/2017)	07/2025 (05/2019) (07/2025)	300.00 (0.00)	249.02
26	Construction of Jasra Bypass with four lane paved shoulder configurationfrom Km 379.670 on NH-76New NH-35 to Km 18.00 on NH-27New NH-30 on EPC in the State of Uttar Pradesh. (MoRTH) 617957	Uttar Pradesh	02/2023 (03/2024)	09/2025 (09/2025) (09/2025)	274.06 (0.00)	138.83
27	Construction of 4-lane highway with paved shoulders from Km 49.155 to Km 74.700 of NH-731A on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) 618165	Uttar Pradesh	01/2022 (02/2024)	06/2026 (01/2026) (06/2026)	1,156.72 (0.00)	534.81
28	Rehabilitation & Upgradation of NH-731A from Km.0.00 to Km.35.00 to 2-lane with paved shoulder under EPC mode (MoRTH) 618167	Uttar Pradesh	03/2021 (08/2022)	11/2025 (08/2023) (11/2025)	264.86 (0.00)	145.42
29	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Near Karri village-Etawah section Km30.000 to Km 57.346 Pakage-II of NH-92 in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) 618229	Uttar Pradesh	04/2020 (08/2022)	04/2025 (02/2024) (04/2025)	211.09 (206.56)	171.85
30	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Bewar-naer Karri village section Km0.00 to Km30.00 Pakage-I of NH-92 in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) 618240	Uttar Pradesh	04/2020 (09/2022)	02/2026 (03/2024) (02/2026)	236.47 (0.00)	162.51
31	Construction and upgradation of existing road to 2-lane with paved shoulder from existing chainage Km 509.725 to Km 528.000 design chainage Km 490.550 to Km 507.850 of NH-58 new NH-07 Benakuli bend to Mana Village in EPC mode under Chardham Programme in the State of Uttarakhand. (MoRTH) 618208	Uttarakhand	02/2019 (11/2019)	11/2025 (10/2021) (11/2025)	180.10 (0.00)	176.62
32	6L of Gundugolanu Design km 1023.280 to Kalaparru Design km 1050.680 of NH-5 New NH-16 (NHAI) 618526	Andhra Pradesh	10/2018 (01/2020)	07/2023 (07/2021) (07/2023)	665.59 (665.59)	643.97
33	8L of Dwarka Expressway Pkg-II RuB near Dwarka Sector 21-DL/HR Border from 5.300 Km.to 9.500 Km. of NH-248BB (NHAI) 619090	Delhi	01/2018 (10/2019)	08/2025 (10/2021) (08/2025)	2,067.67 (2,670.22)	2,403.67
34	Ahmedabad - Dholera Pkg III from km. 48.52 to km. 71.06 [Vejalka Village - Start of DSIR zone] (NHAI) 618503	Gujarat	05/2020 (07/2021)	10/2025 (07/2023) (10/2025)	1,034.04 (1,155.41)	1,125.80
35	Ahmedabad - Dholera Pkg IV from km. 71.06 to km. 109.019 [Start of DSIR zone - Adhelai Village] (NHAI) 618504	Gujarat	05/2020 (12/2021)	06/2025 (12/2023) (06/2025)	1,181.76 (1,358.73)	1,222.79
36	6L Greenfield Kandili - Aluru Section of NH-130-CD Road from km 342500 to km 365033 Package-OD-8 (NHAI) 618680	Odisha	12/2021 (10/2022)	09/2026 (10/2024) (09/2026)	1,492.74 (1,912.84)	1,089.12
37	4 Laning of Talcher to end of Kamakhyanagar Bypass km 8.844 - km 15.725 of NH-149 and km 301.875 - km 335.946 of NH-53 Pkg-I (NHAI) 619157	Odisha	01/2018 (02/2019)	04/2026 (08/2021) (04/2026)	795.18 (810.71)	715.99

Completed Projects During Month

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Actual Date of Completion (Original/Target DoC) (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore
38	Thanamcherla-Jamandlapally 2LPS (NHAI) 619165	Telangana	11/2013 (03/2014)	01/2018 (02/2023) (01/2018)	177.18 (18.65)	8.30
39	Construction of Four Lane Highway form Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package I [from Hridaipur km 0.000 to Shahapur km 42.500] on EPC Mode in the state of Uttar Pradesh. (NHAI) 618883	Uttar Pradesh	10/2022 (07/2023)	06/2026 (07/2025) (06/2026)	1,706.47 (1,579.59)	1,448.04
40	Varanasi Gorakhpur Section Packege IV from km. 149.540 to km. 215.160 Mau-Gorakhpur (NHAI) 618893	Uttar Pradesh	04/2015 (04/2017)	12/2024 (10/2019) (12/2024)	2,966.63 (3,475.65)	3,455.16
41	4L of Najibabad Bypass from Km. 105.423 to Km. 118.373 excluding 2.45 Km. of NH-74 Bypass of NH-119 (NHAI) 619162	Uttar Pradesh	01/2022 (12/2022)	03/2026 (06/2024) (03/2026)	578.02 (566.90)	440.93
42	Earthwork in Formation, Road Work, Construction of Bridges, Blanketing, P. Way Linking works including Supply of P. Way Fittings and Track Ballast in connection with Construction of Railway Siding from Jogighopa Railway Station to MMLP at Jogighopa from Ch. 00 to 3760 on Item Rate basis Package -3, Railway Siding from Jogighopa Railway Station to MMLP (NHIDCL) 618454	Assam	02/2020 (12/2020)	09/2024 (06/2022) (09/2024)	693.97 (0.00)	40.17
43	Development of External Trunk Connectivity and Internal Infrastructure Works at Multi Model Logistics ParkMMLP at Jogighopa in the State of Assam on EPC Mode Package-I Road and Utility Works (NHIDCL) 618455	Assam	02/2020 (09/2020)	09/2024 (04/2022) (09/2024)	693.97 (0.00)	308.85
44	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 33.000 km to 66.390 Km Existing Chainage from km 33.395 to km 67.496 on EPC Mode in Manipur PKG-3 (NHIDCL) 618337	Manipur	03/2021 (09/2021)	02/2026 (03/2023) (02/2026)	467.00 (0.00)	594.01
45	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 13.747 to km 32.835 in the State of Manipur on EPC mode under NHO Package-1B (NHIDCL) 618347	Manipur	04/2020 (07/2020)	02/2026 (06/2022) (02/2026)	241.52 (0.00)	164.85
46	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 125. 000 to Km 166 Package-3 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-3 (NHIDCL) 618380	Mizoram	09/2019 (10/2019)	07/2026 (04/2023) (07/2026)	867.09 (0.00)	532.47
47	Construction for Mitigation Measures of 10 Nos. Landslides, 01 No. Sinking Zones and 1 No. of Minor Bridge in between at Ch. Km 368.00 to Km 433.00 on NH-07 on EPC Mode in Uttarakhand Package-1 (NHIDCL) 618393	Uttarakhand	12/2023 (06/2024)	07/2026 (12/2025) (07/2026)	216.68 (0.00)	117.84
	Total (42)				25,627.52 (18,055.37)	21,779.33

Note: Cumulative Expenditure is as per last reporting by Central Line Ministries/ Departments on the CRIP portal, this may not be the actual completion cost.



Table 4: Newly Added Projects

Newly Added Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Department of Higher Education				
	Education				
1	IIT Gandhinagar - Development of Faculty/Staff Housing with Associated Facilities under Phase-2A <i>(Indian Institute of Technology, Gandhinagar)</i> (858179)	Gujarat	06/2023 (12/2024)	03/2027 (08/2027)	156.00 (0.00)
2	IIT Gandhinagar - Development of Students Hostel Buildings with Associated Facilities under Phase-2A <i>(Indian Institute of Technology, Gandhinagar)</i> (304532)	Gujarat	06/2023 (12/2024)	03/2027 (05/2028)	163.00 (0.00)
3	Engineering, Procurement and Construction (EPC) of Various Buildings and External Infrastructure Development Works of Indian Institute of Management Mumbai campus in Phase-1 <i>(Indian Institute of Management Mumbai)</i> (505106)	Maharashtra	03/2026 (08/2026)	08/2030 (-)	441.85 (0.00)
4	Phase 3B Development of Permanent Campus of IIT Jodhpur <i>(Indian Institute of Technology, Jodhpur)</i> (617421)	Rajasthan	07/2025 (01/2026)	01/2028 (-)	522.89 (0.00)
	Total (4)				1,283.74 (0.00)
	Ministry of Civil Aviation				
	Aviation & Aviation Infrastructure				
5	Construction of 8 Nos. RETs for Runway 07-25, 3 nos. RETs for Runway 12-30, Extension of parallel Taxi Track-R with link Taxi- track and Link Taxi-Track-K1 at Chennai Airport <i>(Airport Authority of India [AAI])</i> (432726)	Tamil Nadu	07/2024 (10/2025)	01/2028 (-)	480.06 (0.00)
	Total (1)				480.06 (0.00)
	Ministry of Coal				
	Coal				
6	RPR OF TAWA III UG MINE - 0.84 <i>(WCL - CIL)</i> (540543)	Madhya Pradesh	03/2026 (03/2026)	03/2032 (-)	374.18 (0.00)
	Total (1)				374.18 (0.00)
	Ministry of Petroleum & Natural Gas				
	Energy Storage				
7	Development of Rail - Fed Road Tanker Loading POL Terminal at Panchgram [Near Silchar], Hailakandi, Assam. <i>(Numaligarh Refinery Limited)</i> (308266)	Assam	08/2025 (08/2025)	10/2027 (-)	433.12 (0.00)
	Total (1)				433.12 (0.00)
	Oil & Gas				
8	Old Naphtha Isomerization Unit [NIU] revamp for MS maximization at Visakh Refinery <i>(Hindustan Petroleum Corporation Limited)</i> (409131)	Andhra Pradesh	03/2025 (03/2025)	07/2028 (-)	449.00 (0.00)
9	2.4 KTPA Green Hydrogen Generation Unit at Numaligarh <i>(Numaligarh Refinery Limited)</i> (891687)	Assam	02/2023 (02/2023)	03/2027 (-)	170.00 (0.00)
10	Drive Conversion of Turbines in CHT, DHDT and DCU. <i>(Mangalore Refinery and Petrochemicals Limited)</i> (503783)	Karnataka	02/2026 (02/2026)	09/2028 (-)	206.24 (0.00)
11	Devanagonthi to Kempe Gowda International Airport (KIAL) ATF Pipeline Project <i>(Mangalore Refinery and Petrochemicals Limited)</i> (368840)	Karnataka	07/2026 (07/2026)	05/2029 (-)	234.00 (0.00)
12	Setting up 167 KTPA Sulphuric Acid Unit and Associated Facilities at Kochi Refinery <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (691992)	Kerala	07/2026 (07/2026)	07/2029 (-)	732.86 (0.00)
13	Capacity Enhancement of VGOHDT unit at Kochi Refinery <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (168896)	Kerala	05/2026 (05/2026)	01/2027 (-)	264.66 (0.00)
14	50 MW Wind Power Plant in Madhya Pradesh <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (244981)	Madhya Pradesh	05/2023 (05/2023)	04/2027 (-)	483.14 (0.00)
15	Vijaipur – BPCL, Bina Pipeline Project <i>(Gas Authority of India Limited [GAIL])</i> (929104)	Madhya Pradesh	09/2025 (09/2025)	09/2027 (-)	449.04 (0.00)
16	Setting up Coprocessing facility in KHT Unit for production of SAF at MR <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (684624)	Maharashtra	01/2026 (01/2026)	12/2027 (-)	677.00 (0.00)
17	GAS Turbine GT-3 upgrade from frame 6B to 6B.03 <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (687613)	Maharashtra	01/2026 (01/2026)	07/2027 (-)	217.81 (0.00)
18	Additional Development of Ratna-I [ADR-I] and NLM-14 Project <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (944988)	Offshore	07/2026 (07/2026)	03/2029 (-)	6,274.00 (0.00)
19	Well Head Platforms for MB-OSN-2005/1, SD4 and BS-17 Field (WHPMSBF) <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (757296)	Offshore	07/2026 (07/2026)	03/2029 (-)	5,519.00 (0.00)
20	Pipeline Replacement Project- PRP-X <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> (785574)	Offshore	07/2026 (07/2026)	05/2027 (-)	4,371.00 (0.00)
21	Group-II/III LOBS Project <i>(Chennai Petroleum Corporation Limited [CPCL])</i> (167179)	Tamil Nadu	03/2026 (03/2026)	10/2028 (-)	1,620.00 (0.00)
	Total (14)				21,667.75 (0.00)

Newly Added Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost (Revised Cost) in Rs. Crore
	Ministry of Power				
	Transmission & Distribution				
22	Transmission System for proposed Green Hydrogen/ Green Ammonia Projects in Kakinada Area (Phase I) (Power Grid Corporation of India Limited [POWERGRID]) (553920)	Andhra Pradesh	06/2026 (06/2026)	12/2028 (-)	1,618.00 (0.00)
23	Transmission system strengthening at Tumkur-II for integration of additional RE potential (2.7 GW) (Power Grid Corporation of India Limited [POWERGRID]) (994914)	Karnataka	05/2026 (05/2026)	05/2029 (-)	1,221.00 (0.00)
24	WR-ER Inter Regional Network Expansion Scheme – Part A (Power Grid Corporation of India Limited [POWERGRID]) (663560)	Multi-States (Chhattisgarh, Jharkhand, West Bengal)	06/2026 (06/2026)	06/2029 (-)	6,444.00 (0.00)
25	Upgradation / Conversion of Udumalpet - Madurai 400kV S/c line to Udumalpet - Madurai 400kV (quad) D/c line (Power Grid Corporation of India Limited [POWERGRID]) (496150)	Tamil Nadu	02/2026 (06/2026)	08/2028 (-)	772.65 (0.00)
	Total (4)				10,055.65 (0.00)
	Ministry of Road Transport & Highways				
	Roads & Highways				
26	4L Access controlled Highway From Vakalpudi Light House to Annavaram on NH-16 section of NH-516F From Km0000 to Km40621 (NHAI) (619046)	Andhra Pradesh	03/2023 (08/2026)	08/2028 (08/2028)	1,439.00 (0.00)
27	Construction of road from Bomdilla 9th Mile - Nafra Lada section of Frontier Highway NH-913 Package 4 Dishum-Sachung-Lada 113.00 to 167.75 54.75km (MoRTH) (619256)	Arunachal Pradesh	03/2024 (07/2026)	07/2030 (-)	1,266.86 (0.00)
28	Construction of road from Km 70.000 to Km 113.000 of Bomdila-Nafra-Lada Section of NH-913 Frontier Highway in the State of Arunachal Pradesh L43.000 Km (MoRTH) (619257)	Arunachal Pradesh	02/2024 (08/2026)	08/2030 (-)	1,240.75 (0.00)
29	Construction of road from Taliha to Tato section of Frontier Highway NH-913 Package 3 km 87.13 to 121.541 34.411km (MoRTH) (619266)	Arunachal Pradesh	03/2024 (08/2026)	08/2029 (-)	735.20 (0.00)
30	Construction of road from km 113.25 to km 160.75 of Huri-Taliha section of NH-913 Pkg 3 Frontier Highway to Intermediate Lane on EPC mode in the State of Arunachal Pradesh (MoRTH) (619267)	Arunachal Pradesh	03/2024 (08/2026)	08/2030 (-)	1,228.64 (0.00)
31	Construction of road from Bomdilla9th Mile- Nafra Lada section of Frontier Highway NH-913 Package 1 9th mile-Nafra 19.554 to 70.00 50.446 (MoRTH) (198592)	Arunachal Pradesh	03/2025 (07/2026)	07/2029 (-)	1,273.44 (0.00)
32	Construction of 6 lane Elevated Structure along with its approaches from Km. 142.000 to Km 144.800 Total Length 2.80 km Gondal on NH27 in the state of Gujarat (NHAI) (619273)	Gujarat	02/2026 (06/2026)	06/2028 (06/2028)	262.28 (0.00)
33	Development of 4-lane with paved shoulders from Budhel Junction to Vartej Y-Junction Km 0900 to Km 9400 on EPC mode under NHO in the State of Gujarat (NHAI) (619276)	Gujarat	12/2025 (07/2026)	12/2027 (12/2026)	247.34 (0.00)
34	Balance work for rehabilitation and upgradation of Sidhi -Singrauli Road from Km 82/400 to Km 187/99 Design Length 105.59 Km of NH-39 Old NH-75E to four lane with paved shoulder in the State of Madhya Pradesh on Item Rate Mode. (NHAI) (619304)	Madhya Pradesh	01/2026 (05/2026)	05/2028 (05/2028)	568.32 (0.00)
35	Rehabilitation and upgradation of Wardha Salod Hirapur - Pulgaon Section of NH 347A from km 134/283 to Km 159/075 [Design Chainage Km 0000 to Km 24792] to two Lanes with paved shoulder configuration in the state of Maharashtra on EPC mode. (MoRTH) (619263)	Maharashtra	03/2025 (07/2026)	12/2027 (-)	252.95 (0.00)
	Total (10)				8,514.78 (0.00)
	Ministry of Steel				
	Metals & Mining				
36	Shaft Sinking Projects at Kandri Mine. (MOIL Limited) (658240)	Maharashtra	06/2025 (04/2026)	04/2030 (-)	196.90 (0.00)
37	Shaft Sinking Projects at Dongri Buzurg Mine. (MOIL Limited) (928129)	Maharashtra	06/2025 (04/2026)	04/2030 (-)	217.45 (0.00)
	Total (2)				414.35 (0.00)




Table 5: Ongoing Projects

North Eastern Region





Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Guwahati Airport New Integrated Terminal Building Construction Project (Adani Airport Holdings Limited) (706724)	Assam	12/2016 (03/2018)	03/2025 (06/2026)	1,712.00 0.00	2,670.23	99.50
2	C/o NITB Imphal Airport (Airport Authority of India [AAI]) (706718)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499.00 0.00	215.10	53.69
3	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793)	Sikkim	11/2023 (12/2023)	06/2026 (06/2027)	323.26 0.00	87.61	36.14
Total (3)					2,534.26 0.00	2,972.94	
Ministry of Coal							
Coal							
4	TIKAK EXTENSION OCP (INVALID CO.) (615820)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 0.00	112.79	89.73
5	TIRAP OCP (INVALID CO.) (615821)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 0.00	105.66	5.00
Total (2)					449.23 0.00	218.45	
Department of Higher Education							
Education							
6	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 0.00	551.30	80.00
7	Tezpur University Projects (Tezpur University) (606112)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 0.00	798.42	97.99
8	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 0.00	385.32	98.00
9	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 0.00	167.55	4.00
10	Establishment of NIT Nagaland (NIT Nagaland) (613013)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 0.00	263.25	98.00
11	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736)	Sikkim	08/2020 (01/2022)	01/2025 (10/2026)	314.06 0.00	292.00	97.00
12	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 0.00	283.56	38.50
Total (7)					2,990.52 0.00	2,741.40	
Department of Sports							
Education							
13	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081)	Manipur	06/2022 (01/2022)	08/2024 (08/2026)	906.47 0.00	577.32	97.70
Total (1)					906.47 0.00	577.32	
Ministry of Power							
Electricity Generation							
14	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31,876.39 0.00	5,118.73	18.12
15	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1,938.85 0.00	107.31	7.85
16	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1,750.07 0.00	80.45	5.80
17	700 MW Tato-II HE Project (North Eastern Electric Power Corporation Limited) (611716)	Arunachal Pradesh	09/2025 (09/2025)	09/2031 (-)	8,146.21 0.00	254.77	6.72
18	Kalai-II Hydro Electric Project [1200 MW] (THDC India Limited) (619311)	Arunachal Pradesh	04/2026 (04/2026)	10/2032 (-)	14,105.83 0.00	190.66	0.00
19	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (03/2027)	6,285.33 0.00	26,575.24	98.07
20	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156)	Sikkim	03/2021 (08/2021)	05/2024 (11/2026)	938.29 0.00	1,726.66	97.86

Ongoing Projects of North-East Region							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
21	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181)	Sikkim	03/2019 (03/2020)	03/2024 (09/2029)	5,748.04 0.00	4,676.46	73.95
	Total (8)				70,789.01 0.00	38,730.28	
Transmission & Distribution							
22	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 0.00	4.19	5.68
23	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223)	Multi-States (Sikkim, Arunachal Pradesh)	10/2014 (10/2014)	12/2018 (03/2027)	4,754.42 0.00	8,173.48	84.00
24	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709)	Multi-States (Tripura, Meghalaya, Assam, Nagaland, Manipur, Mizoram)	12/2014 (03/2016)	12/2018 (03/2027)	5,111.33 0.00	5,577.75	99.20
	Total (3)				10,075.13 0.00	13,755.42	
Ministry of Petroleum & Natural Gas							
Energy Storage							
25	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709755)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 0.00	254.02	89.10
26	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 0.00	116.83	85.70
27	Development of Rail - Fed Road Tanker Loading POL Terminal at Panchgram [Near Silchar], Hailakandi, Assam. (Numaligarh Refinery Limited) (308266)	Assam	08/2025 (08/2025)	10/2027 (-)	433.12 0.00	77.37	23.00
28	LPG Bottling Plant at Mualkhang (Indian Oil Corporation Limited [IOCL]) (617829)	Mizoram	07/2024 (07/2024)	10/2028 (05/2028)	225.71 0.00	33.36	34.50
	Total (4)				1,199.23 0.00	481.58	
Oil & Gas							
29	Numaligarh Refinery Expansion Project (Numaligarh Refinery Limited) (604791)	Assam	07/2020 (07/2020)	07/2024 (03/2027)	12,366.00 0.00	20,845.77	87.70
30	2.4 KTPA Green Hydrogen Generation Unit at Numaligarh (Numaligarh Refinery Limited) (891687)	Assam	02/2023 (02/2023)	03/2027 (-)	170.00 0.00	37.33	45.50
31	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (Numaligarh Refinery Limited) (709865)	Assam	04/2023 (04/2023)	12/2024 (12/2026)	293.50 0.00	81.84	99.00
32	DCU Revamp Project (Numaligarh Refinery Limited) (709864)	Assam	08/2021 (08/2021)	07/2024 (03/2027)	370.00 0.00	315.57	82.70
33	Borholla GGS Life Extension Project [BLEP] (Oil and Natural Gas Corporation Limited [ONGC]) (709850)	Assam	09/2023 (09/2023)	05/2026 (03/2027)	198.70 0.00	110.99	64.30
34	Pipeline Network Project Rudrasagar (Oil and Natural Gas Corporation Limited [ONGC]) (709847)	Assam	01/2023 (01/2023)	04/2026 (04/2027)	481.03 0.00	238.83	55.40
35	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Indian Oil Corporation Limited [IOCL]) (709779)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768.00 0.00	250.84	60.80
36	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Indian Oil Corporation Limited [IOCL]) (709776)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277.00 0.00	237.33	84.80
37	Group Gathering Station, Lakwagaon (Oil India Limited) (619316)	Assam	10/2025 (10/2025)	10/2027 (10/2027)	495.59 0.00	39.97	20.10
38	Coke Drum Structure Package (Numaligarh Refinery Limited) (617836)	Assam	12/2022 (12/2022)	12/2025 (12/2026)	635.28 0.00	506.82	76.50
39	Pipeline Rehabilitation Project, Phase-II (Oil India Limited) (617827)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680.00 0.00	13.78	29.60
40	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Oil India Limited) (616858)	Assam	12/2020 (12/2020)	03/2024 (11/2026)	430.76 0.00	348.65	97.00
41	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Oil India Limited) (604863)	Assam	01/2018 (01/2018)	02/2020 (12/2026)	682.90 0.00	601.12	94.60
42	Augmentation/ Revamping of Dimapur Depot, Dimapur (Indian Oil Corporation Limited [IOCL]) (709786)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 0.00	28.65	44.20
43	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837)	Tripura	03/2022 (03/2022)	05/2024 (10/2026)	209.33 0.00	81.31	72.00
44	North East Gas Grid (Indradhanush Gas Grid Limited) (701346)	Tripura	04/2020 (04/2020)	03/2024 (03/2028)	9,265.00 0.00	7,011.75	88.60

Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (16)				27,550.71 0.00	30,750.55	
	Ministry of Health & Family Welfare						
	Healthcare						
45	Establishment of new GMC Gangtok (Medical Education, Ministry of Health and Family Welfare) (707039)	Sikkim	10/2018 (12/2018)	12/2026 (07/2026)	250.00 0.00	667.21	100.00
	Total (1)				250.00 0.00	667.21	
	Ministry of Railways						
	Railways						
46	Lumding-Furkating section 140 km Umbrella work PB57/2019-20/NR (CAO/C-1/NFR NFR mor) (616701)	Assam	02/2024 (09/2020)	02/2028 (-)	2,123.70 0.00	215.47	15.00
47	New Bongaigaon - Goalpara - Guwahati Kamakhya 176 km (CAO/C-III/NFR NFR mor) (705572)	Assam	09/2016 (08/2019)	03/2026 (03/2026)	4,060.00 0.00	3,860.64	91.00
48	Jiribam-Imphal 110 km (CAO/C-III/NFR NFR mor) (705391)	Manipur	10/2003 (08/2019)	12/2026 (06/2029)	14,323.00 0.00	16,931.50	78.00
49	Murkongselek-Pasighat 26.15 km (CAO/C-II/NFR NFR mor) (705401)	Multi-States (Assam, Arunachal Pradesh)	02/2011 (10/2019)	03/2025 (12/2026)	435.00 0.00	1,057.21	67.00
50	Dimapur-Kohima 88 km (CAO/C-1/NFR NFR mor) (705392)	Multi-States (Assam, Nagaland)	11/2006 (09/2019)	03/2025 (12/2029)	6,663.00 0.00	6,891.03	48.00
	Total (5)				27,604.70 0.00	28,955.85	
	Ministry of Road Transport & Highways						
	Roads & Highways						
51	Construction of Intermediate Lane Road with hard shoulder from design Km 0.000 to Km 17.387 Total length 17.387 km of Hunli to lthun Bridge section on NH-913 Frontier Highway in State of Arunachal Pradesh on EPC mode under NHO-NE (NHIDCL) (618403)	Arunachal Pradesh	02/2024 (01/2025)	01/2027 (01/2027)	275.50 0.00	166.24	60.96
52	Construction of Intermediate Lane Road with hard shoulder from design chainage Km 0.000 to Km 53.040 Existing Length68.500 Km & Total Design length 53.04 km of Tato to Monigong section of NH-913 Frontier Highway on Nafra Bomdila to Vijaynagar along China border in state of Arunachal pradesh on EPC mode (NHIDCL) (618404)	Arunachal Pradesh	12/2023 (05/2025)	11/2027 (11/2027)	625.61 0.00	274.89	23.03
53	Construction of Intermediate Lane of Pango to Jorging Road from 0000 to Design Km Design Km 40000 Design Length 40.00 Km, Pkg-I, Greenfield Alignment in the State of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (618405)	Arunachal Pradesh	01/2024 (01/2025)	07/2027 (07/2027)	898.19 0.00	259.63	40.12
54	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang from Design Km 0.000 to Km 53.000 Design Length 53.000 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Package-I (NHIDCL) (618402)	Arunachal Pradesh	02/2024 (03/2025)	02/2028 (02/2028)	1,262.43 0.00	257.02	22.12
55	Construction of road from Bomdilla9th Mile- Nafra Lada section of Frontier Highway NH-913 Package 1 9th mile-Nafra 19.554 to 70.00 50.446 (MoRTH) (198592)	Arunachal Pradesh	03/2025 (07/2026)	07/2029 (-)	1,273.44 0.00	151.90	0.00
56	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P-P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (10/2026)	450.65 0.00	403.84	96.61
57	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (04/2026)	184.89 0.00	156.42	99.69
58	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (10/2026)	1,718.59 0.00	1,123.53	82.48
59	Construction of 2-Laning with hard shoulders of Demwe-Brahmakund section of NH-13 from Ch.0.00 km to 18.464 km on EPC under SARDP-NE NHO-NE - Balance Work (NHIDCL) (618445)	Arunachal Pradesh	08/2020 (06/2025)	12/2027 (12/2027)	353.90 0.00	26.82	23.20
60	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang Package-III from design Km 60.000 to Km 121.500 Design Length 61.500 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Pkg-3 (NHIDCL) (618401)	Arunachal Pradesh	02/2024 (07/2025)	07/2028 (07/2028)	1,418.67 0.00	93.29	2.50
61	Improvement and Widening to 2 lane with paved Shoulder of NH-15 old NH-52 from Existing Km 770.600 Design Km 24.819 to Existing km 805.750 Design Km 59.885 Kamlang T-Junction to Chowkham, Existing Length 35.150 Km, Design Length-35.066 Km in the state of Arunachal Pradesh on EPC mode Pkg-2 (NHIDCL) (619014)	Arunachal Pradesh	12/2023 (02/2026)	02/2028 (02/2028)	316.73 0.00	35.10	23.90



Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
62	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (619248)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (06/2028)	441.41 0.00	44.87	19.92
63	Construction of road from Bomdilla 9th Mile - Nafra Lada section of Frontier Highway NH-913 Package 4 Dishum-Sachung-Lada 113.00 to 167.75 54.75km (MoRTH) (619256)	Arunachal Pradesh	03/2024 (07/2026)	07/2030 (-)	1,266.86 0.00	107.62	0.00
64	Construction of road from Km 70.000 to Km 113.000 of Bomdila-Nafra-Lada Section of NH-913 Frontier Highway in the State of Arunachal Pradesh L43.000 Km (MoRTH) (619257)	Arunachal Pradesh	02/2024 (08/2026)	08/2030 (-)	1,240.75 0.00	79.00	0.00
65	Construction of road from Taliha to Tato section of Frontier Highway NH-913 Package 3 km 87.13 to 121.541 34.411km (MoRTH) (619266)	Arunachal Pradesh	03/2024 (08/2026)	08/2029 (-)	735.20 0.00	135.42	0.00
66	Construction of road from km 113.25 to km 160.75 of Huri-Taliha section of NH-913 Pkg 3 Frontier Highway to Intermediate Lane on EPC mode in the State of Arunachal Pradesh (MoRTH) (619267)	Arunachal Pradesh	03/2024 (08/2026)	08/2030 (-)	1,228.64 0.00	137.54	0.00
67	Widening/Improvement of Existing 2 lane to 4-Laning of Karimganj-Silchar section of NH-37 from Design Ch 0.000 near Silchar ISBT to Design Ch 15.970 near Kalinagar Pt I on NH-37 in Assam on HAM Mode Pkg-1 (NHIDCL) (618313)	Assam	03/2024 (09/2025)	09/2027 (09/2027)	1,181.55 0.00	178.80	41.64
68	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314)	Assam	03/2023 (02/2024)	08/2026 (03/2027)	1,716.21 0.00	1,057.81	82.60
69	Widening/Improvement to 4-Lane with Paved Shoulder from existing road and Greenfield alignment form Design Ch. 62.800 start of proposed Nilambazar/Cheragi Bypass to Design Ch. 87.700 near Chandkhira Village of NH-8 on Silchar-Churaibari in the state of Assam on HAM Mode Package-5 (NHIDCL) (618312)	Assam	02/2024 (04/2025)	10/2027 (10/2027)	1,258.13 0.00	187.02	14.60
70	Widening/Improvement to 4-Lane with Paved shoulder for existing as well as Greenfield alignment of Badarpur Churaibari section of NH-8 from Design chainage 87.700 Chandkhira to Km. 106.500 Churaibari section Assam-Tripura border in the state of Assam on HAM Mode Package-6 (NHIDCL) (618311)	Assam	03/2024 (03/2025)	03/2027 (03/2027)	870.00 0.00	158.08	44.90
71	Widening/Improvement to 4-L of Karimgani - sutarkandi section of NH 37 from design Ch 0020 Start of proposed Karimganj Bypass from NH -8 to design Chainage Km 14380 near Sutarkandi Spur Connectivity to Indo/Bangladesh Border on Silchar-Churaibari in the State of Assam on HAM Mode Package-7 (NHIDCL) (618310)	Assam	02/2024 (02/2025)	02/2027 (02/2027)	791.79 0.00	135.92	44.50
72	Widening/Improvement to 4-Laning and Greenfield alignment with Paved shoulder of Silchar-Badarpur Churaibari section of NH-37 & NH-8 from Design chainage 38.600 End point of proposed Badarpur Bypass to Km. 62.800 Start point of proposed Nilambazar/Cheragi Bypass in the state of Assam on HAM Mode Package-4 (NHIDCL) (618309)	Assam	02/2024 (08/2025)	08/2027 (08/2027)	1,319.55 0.00	185.17	25.46
73	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308)	Assam	03/2023 (08/2024)	02/2027 (03/2027)	676.18 0.00	358.25	60.05
74	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289)	Assam	03/2020 (06/2020)	12/2022 (03/2026)	224.85 0.00	209.95	97.76
75	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315)	Assam	02/2023 (01/2024)	07/2026 (03/2027)	1,256.90 0.00	635.51	60.43
76	Widening/Improvement to 4-Lane with Paved Shoulder from Ch.5.580 Km to Ch.25.633 Km Design Ch.0.000 Km to Ch.17.737km Km 901.100 to Km 921.145 of old NH-31 of Bilasipara- Guwahati road NH-17 Section Near Chirakuta to near Mowatari, before Chapar Bypass in the state ol Assam on HAM mode Package-1 (NHIDCL) (618288)	Assam	02/2024 (02/2025)	08/2027 (08/2027)	1,081.15 0.00	163.24	35.98
77	Widening/Improvement to 4-Lane with paved Shoulder from Ch. 25.633 Km to Ch. 52.470 Km Design Ch. 21.850 Km to Ch.48.670 Km for Package-2 of Bilasipura- Guwahati road NH-17 Section Near Mowatari, before Chapar Bypass to Tulungia junction with NH-17 in the state of Assam on HAM mode under NHO-NE Package-2 (NHIDCL) (618287)	Assam	11/2023 (12/2024)	06/2027 (06/2027)	1,338.61 0.00	199.15	12.50
78	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286)	Assam	09/2021 (11/2021)	11/2024 (03/2027)	746.76 0.00	447.07	84.69

Ongoing Projects of North-East Region							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
79	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284)	Assam	03/2023 (12/2023)	12/2026 (12/2026)	1,457.59 0.00	996.13	93.96
80	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1,000.27 0.00	506.42	61.78
81	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1,264.90 0.00	633.62	65.64
82	Construction of 2 lane Major Bridge including approaches over Brahmaputra between Majuli on North Bank and Jorhat on South Bank from km. 11.690 to km. 19.715 length of bridge 6,812.5m Package - II on NH-715K in the state of Assam Job no. 715/AS/2020-21/213 (MoRTH) (618160)	Assam	03/2025 (12/2025)	12/2027 (12/2027)	1,019.17 0.00	17.38	5.31
83	Construction of new 2 Lane with paved shoulders of NH Standards from km 0.080 to km 11.690 L11.610 km in Majuli and from km 19.715 to km 27.484 L 7.769 km in Jorhat on the newly declared NH 715K and construction of 1.10 km flyover on NH-715 with its approaches and service roads L1.10 km, Total Length 20.479 km in the State of Assam Job No. 715K/AS/2023-24/256 (MoRTH) (618159)	Assam	02/2024 (09/2025)	03/2027 (03/2027)	382.10 0.00	25.60	7.15
84	Construction of 2 lane Barpeta Bypass from Km 77900Baradi to Km 86150 Deurikuchi Length8.25Km on NH-427 in the state of Assam under EPC ModeJob No.427/AS/2022-23/245 (MoRTH) (618034)	Assam	03/2023 (02/2025)	08/2026 (03/2027)	173.65 0.00	173.65	20.00
85	Construction of 4 lane Gauripur Bypass Starting bfrom Km 852.56 of NH-31Dumardoha Pt-II and Terminating at Km 862.17 Baladmara via. Khudimari Pt.-II, Fulkumari, Charaldanga, Sajuakuti,Geramari Pt.-III and finally meeting at km 862.17 of NH-17New/ NH-31Old in the State of Assam under EPC Mode Job no. 31/AS/ 2023-24/265 (MoRTH) (617896)	Assam	03/2024 (04/2025)	10/2026 (03/2027)	421.15 0.00	55.16	34.00
86	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895)	Assam	03/2022 (04/2023)	04/2025 (12/2026)	535.03 0.00	215.32	76.78
87	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank,Assam and Phulbari on south Bank,Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373)	Assam	05/2019 (12/2020)	09/2028 (09/2028)	4,997.04 0.00	3,133.25	79.36
88	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371)	Assam	03/2022 (11/2024)	11/2026 (11/2026)	613.89 0.00	385.77	89.76
89	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354)	Assam	12/2023 (03/2024)	03/2026 (12/2026)	846.82 0.00	482.38	90.36
90	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353)	Assam	03/2023 (08/2023)	08/2025 (12/2026)	904.04 0.00	563.52	96.70
91	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352)	Assam	03/2023 (08/2023)	08/2025 (12/2026)	860.37 0.00	559.71	97.25
92	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351)	Assam	03/2023 (08/2023)	08/2025 (12/2026)	890.33 0.00	628.77	92.51
93	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436)	Assam	03/2015 (12/2016)	06/2019 (07/2025)	599.00 0.00	433.62	100.00
94	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340)	Assam	01/2023 (05/2023)	05/2025 (10/2026)	458.59 0.00	264.54	89.92
95	Improvement to 4-Lane with Paved Shoulder from existing km 260000 Design Ch.4560 km to existing km Ch.233000 D. Ch.24560 of Silchar near Nutan Dayapur village - Budha Nagar Section Length-20.00 Km of NH-37 under Package Silchar-Jiribam Pkg-1 in the state of Assam on HAM Mode (NHIDCL) (618331)	Assam	01/2024 (01/2025)	01/2028 (01/2028)	957.95 0.00	214.73	48.17



Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
96	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka-Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326)	Assam	01/2023 (11/2023)	11/2025 (06/2026)	516.88 0.00	323.35	99.70
97	Balance work of 4L of NarimbangloJatinga Junction- Harangajoroad section from Km 0.000 to Km 49.230 of NH-27 (NHAI) (619089)	Assam	03/2022 (01/2023)	01/2026 (09/2026)	1,909.98 0.00	1,434.97	98.00
98	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 514.800 to Km 534.800 20.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (619060)	Assam	10/2014 (10/2024)	09/2025 (10/2026)	344.71 0.00	56.61	74.40
99	Construction of 4-Lane Badarpur Bypass from Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village to Design Chainage km 38600 on NH-37 Old NH-44 at Kandigram Chaita Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Pkg-3 (NHIDCL) (619057)	Assam	02/2023 (02/2024)	08/2026 (03/2027)	574.26 0.00	331.19	71.09
100	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 501.800 to Km 514.800 13.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (619013)	Assam	10/2014 (10/2024)	01/2026 (10/2026)	508.76 0.00	114.14	81.27
101	2L with ES of Yagyi - Kalewa section from Milepost 40/0 to Milepost 115/5 in Myanmar (NHAI) (618958)	Assam	12/2017 (05/2018)	06/2023 (12/2027)	1,200.14 0.00	0.00	52.00
102	Guwahati Ring Road in the State of Assam (NHAI) (618934)	Assam	08/2024 (01/2026)	01/2030 (01/2030)	5,729.47 0.00	364.51	1.30
103	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 477.000 to Km 490800 13.800 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (618442)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	358.72 0.00	100.40	100.00
104	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441)	Assam	01/2016 (10/2024)	09/2025 (10/2026)	467.79 0.00	97.88	88.93
105	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 490.800 to Km 534.800, under SARDP- NE on EPC Mode in the state of Assam Pkg- IV Structures & Toll Plaza (NHIDCL) (618440)	Assam	01/2016 (10/2024)	10/2025 (10/2026)	187.09 0.00	16.71	62.67
106	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438)	Assam	01/2016 (01/2023)	07/2024 (08/2025)	385.57 0.00	681.40	100.00
107	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP-NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437)	Assam	01/2016 (09/2024)	03/2025 (08/2025)	274.34 0.00	116.67	100.00
108	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389)	Manipur	09/2021 (08/2022)	02/2024 (10/2026)	310.76 0.00	287.73	97.00
109	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388)	Manipur	09/2021 (07/2023)	01/2025 (12/2026)	315.56 0.00	257.41	94.50
110	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387)	Manipur	03/2023 (03/2024)	03/2026 (12/2026)	578.98 0.00	283.36	80.75
111	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358)	Manipur	09/2021 (11/2021)	05/2023 (12/2025)	311.18 0.00	231.08	87.42
112	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357)	Manipur	09/2021 (11/2021)	05/2023 (01/2026)	477.86 0.00	330.13	84.87
113	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356)	Manipur	03/2021 (06/2021)	12/2022 (04/2026)	234.08 0.00	201.13	98.50
114	Construction of of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355)	Manipur	07/2021 (09/2021)	03/2023 (03/2026)	483.87 0.00	375.87	95.28

Ongoing Projects of North-East Region							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
115	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from Design Chainage km 118850 to km 130000 Package-4A in the State of Manipur on EPC Mode (NHIDCL) (618349)	Manipur	04/2020 (08/2025)	08/2026 (11/2026)	204.12 0.00	115.96	26.53
116	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from km 130.000 to km 141.029 Package-4B in the State of Manipur on EPC Mode (NHIDCL) (618348)	Manipur	06/2020 (11/2025)	11/2026 (11/2026)	177.76 0.00	100.95	14.63
117	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346)	Manipur	04/2020 (07/2020)	06/2022 (09/2026)	232.99 0.00	155.44	100.00
118	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345)	Manipur	06/2020 (08/2020)	08/2022 (10/2026)	365.53 0.00	198.73	88.20
119	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344)	Manipur	03/2021 (08/2021)	08/2023 (12/2026)	673.27 0.00	563.39	85.84
120	Widening to 2-Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 15.940 km to 33.120 Km Existing Chainage Km 15.946 to Km 33.395 Total length17.180 Km in the State of Manipur on EPC mode PKG-2 - Balance Works & Rectification works (NHIDCL) (618338)	Manipur	03/2021 (03/2025)	03/2026 (10/2026)	195.14 0.00	162.73	93.22
121	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336)	Manipur	09/2021 (06/2022)	12/2023 (12/2026)	579.63 0.00	408.21	86.53
122	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335)	Manipur	12/2021 (11/2022)	05/2024 (12/2026)	410.68 0.00	386.28	91.02
123	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334)	Manipur	12/2021 (02/2023)	02/2025 (12/2026)	504.76 0.00	328.00	95.20
124	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao vllage under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333)	Manipur	01/2023 (12/2023)	12/2025 (12/2026)	760.16 0.00	428.17	92.52
125	Widening/Improvement to 2 lane with earthen shoulder of Choithar to Marrem Khullen section of NH-202 of Imphal Ukhrul Jessami Economic Corridor from Design Chainage km 53.110 to km 95.700 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-5 (NHIDCL) (618306)	Manipur	03/2023 (05/2025)	03/2027 (08/2027)	564.05 0.00	173.58	14.50
126	Widening/Improvement to 2 lane with earthen shoulder of Marrem Khullen to Jessami section of NH-202 of Imphal - Ukhrul - Jessami Economic Corridor from Design Chainage km 95.700 to km 140.180 in the State of Manipur on EPC mode under Bharatmala Pariyojana under NHO-NE Package-6 (NHIDCL) (618305)	Manipur	03/2023 (12/2024)	12/2026 (08/2027)	554.66 0.00	230.00	27.34
127	Widening/Improvement to 2 Lane with earthen shoulder of Jessami to Laynen bridge Nagaland border section of NH-29 of Imphal -Ukhrul - Jessami Economic Corridor from km 0.000 to km 11.009 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-7 (NHIDCL) (618304)	Manipur	03/2023 (12/2024)	06/2026 (02/2027)	164.89 0.00	132.28	31.23
128	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416)	Manipur	02/2021 (06/2021)	12/2022 (03/2027)	226.32 0.00	190.19	75.08
129	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415)	Manipur	02/2021 (06/2021)	12/2022 (03/2026)	188.36 0.00	0.00	100.00
130	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298)	Manipur	03/2021 (07/2021)	01/2023 (09/2026)	211.70 0.00	272.30	95.48
131	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Daili to Kuraopokpi section of Imphal-Kohima road NH-02 Design Chainage from Km 274610 to Km 287000 in the state of Manipur on EPC mode Pkg-4B (NHIDCL) (618299)	Manipur	09/2020 (12/2024)	06/2026 (01/2027)	268.98 0.00	210.28	58.70
132	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300)	Manipur	09/2020 (10/2020)	04/2022 (12/2026)	379.39 0.00	314.73	91.39



Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
133	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303)	Manipur	03/2020 (07/2020)	06/2022 (10/2026)	222.77 0.00	140.90	88.96
134	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302)	Manipur	03/2020 (07/2020)	06/2022 (10/2026)	256.04 0.00	195.00	98.12
135	Widening/Improvement of existing 2-lane to 4-Lane Divided Highway from Kuraopokpi to Sekmai section of Imphal-Kohima Road Design Ch. km 287.00 to 297.700 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5A (NHIDCL) (618301)	Manipur	09/2020 (02/2025)	08/2026 (12/2026)	228.97 0.00	143.26	48.36
136	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418)	Meghalaya	09/2021 (05/2022)	05/2024 (03/2027)	359.86 0.00	310.09	83.15
137	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419)	Meghalaya	03/2023 (09/2024)	09/2026 (06/2027)	562.48 0.00	340.17	52.29
138	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420)	Meghalaya	03/2023 (09/2024)	09/2026 (06/2027)	686.03 0.00	360.59	50.95
139	Improvement and Widening two lannig with paved Shoulder of NH 127B from km 31.500 Goeragre to km 63.224 Package-II in state of Meghalaya (MoRTH) (618076)	Meghalaya	12/2023 (05/2025)	05/2027 (-)	504.00 0.00	75.72	4.50
140	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421)	Meghalaya	03/2023 (09/2024)	09/2026 (03/2027)	620.30 0.00	332.96	75.41
141	Improvement and Widening of National Highway No. 127B Darugiri - Songsak - Williamnagar Junction Section to two lane with paved shoulder from design Km 0000 to Km 36635 Design length 36.635 Km existing Km 112000 to Km 151060 of NH-1278 under Bharatmala Pariyojana Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618294)	Meghalaya	03/2023 (09/2025)	09/2027 (09/2027)	801.07 0.00	186.68	27.76
142	Improvement/Widening of New NH-217 Dainadubi-Darugiri section to Two lane with paved shoulder in Meghalaya from design Km 0000 to Km 40840 existing Km 8600 to Km 53000 of Old NH-62 under BMP Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618295)	Meghalaya	03/2023 (03/2025)	03/2027 (03/2027)	705.83 0.00	0.00	49.82
143	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2026)	284.21 0.00	170.81	43.86
144	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II - Balance work Pkg-4 (NHIDCL) (618375)	Meghalaya	07/2020 (04/2024)	04/2026 (10/2026)	445.51 0.00	42.39	53.85
145	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376)	Meghalaya	07/2020 (02/2024)	08/2026 (12/2026)	525.67 0.00	0.00	53.22
146	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377)	Meghalaya	07/2020 (10/2023)	10/2025 (06/2026)	351.12 0.00	243.50	100.00
147	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthern shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE ong-Don-Maw/MG/2020-21/294 (MoRTH) (617885)	Meghalaya	08/2020 (02/2022)	08/2023 (09/2026)	302.88 0.00	232.62	99.62
148	Up-gradation to 2 lane with paved shoutders of Pawlrang - Rulchawm section- of NH-102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 72.030 to km 104.129 including 2.459 km re-alignment section from Tuivai River to Rulchawm connecting km 48.150 of NH-6 [Design Chainage km 68.170 to km 98.579] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-3 Keifang- Tuivai Pkg-3 (NHIDCL) (619010)	Mizoram	12/2021 (11/2023)	05/2025 (07/2026)	500.88 0.00	443.52	99.52
149	2-laning of Zorinpui - Longmasu section of NH-502A from km 0.000 to km 28.244 in the State of Mizoram on EPC mode under NHO-NE, stretch of IMBR (NHIDCL) (618452)	Mizoram	02/2023 (12/2024)	12/2026 (12/2027)	781.85 0.00	48.39	4.71



Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
150	Construction of Twin Tube Uni-directional Aizawl Bypass Tunnel of 2.5 km and its approaches of 2.1 km from km 10.600 to km 15.200 on Sarrang - Phaibawk section of NH-6 in the State of Mizoram on EPC Mode under NHO-NE Package-2 (NHIDCL) (618323)	Mizoram	01/2024 (12/2025)	12/2028 (-)	1,313.28 0.00	0.11	0.00
151	Balance work of widening to two laning/re-alignment and geometric improvement from Km. 11000 to Km. 114618 with rectification of damaged stretches and provision of protection works in vulnerable location of NH-44 in the State of Mizoram. (MoRTH) (619321)	Mizoram	10/2025 (05/2026)	05/2028 (-)	170.96 0.00	0.00	2.00
152	Construction of 2-lane Aizawl Bypass from km 15.200 to km 34.500 Package-3 on Sairang - Phaibawk section of NH-6 in the State of Mizoram under Bharatmala Pariyojna on EPC Mode under NHO-NE (NHIDCL) (618324)	Mizoram	02/2023 (10/2025)	11/2028 (-)	720.72 0.00	102.91	15.10
153	Construction of 4-Laning of West Serawlg-Sairang section of NH-6 from Existing Chainage km 142000 to km 158900 Design Chainage km 123400 to km 136260 on Silchar - Vairengte - Sairang road in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-8 (NHIDCL) (618321)	Mizoram	02/2024 (11/2025)	11/2028 (-)	875.79 0.00	288.71	13.95
154	Construction of 4-Laning of N. Kawnpui N. Mualvum Mualkhang via Khamrang Village section Package-7 of NH-6 from Existing Chainage km 127200 to km 142000 Design Chainage km 111850 to km 123400 on Silchar - Vairengte - Sairang road in the State of Mizoram on EPC mode (NHIDCL) (618320)	Mizoram	02/2024 (10/2025)	10/2028 (-)	866.32 0.00	198.28	18.90
155	4-Laning of Sethawn - N. Kawnpui section Package-6 of NH-6 from Existing Chainage km 107850 to km 126315 Design Chainage km 95500 to km 111850 on Silchar-Vairengte- Sairang road, Vairengte - Sairang Pkg-6 (NHIDCL) (618319)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	595.65 0.00	189.40	6.72
156	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363)	Mizoram	06/2021 (07/2021)	01/2023 (12/2026)	740.58 0.00	494.49	61.34
157	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362)	Mizoram	03/2021 (06/2021)	12/2022 (11/2026)	698.45 0.00	554.29	64.78
158	4-Laning of Kolasib - Sethawn section Package-5 of NH-6 from Existing Chainage km 86000 to km 107850 Design Chainage km 77500 to km 95500 on silchar - vairengte - sairang road under Bharatmala Pariyojna on EPC mode under NHO-NE Vairengte - Sairang Pkg-5 (NHIDCL) (618318)	Mizoram	11/2021 (07/2025)	07/2027 (06/2027)	720.40 0.00	260.12	11.86
159	4-Laning of chhimluang-Kolasib from section pkg-4 of NH-306 & NH-6 existing chainage km 59700 to km 86000 design chainage km 61000 to km 77500 on Silchar-vairengte-sairang road in the state of Mizoram under Bharatmala Pariyojna on EPC mode Vairengte - Sairang Pkg-4 (NHIDCL) (618317)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	561.91 0.00	224.19	17.12
160	4-Laning of Vairengte - Chhimluang section Package-3 of NH-306 from Existing Chainage km 43000 to Km 59700 Design Chainage km 46000 to km 60850 on Silchar - Vairengte- Sairang road in the State of Mizoram under Bharatmala Pariyojna under NHO-NE. Package-1&2 in Assam state (NHIDCL) (618316)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	491.39 0.00	245.24	17.86
161	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379)	Mizoram	09/2019 (10/2019)	04/2023 (08/2026)	752.89 0.00	125.64	95.35
162	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383)	Mizoram	09/2019 (03/2020)	09/2023 (06/2026)	637.06 0.00	551.56	99.82
163	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359)	Multi-States (Arunachal Pradesh, Assam)	03/2023 (09/2024)	03/2027 (03/2027)	665.47 0.00	380.97	96.70
164	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886)	Nagaland	06/2020 (06/2024)	06/2026 (04/2027)	252.20 0.00	65.40	44.46
165	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414)	Nagaland	01/2021 (09/2023)	09/2025 (09/2025)	258.52 0.00	136.09	96.53
166	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	442.54 0.00	0.00	58.50
167	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	497.18 0.00	0.00	85.67

Ongoing Projects of North-East Region							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
168	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	430.24 0.00	0.00	87.00
169	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413)	Nagaland	02/2021 (06/2023)	06/2025 (09/2026)	177.77 0.00	111.89	95.62
170	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422)	Nagaland	03/2021 (09/2023)	09/2025 (07/2026)	161.73 0.00	101.28	99.75
171	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length-20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423)	Nagaland	03/2018 (08/2023)	08/2025 (03/2026)	215.79 0.00	173.12	100.00
172	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290)	Nagaland	07/2020 (10/2020)	04/2022 (12/2026)	202.36 0.00	102.45	46.77
173	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH- 39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291)	Nagaland	07/2020 (06/2023)	06/2025 (12/2026)	159.85 0.00	128.51	39.62
174	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length- 10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292)	Nagaland	07/2020 (10/2020)	10/2022 (10/2027)	277.44 0.00	201.99	71.29
175	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293)	Nagaland	07/2020 (11/2023)	11/2026 (11/2026)	232.29 0.00	120.94	27.39
176	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296)	Nagaland	03/2020 (11/2023)	11/2025 (09/2026)	330.80 0.00	268.18	98.39
177	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328)	Nagaland	03/2016 (09/2023)	09/2025 (09/2026)	562.98 0.00	551.33	84.32
178	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297)	Nagaland	03/2020 (01/2024)	01/2026 (12/2026)	355.79 0.00	0.00	43.13
179	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon Road on EPC Basis from existing road Km. 76.640 to Km 98.065 Design chainage Km. 63.800 to Km. 86.835 Design Length-23.035 Km in the state of Nagaland under SARDP-NE PKG-IV Balance work (NHIDCL) (619059)	Nagaland	03/2018 (09/2023)	09/2025 (12/2026)	323.98 0.00	147.38	79.03
180	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071)	Sikkim	10/2021 (05/2022)	05/2024 (12/2026)	385.15 0.00	254.56	92.00
181	Construction/Up gradation of Existing road to 2 Lane with Paved Shoulder including Geometric Improvement from Ranipool to Pakyong Balance work from Km 2.000 to 16.167 of NH-717-A on EPC basis under SARDP-NE Phase A in the State of Sikkim (NHIDCL) (618426)	Sikkim	03/2018 (01/2023)	07/2024 (12/2026)	264.84 0.00	127.34	87.03
182	Realignment of NH-717A from Design Ch.0.00 Km 77.800 of NH-10 to Design Ch.2.00 Km 3.100 of NH-717A with two lane paved shoulder including Major Bridge of 680 m in the State of Sikkim on EPC Mode-COS work (NHIDCL) (618428)	Sikkim	01/2021 (04/2021)	04/2023 (05/2026)	264.84 0.00	70.71	100.00
183	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450)	Sikkim	07/2020 (10/2020)	05/2022 (12/2026)	292.80 0.00	256.52	65.15
184	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449)	Sikkim	07/2020 (10/2020)	04/2023 (09/2026)	230.45 0.00	249.71	86.19

Ongoing Projects of North-East Region							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
185	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. <i>(NHIDCL)</i> (618448)	Sikkim	10/2020 (12/2020)	12/2023 (05/2027)	816.79 0.00	474.96	64.31
186	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. <i>(NHIDCL)</i> (618447)	Sikkim	01/2021 (02/2021)	02/2024 (05/2027)	410.60 0.00	241.77	82.64
187	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C <i>(NHIDCL)</i> (618446)	Sikkim	10/2020 (05/2021)	05/2024 (09/2026)	493.42 0.00	395.19	79.13
188	Improvement & widening of existing NH-08 to 4-lane with Paved Shoulder from Champak Nagar to Khayerpur section design Km 242500 to Km 261610 in the state of Tripura on EPC basis under NHO-NE <i>(NHIDCL)</i> (618350)	Tripura	12/2023 (09/2024)	09/2026 (03/2027)	920.66 0.00	404.82	48.30
189	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE <i>(NHIDCL)</i> (618417)	Tripura	03/2023 (03/2024)	03/2027 (03/2027)	2,026.05 0.00	462.34	9.20
190	Improvement and Widening to 2-lane with paved shoulder of road from design Km 72.000 Pati Chhari to design Km 107.654 Harina Total length 35.654 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-4 <i>(NHIDCL)</i> (618367)	Tripura	01/2024 (12/2024)	12/2026 (12/2027)	726.90 0.00	100.84	9.50
191	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 <i>(NHIDCL)</i> (618368)	Tripura	01/2024 (09/2024)	09/2026 (05/2027)	670.90 0.00	183.24	14.90
192	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 <i>(NHIDCL)</i> (618369)	Tripura	01/2024 (09/2024)	09/2026 (03/2027)	657.21 0.00	306.14	61.40
193	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 <i>(NHIDCL)</i> (618370)	Tripura	01/2024 (07/2024)	07/2026 (04/2027)	431.78 0.00	265.36	63.15
194	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total length 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work <i>(NHIDCL)</i> (618385)	Tripura	02/2020 (09/2024)	03/2026 (03/2026)	174.43 0.00	67.10	53.14
195	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 <i>(NHIDCL)</i> (618307)	Tripura	02/2022 (01/2023)	01/2025 (01/2026)	456.88 0.00	205.69	54.56
196	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km <i>(NHIDCL)</i> (618411)	Tripura	01/2023 (05/2023)	11/2024 (10/2026)	195.95 0.00	95.54	72.48
	Total (146)				97,618.87 0.00	39,787.33	
	Department of Telecommunications						
	Telecommunication						
197	Amended BharatNet Program - AS <i>(Department of Telecommunications)</i> (240484)	Assam	08/2023 (03/2026)	03/2029 (-)	832.00 0.00	83.16	0.00
198	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya <i>(Department of Telecommunications)</i> (701598)	Meghalaya	09/2019 (09/2020)	03/2022 (06/2026)	971.96 0.00	167.23	100.00
199	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam <i>(Department of Telecommunications)</i> (701597)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2026)	1,255.49 0.00	237.98	99.84
200	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. <i>(BSNL)</i> (709857)	Multi-States (Assam, Arunachal Pradesh, Manipur, Meghalaya, Nagaland, Sikkim, Tripura, Mizoram)	05/2023 (06/2023)	06/2025 (09/2026)	24,544.55 0.00	9,173.85	98.63
201	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT <i>(BSNL)</i> (709856)	Multi-States (Manipur, Arunachal Pradesh, Meghalaya, Sikkim, Mizoram, Nagaland, Assam, Tripura)	05/2023 (05/2023)	08/2024 (08/2026)	645.13 0.00	410.40	100.00
202	Amended BharatNet Program - ARP, NGL, MNP <i>(Department of Telecommunications)</i> (976009)	Multi-States (Manipur, Arunachal Pradesh, Nagaland)	08/2023 (06/2025)	06/2028 (-)	1,168.00 0.00	123.28	0.71

Ongoing Projects of North-East Region

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
203	BharatNet (<i>Department of Telecommunications [DoT]</i>) (706775)	Multi-States (Manipur, Arunachal Pradesh, Sikkim, Nagaland, Assam, Meghalaya, Tripura, Mizoram)	07/2017 (10/2011)	08/2023 (03/2019)	12,709.00 0.00	10,320.00	99.98
204	BharatNet Phase-II (<i>Department of Telecommunications</i>) (547243)	Multi-States (Mizoram, Meghalaya, Arunachal Pradesh, Assam, Nagaland, Sikkim, Tripura, Manipur)	07/2017 (11/2017)	05/2023 (-)	22,174.56 0.00	20,691.72	93.33
205	Saturation 4G mobile coverage of Uncovered Villages through USOF (<i>Department of Telecommunications [DoT]</i>) (400013)	Multi-States (Mizoram, Nagaland, Arunachal Pradesh, Assam, Manipur, Tripura, Sikkim, Meghalaya)	07/2022 (07/2022)	06/2024 (03/2027)	26,316.00 0.00	8,722.82	89.40
206	Amended BharatNet Program - MGH, MZM, TRP (<i>Department of Telecommunications</i>) (462136)	Multi-States (Mizoram, Tripura, Meghalaya)	08/2023 (04/2025)	04/2029 (-)	768.00 0.00	0.00	0.00
207	Amended BharatNet Program - SKM (<i>Department of Telecommunications</i>) (946208)	Sikkim	08/2023 (06/2026)	06/2029 (-)	160.00 0.00	0.00	0.00
	Total (11)				91,544.69 0.00	49,930.44	
	Department of Water Resources, River Development & GR						
	Water Resources						
208	Borolia Irrigation Project (<i>Department of Water Resources, River Development & GR</i>) (701370)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 0.00	44.70	55.44
209	Thoubal Multipurpose Project (<i>Water Resources Department-MN</i>) (701400)	Manipur	04/1997 (04/1997)	12/2019 (12/2026)	1,449.44 0.00	1,848.17	99.00
	Total (2)				1,705.60 0.00	1,892.87	




Table 6: All Ongoing Projects



All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Ministry of Civil Aviation							
Aviation & Aviation Infrastructure							
1	Construction of New Domestic Terminal Building Building and miscellaneous works including maintenance, operations and AICMC at Kadapa Airport <i>(Airport Authority of India [AAI])</i> (612786) (-) (-)	Andhra Pradesh	03/2023 (01/2024)	01/2026 (09/2026)	265.91 0.00	186.36	83.00
2	Construction of New Integrated Terminal Building and associated works including apron to park 3 code E type of aircraft or 6 code C type of aircraft at Vijayawada Airport. <i>(Airport Authority of India [AAI])</i> (701107) (-) (-)	Andhra Pradesh	06/2020 (09/2020)	09/2022 (11/2026)	611.80 0.00	600.58	91.20
3	Construction of New Domestic Terminal Building at Rajahmundry Airport. <i>(Airport Authority of India [AAI])</i> (701121) (-) (-)	Andhra Pradesh	12/2022 (08/2023)	08/2025 (10/2026)	347.15 0.00	190.89	97.00
4	Guwahati Airport New Integrated Terminal Building Construction Project <i>(Adani Airport Holdings Limited)</i> (706724) (-) (-)	Assam	12/2016 (03/2018)	03/2025 (06/2026)	1,712.00 0.00	2,670.23	99.50
5	Development of New Civil Enclave at Bihta <i>(Airport Authority of India [AAI])</i> (612183) (-) (-)	Bihar	08/2024 (04/2025)	03/2027 (-)	1,413.00 0.00	19.44	4.48
6	Development of New Civil Enclave and associated works at Darbhanga Airport <i>(Airport Authority of India [AAI])</i> (612194) (-) (-)	Bihar	07/2024 (07/2024)	07/2026 (11/2026)	911.66 0.00	453.47	72.60
7	Construction of New Domestic Terminal Building [Phase-I and II] and other allied structures at JPNI Airport, Patna <i>(Airport Authority of India [AAI])</i> (701101) (-) (-)	Bihar	10/2018 (10/2018)	05/2026 (08/2026)	1,216.90 0.00	1,216.11	99.35
8	Development of Keshod Airport. <i>(Airport Authority of India [AAI])</i> (619054) (-) (-)	Gujarat	01/2024 (07/2025)	01/2027 (-)	363.10 0.00	109.27	48.76
9	Development of Dholera International Greenfield Airport , Gujarat <i>(Airport Authority of India [AAI])</i> (701126) (-) (-)	Gujarat	06/2022 (07/2022)	06/2026 (09/2026)	1,305.00 0.00	987.56	89.00
10	Construction of NTB complex including apron, taxi track and other associated civil works and electrical & mechanical installations towards Tawi River side at CA Jammu. <i>(Airport Authority of India [AAI])</i> (611047) (-) (-)	Jammu and Kashmir	10/2023 (12/2023)	06/2026 (11/2026)	861.37 0.00	388.13	61.35
11	Construction of New Domestic Terminal Building and Miscellaneous works at Hubli Airport <i>(Airport Authority of India [AAI])</i> (612787) (-) (-)	Karnataka	06/2023 (01/2024)	01/2026 (09/2026)	320.47 0.00	169.11	91.75
12	Construction of New Domestic Terminal Building and Miscellaneous Works at Belagavi Airport. <i>(Airport Authority of India [AAI])</i> (612788) (-) (-)	Karnataka	06/2023 (02/2024)	02/2026 (09/2026)	322.45 0.00	242.16	98.00
13	Development of additional RESA on either end on Runway 10-28 at Calicut Airport. Construction of embankment with slope protection, drainage system and associated works for additional RESA on either end on Runway 10-28 <i>(Airport Authority of India [AAI])</i> (612789) (-) (-)	Kerala	06/2023 (02/2024)	09/2025 (03/2027)	484.57 0.00	246.96	66.14
14	Construction of Terminal Building & Associated works at Leh Airport, Ladakh <i>(Airport Authority of India [AAI])</i> (400010) (-) (-)	Ladakh	07/2018 (09/2018)	09/2021 (09/2026)	480.00 0.00	524.37	93.00
15	C/o NITB Imphal Airport <i>(Airport Authority of India [AAI])</i> (706718) (-) (-)	Manipur	11/2021 (07/2022)	07/2024 (12/2026)	499.00 0.00	215.10	53.69
16	SITC of ATM Automation System and ASMGCS [Including SMR & MLAT] for Mumbai, Navi Mumbai, Jewar [earlier MOPA, without ASMGCS], HIAL & BIAL <i>(Airport Authority of India [AAI])</i> (611570) (-) (-)	Multi-States (Karnataka, Maharashtra, Telangana, Uttar Pradesh)	12/2020 (10/2022)	09/2025 (08/2026)	500.48 0.00	399.77	80.00
17	Development of New Greenfield Airport at Bundi, Kota Rajasthan. <i>(Airport Authority of India [AAI])</i> (618977) (-) (-)	Rajasthan	08/2025 (10/2025)	10/2027 (11/2027)	1,507.00 0.00	99.47	13.80
18	Construction of New Passenger Terminal Building for Domestic Operations at Jodhpur Airport. <i>(Airport Authority of India [AAI])</i> (701127) (-) (-)	Rajasthan	06/2022 (05/2023)	03/2026 (06/2026)	480.00 0.00	348.23	100.00
19	Construction of New Integrated Passenger Terminal Building at Udaipur Airport <i>(Airport Authority of India [AAI])</i> (701128) (-) (-)	Rajasthan	06/2023 (11/2023)	03/2026 (09/2026)	887.00 0.00	588.79	83.71

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
20	Widening of basic strip at Western Side of Runway Chainage 80m to 920m i/c slope stabilization Measures [Balance work] of uphill and Improvement of Storm Water Drainage System at Pakyong Airport, Sikkim on design & build basis [EPC] with integrated 10 years maintenance. (Airport Authority of India [AAI]) (612793) (-) (-)	Sikkim	11/2023 (12/2023)	06/2026 (06/2027)	323.26 0.00	87.61	36.14
21	Construction of 8 Nos. RETs for Runway 07-25, 3 nos. RETs for Runway 12-30, Extension of parallel Taxi Track-R with link Taxi- track and Link Taxi-Track-K1 at Chennai Airport (Airport Authority of India [AAI]) (432726) (-) (-)	Tamil Nadu	07/2024 (10/2025)	01/2028 (-)	480.06 0.00	9.68	3.60
22	Modernization of Chennai Airport, Phase II, Part 2 (Airport Authority of India [AAI]) (611602) (-) (-)	Tamil Nadu	05/2018 (06/2023)	07/2025 (04/2027)	1,207.00 0.00	368.10	49.50
23	Development of Lal Bahadur Shastri International airport, Varanasi including C/o New Terminal Building, Apron Extension, Runway Extension, PTT and allied works. (Airport Authority of India [AAI]) (701113) (-) (-)	Uttar Pradesh	07/2024 (07/2024)	07/2027 (07/2027)	2,869.65 0.00	812.14	35.00
24	Development of New Integrated Civil Enclave at Agra Airport (Airport Authority of India [AAI]) (701122) (-) (-)	Uttar Pradesh	06/2024 (07/2024)	07/2026 (11/2026)	579.00 0.00	245.81	46.24
25	Development of New Civil Enclave at Bagdogra Airport (Airport Authority of India [AAI]) (611495) (-) (-)	West Bengal	08/2024 (09/2024)	03/2027 (03/2027)	1,549.00 0.00	570.75	29.27
26	Re-Construction of Rigid portions of Secondary Runway, K and A Taxiway and Strengthening of C Taxiway at NSCBI Airport Kolkata. (Airport Authority of India [AAI]) (612791) (-) (-)	West Bengal	03/2023 (12/2023)	10/2025 (08/2026)	328.30 0.00	153.75	73.90
	Total (26)				21,825.13 0.00	11,903.84	
	Ministry of Coal						
	Coal						
27	TIKAK EXTENSION OCP (INVALID CO.) (615820) (-) (-)	Assam	07/2022 (07/2022)	07/2031 (-)	159.77 0.00	112.79	89.73
28	TIRAP OCP (INVALID CO.) (615821) (-) (-)	Assam	11/2022 (11/2022)	11/2030 (-)	289.46 0.00	105.66	5.00
29	PORDA CHIMTAPANI OCP [10 MTY] (SECL - CIL) (400144) (-) (-)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	2,310.12 0.00	119.20	11.81
30	BAROUD OC EXPANSION [3.0-10.0M] (SECL - CIL) (400149) (-) (-)	Chhattisgarh	08/2020 (08/2020)	03/2029 (-)	2,309.80 0.00	1,040.67	55.95
31	DIPKA EXPANSION OCP [40 MTY] (SECL - CIL) (400354) (-) (-)	Chhattisgarh	12/2020 (12/2020)	03/2029 (-)	5,241.40 0.00	2,949.65	39.34
32	GEVRA OC [70 MTY] (SECL - CIL) (400424) (-) (-)	Chhattisgarh	03/2016 (03/2016)	03/2023 (03/2027)	11,816.40 0.00	6,984.95	78.48
33	AMERA OC RCE [1.0 MTY] (SECL - CIL) (613798) (-) (-)	Chhattisgarh	02/2015 (02/2015)	03/2026 (-)	335.97 0.00	91.95	42.47
34	AMGAON OC RCE [1.0 MTY] (SECL - CIL) (613799) (-) (-)	Chhattisgarh	07/2015 (07/2015)	03/2026 (-)	316.11 0.00	193.00	78.86
35	JAGANNATHPUR OC RCE PROJECT (SECL - CIL) (613800) (-) (-)	Chhattisgarh	07/2016 (07/2016)	03/2025 (03/2027)	459.49 0.00	280.03	96.15
36	MAHAMAYA OCP [1.50 MTY] (SECL - CIL) (613801) (-) (-)	Chhattisgarh	05/2018 (05/2018)	03/2026 (03/2028)	410.26 0.00	188.90	54.60
37	KATKONA RO UG MINE (SECL - CIL) (615191) (-) (-)	Chhattisgarh	01/2023 (01/2023)	03/2029 (-)	329.21 0.00	62.01	2.01
38	PELMA OC MDO (SECL - CIL) (616234) (-) (-)	Chhattisgarh	10/2022 (10/2022)	03/2033 (-)	1,725.04 0.00	16.71	23.75
39	KUSMUNDA OC EXPANSION PROJECT (SECL - CIL) (617287) (-) (-)	Chhattisgarh	11/2024 (11/2024)	03/2030 (-)	4,516.88 0.00	847.62	23.85

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
40	MANIKPUR OC EXPANSION PROJECT (SECL - CIL) (617288) (-) (-)	Chhattisgarh	01/2025 (01/2025)	03/2029 (-)	382.61 0.00	139.04	21.29
41	RPR FOR DURGAPUR OCP 10 MTY (SECL - CIL) (619171) (-) (-)	Chhattisgarh	09/2025 (09/2025)	03/2032 (-)	2,415.91 0.00	5.36	0.01
42	MADANNAGAR OCP 12 MTY - MDO (SECL - CIL) (619172) (-) (-)	Chhattisgarh	12/2024 (12/2024)	03/2033 (-)	1,859.19 0.00	1.53	0.00
43	HURA C OCP (ECL - CIL) (400018) (-) (-)	Jharkhand	08/2022 (08/2022)	03/2029 (-)	859.41 0.00	457.91	63.30
44	KONAR EXPANSION OCP (CCL - CIL) (400073) (-) (-)	Jharkhand	01/2022 (01/2022)	03/2032 (-)	674.65 0.00	175.59	51.05
45	KARO EXPANSION OCP (CCL - CIL) (400074) (-) (-)	Jharkhand	01/2022 (01/2022)	03/2029 (-)	849.31 0.00	213.82	23.32
46	SANGHMITRA OC (CCL - CIL) (400136) (-) (-)	Jharkhand	03/2024 (03/2024)	03/2032 (-)	2,660.00 0.00	17.34	16.77
47	CHANDRAGUPT OCP (CCL - CIL) (400138) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	973.50 0.00	440.75	25.11
48	KOTRE BASANTPUR PACHMO OCP (Ministry of Coal) (400139) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2032 (-)	625.40 0.00	456.48	46.09
49	Pachwara South Coal Block (NLC India Limited) (400142) (-) (-)	Jharkhand	03/2016 (11/2019)	09/2028 (-)	2,242.90 0.00	1,448.39	87.00
50	RPR MAGADH EXP OCP (Ministry of Coal) (400150) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2028 (-)	6,964.33 0.00	1,880.46	39.48
51	NORTH URIMARI EXPANSION OCP (Ministry of Coal) (400151) (-) (-)	Jharkhand	07/2021 (07/2021)	03/2029 (-)	634.30 0.00	598.45	69.08
52	EPR ROHINI - KARKETTA OCP (Ministry of Coal) (400153) (-) (-)	Jharkhand	01/2021 (01/2021)	03/2028 (-)	995.57 0.00	85.34	24.21
53	EPR PUNDI OCP (Ministry of Coal) (400154) (-) (-)	Jharkhand	11/2020 (11/2020)	03/2027 (-)	639.60 0.00	14.78	11.24
54	EPR ASHOK OC (Ministry of Coal) (400155) (-) (-)	Jharkhand	05/2021 (05/2021)	03/2031 (-)	2,821.07 0.00	186.02	27.96
55	EPR AMRAPALI OCP (CCL - CIL) (400156) (-) (-)	Jharkhand	02/2020 (02/2020)	03/2028 (-)	4,983.57 0.00	1,383.71	43.78
56	RAJRAPPA RCE OCP (CCL - CIL) (400160) (-) (-)	Jharkhand	12/2009 (12/2009)	03/2016 (03/2027)	510.85 0.00	488.71	75.78
57	CHITRA EAST OC (ECL - CIL) (400172) (-) (-)	Jharkhand	08/2018 (08/2018)	03/2026 (03/2028)	513.99 0.00	276.49	53.03
58	JHARKHAND-LAIYO OCP (Ministry of Coal) (400352) (-) (-)	Jharkhand	08/2020 (08/2020)	03/2031 (-)	654.87 0.00	26.54	32.63
59	MOONIDIH XV SEAM UG (BCCL - CIL) (400425) (-) (-)	Jharkhand	08/2011 (08/2011)	03/2019 (09/2026)	1,230.27 0.00	813.42	85.33
60	AMALAGAMATED NTST KUJAMA OCP 8 (BCCL - CIL) (611864) (-) (-)	Jharkhand	01/2023 (01/2023)	03/2030 (-)	4,011.85 0.00	449.34	31.64
61	MURAIH UG PROJECT (BCCL - CIL) (613808) (-) (-)	Jharkhand	02/2011 (02/2011)	04/2014 (12/2026)	339.87 0.00	191.49	70.47
62	TAPIN SOUTH EXPN (CCL - CIL) (615349) (-) (-)	Jharkhand	11/2020 (11/2020)	03/2028 (-)	230.41 0.00	22.02	24.19

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
63	SIRKA OC (CCL - CIL) (615822) (-) (-)	Jharkhand	05/2020 (05/2020)	03/2028 (-)	183.18 0.00	89.92	56.92
64	TETARIAKHAR OC (CCL - CIL) (615843) (-) (-)	Jharkhand	11/2019 (11/2019)	03/2025 (03/2027)	232.64 0.00	51.07	30.17
65	CHUPERBHITA SIMLONG OCP MDO 6 (ECL - CIL) (616225) (-) (-)	Jharkhand	12/2023 (12/2023)	03/2037 (-)	979.08 0.00	0.00	0.05
66	JARANGDIH EXPN. OCP 1.5 MTY (CCL - CIL) (616236) (-) (-)	Jharkhand	02/2020 (02/2020)	03/2029 (-)	372.06 0.00	85.60	33.10
67	BLOCK E OCP (BCCL - CIL) (616253) (-) (-)	Jharkhand	03/2024 (03/2024)	03/2029 (-)	5,850.83 0.00	20.32	4.56
68	Revised Jharia Master Plan for Dealing with Fire, Subsidence & Rehabilitation of affected families in Jharia Coalfield- Reg. (Bharat Coking Coal Limited [BCCL]) (617416) (-) (-)	Jharkhand	06/2025 (07/2025)	12/2028 (-)	5,940.47 0.00	520.75	34.00
69	North Dhadu Western Part OCP (NLC India Limited [NLCIL]) (617764) (-) (-)	Jharkhand	10/2023 (12/2023)	03/2029 (-)	1,354.20 0.00	235.29	40.00
70	AMADAND OCP[4.0MTY] (SECL - CIL) (400148) (-) (-)	Madhya Pradesh	03/2016 (03/2016)	03/2021 (03/2027)	869.44 0.00	333.43	75.15
71	BLOCK B EXPANSION [3.5 TO 8.0 (NCL - CIL) (400162) (-) (-)	Madhya Pradesh	07/2019 (07/2019)	03/2023 (03/2027)	998.71 0.00	548.84	51.53
72	NIGAH I EXPANSION [15 TO 25 MTP (NCL - CIL) (400321) (-) (-)	Madhya Pradesh	11/2020 (11/2020)	03/2025 (03/2028)	1,729.68 0.00	1,001.52	53.74
73	RPR OF TAWA III UG MINE - 0.84 (WCL - CIL) (540543) (-) (-)	Madhya Pradesh	03/2026 (03/2026)	03/2032 (-)	374.18 0.00	0.00	0.01
74	KANCHAN OC EXP (SECL - CIL) (613802) (-) (-)	Madhya Pradesh	12/2014 (12/2014)	03/2026 (03/2028)	371.04 0.00	153.40	58.20
75	JHIRIA WEST OCP [1.5 MTY] (SECL - CIL) (613803) (-) (-)	Madhya Pradesh	01/2024 (01/2024)	03/2029 (-)	366.94 0.00	37.82	41.29
76	RPR TAWA-III UG 0.84 MTY (WCL - CIL) (613804) (-) (-)	Madhya Pradesh	12/2021 (12/2021)	03/2027 (-)	314.09 0.00	17.61	17.78
77	AMALGAMATED DHANKASA & JAMUNIA (WCL - CIL) (615185) (-) (-)	Madhya Pradesh	09/2022 (09/2022)	03/2027 (-)	399.20 0.00	109.67	67.13
78	RPR OF VISHNUPURI UG TO OC (WCL - CIL) (615187) (-) (-)	Madhya Pradesh	11/2022 (11/2022)	03/2029 (-)	220.62 0.00	0.00	11.20
79	URDHAN EXPANSION OC COST PLUS (WCL - CIL) (615194) (-) (-)	Madhya Pradesh	07/2022 (01/2023)	03/2031 (-)	206.88 0.00	27.79	2.02
80	SHARDA UG MINE (WCL - CIL) (615195) (-) (-)	Madhya Pradesh	07/2022 (09/2023)	03/2028 (-)	166.25 0.00	5.27	9.39
81	GANDHIGRAM UG MINE (WCL - CIL) (615206) (-) (-)	Madhya Pradesh	08/2019 (08/2019)	03/2026 (03/2027)	414.15 0.00	22.19	56.88
82	JAYANT EXPN. [20 TO 38 MTPA] (NCL - CIL) (619032) (-) (-)	Madhya Pradesh	02/2025 (02/2025)	03/2032 (-)	25,560.48 0.00	425.01	2.63
83	RPR FOR RAMPUR BATURA OCP (SECL - CIL) (619053) (-) (-)	Madhya Pradesh	05/2025 (05/2025)	03/2030 (-)	1,604.69 0.00	75.35	0.30
84	BHATADI EXPANSION OC (WCL - CIL) (400033) (-) (-)	Maharashtra	02/2020 (05/2022)	03/2028 (-)	580.61 0.00	112.17	36.38

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
85	AMALGAMATED YEKONA I & YEKONA (WCL - CIL) (400177) (-) (-)	Maharashtra	08/2015 (08/2015)	03/2025 (03/2027)	727.28 0.00	564.42	80.77
86	DINESH[MAKARDHOKRA-III] OC (WCL - CIL) (400178) (-) (-)	Maharashtra	02/2020 (02/2020)	03/2027 (-)	822.88 0.00	661.70	40.63
87	DHUPTALA OC [SASTI UG TO OC] (WCL - CIL) (400353) (-) (-)	Maharashtra	02/2019 (10/2021)	03/2028 (-)	711.01 0.00	174.74	19.02
88	SAONER UG MINE -1 EXPANSION 1. (WCL - CIL) (615184) (-) (-)	Maharashtra	01/2022 (01/2022)	03/2028 (-)	228.64 0.00	160.53	70.08
89	SASTI EXPANSION OPENCAST (WCL - CIL) (615186) (-) (-)	Maharashtra	08/2020 (08/2020)	03/2026 (03/2027)	319.04 0.00	114.90	32.33
90	NEW MAJRI UG TO OC 3 MTY COST (WCL - CIL) (615188) (-) (-)	Maharashtra	05/2019 (09/2022)	03/2027 (-)	402.27 0.00	68.74	24.17
91	MAKARDHOKRA EXPN OC 4.9 MTY (WCL - CIL) (615189) (-) (-)	Maharashtra	06/2022 (06/2022)	03/2026 (03/2027)	361.87 0.00	115.46	12.20
92	SINGHORI DEEP OC MIN 2.0 MTY (WCL - CIL) (615190) (-) (-)	Maharashtra	05/2022 (05/2022)	03/2029 (-)	335.75 0.00	54.91	9.64
93	GOKUL EXTENSION OC MINE (WCL - CIL) (615192) (-) (-)	Maharashtra	04/2021 (04/2021)	03/2026 (03/2027)	309.58 0.00	58.86	8.44
94	KOLGAON EXPANSION DEEP OC MINE (WCL - CIL) (615199) (-) (-)	Maharashtra	01/2023 (09/2023)	03/2027 (-)	198.71 0.00	26.84	8.00
95	BALLARPUR NORTH WEST OC MINE (WCL - CIL) (615330) (-) (-)	Maharashtra	12/2022 (12/2022)	03/2029 (-)	360.81 0.00	35.58	5.34
96	GADEGAON OC 3 MTY (WCL - CIL) (615331) (-) (-)	Maharashtra	10/2023 (10/2023)	03/2030 (-)	497.41 0.00	101.95	7.95
97	GHONSA EXPANSION DEEP OC MINE (WCL - CIL) (615914) (-) (-)	Maharashtra	03/2021 (04/2021)	03/2029 (-)	184.71 0.00	15.72	13.03
98	AMLG GAURI PAUNI EXPANSION OC (WCL - CIL) (615916) (-) (-)	Maharashtra	04/2024 (04/2024)	03/2030 (-)	1,225.21 0.00	96.19	4.21
99	GAURIDEEP/GAURI CENTRAL OCP 7. (WCL - CIL) (615917) (-) (-)	Maharashtra	08/2023 (06/2024)	03/2030 (-)	973.07 0.00	1.54	2.31
100	RPR OF BHANEGAON OC (WCL - CIL) (615918) (-) (-)	Maharashtra	02/2017 (09/2022)	03/2028 (-)	405.20 0.00	38.51	16.74
101	N. EXTN. MUNGOLI NIRGUDA D OCP (WCL - CIL) (615919) (-) (-)	Maharashtra	06/2024 (06/2024)	03/2029 (-)	1,024.91 0.00	221.04	27.92
102	NILJAI EXPANSION DEEP OCP (WCL - CIL) (615982) (-) (-)	Maharashtra	08/2016 (08/2016)	03/2022 (03/2027)	319.75 0.00	197.75	79.83
103	UKNI DEEP OC MINE -COST PLUS (WCL - CIL) (616044) (-) (-)	Maharashtra	11/2018 (01/2019)	03/2021 (03/2027)	237.06 0.00	172.53	94.61
104	AMALGAMATED INDER-KAMPTEE DEEP (WCL - CIL) (616050) (-) (-)	Maharashtra	09/2018 (09/2018)	03/2024 (03/2027)	235.90 0.00	130.67	98.97
105	ADASA UG TO OC MINE (WCL - CIL) (616223) (-) (-)	Maharashtra	11/2018 (11/2018)	03/2024 (03/2027)	316.00 0.00	209.29	87.02
106	AMAL GONDEGAON GHATROHANA EXPN (WCL - CIL) (616229) (-) (-)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	668.54 0.00	2.95	2.55
107	WAGHODA UG MINE [1.02 MTY] (WCL - CIL) (617233) (-) (-)	Maharashtra	01/2024 (01/2025)	03/2030 (-)	379.30 0.00	0.00	0.11

All Ongoing Projects							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
108	KOLARPIMPRI EXPANSION OC [2.5 (WCL - CIL) (617278) (-) (-)	Maharashtra	06/2024 (02/2025)	03/2030 (-)	630.37 0.00	0.61	0.44
109	SAONER-III EXPN UG MINE 1.54 (WCL - CIL) (619055) (-) (-)	Maharashtra	08/2025 (08/2025)	03/2032 (-)	444.42 0.00	0.00	0.03
110	BINA KAKRI AMALGAMATION EXPANS (NCL - CIL) (400369) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	08/2020 (08/2020)	03/2024 (03/2027)	836.42 0.00	840.16	92.25
111	KHADIA EXPANSION [10 TO 16 MTP (NCL - CIL) (615183) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	06/2021 (06/2021)	03/2025 (03/2027)	491.67 0.00	276.39	58.23
112	SUBHADRA OCP (MCL - CIL) (400165) (-) (-)	Odisha	05/2021 (05/2021)	04/2032 (-)	1,693.81 0.00	1,335.11	46.78
113	SIARMAL OCP (Mahanadi Coalfields Limited [MCL]) (400166) (-) (-)	Odisha	02/2021 (02/2021)	03/2029 (-)	5,194.95 0.00	3,496.21	61.91
114	BALARAM EXPANSION OCP (MCL - CIL) (400183) (-) (-)	Odisha	08/2020 (08/2020)	03/2029 (-)	3,504.21 0.00	964.20	64.76
115	GOPALJI KANIHA OCP [10 TO 30 M (MCL - CIL) (400185) (-) (-)	Odisha	04/2022 (04/2022)	03/2030 (-)	8,416.19 0.00	1,779.77	36.01
116	INTEGRATED LAKHANPUR-BELPAHAR- (MCL - CIL) (400187) (-) (-)	Odisha	05/2018 (05/2018)	03/2027 (-)	2,434.75 0.00	2,149.98	83.30
117	BHARATPUR RE-ORGANIZATION OCP (MCL - CIL) (400392) (-) (-)	Odisha	11/2018 (11/2018)	03/2029 (-)	2,838.86 0.00	1,716.51	53.54
118	Naini Coal Mine (Singareni Collieries Company Limited [SCCL]) (615857) (-) (-)	Odisha	03/2020 (03/2020)	03/2026 (-)	494.30 0.00	491.33	80.00
119	INTEGRATED KULDA GARJANBAHAL O (MCL - CIL) (616226) (-) (-)	Odisha	04/2023 (04/2023)	03/2033 (-)	3,563.50 0.00	693.62	10.43
120	BHUBANESWARI EXPN OCP 50 MTY (MCL - CIL) (616231) (-) (-)	Odisha	03/2024 (03/2024)	03/2033 (-)	5,366.27 0.00	478.44	34.36
121	HINGULA II OC EXPN PH III 15 M (MCL - CIL) (616232) (-) (-)	Odisha	11/2022 (11/2022)	03/2029 (-)	1,561.85 0.00	284.32	33.89
122	BALABHADRA OCP (MCL - CIL) (616233) (-) (-)	Odisha	04/2023 (04/2023)	03/2030 (-)	978.44 0.00	253.17	19.48
123	Talabira II & III OCP - FMC (NLC India Limited [NLCIL]) (618982) (-) (-)	Odisha	10/2022 (05/2023)	06/2026 (12/2026)	522.45 0.00	334.44	74.80
124	Jawahar Khani Open Cast Mine (Singareni Collieries Company Limited [SCCL]) (615818) (-) (-)	Telangana	12/2021 (12/2021)	03/2025 (03/2027)	297.88 0.00	50.39	20.00
125	Kalyanikhani Opencast Project (Singareni Collieries Company Limited [SCCL]) (615858) (-) (-)	Telangana	03/2016 (05/2017)	03/2026 (-)	384.32 0.00	304.46	77.00
126	Godavarikhani Coal Mine - 5 (Singareni Collieries Company Limited [SCCL]) (615860) (-) (-)	Telangana	07/2019 (05/2019)	03/2025 (03/2026)	607.04 0.00	201.00	71.00
127	Indaram Opencast Project (Singareni Collieries Company Limited [SCCL]) (615861) (-) (-)	Telangana	08/2017 (12/2022)	03/2025 (03/2026)	424.81 0.00	409.12	81.00
128	Goleti Opencast Mine (Singareni Collieries Company Limited [SCCL]) (615862) (-) (-)	Telangana	07/2021 (08/2021)	03/2026 (-)	345.60 0.00	111.94	33.00
129	Venkatesh Khani Coal Mine (Singareni Collieries Company Limited [SCCL]) (615863) (-) (-)	Telangana	10/2020 (06/2020)	03/2026 (-)	484.50 0.00	477.14	97.00
130	Kakatiyakhani OC - 2 Project (Singareni Collieries Company Limited [SCCL]) (615865) (-) (-)	Telangana	08/2017 (09/2017)	03/2025 (03/2026)	442.42 0.00	257.04	64.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
131	MOHANPUR EXPANSION OC -PHASE I (ECL - CIL) (400173) (-) (-)	West Bengal	11/2020 (11/2020)	03/2026 (03/2030)	888.99 0.00	143.68	31.52
132	BONJEMEHARI EXPANSION OCP (ECL - CIL) (400180) (-) (-)	West Bengal	08/2021 (08/2021)	03/2026 (03/2030)	570.11 0.00	88.99	17.13
133	NAKRAKONDA KUMARDIH- B OCP (ECL - CIL) (400181) (-) (-)	West Bengal	08/2018 (08/2018)	03/2029 (-)	502.68 0.00	89.81	28.65
134	TILABONI UG (ECL - CIL) (400186) (-) (-)	West Bengal	01/2023 (01/2023)	03/2029 (-)	749.08 0.00	87.71	12.16
135	JHANJRA EXPANSION UG (ECL - CIL) (400312) (-) (-)	West Bengal	04/2020 (04/2020)	03/2029 (-)	1,210.12 0.00	633.57	52.10
136	SONEPUR BAZARI EXPANSION OCP [(ECL - CIL) (400315) (-) (-)	West Bengal	07/2021 (07/2021)	03/2029 (-)	5,365.88 0.00	629.96	18.50
137	ITAPARA OCP (ECL - CIL) (612816) (-) (-)	West Bengal	12/2023 (12/2023)	03/2030 (-)	929.10 0.00	71.89	8.53
138	SHYAMSUNDARPUR UG INCLUDING SA (ECL - CIL) (613793) (-) (-)	West Bengal	04/2020 (04/2020)	03/2026 (03/2028)	483.65 0.00	84.82	16.79
139	PARASEA-BELBAID UG PROJECT (ECL - CIL) (613794) (-) (-)	West Bengal	01/2023 (01/2023)	03/2028 (-)	389.10 0.00	133.27	23.22
140	PARASCOLE JAMBAD OCP (ECL - CIL) (616230) (-) (-)	West Bengal	11/2024 (11/2024)	03/2037 (-)	1,193.55 0.00	12.32	0.24
	Total (114)				182,868.95 0.00	48,745.33	
	Electricity Generation						
141	50 MW Wind Power Project (NLC India Limited) (617299) (-) (-)	Gujarat	07/2022 (01/2024)	06/2025 (12/2026)	383.84 0.00	333.34	52.00
142	600 MW Khavda Solar Power Project (NLC India Limited [NLCIL]) (617730) (-) (-)	Gujarat	08/2023 (06/2024)	06/2026 (12/2026)	3,335.85 0.00	2,202.23	65.00
143	200 MW SPP part of 510 MW CPSU scheme (NLC India Limited [NLCIL]) (618991) (-) (-)	Gujarat	07/2022 (03/2024)	12/2026 (-)	1,221.41 0.00	71.51	5.00
144	100 MW SPP part of SECI 150 MW Hybrid (NLC India Limited [NLCIL]) (618992) (-) (-)	Gujarat	07/2022 (04/2024)	12/2026 (-)	480.68 0.00	2.75	1.20
145	NLC Talabira Thermal Power Project (NLC India Limited) (400231) (-) (-)	Odisha	01/2017 (01/2024)	03/2030 (-)	27,212.96 0.00	3,606.38	4.10
146	810 MW Solar Power Project - Rajasthan (NLC India Limited [NLCIL]) (618981) (-) (-)	Rajasthan	10/2024 (09/2025)	03/2028 (-)	4,147.07 0.00	249.95	0.00
	Total (6)				36,781.81 0.00	6,466.16	
	Railways						
147	Dharamjaigarh-Korba (Railway) (400203) (-) (-)	Chhattisgarh	05/2018 (03/2017)	12/2026 (08/2026)	1,686.22 0.00	792.73	43.70
148	Shivpur-Kathautia New Rail [BG] Line [49 km] [Package II of Tori-Shivpur-Kathautia line] (Ministry of Coal) (400416) (-) (-)	Jharkhand	02/2018 (05/2022)	06/2025 (06/2027)	1,799.64 0.00	1,784.77	72.00
	Total (2)				3,485.86 0.00	2,577.50	
	Ministry of Power						
	Coal						
149	Tubed Coal Mine (Damodar Valley Corporation) (400192) (-) (-)	Jharkhand	07/2016 (10/2016)	05/2026 (12/2026)	1,581.00 0.00	628.90	37.00
150	Badam Coal Mining project of NTPC (National Thermal Power Corporation [NTPC]) (603293) (-) (-)	Jharkhand	02/2019 (09/2019)	12/2056 (04/2027)	502.00 0.00	442.42	67.86

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
	Total (2)				2,083.00 0.00	1,071.32	
	Electricity Generation						
151	Dibang Multipurpose Project (National Hydroelectric Power Corporation Limited [NHPC]) (602182) (-) (-)	Arunachal Pradesh	02/2023 (02/2023)	02/2032 (02/2032)	31,876.39 0.00	5,118.73	18.12
152	240MW Heo HE Project (North Eastern Electric Power Corporation Limited) (611698) (-) (-)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1,938.85 0.00	107.31	7.85
153	186 MW Tato-I H E Project (North Eastern Electric Power Corporation Limited) (611699) (-) (-)	Arunachal Pradesh	12/2024 (05/2025)	07/2029 (-)	1,750.07 0.00	80.45	5.80
154	700 MW Tato-II HE Project (North Eastern Electric Power Corporation Limited) (611716) (-) (-)	Arunachal Pradesh	09/2025 (09/2025)	09/2031 (-)	8,146.21 0.00	254.77	6.72
155	Kalai-II Hydro Electric Project [1200 MW] (THDC India Limited) (619311) (-) (-)	Arunachal Pradesh	04/2026 (04/2026)	10/2032 (-)	14,105.83 0.00	190.66	0.00
156	Buxar Thermal Power Project [1320 MW] (SJVN Limited) (602579) (-) (-)	Bihar	03/2019 (06/2019)	01/2024 (08/2026)	10,439.09 0.00	13,813.98	95.05
157	Nabinagar Super Thermal Power Project, Stage-II [3x800 MW] (National Thermal Power Corporation [NTPC]) (619051) (-) (-)	Bihar	11/2024 (03/2025)	07/2030 (07/2030)	29,948.00 0.00	3,677.01	16.00
158	Lara Super Thermal Power Project Stage-II [2 x 800 MW] (National Thermal Power Corporation [NTPC]) (611930) (-) (-)	Chhattisgarh	08/2023 (08/2023)	06/2028 (11/2028)	15,530.00 0.00	5,711.52	35.00
159	Sipat Super Thermal Power Project, Stage-III [1x800 MW] (National Thermal Power Corporation [NTPC]) (617188) (-) (-)	Chhattisgarh	09/2024 (09/2024)	09/2029 (09/2029)	9,791.00 0.00	2,042.62	23.21
160	Bagodara Solar Power Project (SJVN Limited) (709747) (-) (-)	Gujarat	03/2021 (05/2021)	12/2025 (12/2025)	339.35 0.00	376.64	51.86
161	Dhaultasidh Hydro Electric Project [66 MW] (SJVN Limited) (602582) (-) (-)	Himachal Pradesh	10/2020 (05/2021)	11/2025 (03/2027)	687.97 0.00	1,284.90	81.00
162	Luhri Stage-I Hydro Electric Project [210 MW] (SJVN Limited) (602593) (-) (-)	Himachal Pradesh	11/2020 (11/2020)	01/2026 (05/2030)	1,810.56 0.00	1,981.17	52.13
163	Sunni Dam Hydro Electric Project [382 MW] (SJVN Limited) (611586) (-) (-)	Himachal Pradesh	01/2023 (01/2023)	04/2028 (12/2029)	2,614.51 0.00	1,173.23	34.96
164	Pakal Dul [Drangdhuran] Hydroelectric Project, 1000 MW (National Hydroelectric Power Corporation Limited [NHPC]) (602525) (-) (-)	Jammu and Kashmir	10/2014 (02/2018)	04/2020 (12/2026)	8,112.12 0.00	9,905.50	87.00
165	Kiru HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (602532) (-) (-)	Jammu and Kashmir	03/2019 (02/2020)	09/2023 (12/2026)	4,287.59 0.00	4,118.03	90.50
166	Rattle HE Project - 850 MW, Rattle Hydroelectric Power Corporation Limited. (National Hydroelectric Power Corporation Limited [NHPC]) (602535) (-) (-)	Jammu and Kashmir	02/2021 (01/2022)	02/2026 (11/2028)	5,281.94 0.00	1,692.33	32.62
167	Kwar HE Project (National Hydroelectric Power Corporation Limited [NHPC]) (605155) (-) (-)	Jammu and Kashmir	05/2022 (11/2022)	11/2026 (03/2028)	4,526.12 0.00	2,015.00	39.67
168	Patratu Thermal Power Station Expansion Project Phase-I [3x800 MW] (National Thermal Power Corporation [NTPC]) (400261) (-) (-)	Jharkhand	11/2017 (11/2017)	03/2023 (04/2027)	18,668.00 0.00	19,405.48	92.50
169	Koderma Thermal Power Station Phase II [2X800 MW] At Koderma, Jharkhand (Damodar Valley Corporation) (611509) (-) (-)	Jharkhand	04/2023 (11/2024)	07/2029 (-)	14,358.00 0.00	2,416.60	15.72
170	Gadarwara Super Thermal Power Project, Stage-II [2x800 MW] (National Thermal Power Corporation [NTPC]) (618976) (-) (-)	Madhya Pradesh	11/2024 (05/2025)	03/2030 (03/2030)	20,446.00 0.00	2,434.64	13.00
171	Subansiri Lower HE Project [2000 MW] (National Hydroelectric Power Corporation Limited [NHPC]) (602096) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	09/2003 (01/2005)	09/2010 (03/2027)	6,285.33 0.00	26,575.24	98.07
172	Talcher Thermal Power Station Stage III [2 x 660 MW] Expansion (National Thermal Power Corporation [NTPC]) (602961) (-) (-)	Odisha	08/2022 (09/2022)	05/2027 (05/2028)	11,843.75 0.00	7,146.85	56.50

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
173	Darlipali Super Thermal Power Project, Stage-II [1x800 MW] (National Thermal Power Corporation [NTPC]) (619056) (-) (-)	Odisha	11/2025 (11/2025)	01/2031 (01/2031)	11,131.00 0.00	582.74	3.25
174	TEESTA-VI HE PROJECT, SIKKIM [500 MW], executed by LANCO TEESTA HYDRO POWER LIMITED [A wholly owned Subsidiary of NHPC LTD. acquired through NCLT] (National Hydroelectric Power Corporation Limited [NHPC]) (602181) (-) (-)	Sikkim	03/2019 (03/2020)	03/2024 (09/2029)	5,748.04 0.00	4,676.46	73.95
175	Rangit-IV HE Project [120 MW] executed by Jal Power Corporation Ltd. [JPCL] - A wholly owned subsidiary of NHPC Ltd. acquired through NCLT (National Hydroelectric Power Corporation Limited [NHPC]) (605156) (-) (-)	Sikkim	03/2021 (08/2021)	05/2024 (11/2026)	938.29 0.00	1,726.66	97.86
176	Telangana Super Thermal Power Project , Stage-II [3 x 800 MW] (National Thermal Power Corporation [NTPC]) (619341) (-) (-)	Telangana	03/2026 (03/2026)	01/2032 (-)	29,344.85 0.00	733.63	1.04
177	Meja Thermal Power Project, Stage-II , (3x800 MW) (National Thermal Power Corporation [NTPC]) (298178) (-) (-)	Uttar Pradesh	06/2026 (06/2026)	12/2032 (-)	38,358.00 0.00	1,027.77	0.11
178	Singrauli Super Thermal Power Project, Stage-III [2x800 MW] (National Thermal Power Corporation [NTPC]) (612142) (-) (-)	Uttar Pradesh	03/2024 (03/2024)	02/2030 (02/2030)	17,195.00 0.00	4,046.64	25.35
179	Tapovan-Vishnugad HEP [4x130 MW] (National Thermal Power Corporation [NTPC]) (602185) (-) (-)	Uttarakhand	11/2006 (11/2006)	03/2013 (07/2029)	2,978.00 0.00	7,887.36	76.18
180	Vishnugad Pipalkoti Hydro Electric Project [444 MW] (THDC India Limited) (602195) (-) (-)	Uttarakhand	08/2008 (01/2014)	12/2022 (06/2028)	3,860.35 0.00	5,906.00	82.00
181	Raghunathpur Thermal Power Station Phase II [2X660 MW] at Raghunathpur, Purulia, West Bengal (Damodar Valley Corporation) (400062) (-) (-)	West Bengal	01/2023 (02/2025)	08/2029 (-)	17,673.00 0.00	2,395.67	14.50
182	Rammam-III HEPP [3x40 MW] (National Thermal Power Corporation [NTPC]) (602184) (-) (-)	West Bengal	09/2014 (09/2014)	09/2019 (09/2029)	1,381.84 0.00	1,701.35	59.63
183	Installation of FGD for 4x210 & 2x250 MW MTPS U 1-6 (Damodar Valley Corporation) (602538) (-) (-)	West Bengal	06/2019 (02/2021)	01/2024 (09/2026)	1,037.00 0.00	1,146.29	97.00
	Total (33)				352,432.05 0.00	143,353.23	
Transmission & Distribution							
184	Transmission System for proposed Green Hydrogen/ Green Ammonia Projects in Kakinada Area (Phase I) (Power Grid Corporation of India Limited [POWERGRID]) (553920) (-) (-)	Andhra Pradesh	06/2026 (06/2026)	12/2028 (-)	1,618.00 0.00	16.18	0.50
185	Transmission system strengthening at Kurnool- III PS for integration of additional RE generation projects [POWERGRID Kurnool III PS RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617183) (-) (-)	Andhra Pradesh	03/2025 (03/2025)	12/2027 (-)	2,886.00 0.00	983.26	45.96
186	North Eastern Region Expansion Scheme-XXIII [NERES-XXIII] (Power Grid Corporation of India Limited [POWERGRID]) (617375) (-) (-)	Arunachal Pradesh	08/2025 (08/2025)	02/2028 (-)	209.38 0.00	4.19	5.68
187	Transmission system for evacuation of Power from REZ in Rajasthan [20 GW] under phase-III Part-D Phase-II (Power Grid Corporation of India Limited [POWERGRID]) (615336) (-) (-)	Delhi	11/2023 (10/2024)	02/2026 (12/2026)	284.00 0.00	99.40	51.74
188	Transmission system for Evacuation of Additional 7 GW RE power from Khavda RE park under Phase-III Part B [Vataman Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (612139) (-) (-)	Gujarat	12/2023 (12/2023)	12/2025 (12/2026)	4,231.00 0.00	3,175.79	74.00
189	Transmission System for Evacuation of Power from Potential Energy Renewable Zone in Khavda Area of Gujarat under Ph-IV [7GW] Part E2 (Power Grid Corporation of India Limited [POWERGRID]) (612855) (-) (-)	Gujarat	05/2024 (05/2024)	05/2026 (09/2026)	697.00 0.00	634.27	91.00
190	Augmentation of Transformation Capacity at jam Khambhaliya PS [GIS] [SPV Name POWERGRID Jam Khambhaliya Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615342) (-) (-)	Gujarat	10/2024 (10/2024)	07/2026 (04/2027)	329.00 0.00	85.54	35.33
191	Provision of Dynamic Reactive Compensation at Khavda pooling Station 1 [KPS1] and Khavda Pooling station 3 [KPS3] (Power Grid Corporation of India Limited [POWERGRID]) (615343) (-) (-)	Gujarat	11/2024 (11/2024)	11/2026 (-)	501.00 0.00	30.06	11.67

All Ongoing Projects							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
192	Transmission System for Evacuation of Power from Potential Renewable Energy Zone in Khavda area of Gujarat under Phase-IV [7GW] Part B [SPV Name POWERGRID South Olpad Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615345) (-) (-)	Gujarat	10/2024 (10/2024)	10/2026 (10/2027)	4,766.00 0.00	2,240.00	41.32
193	Augmentation of Transformation Capacity at KPS1 [GIS] and KPS2 [GIS] [Phase-V Part B1 and Part B2 Scheme] [SPV Name- POWERGRID KPS1 and 2 Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617069) (-) (-)	Gujarat	02/2025 (02/2025)	02/2027 (-)	466.00 0.00	168.13	47.50
194	Augmentation of Banaskantha [Raghanesda] PS [GIS] [POWERGRID Banaskantha Transco Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617182) (-) (-)	Gujarat	03/2025 (03/2025)	03/2027 (-)	172.00 0.00	65.36	45.00
195	Augmentation of Transformation Capacity at Bhuj-II PS [GIS] (Power Grid Corporation of India Limited [POWERGRID]) (617391) (-) (-)	Gujarat	02/2025 (02/2025)	11/2026 (06/2027)	488.29 0.00	24.41	14.00
196	Jamnagar Transmission Limited (Adani Transmission Limited) (617405) (-) (-)	Gujarat	10/2024 (10/2024)	10/2026 (09/2027)	4,000.00 0.00	698.00	25.00
197	Provision of ICT Augmentation & Bus Reactor at Bhuj-II PS (Power Grid Corporation of India Limited [POWERGRID]) (617801) (-) (-)	Gujarat	03/2025 (03/2025)	12/2026 (06/2027)	581.74 0.00	46.54	13.50
198	KPSIII HVDC Transmission Limited (Adani Transmission Limited) (619026) (-) (-)	Gujarat	12/2025 (12/2025)	12/2029 (-)	19,000.00 0.00	20.65	1.00
199	Transmission System for Reliable Power Supply to Dholera (Power Grid Corporation of India Limited [POWERGRID]) (619029) (-) (-)	Gujarat	09/2024 (09/2024)	03/2026 (12/2026)	319.42 0.00	79.85	36.80
200	Khavda IVA Power Transmission Limited (Adani Transmission Limited) (619049) (-) (-)	Gujarat	08/2024 (08/2024)	08/2026 (03/2027)	4,500.00 0.00	2,772.70	75.00
201	Transmission Scheme for evacuation of Power from Ratle HEP [850 MW] & kiru [624 MW] Part B (Power Grid Corporation of India Limited [POWERGRID]) (617179) (-) (-)	Jammu and Kashmir	07/2024 (07/2024)	07/2026 (06/2027)	218.60 0.00	3.72	1.70
202	Implementation of Transmission Systems in the State of Jharkhand consisting of 400/220/132/33 kV transmission lines and substations under Jharkhand Consultancy Project (Power Grid Corporation of India Limited [POWERGRID]) (617326) (-) (-)	Jharkhand	02/2012 (02/2012)	03/2026 (06/2027)	1,842.25 0.00	1,648.05	96.50
203	Transmission Scheme for Integration of Renewable Energy Zone [Phase II] in Koppal II [Phase A&B] and gadag II[Phase A] in Karnataka [POWERGRID KOPPAL GADAG TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (612140) (-) (-)	Karnataka	12/2023 (12/2023)	12/2025 (09/2026)	4,445.00 0.00	4,178.30	97.13
204	System Strengthening at Koppal-II and GadagII for integration of RE generation projects [SPV Name POWERGRID Koppal Gadag Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616672) (-) (-)	Karnataka	01/2025 (01/2025)	06/2027 (-)	1,354.00 0.00	365.58	45.27
205	Augmentation of Transformation Capacity by 3x500 MVA, 400/220 KV ICTS [6th-8th] and 1x1500 MVA, 765/400 KV ICT [4th] at Bidar PS [SPV Name- POWERGRID Bidar Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617068) (-) (-)	Karnataka	02/2025 (02/2025)	06/2027 (-)	288.00 0.00	43.20	29.25
206	Transmission Scheme for integration of Davanagere/ Chitradurga and Bellary REZ in Karnataka [POWERGRID Chitradurga Bellary REZ Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617184) (-) (-)	Karnataka	03/2025 (03/2025)	09/2027 (-)	3,453.00 0.00	690.60	25.17
207	Transmission System Strengthening at Davanagere for Integration of RE Generation [SPV Name - POWERGRID Davanagere Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617803) (-) (-)	Karnataka	09/2025 (09/2025)	09/2027 (-)	379.00 0.00	17.06	2.50
208	Transmission System Strengthening for integration of additional RE Potential at Davanagere [0.25 GW] and Bellary [2.75 GW] (Power Grid Corporation of India Limited [POWERGRID]) (619228) (-) (-)	Karnataka	02/2026 (02/2026)	02/2028 (-)	1,111.00 0.00	44.44	1.00
209	Transmission system strengthening at Tumkur-II for integration of additional RE potential (2.7 GW) (Power Grid Corporation of India Limited [POWERGRID]) (994914) (-) (-)	Karnataka	05/2026 (05/2026)	05/2029 (-)	1,221.00 0.00	24.42	1.00
210	Augmentation of 1x500 MVA 400/220kV ICT [3rd] at Thrissur VSC HVDC Station in Kerala (Power Grid Corporation of India Limited [POWERGRID]) (619028) (-) (-)	Kerala	08/2025 (08/2025)	08/2027 (12/2027)	173.14 0.00	2.08	1.50

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
211	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5GW] [Jaisalmer/Barmer Complex] Part H1 [POWERGRID KURAWAR TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615344) (-) (-)	Madhya Pradesh	10/2024 (10/2024)	10/2026 (06/2027)	3,674.00 0.00	1,726.78	60.34
212	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part C [SPV Name POWERGRID Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615346) (-) (-)	Madhya Pradesh	08/2024 (08/2024)	08/2026 (02/2027)	2,708.00 0.00	1,760.20	74.28
213	Implementation of LILO of both circuits of 400KV vindhyachal PS-Sasan D/C Line at Hindalco Switchyard (Power Grid Corporation of India Limited [POWERGRID]) (617272) (-) (-)	Madhya Pradesh	06/2024 (06/2024)	12/2026 (-)	370.00 0.00	162.81	57.62
214	Transmission System for evacuation of power from Mahan Energen Limited Generating Station in Madhya Pradesh [SPV Name - POWERGRID MEL Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617279) (-) (-)	Madhya Pradesh	06/2025 (06/2025)	12/2027 (-)	558.00 0.00	184.14	19.32
215	Augmentation of Transformation Capacity and Implementation of Line Bays at Mandsaur S/S for RE Interconnection [SPV Name- POWERGRID Mandsaur I RE Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617802) (-) (-)	Madhya Pradesh	10/2025 (10/2025)	03/2028 (-)	319.00 0.00	17.92	6.00
216	Mahan Transmission Limited (Adani Transmission Limited) (619024) (-) (-)	Madhya Pradesh	03/2025 (03/2025)	04/2027 (-)	3,125.32 0.00	734.79	45.00
217	WRNES Talegaon Power Transmission Limited (Adani Transmission Limited) (619027) (-) (-)	Maharashtra	05/2025 (05/2025)	01/2028 (-)	2,000.00 0.00	29.00	6.00
218	Network Expansion Scheme in Maharashtra for removal of Transmission constraints in Pune Region-I [765/400kV AIS Pune East] (Power Grid Corporation of India Limited [POWERGRID]) (619227) (-) (-)	Maharashtra	03/2026 (03/2026)	03/2028 (-)	1,420.00 0.00	63.61	4.32
219	Transmission System for Integration of Kurnool-IV REZ Phase-I [for 4.5 GW] [POWERGRID Kurnool-IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617185) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	03/2025 (03/2025)	03/2027 (09/2027)	5,550.00 0.00	1,963.00	34.50
220	Transmission System for Integration of Ananthapur 2 REZ Phase 1 for 4.5 GW. SPV Name Anantapuram 2 REZ Transmission Ltd (Sterlite Power) (617806) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	08/2024 (03/2025)	03/2027 (-)	4,535.99 0.00	1,785.57	70.00
221	Inter-Regional Strengthening between SR Grid and ER Grid (Power Grid Corporation of India Limited [POWERGRID]) (619030) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	02/2026 (02/2026)	08/2028 (-)	2,722.50 0.00	198.74	3.00
222	Comprehensive Scheme for Strengthening of Transmission and Distribution [T&D] Systems [CSST&DS] in Arunachal Pradesh and Sikkim (Power Grid Corporation of India Limited [POWERGRID]) (602223) (-) (-)	Multi-States (Arunachal Pradesh, Sikkim)	10/2014 (10/2014)	12/2018 (03/2027)	4,754.42 0.00	8,173.48	84.00
223	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT [NERPSIP] (Power Grid Corporation of India Limited [POWERGRID]) (607709) (-) (-)	Multi-States (Assam, Manipur, Meghalaya, Mizoram, Nagaland, Tripura)	12/2014 (03/2016)	12/2018 (03/2027)	5,111.33 0.00	5,577.75	99.20
224	Eastern Region Expansion Scheme-43 [ERES-43] (Power Grid Corporation of India Limited [POWERGRID]) (617271) (-) (-)	Multi-States (Bihar, Odisha, West Bengal)	09/2024 (09/2024)	03/2026 (09/2026)	342.69 0.00	150.92	29.75
225	Inter-regional [NR-WR] Transmission System strengthening to relieve the loading of 765 kV Vindhyachal-Varanasi D/c line (Power Grid Corporation of India Limited [POWERGRID]) (617807) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2025 (10/2025)	10/2027 (-)	2,368.00 0.00	165.76	8.06
226	Eastern Region Expansion Scheme-44 [ERES-44] (Power Grid Corporation of India Limited [POWERGRID]) (617270) (-) (-)	Multi-States (Bihar, West Bengal)	11/2024 (11/2024)	05/2026 (09/2027)	408.94 0.00	6.13	1.50
227	WR-ER Inter Regional Network Expansion Scheme – Part A (Power Grid Corporation of India Limited [POWERGRID]) (663560) (-) (-)	Multi-States (Chhattisgarh, Jharkhand, West Bengal)	06/2026 (06/2026)	06/2029 (-)	6,444.00 0.00	12.88	0.10
228	Transmission Scheme for Evacuation of power from REZ in Rajasthan [20 GW] under Phase-III Part D Phase I [Sikar Khetri Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612132) (-) (-)	Multi-States (Delhi, Haryana, Rajasthan)	02/2024 (02/2024)	08/2025 (03/2027)	2,423.00 0.00	2,253.39	94.00
229	Transmission system for evacuation of power from REZ in Rajasthan 20GW under Phase-III Part J (Power Grid Corporation of India Limited [POWERGRID]) (611735) (-) (-)	Multi-States (Delhi, Rajasthan)	12/2022 (12/2022)	03/2025 (12/2026)	331.00 0.00	248.25	73.60

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
230	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM POTENTIAL RENEWABLE ENERGY ZONE IN KHAVDA AREA OF GUJARAT UNDER PHASE-V [8 GW] PART A [SPV Name POWERGRID West Central Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615347) (-) (-)	Multi-States (Gujarat, Maharashtra)	11/2024 (11/2024)	05/2029 (-)	24,819.00 0.00	3,166.90	19.57
231	Transmission system for evacuation of power from Rajasthan REZ Ph-IV [Part-3/6GW] [Bikaner complex] Part A [SPV Name POWERGRID Bikaner IV Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615339) (-) (-)	Multi-States (Haryana, Punjab, Rajasthan)	11/2024 (11/2024)	11/2026 (04/2027)	5,969.00 0.00	2,268.22	38.00
232	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH-IV [PART-3/ 6 GW] [BIKANER COMPLEX] PART B [SPV Name POWERGRID Sivani Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615340) (-) (-)	Multi-States (Haryana, Rajasthan)	11/2024 (11/2024)	11/2026 (03/2027)	5,357.00 0.00	2,035.66	40.00
233	Inter-Regional Strengthening between SR Grid and WR Grid (Power Grid Corporation of India Limited [POWERGRID]) (617808) (-) (-)	Multi-States (Karnataka, Maharashtra)	10/2025 (10/2025)	10/2027 (-)	1,007.00 0.00	60.42	3.00
234	Transmission Scheme for Solar Energy Zone in Bidar [2500 MW], Karnataka [Bidar Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612138) (-) (-)	Multi-States (Karnataka, Telangana)	02/2024 (02/2024)	02/2026 (08/2026)	1,368.00 0.00	1,299.60	98.44
235	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part D [SPV Name POWERGRID Beawar Mandsaur Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615333) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (12/2026)	2,227.00 0.00	1,158.04	54.24
236	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW] [Jaisalmer/Barmer Complex] Part E [SPV Name POWERGRID Mewar Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615334) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	08/2024 (08/2024)	08/2026 (04/2027)	3,251.00 0.00	2,048.13	48.23
237	Rajasthan REZ Ph-V [Part-1- 4 GW] [Sirohi/Nagaur] Complex [POWERGRID Sirohi Khandwa Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617186) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	03/2025 (03/2025)	03/2027 (06/2027)	5,028.00 0.00	1,608.96	38.76
238	RAJASTHAN PART I POWER TRANSMISSION LIMITED (Adani Transmission Limited) (619025) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	01/2025 (01/2025)	07/2029 (-)	25,000.00 0.00	805.05	12.00
239	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part D [Neemrana Bareilly Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612133) (-) (-)	Multi-States (Rajasthan, Uttar Pradesh)	12/2023 (12/2023)	12/2025 (04/2027)	3,271.00 0.00	2,747.65	73.61
240	Transmission System for evacuation of Power from Rajasthan REZ Ph-IV [Part-4 3.5 GW] Part A [SPV name POWERGRID Ghiror Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616670) (-) (-)	Multi-States (Rajasthan, Uttar Pradesh)	12/2024 (12/2024)	12/2026 (06/2027)	5,846.00 0.00	2,074.73	44.31
241	Transmission system for evacuation of power from REZ in Rajasthan 20 GW under Phase-III part C1 (Power Grid Corporation of India Limited [POWERGRID]) (611949) (-) (-)	Rajasthan	10/2023 (10/2023)	04/2025 (08/2026)	1,160.00 0.00	1,154.20	99.93
242	Transmission System for Evacuation of power from Rajasthan REZ Ph-IV [Part-1] [Bikaner Complex] Part A [Bikaner Neemrana Transmission Ltd] (Power Grid Corporation of India Limited [POWERGRID]) (612134) (-) (-)	Rajasthan	12/2023 (12/2023)	12/2025 (04/2027)	4,741.00 0.00	3,887.62	79.99
243	Transmission System for Evacuation of Power from Rajasthan REZ Ph-IV [Part-2 5.5 GW][Jaisalmer/Barmer Complex] Part B [SPV Name POWERGRID Sirohi Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615332) (-) (-)	Rajasthan	08/2024 (08/2024)	08/2026 (03/2027)	3,279.00 0.00	1,977.89	62.14
244	Transmission System Strengthening for Interconnections of Bhadla-III & Bikaner III Complex [SPV Name POWERGRID BHADLA BIKANER TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615335) (-) (-)	Rajasthan	08/2024 (08/2024)	08/2026 (03/2027)	1,382.00 0.00	695.69	62.30
245	Additional Transmission System for evacuation of Power from Bhadla-III PS as part of Rajasthan REZ Phase III Scheme [20 GW] [SPV Name POWERGRID Bhadla-III Power Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (615337) (-) (-)	Rajasthan	08/2024 (08/2024)	02/2026 (09/2026)	369.00 0.00	302.58	92.95
246	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM RAJASTHAN REZ PH -IV [PART-2 5.5 GW] [JAISALMER/BARMER COMPLEX] PART F [SPV Name POWERGRID BARMER I TRANSMISSION LIMITED] (Power Grid Corporation of India Limited [POWERGRID]) (615338) (-) (-)	Rajasthan	11/2024 (11/2024)	11/2026 (06/2027)	2,735.00 0.00	1,203.40	50.13

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
247	Augmentation at Fatehgarh-II PS, Fatehgarh-IV PS [Section-II] and Barmer-I PS [POWERGRID Fatehgarh Barmer Augmentation Transmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (617181) (-) (-)	Rajasthan	03/2025 (03/2025)	12/2026 (06/2027)	404.00 0.00	40.40	18.40
248	Upgradation / Conversion of Udumalpet - Madurai 400kV S/c line to Udumalpet - Madurai 400kV (quad) D/c line (Power Grid Corporation of India Limited [POWERGRID]) (496150) (-) (-)	Tamil Nadu	02/2026 (06/2026)	08/2028 (-)	772.65 0.00	0.00	0.50
249	Transmission System under ISTS for evacuation of Power from Kudankulam Unit-3&4 [2x1000 MW] [SPV Name POWERGRID Kudankulam Tarnsmission Limited] (Power Grid Corporation of India Limited [POWERGRID]) (616671) (-) (-)	Tamil Nadu	01/2025 (01/2025)	12/2026 (03/2027)	548.00 0.00	219.20	28.63
250	Transmission System for Strengthening to facilitate evacuation of power from Bhadla/Bikaner Complex (Power Grid Corporation of India Limited [POWERGRID]) (617269) (-) (-)	Uttar Pradesh	12/2024 (12/2024)	06/2026 (12/2026)	212.81 0.00	21.28	14.70
	Total (67)				207,446.47 0.00	72,152.52	
	Ministry of Housing & Urban Affairs						
	Construction						
251	Construction of One Tower of Office Complex and another Tower of Residential quarters i/c internal water supply, sanitary installation and all development and bulk services, Horticulture works on EPC Mode-I basis i/c comprehensive operation and maintenance of Civil, E&M services for 7 years after completion of original construction work for Ranga Reddy, Secunderabad, Medchal, Auditl, Audit-II Commissionerates of Central Tax at Khajaguda, Serilingampally, Hyderabad. (Central Public Works Department - CPWD) (617412) (-) (-)	Telangana	03/2024 (11/2024)	09/2027 (-)	644.00 0.00	206.31	29.00
	Total (1)				644.00 0.00	206.31	
	Real Estate						
252	Integrated Command control Center [ICCC] - Construction and Development of Integrated Command Control Center with Security, Surveillance, ITMS, Connecting Port, Ship Service, Smart Solid Waste Management, Smart Public Transport System (ministry of housing and urban affairs) (707229) (-) (-)	Andaman & Nicobar	07/2021 (11/2021)	05/2023 (10/2025)	209.88 0.00	37.35	97.00
253	Redevelopment of Seven General Pool Residential Accommodation [GPRA] Colonies in Delhi (National Buildings Construction Corporation [NBCC]) (400188) (-) (-)	Delhi	07/2016 (05/2018)	12/2025 (12/2025)	32,850.00 0.00	14,370.45	46.70
254	Rehabilitation in Junavadaj Area Smart City Project (ministry of housing and urban affairs) (701719) (-) (-)	Gujarat	02/2016 (06/2016)	07/2022 (07/2026)	539.00 0.00	623.44	98.50
255	Green Building Development Project (ministry of housing and urban affairs) (701766) (-) (-)	Uttarakhand	11/2019 (08/2019)	11/2023 (12/2026)	150.97 0.00	62.73	40.32
	Total (4)				33,749.85 0.00	15,093.97	
	Urban Public Transport						
256	Patna Metro Rail Project (Patna Metro Rail Corporation Ltd. [PMRCL]) (702627) (-) (-)	Bihar	02/2019 (02/2019)	02/2024 (06/2027)	13,365.77 0.00	5,198.09	50.05
257	Delhi Metro Rail Phase-IV [2 Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (617207) (-) (-)	Delhi	03/2024 (03/2024)	03/2029 (-)	8,399.81 0.00	228.48	4.57
258	Delhi Metro Rail Phase V A (Delhi Metro Rail Corporation Limited [DMRC]) (619031) (-) (-)	Delhi	01/2026 (01/2026)	12/2028 (-)	12,014.91 0.00	296.94	6.37
259	DMRTS Phase - IV [3 Priority Corridors] (Delhi Metro Rail Corporation Limited [DMRC]) (702632) (-) (-)	Delhi	07/2019 (07/2019)	03/2025 (12/2026)	24,948.65 0.00	21,685.59	84.28
260	Surat Metro Rail Project (Gujarat Metro Rail Corporation Limited [GMRCL]) (702630) (-) (-)	Gujarat	03/2019 (03/2019)	03/2024 (03/2027)	12,020.32 0.00	9,535.85	82.80
261	Metro connectivity from Millennium City Centre to Cyber City with Spur to Dwarka Expressway, Gurugram. (Gurugram Metro Rail Limited [GMRL]) (619022) (-) (-)	Haryana	07/2023 (08/2024)	07/2027 (-)	5,452.72 0.00	206.10	10.43
262	Bangalore Metro Rail Project - PHASE-3 (Bengaluru Metro Rail) (612878) (-) (-)	Karnataka	09/2024 (06/2026)	05/2031 (-)	15,611.00 0.00	0.00	3.90
263	Construction of Bangalore Metro Rail Project Phase 2. (Bengaluru Metro Rail) (702635) (-) (-)	Karnataka	02/2014 (02/2016)	03/2021 (09/2026)	26,405.14 0.00	29,844.97	96.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
264	Construction Bangalore Metro Rail Project Phase-2A & 2B <i>(Bengaluru Metro Rail)</i> (702665) (-) (-)	Karnataka	06/2021 (01/2019)	06/2026 (06/2026)	14,788.10 0.00	11,079.30	68.00
265	Kochi Metro Rail Phase 2 Development Project <i>(CSPCC Projects)</i> (702664) (-) (-)	Kerala	11/2022 (11/2022)	11/2026 (11/2026)	1,957.05 0.00	816.80	41.20
266	Bhopal Metro Rail Project <i>(Madhya Pradesh Metro Rail Co Limited [MPMRCL])</i> (702625) (-) (-)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (06/2028)	6,941.40 0.00	4,571.69	63.10
267	Indore Metro Rail Project <i>(Madhya Pradesh Metro Rail Co Limited [MPMRCL])</i> (702626) (-) (-)	Madhya Pradesh	11/2018 (11/2018)	11/2022 (12/2028)	7,500.80 0.00	5,190.14	66.04
268	PCMC To Nigdi- Extension Of North South Corridor Of Phase-1 <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (617225) (-) (-)	Maharashtra	10/2023 (10/2023)	01/2027 (-)	910.18 0.00	336.07	50.47
269	Pune Metro Phase-1 Extension line towards south from Swargate to Katraj <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (617226) (-) (-)	Maharashtra	09/2024 (09/2024)	03/2029 (-)	2,954.53 0.00	204.36	9.66
270	Thane Integral Ring Metro Rail Project <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (617327) (-) (-)	Maharashtra	09/2024 (09/2024)	09/2029 (-)	12,200.10 0.00	136.27	10.56
271	Pune Metro Rail Project Phase-2 Corridor 2A Vanaz to Chandani Chowk and Corridor 2B Ramwadi to Wagholi/Vitthalwadi <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (618971) (-) (-)	Maharashtra	07/2025 (07/2025)	07/2029 (-)	3,626.24 0.00	64.72	3.70
272	Pune Metro Rail Project Phase-2 Line-4 Kharadi to Khadakwasla with Spur Line 4A Nal Stop - Warje - Manikbaug <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (618985) (-) (-)	Maharashtra	12/2025 (12/2025)	12/2030 (-)	9,857.85 0.00	10.46	1.63
273	New Suburba Station Development Project <i>(ministry of housing and urban affairs)</i> (701745) (-) (-)	Maharashtra	04/2018 (03/2019)	07/2022 (-)	262.76 0.00	163.21	48.00
274	Kalyan Station Precinct Improvement Project <i>(ministry of housing and urban affairs)</i> (701991) (-) (-)	Maharashtra	04/2018 (07/2020)	07/2023 (06/2026)	600.00 0.00	540.10	86.00
275	Nagpur Metro Rail Phase II Development Project <i>(Maharashtra Metro Rail Corporation Limited [MMRCL])</i> (702658) (-) (-)	Maharashtra	12/2022 (12/2022)	12/2027 (-)	6,708.00 0.00	2,364.49	43.30
276	Delhi Metro Rail Phase-IV [Rithala - Kundli Corridor] <i>(Delhi Metro Rail Corporation Limited [DMRC])</i> (617206) (-) (-)	Multi-States (Delhi, Haryana)	01/2025 (01/2025)	01/2029 (-)	6,230.99 0.00	818.42	6.84
277	Jaipur Metro Rail Project Phase 2 (Pralhadpura to Todi Mod) <i>(Rajasthan Metro Rail Corporation)</i> (245986) (-) (-)	Rajasthan	04/2026 (04/2026)	10/2031 (-)	13,037.66 0.00	1.79	1.79
278	Rajasthan Metro Rail Project Phase 1C from Badi Chaupar to Transport Nagar via Galta Gate <i>(Rajasthan Metro Rail Corporation)</i> (612066) (-) (-)	Rajasthan	10/2025 (09/2023)	04/2027 (-)	980.08 0.00	103.03	0.00
279	Jaipur Metro Phase 1D Project from Mansarovar to Ajmer Road Chauraha <i>(Rajasthan Metro Rail Corporation)</i> (612068) (-) (-)	Rajasthan	05/2026 (12/2023)	03/2026 (-)	204.81 0.00	23.34	12.48
280	Chennai Metro Rail Phase-II Development Project <i>(Chennai Metro Rail Limited [CMRL])</i> (702668) (-) (-)	Tamil Nadu	10/2024 (11/2020)	08/2029 (-)	63,246.00 0.00	35,228.00	56.53
281	Extension of Aqua Line Metro Corridor from Noida Sector-142 station to Botanical Garden, Noida of Noida Metro Rail Corporation <i>(Noida Metro Rail Corporation Ltd. [NMRCL])</i> (616221) (-) (-)	Uttar Pradesh	03/2026 (03/2026)	03/2030 (-)	2,254.35 0.00	0.00	0.00
282	LUCKNOW METRO RAIL PROJECT PHASE-1B EAST WEST CORRIDOR <i>(Uttar Pradesh metro rail corporation [UPMRC])</i> (619052) (-) (-)	Uttar Pradesh	09/2025 (05/2026)	04/2031 (-)	5,801.05 0.00	15.05	2.20
283	Kanpur Metro Rail Project <i>(Uttar Pradesh metro rail corporation [UPMRC])</i> (702628) (-) (-)	Uttar Pradesh	05/2019 (11/2019)	05/2024 (03/2027)	11,076.48 0.00	9,542.15	83.80
284	Agra Metro Rail Project <i>(Uttar Pradesh metro rail corporation [UPMRC])</i> (702629) (-) (-)	Uttar Pradesh	05/2019 (12/2020)	05/2024 (06/2027)	8,379.62 0.00	6,458.78	73.80
	Total (29)				297,736.37 0.00	144,664.19	

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Waste & Water							
285	ESR - 8 nos., distribution system - 216 Km, new house service connections - 38760 nos. upgrading of feeder mains, pumping station etc. - Phase II <i>(Ministry of Housing & Urban Affairs)</i> (702674) (-) (-)	Andhra Pradesh	02/2017 (07/2018)	03/2023 (08/2026)	172.22 0.00	88.86	82.00
286	Muzaffarpur Storm Water Drainage Phase-I Project <i>(Ministry of Housing & Urban Affairs)</i> (702699) (-) (-)	Bihar	11/2016 (02/2019)	10/2023 (06/2026)	158.78 0.00	135.72	85.00
287	Sewerage Management Scheme Part-3 Implementation <i>(Ministry of Housing & Urban Affairs)</i> (702734) (-) (-)	Haryana	03/2017 (11/2017)	09/2023 (09/2026)	278.01 0.00	228.49	88.00
288	Dhanbad Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702741) (-) (-)	Jharkhand	02/2017 (12/2018)	03/2023 (06/2026)	216.55 0.00	129.16	76.00
289	SAAP-3 Water Supply Infrastructure SAAP-3 Project <i>(Ministry of Housing & Urban Affairs)</i> (702742) (-) (-)	Jharkhand	02/2017 (12/2018)	10/2023 (06/2026)	159.31 0.00	87.50	67.00
290	Augmentation and Strenghthning of Urban Water Supply Phase 1 - SAAP 3 <i>(Ministry of Housing & Urban Affairs)</i> (702746) (-) (-)	Jharkhand	02/2017 (12/2018)	03/2023 (06/2026)	278.28 0.00	186.50	81.00
291	Belgavi Improvement in Sewerage System Project <i>(Ministry of Housing & Urban Affairs)</i> (702760) (-) (-)	Karnataka	12/2015 (10/2016)	07/2023 (06/2026)	162.73 0.00	79.50	80.00
292	Indore Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702793) (-) (-)	Madhya Pradesh	12/2016 (11/2017)	03/2023 (06/2026)	287.17 0.00	252.50	99.00
293	Satna Sewerage Management and Treatment Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702808) (-) (-)	Madhya Pradesh	11/2015 (12/2016)	03/2024 (08/2026)	191.56 0.00	200.32	97.00
294	Singrauli Sewerage Management and Treatment Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702810) (-) (-)	Madhya Pradesh	05/2016 (11/2017)	03/2023 (06/2026)	402.01 0.00	387.75	91.00
295	Kalyan-Dombivali Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702833) (-) (-)	Maharashtra	07/2016 (09/2019)	10/2023 (08/2026)	194.20 0.00	136.56	75.00
296	Jalandhar Water Supply Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (703021) (-) (-)	Punjab	11/2016 (08/2020)	08/2023 (08/2026)	258.53 0.00	161.02	90.00
297	Patiala Water Supply Infrastructure Part-2 Project <i>(Ministry of Housing & Urban Affairs)</i> (703057) (-) (-)	Punjab	11/2016 (08/2020)	10/2023 (08/2026)	287.00 0.00	219.34	99.00
298	Jhansi Water Supply Infrastructure Phase-II Project <i>(Ministry of Housing & Urban Affairs)</i> (702949) (-) (-)	Uttar Pradesh	03/2017 (06/2019)	07/2023 (08/2026)	561.74 0.00	506.52	96.00
299	Lucknow Sewerage Management Infrastructure Project <i>(Ministry of Housing & Urban Affairs)</i> (702958) (-) (-)	Uttar Pradesh	09/2016 (05/2019)	03/2023 (08/2026)	142.46 0.00	152.65	95.00
	Total (15)				3,750.55 0.00	2,952.39	
Ministry of Mines							
Construction							
300	Construction of Basement + Ground Floor+ 10 Storeyed building for State of the Art Director General, GSI Building at plot No.GN-40, Sector-V, Salt Lake, Kolkata <i>(Central Public Works Department [CPWD])</i> (617280) (-) (-)	West Bengal	04/2019 (02/2020)	08/2026 (-)	255.37 0.00	98.96	64.00
	Total (1)				255.37 0.00	98.96	
Metals & Mining							
301	Expansion of Malanjkhand Copper Project <i>(Hindustan Copper Limited [HCL])</i> (400426) (-) (-)	Madhya Pradesh	09/2011 (04/2015)	04/2020 (03/2029)	1,856.36 0.00	1,059.82	32.00
302	Expansion of Alumina Refinery Plant with addition of 5th Stream having capacity enhancement of 1.0 Million Tonee Per Annum <i>(National Aluminium Company Limited [NALCO])</i> (400141) (-) (-)	Odisha	04/2017 (04/2017)	12/2022 (06/2026)	4,103.00 0.00	5,075.89	96.03
303	Pottangi Bauxite Mines Project <i>(National Aluminium Company Limited [NALCO])</i> (400299) (-) (-)	Odisha	05/2018 (05/2018)	03/2025 (11/2026)	1,381.00 0.00	770.37	52.50

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
304	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PANCHPATMAILI MINES (National Aluminium Company Limited [NALCO]) (709831) (-) (-)	Odisha	11/2017 (11/2019)	05/2025 (06/2026)	483.00 0.00	455.73	93.36
305	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU (National Aluminium Company Limited [NALCO]) (709832) (-) (-)	Tamil Nadu	09/2017 (12/2017)	03/2025 (03/2026)	166.00 0.00	135.00	70.00
	Total (5)				7,989.36 0.00	7,496.81	
Department of Higher Education							
Education							
306	Construction of Permanent Campus of Central Tribal University of Andhra Pradesh Phase-1 (Central Tribal University of Andhra Pradesh) (613008) (-) (-)	Andhra Pradesh	09/2019 (12/2023)	06/2027 (-)	305.00 0.00	87.46	46.78
307	Construction of Permanent Campus of National Institute of Technology Arunachal Pradesh (National Institute of Technology, Arunachal Pradesh) (612898) (-) (-)	Arunachal Pradesh	09/2009 (03/2013)	08/2026 (08/2024)	592.61 0.00	551.30	80.00
308	Tezpur University Projects (Tezpur University) (606112) (-) (-)	Assam	05/2019 (06/2021)	11/2023 (12/2025)	153.71 0.00	798.42	97.99
309	Additional Campus of NITPatna (NIT Patna) (606013) (-) (-)	Bihar	07/2022 (08/2022)	07/2024 (01/2026)	499.21 0.00	449.96	99.00
310	Phase B Construction of Permanent Campus of IIT Bhilai (Indian Institute of Technology, Bhilai) (617877) (-) (-)	Chhattisgarh	05/2025 (01/2026)	10/2028 (-)	1,188.97 0.00	1.92	0.00
311	Delhi University Eastern Campus at Surajmal Vihar (Delhi University) (616886) (-) (-)	Delhi	09/2024 (03/2025)	10/2026 (-)	373.00 0.00	33.03	15.00
312	IIT Gandhinagar - Development of Students Hostel Buildings with Associated Facilities under Phase-2A (Indian Institute of Technology, Gandhinagar) (304532) (-) (-)	Gujarat	06/2023 (12/2024)	03/2027 (05/2028)	163.00 0.00	45.22	18.50
313	Construction of permanent campus of Central University of Gujarat at Village kundhela, Dist. Vadodara, Gujarat. (Central University of Gujarat) (612916) (-) (-)	Gujarat	12/2020 (02/2021)	03/2025 (03/2026)	490.63 0.00	342.26	86.00
314	IIT Gandhinagar - Development of Faculty/Staff Housing with Associated Facilities under Phase-2A (Indian Institute of Technology, Gandhinagar) (858179) (-) (-)	Gujarat	06/2023 (12/2024)	03/2027 (08/2027)	156.00 0.00	130.36	45.00
315	Establishment of Permanent campus Phase 1 of IIM Sirmaur (Indian Institute of Management, Sirmaur) (602099) (-) (-)	Himachal Pradesh	09/2018 (08/2020)	10/2023 (09/2026)	392.51 0.00	340.11	98.60
316	Hostel blocks & dining hall block (Indian Institute of Technology, Mandi) (612128) (-) (-)	Himachal Pradesh	03/2023 (03/2024)	03/2026 (09/2026)	166.66 0.00	138.26	94.00
317	Construction of Permanent Campus for IIM Jammu Phase-1 at Jagti, Nagrota, Jammu, J&K (Indian Institute of Management, Jammu) (602098) (-) (-)	Jammu and Kashmir	03/2019 (10/2020)	06/2023 (11/2025)	424.93 0.00	484.52	96.00
318	CONSTRUCTION OF PERMANENT CAMPUS FOR IIT PALAKKAD UNDER PHASE 1A (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (606431) (-) (-)	Kerala	07/2017 (03/2020)	06/2022 (06/2026)	1,006.45 0.00	707.03	89.50
319	Phase B of Construction of Permanent Campus of IIT Palakkad (INDIAN INSTITUTE OF TECHNOLOGY PALAKKAD) (617878) (-) (-)	Kerala	05/2025 (01/2026)	10/2028 (-)	1,527.00 0.00	9.80	0.50
320	Phase III A works at IIT Indore [03 Hostels, 01 Studio Apartment, 01 Housing, Heavy & Sophisticated lab complex, Academic POD and Infrastructure for center of excellence] (Indian Institute of Technology, Indore) (611957) (-) (-)	Madhya Pradesh	12/2023 (04/2024)	02/2027 (-)	496.28 0.00	97.35	69.99
321	Engineering, Procurement and Construction (EPC) of Various Buildings and External Infrastructure Development Works of Indian Institute of Management Mumbai campus in Phase-1 (Indian Institute of Management Mumbai) (505106) (-) (-)	Maharashtra	03/2026 (08/2026)	08/2030 (-)	441.85 0.00	0.00	0.00
322	Construction and Developement of National Institute of Technology Meghalaya Permanent Campus at Sohra (National Institute of Technology, Meghalaya) (612885) (-) (-)	Meghalaya	09/2009 (09/2014)	03/2022 (10/2026)	494.52 0.00	385.32	98.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
323	Construction of Permanent Campus for NIT Mizoram at Lengpui, Aizawl (NIT Mizoram) (612876) (-) (-)	Mizoram	09/2009 (06/2014)	12/2029 (03/2022)	474.23 0.00	167.55	4.00
324	Establishment of NIT Nagaland (NIT Nagaland) (613013) (-) (-)	Nagaland	09/2009 (12/2014)	12/2025 (-)	275.63 0.00	263.25	98.00
325	IISER BERHAMPUR (Indian Institutes of Science Education and Research, Behrampur) (610315) (-) (-)	Odisha	10/2018 (09/2019)	03/2021 (10/2026)	1,229.32 0.00	874.09	98.50
326	Construction of IIT Bhubaneswar -Phase III (Indian Institute of Technology, Bhubaneshwar) (611961) (-) (-)	Odisha	02/2024 (05/2024)	11/2026 (-)	454.27 0.00	103.04	11.57
327	1000 seater Boys hostel, 500 seater Girls hostel, 1.5 MLD Sewage Treatment Plant and Faculty Residence - 72 nos. Flats (NIT Rourkela) (619033) (-) (-)	Odisha	09/2023 (01/2024)	06/2026 (08/2027)	198.97 0.00	57.01	53.00
328	Construction of Permanent Campus of Indian Institute of Management [IIM] Amritsar, Punjab, Phase-I (Indian intitue of Management, Amritsar) (605292) (-) (-)	Punjab	10/2019 (07/2020)	06/2023 (11/2026)	348.31 0.00	294.73	92.69
329	Construction of Girls Hostel 400 seater, Boys Hostel 600 seater, Academic Block, International Hostel 100 seater, VC Residence and Purchase of Equipment (Central University of Punjab) (617221) (-) (-)	Punjab	08/2024 (04/2025)	10/2027 (-)	210.99 0.00	107.71	65.00
330	Phase 3B Development of Permanent Campus of IIT Jodhpur (Indian Institute of Technology, Jodhpur) (617421) (-) (-)	Rajasthan	07/2025 (01/2026)	01/2028 (-)	522.89 0.00	29.47	10.31
331	Construction of Sikkim University Campus Phase-I Package-II at Yangang, South Sikkim (Sikkim University) (609736) (-) (-)	Sikkim	08/2020 (01/2022)	01/2025 (10/2026)	314.06 0.00	292.00	97.00
332	Establishment of Permanent Campus of NIT Sikkim at Khamdong-Gangtok District (NIT Sikkim) (612883) (-) (-)	Sikkim	02/2024 (03/2024)	02/2028 (12/2026)	685.76 0.00	283.56	38.50
333	Construction of Precast housing and hostels at IIT Hyderabad (Indian Institute of Technology, Hyderabad) (609996) (-) (-)	Telangana	09/2022 (11/2022)	10/2024 (01/2026)	262.00 0.00	225.58	91.10
334	Banaras Hindu University [Kayakalp of Institute of Medical Sciences] (Banaras Hindu University) (606479) (-) (-)	Uttar Pradesh	06/2020 (06/2020)	09/2022 (07/2027)	246.00 0.00	214.03	99.20
335	Construction & Development of Infrastructural Facilities in the main campus of NIT Uttarakhand at Sumari, Pauri Garhwal (National Institute of Technology Uttarakhand) (611963) (-) (-)	Uttarakhand	06/2020 (04/2024)	09/2027 (-)	650.85 0.00	414.41	66.00
336	HEFA projects on development of student hostels, playgrounds, departmental buildings, class room complex and other campus facilities in IIT Kharagpur (Indian Institute of Technology, Kharagpur) (609019) (-) (-)	West Bengal	06/2018 (04/2019)	03/2023 (12/2026)	500.00 0.00	420.10	96.74
	Total (31)				15,245.61 0.00	8,348.85	
	Department of Sports						
	Education						
337	National Sports University [NSU], Imphal [Manipur] (Department of Sports & Youth Affairs) (400081) (-) (-)	Manipur	06/2022 (01/2022)	08/2024 (08/2026)	906.47 0.00	577.32	97.70
	Total (1)				906.47 0.00	577.32	
	Ministry of Petroleum & Natural Gas						
	Energy Storage						
338	Development of Rail - Fed Road Tanker Loading POL Terminal at Panchgram [Near Silchar], Hailakandi, Assam. (Numaligarh Refinery Limited) (308266) (-) (-)	Assam	08/2025 (08/2025)	10/2027 (-)	433.12 0.00	77.37	23.00
339	Construction of LPG Facilities at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709754) (-) (-)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	156.36 0.00	116.83	85.70
340	Setting up of new rail fed POL facility at Kamardanga, Assam (Hindustan Petroleum Corporation Limited) (709755) (-) (-)	Assam	03/2023 (03/2023)	07/2027 (07/2027)	384.04 0.00	254.02	89.10

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
341	Capacity Augmentation of Kandla LPG Import Terminal [KLIT] from 0.6 MMTPA to 2.5 MMTPA (Indian Oil Corporation Limited [IOCL]) (617839) (-) (-)	Gujarat	05/2023 (05/2023)	07/2026 (12/2026)	356.86 0.00	169.74	68.50
342	Andheri Residential Towers, Mumbai (Indian Oil Corporation Limited [IOCL]) (604833) (-) (-)	Maharashtra	06/2017 (06/2017)	05/2025 (06/2027)	281.35 0.00	294.89	88.00
343	Setting up of 50 MW [plus/minus 5 percent] Wind Power Plant for Captive Consumption at MR (Bharat Petroleum Corporation Limited [BPCL]) (619313) (-) (-)	Maharashtra	05/2023 (05/2023)	04/2027 (04/2027)	483.14 0.00	381.29	81.10
344	LPG Bottling Plant at Mualkhang (Indian Oil Corporation Limited [IOCL]) (617829) (-) (-)	Mizoram	07/2024 (07/2024)	10/2028 (05/2028)	225.71 0.00	33.36	34.50
345	Petrochemical evacuation marketing terminal at Barmer, Rajasthan (Hindustan Petroleum Corporation Limited) (709759) (-) (-)	Rajasthan	12/2023 (12/2023)	12/2026 (12/2026)	461.05 0.00	256.76	98.40
346	Laying of POL Pipelines in Common Corridor for proposed grass root terminal at Vallur [Chennai] (Indian Oil Corporation Limited [IOCL]) (400043) (-) (-)	Tamil Nadu	01/2022 (01/2022)	05/2026 (03/2027)	829.00 0.00	388.90	82.30
347	Multi Product Pipeline from Irugur to Devangonchi (Department of Water Resources, River Development & GR) (400301) (-) (-)	Tamil Nadu	11/2012 (11/2012)	02/2017 (09/2026)	678.00 0.00	1,237.73	87.90
348	Kandla Gorakhpur LPG Pipeline (Indian Oil Corporation Limited [IOCL]) (400012) (-) (-)	Uttar Pradesh	12/2018 (12/2018)	12/2021 (10/2026)	10,088.00 0.00	8,598.52	96.30
349	Grass-root Terminal at Mirzapur, Uttar Pradesh (Indian Oil Corporation Limited [IOCL]) (604852) (-) (-)	Uttar Pradesh	09/2022 (09/2022)	11/2026 (11/2026)	980.45 0.00	312.19	77.60
350	Paradip-Numaligarh Crude Oil Pipeline [PNCPL] & Crude Oil Import Terminal [COIT] at Paradip (Numaligarh Refinery Limited) (701349) (-) (-)	West Bengal	01/2019 (01/2019)	07/2024 (10/2026)	10,228.00 0.00	11,236.46	93.60
Total (13)					25,585.08 0.00	23,358.06	
Oil & Gas							
351	KG-DWN-98/2 Cluster - II Development Project - NELP Block (Oil and Natural Gas Corporation Limited [ONGC]) (400120) (-) (-)	Andhra Pradesh	03/2016 (03/2016)	06/2020 (09/2026)	34,012.00 0.00	33,198.79	97.00
352	Old Naphtha Isomerization Unit [NIU] revamp for MS maximization at Visakh Refinery (Hindustan Petroleum Corporation Limited) (409131) (-) (-)	Andhra Pradesh	03/2025 (03/2025)	07/2028 (-)	449.00 0.00	24.57	7.70
353	Provision of four bitumen tanks with capacity of 5 TMT each at Visakh Refinery (Hindustan Petroleum Corporation Limited) (619226) (-) (-)	Andhra Pradesh	09/2025 (09/2025)	03/2028 (03/2028)	258.34 0.00	11.76	23.20
354	HP-COAT [Crude to Olefins and Aromatics Technology] demo unit at Visakh Refinery (Hindustan Petroleum Corporation Limited) (709752) (-) (-)	Andhra Pradesh	09/2021 (09/2021)	06/2024 (02/2027)	160.00 0.00	159.74	94.10
355	Numaligarh Refinery Expansion Project (Numaligarh Refinery Limited) (604791) (-) (-)	Assam	07/2020 (07/2020)	07/2024 (03/2027)	12,366.00 0.00	20,845.77	87.70
356	Development of Surface Facilities for production and evacuation of Crude Oil and Natural Gas from Nadua and East Khagorija (Oil India Limited) (604863) (-) (-)	Assam	01/2018 (01/2018)	02/2020 (12/2026)	682.90 0.00	601.12	94.60
357	Construction of Field Gas Gathering Station at Baghjan area for collection, processing & transportation of natural Gas to be produced from Baghjan Field (Oil India Limited) (616858) (-) (-)	Assam	12/2020 (12/2020)	03/2024 (11/2026)	430.76 0.00	348.65	97.00
358	Pipeline Rehabilitation Project, Phase-II (Oil India Limited) (617827) (-) (-)	Assam	12/2024 (12/2024)	12/2029 (12/2029)	680.00 0.00	13.78	29.60
359	Coke Drum Structure Package (Numaligarh Refinery Limited) (617836) (-) (-)	Assam	12/2022 (12/2022)	12/2025 (12/2026)	635.28 0.00	506.82	76.50
360	Group Gathering Station, Lakwagaon (Oil India Limited) (619316) (-) (-)	Assam	10/2025 (10/2025)	10/2027 (10/2027)	495.59 0.00	39.97	20.10
361	Augmentation/Revamping of Facilities at existing Guwahati Terminal at Betkuchi (Indian Oil Corporation Limited [IOCL]) (709776) (-) (-)	Assam	04/2022 (04/2022)	09/2026 (09/2026)	277.00 0.00	237.33	84.80

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
362	Capacity Expansion of Digboi Refinery from 0.65 to 1.0 MMTPA (Indian Oil Corporation Limited [IOCL]) (709779) (-) (-)	Assam	06/2022 (06/2022)	03/2026 (07/2027)	768.00 0.00	250.84	60.80
363	Pipeline Network Project Rudrasagar (Oil and Natural Gas Corporation Limited [ONGC]) (709847) (-) (-)	Assam	01/2023 (01/2023)	04/2026 (04/2027)	481.03 0.00	238.83	55.40
364	Borholla GGS Life Extension Project [BLEP] (Oil and Natural Gas Corporation Limited [ONGC]) (709850) (-) (-)	Assam	09/2023 (09/2023)	05/2026 (03/2027)	198.70 0.00	110.99	64.30
365	DCU Revamp Project (Numaligarh Refinery Limited) (709864) (-) (-)	Assam	08/2021 (08/2021)	07/2024 (03/2027)	370.00 0.00	315.57	82.70
366	Power Recovery Turbine [PRT] in PFCCU unit as an Energy Conservation Scheme (Numaligarh Refinery Limited) (709865) (-) (-)	Assam	04/2023 (04/2023)	12/2024 (12/2026)	293.50 0.00	81.84	99.00
367	2.4 KTPA Green Hydrogen Generation Unit at Numaligarh (Numaligarh Refinery Limited) (891687) (-) (-)	Assam	02/2023 (02/2023)	03/2027 (-)	170.00 0.00	37.33	45.50
368	Setting up of LPG Plant with Rail Unloading Facility at Hathua, Dist. Gopalganj, Bihar (Bharat Petroleum Corporation Limited [BPCL]) (617304) (-) (-)	Bihar	10/2023 (10/2023)	03/2027 (03/2027)	340.15 0.00	191.00	56.50
369	Barauni Refinery Capacity Expansion from 6.0 to 9.0 MMTPA (Indian Oil Corporation Limited [IOCL]) (701324) (-) (-)	Bihar	01/2020 (01/2020)	04/2023 (12/2026)	14,810.00 0.00	13,220.97	92.20
370	Installation of Bitumen Manufacturing Unit along with allied facilities at Barauni Refinery (Indian Oil Corporation Limited [IOCL]) (709777) (-) (-)	Bihar	01/2022 (01/2022)	04/2025 (06/2027)	389.35 0.00	128.43	68.70
371	City Gas Distribution Projects at Darbhanga, Madhubani, Supaul, Sitamarhi and Sheohar districts (Bharat Petroleum Corporation Limited [BPCL]) (709792) (-) (-)	Bihar	12/2022 (12/2022)	03/2030 (03/2030)	3,638.00 0.00	508.68	33.70
372	City Gas Distribution Projects at Gopalganj, Siwan, West Champaran, East Champaran and Deoria districts (Bharat Petroleum Corporation Limited [BPCL]) (709793) (-) (-)	Bihar	12/2022 (12/2022)	06/2030 (06/2030)	3,919.00 0.00	534.37	30.30
373	City Gas Distribution [CGD] Project in Kondagaon, Bastar, Sukma, Narayanpur, Bijapur & Dantewada GA (GAIL Gas) (617819) (-) (-)	Chhattisgarh	06/2022 (06/2022)	06/2030 (06/2030)	557.04 0.00	11.63	2.20
374	Redevelopment of Sobhasan Complex (Oil and Natural Gas Corporation Limited [ONGC]) (400087) (-) (-)	Gujarat	08/2021 (08/2021)	03/2027 (03/2027)	885.63 0.00	1,131.85	96.90
375	Redevelopment of Santhal Field [Onshore-Mehsana Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (400167) (-) (-)	Gujarat	02/2017 (02/2017)	03/2026 (12/2026)	1,162.56 0.00	1,131.85	97.20
376	Redevelopment of Linch Field (Oil and Natural Gas Corporation Limited [ONGC]) (400169) (-) (-)	Gujarat	04/2021 (04/2021)	03/2025 (10/2026)	631.03 0.00	635.90	94.50
377	Petrochemical and Lube Integration Project at Gujarat Refinery (Indian Oil Corporation Limited [IOCL]) (701329) (-) (-)	Gujarat	09/2020 (09/2020)	08/2024 (11/2026)	18,936.00 0.00	13,954.28	89.90
378	Installation of new Biturox Unit along with allied facilities at Gujarat Refinery (Indian Oil Corporation Limited [IOCL]) (709778) (-) (-)	Gujarat	01/2022 (01/2022)	08/2025 (12/2026)	328.29 0.00	225.29	88.60
379	Commercial Polymer Flooding Project in Bechraji field (Oil and Natural Gas Corporation Limited [ONGC]) (709838) (-) (-)	Gujarat	01/2022 (01/2022)	11/2024 (05/2027)	621.40 0.00	283.60	50.00
380	Restoration of Gas Terminal, Phase-I [Part-A], Hazira (Oil and Natural Gas Corporation Limited [ONGC]) (709840) (-) (-)	Gujarat	05/2022 (05/2022)	02/2025 (09/2026)	249.43 0.00	219.56	97.70
381	Old Pipe Line Replacement [OPRP] Group-A (Oil and Natural Gas Corporation Limited [ONGC]) (709841) (-) (-)	Gujarat	07/2021 (07/2021)	07/2025 (11/2026)	173.03 0.00	168.22	94.60
382	Kalol Redevelopment Project, Ahmedabad Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709842) (-) (-)	Gujarat	08/2022 (08/2022)	03/2027 (03/2027)	1,487.41 0.00	946.45	67.20
383	Revamping of SV Stations, Gas Terminal & Kribhco Terminal (Oil and Natural Gas Corporation Limited [ONGC]) (709845) (-) (-)	Gujarat	11/2022 (11/2022)	08/2026 (02/2028)	837.34 0.00	531.84	71.60

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
384	Indian Oil Technology Development and Deployment Centre at R&D Campus-II, Faridabad <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(604853)</i> (-) (-)	Haryana	06/2019 (06/2019)	12/2022 (07/2027)	2,281.94 0.00	1,922.10	65.50
385	Poly Butadiene Rubber plant at Panipat <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(611917)</i> (-) (-)	Haryana	03/2022 (03/2022)	03/2025 (12/2026)	1,459.00 0.00	1,570.15	90.90
386	Change of service of existing Mundra-Panipat Pipeline [Panipat - Churwa section] from Crude oil to Product <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(619196)</i> (-) (-)	Haryana	05/2025 (05/2025)	04/2027 (04/2027)	359.00 0.00	58.24	46.40
387	Capacity Expansion of Panipat Refinery from 15 to 25 MMTPA <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(701289)</i> (-) (-)	Haryana	02/2021 (02/2021)	09/2024 (12/2026)	34,627.00 0.00	28,279.45	94.70
388	Installation of Multiple Effect Evaporator [MEE] for ETP-1, 2 & 4 of Panipat Refinery and Petrochemical Complex. <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(709783)</i> (-) (-)	Haryana	12/2020 (12/2020)	06/2023 (10/2026)	165.13 0.00	197.46	93.00
389	City Gas Distribution Project at Jammu, Udhampur, Reasi, Samba and Kathua Districts <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(709773)</i> (-) (-)	Jammu and Kashmir	03/2022 (03/2022)	09/2034 (09/2034)	538.00 0.00	4.47	0.60
390	Development of Jharia CBM Block [Phase-1] <i>(Oil and Natural Gas Corporation Limited [ONGC])</i> <i>(610984)</i> (-) (-)	Jharkhand	11/2019 (11/2019)	01/2024 (09/2026)	431.00 0.00	268.74	66.20
391	Laying of Natural Gas Pipeline from Hazaribagh to Ranchi [HRPL] <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(709785)</i> (-) (-)	Jharkhand	02/2023 (02/2023)	02/2026 (03/2027)	202.07 0.00	66.68	58.90
392	Devanagonthi to Kempe Gowda International Airport (KIAL) ATF Pipeline Project <i>(Mangalore Refinery and Petrochemicals Limited)</i> <i>(368840)</i> (-) (-)	Karnataka	07/2026 (07/2026)	05/2029 (-)	234.00 0.00	0.00	0.00
393	Drive Conversion of Turbines in CHT, DHDT and DCU. <i>(Mangalore Refinery and Petrochemicals Limited)</i> <i>(503783)</i> (-) (-)	Karnataka	02/2026 (02/2026)	09/2028 (-)	206.24 0.00	0.48	12.30
394	Power System Upgradation Project <i>(Mangalore Refinery and Petrochemicals Limited)</i> <i>(612790)</i> (-) (-)	Karnataka	10/2023 (10/2023)	11/2025 (09/2026)	385.00 0.00	273.54	92.00
395	Demo Bio-ATF Project <i>(Mangalore Refinery and Petrochemicals Limited)</i> <i>(616879)</i> (-) (-)	Karnataka	03/2024 (03/2024)	01/2027 (01/2027)	364.00 0.00	102.06	60.20
396	City Gas Distribution Maharashtra Natural Gas Limited <i>(Gas Authority of India Limited [GAIL])</i> <i>(701338)</i> (-) (-)	Karnataka	01/2006 (01/2006)	06/2031 (06/2031)	5,535.00 0.00	4,537.07	47.00
397	Revamping/ Augmentation of facilities at existing port terminal at Mangalore <i>(Indian Oil Corporation Limited [IOCL])</i> <i>(709774)</i> (-) (-)	Karnataka	01/2022 (01/2022)	12/2025 (06/2027)	463.00 0.00	332.16	85.60
398	Capacity Enhancement of VGOHDT unit at Kochi Refinery <i>(Bharat Petroleum Corporation Limited [BPCL])</i> <i>(168896)</i> (-) (-)	Kerala	05/2026 (05/2026)	01/2027 (-)	264.66 0.00	0.00	21.20
399	Augmentation of CCKPL and IDPL Pipelines capacity along with setting up of Palakkad TOP <i>(Bharat Petroleum Corporation Limited [BPCL])</i> <i>(617838)</i> (-) (-)	Kerala	09/2024 (09/2024)	08/2028 (08/2028)	1,130.00 0.00	340.39	51.10
400	Setting up 167 KTPA Sulphuric Acid Unit and Associated Facilities at Kochi Refinery <i>(Bharat Petroleum Corporation Limited [BPCL])</i> <i>(691992)</i> (-) (-)	Kerala	07/2026 (07/2026)	07/2029 (-)	732.86 0.00	0.00	0.50
401	Setting up Polypropylene Unit at Kochi Refinery <i>(Bharat Petroleum Corporation Limited [BPCL])</i> <i>(709799)</i> (-) (-)	Kerala	12/2023 (12/2023)	10/2027 (11/2027)	4,460.00 0.00	1,077.50	50.10
402	50 MW Wind Power Plant in Madhya Pradesh <i>(Bharat Petroleum Corporation Limited [BPCL])</i> <i>(244981)</i> (-) (-)	Madhya Pradesh	05/2023 (05/2023)	04/2027 (-)	483.14 0.00	183.53	67.50
403	C2/C3 Vijaipur Pata Pipeline <i>(Gas Authority of India Limited [GAIL])</i> <i>(617830)</i> (-) (-)	Madhya Pradesh	05/2024 (05/2024)	01/2027 (01/2027)	1,792.00 0.00	550.50	74.60
404	Ethylene Cracker Project at Bina Refinery including downstream Petrochemical Plants and expansion of Refinery <i>(Bharat Petroleum Corporation Limited [BPCL])</i> <i>(709798)</i> (-) (-)	Madhya Pradesh	05/2023 (05/2023)	05/2028 (05/2028)	43,367.00 0.00	6,688.50	36.60

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
405	Vijaipur – BPCL, Bina Pipeline Project (Gas Authority of India Limited [GAIL]) (929104) (-) (-)	Madhya Pradesh	09/2025 (09/2025)	09/2027 (-)	449.04 0.00	1.40	16.40
406	500 KTA PDHPP Project, Usar (Gas Authority of India Limited [GAIL]) (400168) (-) (-)	Maharashtra	04/2021 (04/2021)	04/2025 (06/2027)	8,797.00 0.00	8,971.88	92.40
407	Lube Modernization & Bottom Upgradation Project at Mumbai Refinery (Hindustan Petroleum Corporation Limited) (616933) (-) (-)	Maharashtra	12/2024 (12/2024)	03/2028 (08/2029)	4,679.00 0.00	326.17	15.80
408	Petro Resid Fluidized Catalytic Cracking [PRFCC] Unit and its associated facilities at Mumbai Refinery (Bharat Petroleum Corporation Limited [BPCL]) (619223) (-) (-)	Maharashtra	05/2025 (05/2025)	09/2029 (09/2029)	13,626.00 0.00	109.00	8.40
409	Augmentation of DUPL-DPPL Pipeline (Gas Authority of India Limited [GAIL]) (619224) (-) (-)	Maharashtra	06/2025 (06/2025)	03/2028 (03/2028)	844.00 0.00	1.60	19.70
410	Installation of Compression facility at GAIL Usar (Gas Authority of India Limited [GAIL]) (619225) (-) (-)	Maharashtra	04/2025 (04/2025)	04/2027 (04/2027)	260.20 0.00	0.00	0.00
411	ONGC-BP Redevelopment Phase-1 Scheme of Mumbai High Field (Oil and Natural Gas Corporation Limited [ONGC]) (619328) (-) (-)	Maharashtra	11/2025 (11/2025)	03/2027 (03/2027)	3,713.40 0.00	2,461.06	56.30
412	Setting up Coprocessing facility in KHT Unit for production of SAF at MR (Bharat Petroleum Corporation Limited [BPCL]) (684624) (-) (-)	Maharashtra	01/2026 (01/2026)	12/2027 (-)	677.00 0.00	10.54	19.20
413	GAS Turbine GT-3 upgrade from frame 6B to 6B.03 (Bharat Petroleum Corporation Limited [BPCL]) (687613) (-) (-)	Maharashtra	01/2026 (01/2026)	07/2027 (-)	217.81 0.00	0.02	12.50
414	City Gas Distribution Project at Beed, Jalgaon and Jalna Districts (Indian Oil Corporation Limited [IOCL]) (709771) (-) (-)	Maharashtra	03/2022 (03/2022)	09/2031 (09/2031)	865.00 0.00	89.81	3.40
415	Construction of Additional Tankages and Allied Facilities at JNPT Terminal (Indian Oil Corporation Limited [IOCL]) (709780) (-) (-)	Maharashtra	04/2022 (04/2022)	08/2026 (12/2027)	341.43 0.00	305.01	73.10
416	POL & LOBS Installations with Receipt Pipelines at Rasayani (Bharat Petroleum Corporation Limited [BPCL]) (709797) (-) (-)	Maharashtra	05/2023 (05/2023)	05/2026 (09/2026)	2,585.00 0.00	1,565.53	92.50
417	Visakh Raipur Pipeline Project (Hindustan Petroleum Corporation Limited) (616254) (-) (-)	Multi-States (Chhattisgarh, Odisha)	09/2024 (09/2024)	09/2027 (09/2027)	2,212.00 0.00	576.00	39.90
418	Augmentation/ Revamping of Dimapur Depot, Dimapur (Indian Oil Corporation Limited [IOCL]) (709786) (-) (-)	Nagaland	08/2023 (08/2023)	11/2027 (11/2027)	227.62 0.00	28.65	44.20
419	Integrated Para Xylene [PX] and Purified Terephthalic Acid [PTA] Project at Paradip Refinery (Indian Oil Corporation Limited [IOCL]) (604859) (-) (-)	Odisha	07/2020 (07/2020)	01/2024 (09/2026)	13,805.00 0.00	8,995.00	95.20
420	City Gas Distribution [CGD] Project in Gajapati, Kandhamal, Boudh, & Sonepur GA (GAIL Gas) (617818) (-) (-)	Odisha	02/2022 (02/2022)	12/2031 (12/2031)	514.91 0.00	25.77	6.00
421	CUF POL Depot at Sadashibpur [Meramundali], Odisha (Bharat Petroleum Corporation Limited [BPCL]) (709800) (-) (-)	Odisha	04/2021 (04/2021)	03/2026 (09/2026)	393.54 0.00	237.30	87.40
422	Life Extension of 48 well platforms of Mumbai High & Heera Fields (Oil and Natural Gas Corporation Limited [ONGC]) (400119) (-) (-)	Offshore	12/2015 (12/2015)	04/2018 (10/2026)	3,190.69 0.00	3,123.20	90.00
423	PRP-VIII [Group-A] (Oil and Natural Gas Corporation Limited [ONGC]) (616950) (-) (-)	Offshore	09/2024 (09/2024)	02/2026 (03/2027)	1,589.40 0.00	663.00	61.30
424	Pipeline Replacement Project- PRP-IX (Oil and Natural Gas Corporation Limited [ONGC]) (619314) (-) (-)	Offshore	08/2025 (08/2025)	05/2027 (05/2027)	3,471.72 0.00	1,250.00	29.30
425	Daman Upside Development Project (Oil and Natural Gas Corporation Limited [ONGC]) (709839) (-) (-)	Offshore	06/2022 (06/2022)	10/2025 (12/2026)	4,144.41 0.00	6,302.50	92.90
426	MHN TCPP PGC BGC Project [MTPBP] (Oil and Natural Gas Corporation Limited [ONGC]) (709848) (-) (-)	Offshore	06/2022 (06/2022)	05/2026 (12/2026)	2,329.45 0.00	1,940.25	96.10

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
427	PRP-VIII Group B [NH & BS Asset] (Oil and Natural Gas Corporation Limited [ONGC]) (709849) (-) (-)	Offshore	06/2024 (06/2024)	02/2026 (12/2026)	2,546.90 0.00	3,003.90	98.70
428	Integrated Development of 4 Contract Areas under DSF-II (Oil and Natural Gas Corporation Limited [ONGC]) (709851) (-) (-)	Offshore	05/2023 (05/2023)	04/2027 (04/2027)	6,183.79 0.00	2,053.00	48.70
429	Well Head Platforms for MB-OSN-2005/1, SD4 and BS-17 Field (WHPMSBF) (Oil and Natural Gas Corporation Limited [ONGC]) (757296) (-) (-)	Offshore	07/2026 (07/2026)	03/2029 (-)	5,519.00 0.00	0.00	0.00
430	Pipeline Replacement Project- PRP-X (Oil and Natural Gas Corporation Limited [ONGC]) (785574) (-) (-)	Offshore	07/2026 (07/2026)	05/2027 (-)	4,371.00 0.00	0.00	0.00
431	Additional Development of Ratna-I [ADR-I] and NLM-14 Project (Oil and Natural Gas Corporation Limited [ONGC]) (944988) (-) (-)	Offshore	07/2026 (07/2026)	03/2029 (-)	6,274.00 0.00	0.00	0.00
432	2G Ethanol Biorefinery at Bathinda (Hindustan Petroleum Corporation Limited) (400171) (-) (-)	Punjab	05/2020 (05/2020)	02/2023 (12/2026)	1,421.46 0.00	1,297.86	95.90
433	Gurdaspur Jammu Pipeline (Gas Authority of India Limited [GAIL]) (612853) (-) (-)	Punjab	07/2023 (07/2023)	07/2026 (09/2026)	521.90 0.00	349.20	92.30
434	City Gas Distribution Project at Pathankot District (Indian Oil Corporation Limited [IOCL]) (709770) (-) (-)	Punjab	03/2022 (03/2022)	09/2033 (09/2033)	151.00 0.00	9.05	2.00
435	Mehsana-Bhatinda & Bhatinda-Jammu Natural Gas Pipeline (Indian Oil Corporation Limited [IOCL]) (701330) (-) (-)	Rajasthan	07/2011 (07/2011)	06/2024 (03/2027)	7,392.00 0.00	6,365.13	90.20
436	City Gas Distribution Projects at Fazilka [except area already authorized], Ganganagar and Hanumangarh districts (Bharat Petroleum Corporation Limited [BPCL]) (709794) (-) (-)	Rajasthan	12/2022 (12/2022)	06/2030 (06/2030)	3,207.00 0.00	431.76	31.90
437	Group-II/III LOBS Project (Chennai Petroleum Corporation Limited [CPCL]) (167179) (-) (-)	Tamil Nadu	03/2026 (03/2026)	10/2028 (-)	1,620.00 0.00	77.53	2.20
438	CBR 9 MMTPA Project (Chennai Petroleum Corporation Limited [CPCL]) (604795) (-) (-)	Tamil Nadu	09/2021 (09/2021)	06/2025 (10/2028)	31,580.00 0.00	1,615.53	10.20
439	Kochi - Kootanad - Bangalore - Mangalore Pipeline Phase-II (Gas Authority of India Limited [GAIL]) (701228) (-) (-)	Tamil Nadu	06/2009 (06/2009)	12/2012 (09/2026)	2,915.00 0.00	4,897.90	97.60
440	Laying of new 28 inch Desal Water Pipeline and 10 inch Reject Water Pipeline between CPCL Manali Refinery and CPCL Desalination plant at Ennore (Chennai Petroleum Corporation Limited [CPCL]) (709750) (-) (-)	Tamil Nadu	01/2024 (01/2024)	09/2025 (12/2026)	205.00 0.00	117.98	79.10
441	City Gas Distribution Projects at the Nilgiris and Erode districts (Bharat Petroleum Corporation Limited [BPCL]) (709796) (-) (-)	Tamil Nadu	12/2022 (12/2022)	03/2030 (03/2030)	3,685.00 0.00	322.83	25.60
442	ATF Pipeline from BPCLs Malkapur POL Installation to Hyderabad International airport (Bharat Petroleum Corporation Limited [BPCL]) (617822) (-) (-)	Telangana	03/2025 (03/2025)	09/2027 (09/2027)	215.00 0.00	47.50	34.10
443	North East Gas Grid (Indradhanush Gas Grid Limited) (701346) (-) (-)	Tripura	04/2020 (04/2020)	03/2024 (03/2028)	9,265.00 0.00	7,011.75	88.60
444	Creation of Gas Dehydration Facilities, Tripura Asset (Oil and Natural Gas Corporation Limited [ONGC]) (709837) (-) (-)	Tripura	03/2022 (03/2022)	05/2024 (10/2026)	209.33 0.00	81.31	72.00
445	Kanpur LPG Bottling Plant (Bharat Petroleum Corporation Limited [BPCL]) (619191) (-) (-)	Uttar Pradesh	09/2025 (09/2025)	09/2027 (09/2027)	202.00 0.00	133.17	65.00
446	Bulk Loading Hub- Kanpur (Bharat Petroleum Corporation Limited [BPCL]) (619312) (-) (-)	Uttar Pradesh	09/2025 (09/2025)	09/2027 (09/2027)	186.00 0.00	107.80	65.00
447	Revamping / Augmentation of Facilities at Mathura Bitumen Plant (Indian Oil Corporation Limited [IOCL]) (709781) (-) (-)	Uttar Pradesh	04/2022 (04/2022)	06/2027 (06/2027)	260.12 0.00	25.84	58.80
448	City Gas Distribution Projects at Lakhimpur Kheri , Sitapur, Bahraich, Shravasti,Balrampur, Siddharth Nagar & Maharajganj districts (Bharat Petroleum Corporation Limited [BPCL]) (709795) (-) (-)	Uttar Pradesh	12/2022 (12/2022)	06/2030 (06/2030)	16,654.00 0.00	763.51	20.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
449	Durgapur - Haldia Pipeline [Section-3B of JHBDPL Project] <i>(Gas Authority of India Limited [GAIL])</i> (617302) (-) (-)	West Bengal	03/2017 (03/2017)	12/2020 (09/2026)	1,740.00 0.00	2,392.60	95.70
450	Siliguri-Jhapa Pipeline Project <i>(Indian Oil Corporation Limited [IOCL])</i> (617828) (-) (-)	West Bengal	09/2024 (09/2024)	08/2029 (08/2029)	267.00 0.00	3.40	17.50
451	Siliguri Marketing Terminal [SMT] Capacity Augmentation Project <i>(Numaligarh Refinery Limited)</i> (617837) (-) (-)	West Bengal	11/2021 (11/2021)	12/2025 (10/2026)	484.00 0.00	321.23	90.00
452	Dhamra Haldia Pipeline Project <i>(Gas Authority of India Limited [GAIL])</i> (701344) (-) (-)	West Bengal	03/2020 (03/2020)	11/2022 (09/2026)	1,030.65 0.00	929.00	94.50
453	City Gas Distribution Project at East Mednipore, West Mednipore & Jhargram Districts <i>(Indian Oil Corporation Limited [IOCL])</i> (709772) (-) (-)	West Bengal	03/2022 (03/2022)	06/2031 (06/2031)	609.00 0.00	64.84	3.10
454	City Gas Distribution Projects at Alipurduar and Cooch Behar <i>(Bharat Petroleum Corporation Limited [BPCL])</i> (709791) (-) (-)	West Bengal	12/2022 (12/2022)	03/2030 (03/2030)	1,017.00 0.00	246.55	44.00
	Total (104)				379,839.57 0.00	206,954.50	
Ministry of Health & Family Welfare							
Healthcare							
455	AIIMS Darbhanga <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701172) (-) (-)	Bihar	09/2020 (09/2020)	07/2029 (-)	2,006.07 0.00	40.33	1.13
456	Establishment of new GMC Jamui <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707020) (-) (-)	Bihar	03/2019 (10/2022)	10/2025 (-)	250.00 0.00	103.41	32.00
457	Establishment of new GMC Korba <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707044) (-) (-)	Chhattisgarh	02/2023 (10/2023)	12/2026 (-)	325.00 0.00	179.59	56.00
458	Establishment of new GMC Mahasamund <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707045) (-) (-)	Chhattisgarh	10/2023 (10/2023)	05/2026 (-)	325.00 0.00	321.70	84.00
459	Establishment of new GMC Kanker <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707046) (-) (-)	Chhattisgarh	02/2020 (09/2024)	03/2027 (-)	325.00 0.00	37.10	45.00
460	Setting up IT Infrastructure including Network Security and Hosting at AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617882) (-) (-)	Delhi	09/2025 (09/2025)	09/2026 (-)	358.19 0.00	53.73	50.00
461	Redevelopment of Residential colonies at Ayur Vigyan Nagar and West Ansari Nagar campuses of AIIMS, New Delhi <i>(PMSSY AND Institute of NATIONAL Importance)</i> (617883) (-) (-)	Delhi	10/2016 (06/2022)	06/2027 (-)	4,441.00 0.00	44.44	57.00
462	AIIMS Rajkot <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701170) (-) (-)	Gujarat	01/2019 (01/2019)	03/2026 (12/2026)	1,195.00 0.00	809.29	94.10
463	Establishment of new GMC Panchmahal <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707049) (-) (-)	Gujarat	09/2022 (09/2022)	03/2026 (-)	325.00 0.00	467.35	98.00
464	Establishment of new GMC Porbandar <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707050) (-) (-)	Gujarat	04/2022 (10/2022)	09/2024 (-)	325.00 0.00	936.84	81.00
465	AIIMS Majra Rewari Haryana <i>(Ministry of Health and Family Welfare)</i> (701173) (-) (-)	Haryana	02/2019 (02/2019)	12/2026 (12/2026)	1,299.00 0.00	772.62	69.70
466	AIIMS Kashmir at Awantipora Jammu & Kashmir <i>(PMSSY AND Institute of NATIONAL Importance)</i> (701167) (-) (-)	Jammu and Kashmir	01/2019 (03/2019)	12/2025 (12/2026)	1,828.00 0.00	1,624.30	80.00
467	Establishment of new GMC Udhampur <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707051) (-) (-)	Jammu and Kashmir	09/2019 (01/2022)	03/2027 (-)	325.00 0.00	226.08	85.00
468	Establishment of new GMC Koderma <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707021) (-) (-)	Jharkhand	09/2023 (02/2024)	08/2026 (-)	250.00 0.00	271.00	40.00
469	Establishment of new GMC Chaibasa [Singhbhum] <i>(Medical Education, Ministry of Health and Family Welfare)</i> (707022) (-) (-)	Jharkhand	06/2018 (03/2023)	09/2025 (09/2026)	250.00 0.00	333.10	83.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
470	Establishment of new GMC Rajgarh (Medical Education, Ministry of Health and Family Welfare) (707058) (-) (-)	Madhya Pradesh	12/2021 (11/2022)	04/2024 (-)	325.00 0.00	179.50	86.00
471	Establishment of new GMC Mandla (Medical Education, Ministry of Health and Family Welfare) (707059) (-) (-)	Madhya Pradesh	08/2023 (10/2023)	04/2026 (-)	325.00 0.00	89.41	45.50
472	Establishment of new GMC Kapurthala (Medical Education, Ministry of Health and Family Welfare) (707069) (-) (-)	Punjab	11/2019 (07/2027)	12/2028 (-)	325.00 0.00	50.00	1.00
473	Establishment of new GMC Hoshiarpur (Medical Education, Ministry of Health and Family Welfare) (707070) (-) (-)	Punjab	01/2020 (03/2026)	12/2028 (-)	325.00 0.00	2.04	5.00
474	Establishment of new GMC Gangtok (Medical Education, Ministry of Health and Family Welfare) (707039) (-) (-)	Sikkim	10/2018 (12/2018)	12/2026 (07/2026)	250.00 0.00	667.21	100.00
475	ALL India Institute of Medical Sciences-AIIMS Madurai (PMSSY AND Institute of NATIONAL Importance) (701168) (-) (-)	Tamil Nadu	12/2018 (12/2018)	08/2022 (10/2026)	1,264.00 0.00	567.36	57.00
476	AIIMS Bibinagar (PMSSY AND Institute of NATIONAL Importance) (701171) (-) (-)	Telangana	12/2018 (07/2022)	06/2026 (12/2026)	1,028.00 0.00	1,037.55	87.71
477	Establishment of new GMC Rudrapur (Medical Education, Ministry of Health and Family Welfare) (707086) (-) (-)	Uttarakhand	10/2022 (02/2024)	12/2026 (-)	325.00 0.00	353.01	95.00
478	Establishment of new GMC Pithoragarh (Medical Education, Ministry of Health and Family Welfare) (707087) (-) (-)	Uttarakhand	08/2021 (04/2023)	12/2026 (-)	325.00 0.00	470.18	78.00
	Total (24)				18,319.26 0.00	9,637.14	
	Ministry of Labour and Employment						
	Healthcare						
479	Construction of 350 beds + 50 Super Specialty beds ESIC Hospital Sheelanagar, Visakhapatnam, Andhra Pradesh (Employee's State Insurance Company [ESIC]) (612167) (-) (-)	Andhra Pradesh	02/2021 (04/2023)	10/2025 (08/2026)	384.27 0.00	286.38	96.00
480	350 Bedded [Upgradable to 500 beds] ESI Hospital at Sanand (Employee's State Insurance Company [ESIC]) (612186) (-) (-)	Gujarat	06/2022 (04/2023)	03/2026 (05/2027)	558.12 0.00	92.20	32.00
481	Demolition, Construction and upgradation of ESI Hospital, Kalol, Gujarat from 50 beds to 150 beds. (Employee's State Insurance Company [ESIC]) (612211) (-) (-)	Gujarat	08/2022 (10/2023)	10/2025 (11/2026)	205.87 0.00	68.90	61.00
482	Construction of 200 bed ESI Hospital at Bommasandra, Karnataka (Employee's State Insurance Company [ESIC]) (612745) (-) (-)	Karnataka	02/2015 (10/2024)	01/2027 (05/2027)	278.00 0.00	80.52	38.00
483	Construction of 100 bed ESI Hospital and Staff Quarters [32 Nos.] at Harohalli, Karnataka (Employee's State Insurance Company [ESIC]) (612748) (-) (-)	Karnataka	07/2019 (03/2025)	02/2027 (-)	150.92 0.00	31.05	32.05
484	Construction of 200 Bedded ESIC Hospital at Butibori, Nagpur, Maharashtra. (Employee's State Insurance Company [ESIC]) (612213) (-) (-)	Maharashtra	10/2013 (08/2022)	08/2025 (09/2026)	194.93 0.00	116.22	67.00
485	Upgradation & Extension of ESIC Hospital and Construction of PG Hostel / Staff Housing for ESIC Hospital at Andheri, Mumbai (Employee's State Insurance Company [ESIC]) (616691) (-) (-)	Maharashtra	12/2008 (06/2009)	08/2025 (09/2026)	260.13 0.00	216.46	89.00
486	Construction of 100 Bedded ESI Hospital at Duburi, Odisha. (Employee's State Insurance Company [ESIC]) (612513) (-) (-)	Odisha	12/2010 (02/2025)	06/2027 (-)	164.60 0.00	17.52	7.20
487	CONSTRUCTION OF 300 BEDDED HOSPITAL AT HARIDWAR (Employee's State Insurance Company [ESIC]) (612259) (-) (-)	Uttarakhand	02/2021 (12/2021)	10/2024 (07/2026)	102.40 0.00	340.30	91.50
	Total (9)				2,299.24 0.00	1,249.55	
	Department for Promotion of Industry & Internal Trade						
	Logistics Infrastructure						
488	Integrated Multi Modal Logistics Hub at Nangal Chaudhary in Haryana - Other Trunk Infrastructure Development Phase 1 (NICDC) (707410) (-) (-)	Haryana	05/2018 (12/2021)	12/2023 (05/2028)	763.00 0.00	430.00	60.00
	Total (1)				763.00 0.00	430.00	

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
Real Estate							
489	Orvakal Industrial Area (NICDC) (617727) (-) (-)	Andhra Pradesh	08/2024 (10/2025)	10/2028 (-)	2,786.00 0.00	446.32	18.14
490	Kopparthy Industrial Area (NICDC) (617729) (-) (-)	Andhra Pradesh	08/2024 (10/2025)	10/2028 (-)	2,136.00 0.00	39.75	5.56
491	Krishnapatnam Node - Phase 1 - Roads and Services Development (National Industrial Corridor Development Corporation) (701658) (-) (-)	Andhra Pradesh	12/2020 (02/2024)	02/2027 (-)	2,139.44 0.00	1,020.50	48.30
492	Gaya Integrated Manufacturing Cluster IMC in Bihar (National Industrial Corridor Development Corporation) (707420) (-) (-)	Bihar	08/2024 (04/2026)	04/2029 (-)	1,339.02 0.00	0.00	5.00
493	Tumakuru Node - Phase 1 - Roads and Services Development (NICDC) (701657) (-) (-)	Karnataka	12/2020 (02/2023)	09/2026 (09/2027)	1,701.81 0.00	375.68	28.65
494	Development of Palakkad Node under extension of CBIC to Kochi (National Industrial Corridor Development Corporation) (701668) (-) (-)	Kerala	08/2024 (10/2025)	04/2029 (-)	3,805.00 0.00	58.62	5.37
495	IMC Rajpura - Patiala Development Project (National Industrial Corridor Development Corporation) (701662) (-) (-)	Punjab	08/2024 (03/2026)	09/2028 (-)	1,367.72 0.00	0.00	4.95
496	Development of Jodhpur Pali Marwar Industrial Area JPMIA in Rajasthan (National Industrial Corridor Development Corporation) (603210) (-) (-)	Rajasthan	08/2024 (01/2026)	07/2028 (-)	921.66 0.00	0.00	7.50
497	Development of Zaheerabad Node under Hyderabad Nagpur Industrial Corridor (National Industrial Corridor Development Corporation) (601812) (-) (-)	Telangana	08/2024 (02/2026)	02/2029 (-)	2,360.00 0.00	63.19	5.72
498	IMC at Prayagraj (National Industrial Corridor Development Corporation) (707419) (-) (-)	Uttar Pradesh	08/2024 (04/2026)	06/2027 (-)	658.00 0.00	75.63	29.32
499	Development of IMC Khurpia Farms under AKIC Project (National Industrial Corridor Development Corporation) (701661) (-) (-)	Uttarakhand	08/2024 (03/2026)	09/2028 (-)	1,265.37 0.00	14.89	4.10
Total (11)					20,480.02 0.00	2,094.58	
Ministry of Steel							
Metals & Mining							
500	Capacity expansion of Deposit-14 and 14 NMZ at Kirandul (National Mineral Development Corporation Limited [NMDC]) (615202) (-) (-)	Chhattisgarh	08/2021 (07/2022)	12/2028 (03/2028)	1,700.00 0.00	303.01	25.27
501	Shaft Sinking Projects at Kandri Mine. (MOIL Limited) (658240) (-) (-)	Maharashtra	06/2025 (04/2026)	04/2030 (-)	196.90 0.00	2.85	0.90
502	Shaft Sinking Projects at Dongri Buzurg Mine. (MOIL Limited) (928129) (-) (-)	Maharashtra	06/2025 (04/2026)	04/2030 (-)	217.45 0.00	3.94	0.60
Total (3)					2,114.35 0.00	309.80	
Steel							
503	Installation of 140 TPH Walking Beam type Reheating Furnace in Plate Mill at BSP (Steel Authority of India Limited [SAIL]) (505491) (-) (-)	Chhattisgarh	02/2026 (03/2026)	03/2028 (-)	268.36 0.00	0.00	0.00
504	Replacement of Hot Leveller No.1 of Plate Mill at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617243) (-) (-)	Chhattisgarh	07/2024 (08/2024)	07/2026 (-)	198.62 0.00	129.25	83.33
505	Replacement of Converter Vessels, Trunnion Rings, Support System & Installation of Secondary Emission at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617255) (-) (-)	Chhattisgarh	10/2023 (12/2023)	06/2026 (09/2026)	471.83 0.00	272.56	78.97
506	Rebuilding of Coke Oven Battery No.7 & 8 at Bhilai Steel Plant (Steel Authority of India Limited [SAIL]) (617256) (-) (-)	Chhattisgarh	11/2023 (01/2024)	10/2025 (09/2026)	884.10 0.00	702.09	95.99
507	NMDC Slurry Pipeline Project Phase-1 (National Mineral Development Corporation Limited [NMDC]) (706811) (-) (-)	Chhattisgarh	11/2015 (09/2020)	06/2023 (08/2026)	2,907.00 0.00	3,684.95	96.80
508	SCREENING PLANT-III AT KIRANDUL (National Mineral Development Corporation Limited [NMDC]) (709826) (-) (-)	Chhattisgarh	01/2009 (10/2021)	01/2026 (07/2027)	2,718.84 0.00	1,763.55	83.82

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
509	Super accelerated cooling system (Uniform Cooling) for high strength plates in Plate Mill at BSP (Steel Authority of India Limited (SAIL)) (944288) (-) (-)	Chhattisgarh	06/2025 (06/2025)	12/2026 (-)	192.21 0.00	79.05	65.15
510	New Sinter Plant at BSL, SAIL (Steel Authority of India Limited (SAIL)) (400174) (-) (-)	Jharkhand	03/2015 (10/2015)	10/2027 (06/2027)	1,034.01 0.00	1,075.46	66.50
511	Replacement of existing Grinders in CRM-I & II at Bokaro Steel Plant (Steel Authority of India Limited (SAIL)) (617249) (-) (-)	Jharkhand	01/2025 (02/2025)	01/2027 (-)	211.94 0.00	143.18	69.27
512	Secondary Emission Control in Converters of SMS-II at Bokaro Steel Plant (Steel Authority of India Limited (SAIL)) (617250) (-) (-)	Jharkhand	01/2025 (02/2025)	10/2026 (04/2027)	207.13 0.00	110.21	57.59
513	Replacement of remaining 04 sets of Battery Cyclones with 04 Nos. of ESPs in Sinter Plant-1 at Bokaro Steel Plant (Steel Authority of India Limited (SAIL)) (617254) (-) (-)	Jharkhand	03/2024 (04/2024)	06/2026 (04/2027)	260.37 0.00	131.44	56.28
514	Rebuilding of Coke Oven Battery No.6 at Bokaro Steel Plant (Steel Authority of India Limited (SAIL)) (617257) (-) (-)	Jharkhand	11/2023 (12/2023)	11/2026 (11/2027)	627.31 0.00	365.64	70.50
515	Construction of Screening Plant-II for Donimalai and Kumaraswamy Iron Ore Mining Complex of NMDC Limited at Ballari Dt, Karnataka. (National Mineral Development Corporation Limited (NMDC)) (400121) (-) (-)	Karnataka	11/2014 (06/2024)	08/2026 (-)	1,043.63 0.00	658.17	72.70
516	Stamp Charge Battery No.7 Coke Dry Cooling Plant at RSP (Steel Authority of India Limited (SAIL)) (478482) (-) (-)	Odisha	02/2026 (02/2026)	08/2028 (-)	1,064.55 0.00	75.81	0.00
517	Implementation of Treatment System-2 Under ZLD at RSP (Steel Authority of India Limited (SAIL)) (589703) (-) (-)	Odisha	02/2025 (03/2025)	09/2026 (-)	216.02 0.00	147.99	93.66
518	New Product Testing Laboratory for NPM, SPP & NHSM at RSP (Steel Authority of India Limited (SAIL)) (635651) (-) (-)	Odisha	06/2025 (07/2025)	08/2027 (-)	155.26 0.00	57.69	73.86
519	Stamp Charge Battery No.7 Battery Proper at RSP (Steel Authority of India Limited (SAIL)) (738679) (-) (-)	Odisha	09/2024 (10/2024)	03/2028 (-)	2,584.41 0.00	1,251.00	59.41
520	Stamp Charge Battery No.7 By-product Plant at RSP (Steel Authority of India Limited (SAIL)) (834015) (-) (-)	Odisha	09/2024 (10/2024)	03/2028 (-)	1,140.07 0.00	219.86	23.27
521	Stamp Charge Battery No.12 By-product Plant at IISCO Steel Plant (Steel Authority of India Limited (SAIL)) (364934) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	999.46 0.00	100.91	18.87
522	Stamp Charge Battery No.12 Coke Dry Cooling Plant at IISCO Steel Plant (Steel Authority of India Limited (SAIL)) (425828) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	706.51 0.00	143.16	13.70
523	Rebuilding of COB 4 at Durgapur Steel Plant (Steel Authority of India Limited (SAIL)) (612781) (-) (-)	West Bengal	09/2023 (09/2023)	09/2027 (09/2027)	916.78 0.00	248.36	38.83
524	Installation of New Bar Mill at Durgapur Steel Plant (Steel Authority of India Limited (SAIL)) (617242) (-) (-)	West Bengal	07/2024 (08/2024)	06/2027 (-)	2,115.44 0.00	994.10	69.61
525	Up-gradation of Blast Furnace No. 3 at Durgapur Steel Plant (Steel Authority of India Limited (SAIL)) (617246) (-) (-)	West Bengal	09/2024 (10/2024)	10/2027 (10/2027)	758.09 0.00	330.78	64.17
526	Third Ladle Furnace in Secondary Refinery Unit at IISCO Steel Plant (Steel Authority of India Limited (SAIL)) (617248) (-) (-)	West Bengal	11/2024 (12/2024)	07/2026 (11/2026)	227.96 0.00	119.14	73.31
527	Revamping of Air Pollution Control Systems of SP-1 at Durgapur Steel Plant (Steel Authority of India Limited (SAIL)) (617251) (-) (-)	West Bengal	07/2024 (12/2024)	05/2026 (12/2026)	196.40 0.00	73.24	57.33
528	Stamp Charge Battery No.12 Battery Proper at IISCO Steel Plant (Steel Authority of India Limited (SAIL)) (617338) (-) (-)	West Bengal	01/2025 (02/2025)	07/2028 (-)	2,518.39 0.00	485.99	30.51
	Total (26)				24,624.69 0.00	13,363.58	
	Ministry of Railways						
	Railways						
529	Nadikude-Srikalahasti 308.7 km (CAO/C/SCoR SCoR mor) (400298) (-) (-)	Andhra Pradesh	03/2012 (10/2019)	05/2027 (03/2028)	2,312.00 0.00	2,535.68	2.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
530	Doubling between Gooty-Pendakallu 29.225 km PB73/2023-24/NR (CAO/C/SCoR SCoR mor) (611752) (-) (-)	Andhra Pradesh	03/2023 (06/2024)	03/2027 (03/2027)	351.83 0.00	157.67	45.00
531	South Central Railway - Rail road over double line between Guntakal West-Mallapa Gate 9.64 km PB34/CR/2023-24 (CAO/C/SCoR SCoR mor) (611754) (-) (-)	Andhra Pradesh	07/2023 (11/2024)	07/2026 (-)	293.30 0.00	94.62	33.00
532	Flyover between Pendurthi-Simhachalam North to avoid surface crossing at Simhachalam 7.135 km PB73/2023-24/NR (CAO/C/SCoR SCoR mor) (612827) (-) (-)	Andhra Pradesh	04/2023 (04/2024)	04/2027 (-)	183.65 0.00	28.73	22.00
533	3rd & 4 th line Vadlapudi-Gate Jn. incl. tie line between Gangavaram Port-Visakhapatnam Steel Plant12.04 km PB73/2023-24/NR (CAO/C/SCoR SCoR mor) (616697) (-) (-)	Andhra Pradesh	04/2023 (02/2024)	06/2026 (-)	154.28 0.00	89.66	88.00
534	South Central Railway- 3rd line between Gudur-Renigunta stations 83.17 km PB34/CR/2023-24 (CAO/C/SCoR SCoR mor) (617216) (-) (-)	Andhra Pradesh	10/2024 (03/2026)	03/2027 (-)	877.34 0.00	53.46	0.00
535	Lumding-Furkating section 140 km Umbrella work PB57/2019-20/NR (CAO/C-1/NFR NFR mor) (616701) (-) (-)	Assam	02/2024 (09/2020)	02/2028 (-)	2,123.70 0.00	215.47	15.00
536	New Bongaigaon - Goalpara - Guwahati Kamakhya 176 km (CAO/C-III/NFR NFR mor) (705572) (-) (-)	Assam	09/2016 (08/2019)	03/2026 (03/2026)	4,060.00 0.00	3,860.64	91.00
537	Sakri-Hasanpur 79 km (CAO/Con/North/MHX ECR mor) (400254) (-) (-)	Bihar	12/2023 (01/2020)	12/2024 (03/2027)	735.20 0.00	615.76	80.00
538	East Central Railway - Construction of Bulb line at Nabinagar Ankorah 17.49Km PB45/ECOR/2024-25. (CAO/Con/South/MHX ECR mor) (617231) (-) (-)	Bihar	06/2024 (09/2025)	06/2028 (-)	611.74 0.00	0.00	0.00
539	Narkatiaganj-Raxaul-Sitamarhi-Darbhangha & Sitamarhi-Muzaffarpur Sections doubling 256 km Umbrella work PB57/2019-20/NR (CAO/Con/North/MHX ECR mor) (617239) (-) (-)	Bihar	11/2024 (11/2025)	11/2029 (03/2030)	4,079.95 0.00	29.38	0.00
540	Hajipur-Sagauli via Vaishali 148.3 km (CAO/Con/North/MHX ECR mor) (705366) (-) (-)	Bihar	10/2007 (12/2019)	03/2020 (06/2027)	2,067.00 0.00	2,889.67	74.00
541	Araria-Supaul 92 km (CAO/Con/North/MHX ECR mor) (705368) (-) (-)	Bihar	08/2009 (12/2019)	03/2024 (01/2027)	1,605.00 0.00	2,179.84	40.00
542	Fatuah-Islampur incl. material modification for extension of new line from Neora to Daniawan Daniawan to Biharsharif Biharsharif to Barbigha Barbigha to Sheikhpura (CAO/Con/South/MHX ECR mor) (705373) (-) (-)	Bihar	08/2002 (04/2020)	03/2023 (08/2025)	1,473.00 0.00	3,044.61	95.00
543	Samastipur-Darbhangha 38 km (CAO/Con/North/MHX ECR mor) (705526) (-) (-)	Bihar	11/2015 (08/2019)	03/2025 (10/2025)	519.00 0.00	751.29	92.00
544	Sagauli - Valmikinagar 109.7 km (CAO/Con/North/MHX ECR mor) (705527) (-) (-)	Bihar	03/2018 (12/2019)	12/2025 (12/2025)	1,216.00 0.00	1,464.50	91.00
545	Muzaffarpur - Sagauli 100.6 km (CAO/Con/North/MHX ECR mor) (705528) (-) (-)	Bihar	03/2018 (12/2019)	06/2024 (06/2026)	1,586.00 0.00	1,564.08	99.00
546	Barauni-Bachwara 16 km - 3rd & 4th line incl Barauni yard remodelling 32 km Umbrella work PB57/2019-20/NR (CAO/Con/North/MHX ECR mor) (706860) (-) (-)	Bihar	10/2022 (06/2023)	08/2025 (10/2026)	645.00 0.00	237.70	38.00
547	Jhajha - Batia 20 km Umbrella work PB23/2018-19/NR (CAO/Con/South/MHX ECR mor) (900874) (-) (-)	Bihar	02/2019 (01/2020)	03/2028 (01/2030)	588.18 0.00	29.78	0.00
548	Kirandul-Jagdalpur 150 km (CAO/C/ECOR ECoR mor) (400291) (-) (-)	Chhattisgarh	02/2013 (11/2019)	03/2020 (04/2027)	1,589.00 0.00	1,369.01	89.00
549	Nipania-Bhatapra 14.4 km 4th line PB72/NR/2022-23 (CAOC/SECR SECR mor) (612815) (-) (-)	Chhattisgarh	12/2022 (05/2024)	03/2027 (-)	170.49 0.00	13.63	3.00
550	Boridand-Ambikapur 118.81 km Umbrella work PB57/2019-20/NR (CAOC/SECR SECR mor) (706854) (-) (-)	Chhattisgarh	06/2022 (03/2023)	06/2030 (06/2030)	1,376.00 0.00	512.14	38.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
551	4th line - Rajnandgaon-Dongarhgarh 31.2 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709818) (-) (-)	Chhattisgarh	09/2022 (03/2024)	01/2027 (01/2027)	328.34 0.00	101.52	5.00
552	3rd & 4th line - Saragbundia & Madwarani 12.2 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709819) (-) (-)	Chhattisgarh	09/2022 (05/2025)	12/2026 (12/2026)	167.64 0.00	28.49	10.00
553	Anand Vihar-Tilak Bridge - 3rd & 4th line 9.77 km (CAOC/NR NR mor) (705583) (-) (-)	Delhi	06/2012 (01/2020)	03/2023 (12/2027)	667.00 0.00	400.84	23.00
554	Chandorgaon-Cansaulim rail flyover 16 km Umbrella work PB57/2019-20/NR (CAOC/SWR SWR mor) (706865) (-) (-)	Goa	NA (01/2022)	03/2031 (-)	1,892.00 0.00	0.00	0.00
555	Kosamba- Umarpada 69.70 Km PB32/WR/2023-24 (CAOCWR WR mor) (611918) (-) (-)	Gujarat	07/2023 (01/2024)	03/2027 (-)	468.00 0.00	161.50	31.00
556	New BG line between Naliya - Jakhau Port 24.88 Km (CAOCWR WR mor) (611943) (-) (-)	Gujarat	02/2023 (08/2024)	01/2028 (02/2028)	410.26 0.00	11.90	5.00
557	Petlad-Bhadran 22.5 km (CAOCWR WR mor) (611945) (-) (-)	Gujarat	05/2022 (04/2023)	05/2030 (05/2030)	307.11 0.00	115.19	32.00
558	Samlaya-Timba Road 53.53 km (CAOCWR WR mor) (611970) (-) (-)	Gujarat	02/2023 (05/2023)	03/2030 (03/2030)	670.17 0.00	202.51	25.00
559	Samni-Jambusar 24.08 km (CAOCWR WR mor) (611971) (-) (-)	Gujarat	05/2022 (08/2022)	03/2030 (03/2030)	350.00 0.00	189.28	40.00
560	Western Railway- Samakhiali-Gandhidham Quadrupiling 53 km PB34/CR/2023-24 (CAOCWR WR mor) (611974) (-) (-)	Gujarat	08/2023 (04/2024)	12/2026 (12/2027)	1,430.00 0.00	796.21	50.00
561	Barejadi Nandej Geratpur - Sanand - 4th line 38.20 km (CAOCWR WR mor) (612072) (-) (-)	Gujarat	02/2023 (02/2024)	03/2027 (07/2028)	961.67 0.00	569.92	25.00
562	Miyagam-Karjan-Dabhoi-Samlaya 96.46 km- Gauge conversion with electrification (CAOCWR WR mor) (705458) (-) (-)	Gujarat	01/2017 (08/2019)	12/2026 (12/2026)	483.88 0.00	886.85	34.00
563	Rajkot-Kanalus 111.20 km (CAOCWR WR mor) (706763) (-) (-)	Gujarat	10/2021 (12/2019)	10/2026 (06/2026)	1,080.58 0.00	1,148.79	90.00
564	Nadiad-Petlad 37.26 km (CAOCWR WR mor) (709812) (-) (-)	Gujarat	05/2022 (10/2023)	06/2030 (06/2030)	461.91 0.00	150.35	30.00
565	New BG line intersection 5 nos between Geratpur-Sanand & Botad-Ahmedabad 16.51 km PB29/NR/2022-23 (CAOCWR WR mor) (709813) (-) (-)	Gujarat	10/2022 (10/2023)	10/2027 (10/2027)	437.21 0.00	602.87	22.00
566	Doubling between Bhiwani - Dobh Bahali PB73/2023-24/NR (CAOC/NWR NWR mor) (611884) (-) (-)	Haryana	02/2023 (11/2023)	06/2027 (02/2028)	471.00 0.00	350.86	78.00
567	Pradhankhunta Jn-Patherdih Bazar-Bhojudih 17.1 km Umbrella work PB57/2019-20/NR (CAO/Con/South/MHX ECR mor) (617372) (-) (-)	Jharkhand	11/2022 (12/2023)	11/2027 (03/2026)	349.22 0.00	166.86	60.00
568	Koderma-Barkakana Arigada 133 Km (CAO/Con/South/MHX ECR mor) (617832) (-) (-)	Jharkhand	06/2025 (06/2026)	12/2029 (-)	2,887.11 0.00	0.85	0.00
569	Gomoh - Flyover for down trains 20 km (CAO/Con/South/MHX ECR mor) (705765) (-) (-)	Jharkhand	01/2018 (06/2020)	03/2026 (03/2026)	686.00 0.00	543.45	65.00
570	Lodhma-Piska - Link line bypassing Hatia / Ranchi with Y connection 17.2 km (CAO/C/SER SER mor) (705785) (-) (-)	Jharkhand	08/2021 (09/2021)	06/2026 (05/2027)	473.00 0.00	345.49	14.00
571	Gadag - Wadi 257.26 km (CAOC/SWR SWR mor) (705490) (-) (-)	Karnataka	04/2013 (09/2019)	03/2027 (12/2027)	2,842.00 0.00	2,324.01	35.00
572	Kadur-Chickmagalur-Sakleshpur 93 km (CAOC/SWR SWR mor) (705492) (-) (-)	Karnataka	01/2014 (02/2023)	06/2025 (12/2025)	825.00 0.00	801.77	83.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
573	Hubli-Ankola 167 km (CAOC/SWR SWR mor) (705493) (-) (-)	Karnataka	01/1999 (05/2022)	03/2005 (03/2030)	5,174.00 0.00	186.31	10.00
574	Bagalkot-Kudachi 142 km (CAOC/SWR SWR mor) (705495) (-) (-)	Karnataka	02/2010 (01/2021)	03/2027 (01/2027)	1,378.00 0.00	808.19	35.00
575	Bangalore-Whitefield-Bangalore City-Krishnarajapuram 23.08 km - Quadrupling (CPM/GS/SBC SWR mor) (705663) (-) (-)	Karnataka	03/2018 (02/2020)	02/2026 (02/2026)	493.00 0.00	459.94	70.00
576	Shimoga-Shikaripura-Ranebennur 103 km umbrella work PB23/2018-19/NR (CAOC/SWR SWR mor) (705761) (-) (-)	Karnataka	09/2019 (02/2023)	12/2027 (06/2028)	1,454.00 0.00	107.72	14.00
577	Kumbalam-Turavur - Patch doubling 15.59 km (CAO/CN/ERS SR mor) (705638) (-) (-)	Kerala	04/2023 (02/2024)	03/2027 (03/2027)	813.00 0.00	404.17	30.00
578	Ernakulam-Kumbalam - Patch doubling 7.71 km (CAO/CN/ERS SR mor) (705639) (-) (-)	Kerala	04/2023 (02/2024)	03/2028 (02/2027)	601.00 0.00	313.99	25.00
579	Gwalior-Sheorpurkalan with extension to Kota 284 km (CAO/C/NCR NCR mor) (705419) (-) (-)	Madhya Pradesh	02/2010 (09/2020)	03/2025 (02/2026)	2,913.00 0.00	3,112.88	91.00
580	Satna - Rewa 50 km (CE/C-4/WCR WCR mor) (705659) (-) (-)	Madhya Pradesh	11/2015 (09/2019)	03/2026 (03/2026)	500.00 0.00	620.14	88.00
581	Katni - Grade separator / bypass 21.50 km (GM IRCON KATNI WCR mor) (705661) (-) (-)	Madhya Pradesh	08/2016 (11/2019)	09/2024 (09/2026)	1,248.00 0.00	1,839.46	84.00
582	Nimach-Ratlam 133 km (CAOCWR WR mor) (705933) (-) (-)	Madhya Pradesh	10/2021 (01/2022)	10/2027 (10/2027)	1,095.88 0.00	1,496.21	100.00
583	Aurangabad-Ankai 98.25 km (CAOCON/SCR SCR mor) (611751) (-) (-)	Maharashtra	05/2023 (04/2025)	12/2025 (-)	960.64 0.00	401.33	0.00
584	Pachora-Jamner with extension upto Malkapur-Narrow gauge to broad gauge 84 km (CAOC/CR CR mor) (612845) (-) (-)	Maharashtra	08/2022 (01/2020)	08/2027 (-)	955.39 0.00	308.07	10.00
585	Doubling between Parbhani-Parli Vajinath stations 64.71 km PB34/CR/2023-24 (CAOCON/SCR SCR mor) (617215) (-) (-)	Maharashtra	12/2023 (11/2024)	03/2028 (-)	769.93 0.00	178.50	1.00
586	Central Railway - Double chord line between Nilaje and Kopar 4.495 km PB34/CR/2023-24 (CAOC/CR CR mor) (617364) (-) (-)	Maharashtra	07/2023 (01/2025)	07/2028 (-)	338.33 0.00	58.47	15.00
587	Ahmednagar - Beed - Parli - Vajinath New Broad Gauge Line Railway Project [261.3 km] (CAOC/CR CR mor) (705356) (-) (-)	Maharashtra	02/1997 (08/2022)	12/2026 (03/2026)	2,538.67 0.00	5,084.82	93.00
588	Baramati - Lonand 54 km (CAOC/CR CR mor) (705357) (-) (-)	Maharashtra	02/1999 (04/2023)	03/2027 (03/2027)	138.48 0.00	1,160.74	60.00
589	Wadsa-Gadchiroli 49.5 km (CAOC/SECR SECR mor) (705479) (-) (-)	Maharashtra	05/2017 (08/2023)	03/2027 (03/2027)	1,886.00 0.00	1,015.46	69.00
590	Kalyan-Kasara - 3rd line 67.62 km (CAOC/CR CR mor) (705498) (-) (-)	Maharashtra	09/2015 (04/2023)	12/2026 (12/2026)	792.89 0.00	1,165.98	73.00
591	Wardha Sevagram-Nagpur - 3rd line 76.3 km (CAOC/CR CR mor) (705500) (-) (-)	Maharashtra	09/2015 (07/2020)	12/2025 (10/2026)	540.02 0.00	841.24	93.00
592	Wardha-Balharshah - 3rd line 132 km (CAOC/CR CR mor) (705502) (-) (-)	Maharashtra	03/2016 (09/2019)	12/2025 (02/2026)	1,384.72 0.00	1,911.26	86.00
593	Daund - Manmad 247.50 km (CAOC/CR CR mor) (705504) (-) (-)	Maharashtra	10/2017 (09/2022)	12/2025 (03/2026)	2,081.27 0.00	3,270.66	95.00
594	Wardha-Nagpur - 4th line 78.70 km (CAOC/CR CR mor) (705505) (-) (-)	Maharashtra	04/2017 (08/2021)	12/2025 (10/2026)	637.95 0.00	1,094.89	93.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
595	Solapur-Osmanabad - New line via Tuljapur 84.44 km umbrella work PB23/2018-19/NR (CAOC/CR CR mor) (705735) (-) (-)	Maharashtra	01/2019 (01/2024)	03/2027 (03/2028)	904.92 0.00	1,232.63	38.00
596	Jiribam-Imphal 110 km (CAO/C-III/NFR NFR mor) (705391) (-) (-)	Manipur	10/2003 (08/2019)	12/2026 (06/2029)	14,323.00 0.00	16,931.50	78.00
597	Marikuppam-Kuppam 23.7 km (CAOC/SWR SWR mor) (705491) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	10/2011 (09/2019)	06/2026 (06/2026)	297.00 0.00	145.88	20.00
598	Kottavalasa-Koraput 189.278 km (CAO/C/ECOR ECoR mor) (705512) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	12/2015 (11/2019)	03/2022 (03/2028)	2,500.00 0.00	2,358.96	74.00
599	Tirupati-Pakala-Katpadi Doubling 104.39 Km Item83/NR/2024-25 (CAO/C/SCoR SCoR mor) (617210) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	04/2025 (12/2025)	04/2029 (-)	1,215.56 0.00	0.00	0.00
600	Renigunta 9.60 km, Wadi 7.60 km & Gooty 3.8 km - Bypass (CAO/C/SCoR SCoR mor) (705610) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	04/2016 (02/2021)	12/2025 (03/2026)	302.00 0.00	421.36	50.00
601	Doubling between Motumari Vishnupuram 88.81 km and Rail over Rail RoR at Motumari 10.877 Km (CAO/C/SCoR SCoR mor) (616857) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	02/2024 (03/2025)	03/2029 (-)	1,595.55 0.00	327.62	22.00
602	South Central Railway- Rail connectivity to Amaravati, Capital of Andhra Pradesh Errupalem- Amaravati- Namburu New line 57 km PB7/WR/2023-24 (CAO/C/SCoR SCoR mor) (617214) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	11/2024 (01/2026)	03/2027 (-)	2,047.40 0.00	155.00	0.00
603	Vijayawada19.50 km & Kazipet10.65 km -Bypass line (CAO/C/SCoR SCoR mor) (705632) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	04/2016 (07/2020)	01/2025 (12/2025)	647.00 0.00	711.08	90.00
604	Murkongselek-Pasighat 26.15 km (CAO/C-II/NFR NFR mor) (705401) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	02/2011 (10/2019)	03/2025 (12/2026)	435.00 0.00	1,057.21	67.00
605	Dimapur-Kohima 88 km (CAO/C-1/NFR NFR mor) (705392) (-) (-)	Multi-States (Assam, Nagaland)	11/2006 (09/2019)	03/2025 (12/2029)	6,663.00 0.00	6,891.03	48.00
606	Koderma-Tilaiya 68 km (CAO/Con/South/MHX ECR mor) (705375) (-) (-)	Multi-States (Bihar, Jharkhand)	11/2004 (08/2019)	02/2025 (02/2026)	1,626.00 0.00	2,272.44	90.00
607	Pirpainti - Jasidih 97 km (CAOC/ER ER mor) (705385) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2014 (08/2019)	03/2028 (03/2028)	2,555.00 0.00	1,779.91	40.00
608	Multi tracking of Son Nagar-Andal 374.53 rkm & 814.38 tkm PB34/ECOR/2023-24 (CAO/Con/South/MHX ECR mor) (616699) (-) (-)	Multi-States (Bihar, Jharkhand, Uttar Pradesh, West Bengal)	08/2023 (03/2024)	03/2028 (-)	12,333.57 0.00	1,350.85	3.00
609	Gorakhpur-Valmikinagar Doubling project (CONSTRUCTION / NE-RAILWAY) (617224) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	08/2023 (03/2024)	12/2027 (-)	1,120.00 0.00	442.70	46.00
610	Construction of surface traingle between Bhadaura and new crossing station Karma Dildarnagar-Taraghat line 11.1 km PB72/NR/2022-23 (CAO/Con/South/MHX ECR mor) (617333) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2022 (05/2024)	02/2027 (-)	199.96 0.00	64.59	0.00
611	Chhapra-Ballia - Patch doubling 65 km (CONSTRUCTION / NE-RAILWAY) (705562) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2013 (01/2020)	02/2025 (05/2026)	963.00 0.00	1,008.54	95.00
612	Katihar-Kumedpur & Katihar-Mukuria 64.5 km Umbrella work PB57/2019-20/NR (CAO/C-II/NFR NFR mor) (617245) (-) (-)	Multi-States (Bihar, West Bengal)	08/2022 (07/2020)	08/2027 (02/2027)	942.64 0.00	952.95	65.00
613	Rajnandgaon-Nagpur - 3rd line 228 km (CAOC/SECR SECR mor) (705617) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2016 (12/2019)	12/2024 (06/2026)	3,545.00 0.00	3,147.30	95.00
614	4th line - Bhatapara-Hathband 8.8 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709815) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2022 (09/2024)	01/2027 (12/2027)	177.03 0.00	21.08	3.00
615	4th line - Bhilai-Bhilai nagar 8.8 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709816) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2022 (09/2024)	02/2027 (02/2027)	177.34 0.00	39.39	3.00
616	4th line - Dadhapara-Belha 9.2 km PB72/NR/2022-23 (CAOC/SECR SECR mor) (709817) (-) (-)	Multi-States (Chhattisgarh, Maharashtra)	09/2022 (02/2024)	11/2026 (11/2026)	169.06 0.00	65.72	10.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
617	Jagdalspur-Koraput 110.22 km (CAO/C/ECOR ECoR mor) (705511) (-) (-)	Multi-States (Chhattisgarh, Odisha)	12/2015 (11/2019)	03/2024 (12/2026)	1,547.00 0.00	1,391.95	90.00
618	Jharsuguda - Bilaspur - 4th line 206 km (CAOC/SECR SECR mor) (705616) (-) (-)	Multi-States (Chhattisgarh, Odisha)	09/2016 (09/2020)	10/2024 (03/2026)	2,140.00 0.00	2,547.36	88.00
619	Dahod-Indore via Sardarpur, Jhabua & Dhar 200.97 km incl. material modification for change in alignment via Amjhera 4.82 km (CAOCWR WR mor) (705453) (-) (-)	Multi-States (Gujarat, Madhya Pradesh)	06/2012 (09/2019)	02/2027 (02/2027)	456.07 0.00	4,565.59	57.00
620	Chhota Udepur-Dhar 157 km (CAOCWR WR mor) (705454) (-) (-)	Multi-States (Gujarat, Madhya Pradesh)	02/2007 (08/2019)	12/2025 (12/2025)	1,794.00 0.00	1,861.88	58.00
621	Taranga Hill-Abu Road via Ambaji 116.65 km (CAOC/NWR NWR mor) (400022) (-) (-)	Multi-States (Gujarat, Rajasthan)	07/2022 (11/2022)	07/2030 (07/2030)	2,798.00 0.00	2,061.73	50.00
622	Chandigarh-Baddi 33.23 km (CAOC/NR NR mor) (705424) (-) (-)	Multi-States (Haryana, Himachal Pradesh)	02/2018 (11/2019)	12/2026 (12/2026)	1,540.00 0.00	1,103.12	48.00
623	Nangal Dam-Talwara 83.74 km - New broad gauge line & taking over siding Mukerian-Talwara 29.16 km (CAOC/NR NR mor) (705410) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/1983 (11/2019)	12/2025 (12/2027)	2,018.00 0.00	2,998.72	84.00
624	Bondamunda - Ranchi 158.50 km (CAO/C/SER SER mor) (705628) (-) (-)	Multi-States (Jharkhand, Odisha)	03/2016 (05/2020)	06/2025 (06/2026)	3,029.00 0.00	2,706.77	95.00
625	Buramara - Chakulia 59.96 km PB9/SECR/2023-24 (CAO/C/SER SER mor) (616588) (-) (-)	Multi-States (Jharkhand, Odisha, West Bengal)	08/2024 (07/2025)	12/2029 (-)	1,459.13 0.00	12.55	2.00
626	3rd line between Chandil - Anara- Damodar section 121.26 km (CAO/C/SER SER mor) (616227) (-) (-)	Multi-States (Jharkhand, West Bengal)	09/2024 (10/2025)	09/2029 (-)	1,932.01 0.00	10.27	0.00
627	Kharagpur-Adityapur - 3rd line 132 km (CMD / RVNL RVNL mor) (705668) (-) (-)	Multi-States (Jharkhand, West Bengal)	09/2016 (08/2020)	03/2025 (06/2026)	3,250.00 0.00	3,297.43	98.00
628	Baiyyappanahalli-Hosur 48 km (M.D/KRIDE SWR mor) (703586) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	04/2019 (11/2022)	12/2024 (01/2026)	498.70 0.00	700.64	85.00
629	Trivandrum - Kanyakumari 86.56 km (CAO/CN/ERS SR mor) (705635) (-) (-)	Multi-States (Kerala, Tamil Nadu)	08/2017 (08/2019)	03/2024 (06/2028)	1,432.00 0.00	3,294.98	60.00
630	Ratlam-Mhow-Khandwa-Akola 472.64 km including material modification for Fatehabad-Chandrawati Ganj-Ujjain 22.96 km and Rau-DADN doubling 9.40 km (CAOCWR WR mor) (705457) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	01/2008 (07/2019)	03/2027 (09/2028)	1,656.25 0.00	5,084.39	75.00
631	Itarsi-Nagpur bal. 280 km (CAOC/CR CR mor) (705507) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	09/2016 (02/2020)	03/2027 (12/2027)	2,449.91 0.00	2,318.11	55.00
632	Ramganj Mandi-Bhopal 262 km (CPM/Kota WCR mor) (705481) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	02/2000 (08/2019)	12/2025 (12/2027)	3,032.00 0.00	4,554.84	88.00
633	Nimach-Badi Sadri NL Project 48 km (CAOC/NWR NWR mor) (705764) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan)	10/2018 (08/2020)	03/2026 (06/2026)	495.00 0.00	577.16	60.00
634	Mathura-Jhansi - 3rd line 273.80 km (CMD / RVNL RVNL mor) (705667) (-) (-)	Multi-States (Madhya Pradesh, Rajasthan, Uttar Pradesh)	09/2016 (09/2021)	12/2023 (12/2026)	5,961.00 0.00	5,725.22	94.00
635	Lalitpur-Satna, Rewa-Singrauli & Mahoba-Khajuraho 541 km (CE/C-4/WCR WCR mor) (705480) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	01/2007 (07/2019)	03/2027 (12/2027)	8,914.00 0.00	6,694.70	73.00
636	Jhansi-Bina - 3rd line 152.57 km (CAO/C/NCR NCR mor) (705598) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	09/2016 (10/2019)	03/2022 (03/2026)	2,002.00 0.00	1,949.80	98.00
637	Bangriposi - Gorumahisani 85.60 km PB9/SECR/2023-24 (CAO/C/SER SER mor) (616586) (-) (-)	Multi-States (Odisha, West Bengal)	08/2024 (07/2025)	12/2029 (-)	2,269.49 0.00	7.84	2.00
638	Narayangarh - Bhadrak - 3rd line 155 km (CAO/C/SER SER mor) (705629) (-) (-)	Multi-States (Odisha, West Bengal)	03/2019 (11/2019)	12/2025 (01/2027)	2,400.00 0.00	2,927.26	87.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
639	Tiruchchirappalli-Nagore-Karaikal with extension of Nagapattinam-Velankani-Tiruthiraipundi incl. new material modification of Karaikal - Peralam 23 km new line (CAOC/SR SR mor) (400223) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	11/1995 (12/2019)	03/2025 (03/2028)	713.00 0.00	1,271.33	80.00
640	Sainthia, Sitarampur, Mughalsarai, Allahabad & Etawah - Bypass 35 km (CAOC/ER ER mor) (602797) (-) (-)	Multi-States (Uttar Pradesh, West Bengal)	08/2017 (04/2024)	03/2027 (03/2027)	461.64 0.00	208.47	15.00
641	Brundamal - Jharsuguda - Fly-over connection for joining down line 6.6 km (CAO/C/ECOR ECoR mor) (400232) (-) (-)	Odisha	01/2014 (02/2024)	12/2026 (12/2026)	297.00 0.00	49.63	55.00
642	3rd & 4th line between Sarla - Sason 8 km PB73/2023-24/NR (CAO/C/ECOR ECoR mor) (612834) (-) (-)	Odisha	04/2023 (12/2023)	12/2025 (-)	252.00 0.00	188.33	88.00
643	Rourkela-Bondamunda A-Cabin 5th line 10 km Umbrella work PB57/2019-20/NR (CAO/C/SER SER mor) (615915) (-) (-)	Odisha	09/2022 (12/2023)	09/2024 (11/2026)	244.99 0.00	162.31	50.00
644	Flyover between Siju & Paradeep coaching yard 7 km PB73/2023-24/NR (CAO/C/ECOR ECoR mor) (616694) (-) (-)	Odisha	04/2023 (05/2025)	07/2028 (-)	200.77 0.00	55.95	1.00
645	Construction of Paradeep- Badabandha 3rd & 4th line 18.51 km PB34/ECOR/2023-24 (CAO/C/ECOR ECoR mor) (616695) (-) (-)	Odisha	08/2023 (03/2025)	11/2028 (-)	300.15 0.00	21.63	10.00
646	Gunupur - Therubali new line 73.62 km (CAO/C/ECOR ECoR mor) (616839) (-) (-)	Odisha	08/2024 (03/2025)	12/2029 (-)	1,165.89 0.00	2.55	0.00
647	Khurda Road-Bolangir 301 km (CAO/C/ECOR ECoR mor) (705358) (-) (-)	Odisha	03/1994 (09/2019)	12/2026 (12/2026)	3,792.00 0.00	4,864.86	93.00
648	Talcher-Bimlagarh 154 km (CAO/C/ECOR ECoR mor) (705359) (-) (-)	Odisha	03/2004 (09/2019)	03/2025 (03/2029)	1,928.00 0.00	2,194.73	56.00
649	Bhadrak-Nergundi - 3rd line 80 km (CAO/C/ECOR ECoR mor) (705510) (-) (-)	Odisha	03/2012 (11/2019)	11/2024 (01/2026)	1,284.00 0.00	1,404.45	85.00
650	Koraput-Singapur Road 164.56 km (CAO/C/ECOR ECoR mor) (705513) (-) (-)	Odisha	12/2015 (11/2019)	12/2027 (03/2028)	2,362.00 0.00	2,124.38	56.00
651	Budhapank-Salegaon via Rajatgarh - 3rd & 4th line 85 85 km (CAO/C/ECOR ECoR mor) (705515) (-) (-)	Odisha	12/2015 (10/2019)	03/2026 (03/2026)	1,173.00 0.00	2,226.10	86.00
652	Jeypore - Navarangpur 38 km (CAO/C/ECOR ECoR mor) (705741) (-) (-)	Odisha	07/2017 (10/2020)	07/2028 (12/2029)	748.00 0.00	16.28	1.00
653	Jeypore - Malkangiri 130 km (CAO/C/ECOR ECoR mor) (705742) (-) (-)	Odisha	02/2018 (10/2020)	07/2033 (07/2033)	2,344.00 0.00	738.60	6.00
654	Ludhiana-Kila Raipur 19 km with freight line at Gill station (CAOC/NR NR mor) (705783) (-) (-)	Punjab	03/2019 (03/2022)	03/2025 (02/2027)	237.64 0.00	109.63	70.00
655	Nathdwara Mavli - Devgarh Madariya 82.542 km (CAOC/NWR NWR mor) (611855) (-) (-)	Rajasthan	01/2023 (07/2023)	06/2028 (-)	968.92 0.00	830.89	75.00
656	Pushkar - Merta Katyasani 51.346 km (CAOC/NWR NWR mor) (616841) (-) (-)	Rajasthan	02/2024 (02/2023)	12/2026 (12/2028)	799.64 0.00	242.08	7.00
657	Ajmer-Chanderiya section 178.28 km Umbrella work PB57/2019-20/NR (CAOC/NWR NWR mor) (616843) (-) (-)	Rajasthan	02/2024 (09/2020)	06/2027 (03/2028)	1,634.79 0.00	560.17	23.00
658	North Western Railway - New line between Ramdevra and Pokhran via Bhairav Gufa - Kailash Tekri 13.38 Km PB30/NR/2025-26 (CAOC/NWR NWR mor) (617404) (-) (-)	Rajasthan	04/2025 (03/2026)	03/2028 (-)	189.21 0.00	57.40	3.00
659	Gudha-Thathana Mithri - Construction of dedicated test track for testing and trial of rolling stocks and infrastructure components umbrella work PB23/2018-19/NR (CAOC/NWR NWR mor) (705752) (-) (-)	Rajasthan	04/2019 (09/2020)	11/2026 (11/2026)	819.48 0.00	326.20	95.00
660	Dedicatedtest track for RDSO Phase-2 34 km Umbrella work PB22/2019-20/NR (CAOC/NWR NWR mor) (706836) (-) (-)	Rajasthan	11/2021 (10/2022)	11/2026 (-)	466.42 0.00	586.33	98.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
661	Sawaimadhopur - Bypass line 6.98 km Umbrella work PB57/2019-20/NR (CAOC/NWR NWR mor) (706866) (-) (-)	Rajasthan	12/2022 (12/2023)	03/2026 (05/2027)	304.00 0.00	188.07	72.00
662	Madurai-Tuticorin via Aruppukkottai 143.5 km (CAOC/SR SR mor) (705489) (-) (-)	Tamil Nadu	04/2011 (08/2019)	07/2021 (01/2031)	601.43 0.00	351.21	14.00
663	Bahraich - Khalilabad via Bhinga, Shravasti, Balrampur, Utraula, Domriyaganj, Mehdawal, Bansi 240.26 km (CAOC/NER NER mor) (400204) (-) (-)	Uttar Pradesh	10/2018 (08/2021)	10/2030 (10/2030)	4,939.78 0.00	1,767.82	16.00
664	Sahjanwa - Dohrighat 81.17 km (CAOC/NER NER mor) (400205) (-) (-)	Uttar Pradesh	08/2019 (06/2022)	03/2029 (03/2029)	1,319.75 0.00	749.57	1.00
665	Varanasi- Pt. Deen Dayal Upadhyaya - Multitracking 15 km, including construction of a new Rail- cum- Road Bridge across Ganga River (CAOC/C-II/IR NR mor) (617213) (-) (-)	Uttar Pradesh	10/2024 (07/2025)	10/2029 (-)	2,464.46 0.00	119.36	7.00
666	Anand Nagar - Ghughuli via Maharajganj 53.37 km (CONSTRUCTION / NE-RAILWAY) (617252) (-) (-)	Uttar Pradesh	08/2023 (10/2023)	03/2028 (-)	958.27 0.00	894.10	14.00
667	Doubling between Jaunpur Jn - Zaffarabad 6.28 km PB73/2023-24/NR (CAOC/IR NR mor) (617370) (-) (-)	Uttar Pradesh	03/2023 (01/2025)	01/2027 (-)	180.66 0.00	79.74	22.00
668	Burhwal - Gonda - 3rd line 61.72 km (CAOC/NER NER mor) (705567) (-) (-)	Uttar Pradesh	11/2017 (09/2019)	03/2025 (05/2026)	1,016.00 0.00	795.57	100.00
669	Janghai - Pratapgarh - Amethi 87 km (CAO/C-II/IR NR mor) (705588) (-) (-)	Uttar Pradesh	11/2017 (11/2019)	03/2025 (03/2026)	722.00 0.00	1,231.85	80.00
670	Lalitpur - Birari with flyover at Lalitpur 15.80 km (CAO/C/NCR NCR mor) (705766) (-) (-)	Uttar Pradesh	03/2017 (01/2023)	12/2024 (01/2026)	304.44 0.00	287.94	85.00
671	Mughalsarai - Allahabad - 3rd line 150 km (CAO/C/NCR NCR mor) (705772) (-) (-)	Uttar Pradesh	08/2019 (12/2020)	12/2026 (03/2027)	2,649.00 0.00	2,069.77	78.00
672	Bhandai - Flyover for Etawah bound down trains 10 km (CAO/C/NCR NCR mor) (705777) (-) (-)	Uttar Pradesh	04/2019 (10/2024)	02/2026 (02/2027)	250.18 0.00	147.35	11.00
673	Bhatni - Aunrihar with electrification 125 km excl Indara - Mau 116.95 km (CMD / RVNL RVNL mor) (705780) (-) (-)	Uttar Pradesh	03/2018 (07/2019)	03/2024 (06/2026)	2,529.00 0.00	2,296.77	94.00
674	Barabanki-Malhaur - 3rd & 4th Line 32.84 km (CAO/C-II/IR NR mor) (705782) (-) (-)	Uttar Pradesh	01/2019 (11/2020)	03/2025 (08/2026)	407.00 0.00	444.86	77.00
675	Kalinarayanpur-Krishnanagar with Krishnanagar-Shantipur-Nabadwipghat - GC, Krishnanagar-Chartala, MM for Krishnanagar-Chapra-NL, Naihati-Ranaghat-3rd line, Nabadwipghat-Nabadwipdham upto BB loop 9.58 km, Ranaghat-Lalgola-strengthening bridge No.2 (CAOC/ER ER mor) (400247) (-) (-)	West Bengal	07/2015 (09/2019)	02/2027 (03/2028)	1,000.00 0.00	926.51	49.00
Total (147)					225,802.03 0.00	185,840.10	
Ministry of Road Transport & Highways							
Roads & Highways							
676	Rehabilitation and up-gradation and completion of balance works of the section from Km 107.760 km to 129.445 km After Middle strait to Humphrey, Km 130.600 to 138.300 After Humphrey to Kadamtala of NH-4 Intermediate/2-Lane with hard shoulder in the Union Territory of Andaman & Nicobar Islands on EPC basis Package- IIIA (NHIDCL) (619184) (-) (-)	Andaman & Nicobar	02/2018 (03/2024)	09/2025 (12/2026)	207.45 0.00	0.00	81.95
677	Rehabilitation and up-gradation and completion of balance work of section from Km 155.00 to Km 181.00 End of Jarwa to Rangat of NH -4 Total length 26 Km to Intermediate Lane/2-lane with hard shoulders in the UT of A&N Islands on EPC basis - Package-III.B Balance work (NHIDCL) (619185) (-) (-)	Andaman & Nicobar	02/2018 (05/2024)	10/2025 (03/2027)	183.56 0.00	163.63	53.81
678	Construction of Balance works of Major Bridge over Middle Strait Creek between Km.106.590 to km108.553 of NH-04 connecting South Andaman & Baratang Island in the Union Territory of Andaman & Nicobar Islands on EPC basis (NHIDCL) (619186) (-) (-)	Andaman & Nicobar	03/2015 (05/2024)	02/2026 (12/2026)	262.96 0.00	112.15	12.98

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
679	Gudivada Town 2 RoB, and Road improvement NH-165 (MoRTH) (617984) (-) (-)	Andhra Pradesh	03/2022 (05/2023)	05/2025 (03/2027)	317.22 0.00	234.36	75.20
680	Widening to two lane with paved shoulders from Km 0/0 to 64/020 Pamarru to Akiveedu (MoRTH) (617985) (-) (-)	Andhra Pradesh	03/2020 (11/2021)	11/2023 (05/2027)	529.54 0.00	441.10	74.41
681	Kurnool/Kadapa Border-Jammalamadugu section of NH-167K i.e. Design Ch. Km 248010 to km 269900 to 2 (MoRTH) (617986) (-) (-)	Andhra Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	292.63 0.00	0.00	95.77
682	Nandyala-Kurnool/Kadapa Border section of NH-167K i.e. Km 186/000 to Km 250/000Design Ch.186000 to 248010 to 2LPS (MoRTH) (617987) (-) (-)	Andhra Pradesh	10/2024 (09/2025)	09/2027 (09/2027)	691.81 0.00	256.39	49.71
683	Sangameswaram - Atmakuru section from Km 96 to Km 124 & Velegodu- Nandyal section including Nandyal Bypass from Km 143/6 to 185/9 NH-167K (MoRTH) (617988) (-) (-)	Andhra Pradesh	10/2024 (07/2025)	07/2027 (07/2027)	776.17 0.00	350.30	49.44
684	Rehabilitation and up-gradation of NH-167 from Km 14/900 to Km70/000 Design Ch. 14/900 to 69/700 Chintakunta to Adoni section to two lane with paved shoulders in the State of Andhra Pradesh under Corridor Approach through Engineering, Procurement (MoRTH) (617991) (-) (-)	Andhra Pradesh	11/2016 (05/2017)	05/2019 (12/2026)	290.15 0.00	205.04	91.90
685	4-laning of Puttaparthi-Koduru Section of NH-342 (MoRTH) (618013) (-) (-)	Andhra Pradesh	10/2022 (11/2023)	11/2025 (10/2026)	1,318.59 0.00	640.13	94.42
686	Rehabilitation and Up-gradation of existin of road from 2-lane to 2-lane with paved shoulders from km. 0.00 to km 53.590 total length-53.590 km of Raychoti to Vempalli section of NH-440 in the State of Andhra Pradesh on EPC mode. (MoRTH) (618037) (-) (-)	Andhra Pradesh	12/2021 (05/2022)	05/2024 (09/2026)	439.82 0.00	213.12	90.20
687	Gorantla - Hindupur section from Km 120/300 to 165/000 of NH716G in the State of Andhra Pradesh (MoRTH) (618052) (-) (-)	Andhra Pradesh	10/2024 (08/2025)	08/2027 (08/2027)	808.70 0.00	187.44	43.87
688	Muddanur to B. Kothapalli section of NH-716G from Km. 0/000 to Km. 56/500 56.500 Km in the State of Andhra Pradesh on EPC mode Job no. 741 (MoRTH) (618053) (-) (-)	Andhra Pradesh	10/2024 (08/2025)	08/2027 (08/2027)	1,019.97 0.00	0.00	33.55
689	Kondamodu to Perecherla Section Design Ch. Km 000 to Km 49917 of NH-167AG to to 4LPS (MoRTH) (618101) (-) (-)	Andhra Pradesh	10/2024 (04/2025)	04/2027 (04/2027)	881.61 0.00	430.77	57.76
690	Rehabilitation and upgradation from Km 22300 to 58635 of MudireddyPalle to Kadapa/Nellore Border via porumamilla Section of NH 167 Two Lane with paved Shoulder in (MoRTH) (618103) (-) (-)	Andhra Pradesh	03/2022 (10/2024)	04/2026 (07/2026)	279.29 0.00	168.70	90.33
691	Rehabilitation and upgradation of NH 326A from km 0/0 to 41/979 excluding km 2/255 to 3/372 and km 36/820 to 38/275 Odisha border to Narasamapeta to two lane with paved Shoulders in the State of Andhra Pradesh under NHO on EPC Mode (MoRTH) (618125) (-) (-)	Andhra Pradesh	03/2018 (09/2018)	03/2020 (10/2025)	228.32 0.00	183.07	100.00
692	Widening of Existing Road to Two Lane with Paved Shoulder Configuration from Km 0.00 to 26.000 & Km 45.200 To 59.622 Of NH 365BB in the State of Andhra Pradesh Under Annual Plan 2023-24 through EPC Mode (MoRTH) (618193) (-) (-)	Andhra Pradesh	01/2024 (04/2025)	12/2026 (03/2027)	368.63 0.00	134.99	45.62
693	Rehabilitation and upgradation of New NH 544DD from design Chainage Km. 56/000 to 102/20 of Kalyandrg - Molakalmuru Section (MoRTH) (618194) (-) (-)	Andhra Pradesh	03/2018 (08/2018)	02/2020 (09/2025)	294.13 0.00	257.77	98.52
694	Rehabilitation and Up-gradation of Dhindi - Digamarru section from Km 126/510 to Km 135/740 of NH -214 New NH -216 and digamarru -Losari section from Km 0/000 tp Km 34/230 of NH-214 A New Nh-216 to two lane with paved shoulder in the state of AP-NH (MoRTH) (618236) (-) (-)	Andhra Pradesh	02/2016 (05/2016)	05/2018 (11/2023)	316.06 0.00	283.54	100.00
695	Rehabilitation and Up-gradation of Thimmapuram to Gurajanapalli section from Km 26/150 to Km 41/161 of NH - 214 New NH - 216 to two lane with paved shoulder in the state of Andhra Pradesh under NHDP-IV (MoRTH) (618238) (-) (-)	Andhra Pradesh	08/2016 (01/2017)	07/2018 (09/2026)	350.61 0.00	481.30	98.20

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
696	Rehabilitation & Upgradation of NH214 New NH-216 from Km 34/230 to Km 84/550 Losari to Machavaram Section to two lane with paved shoulder in the state of Andhrapradesh under NHDP-IV through Engineering, Procurement& Construction EPC mode. (MoRTH) (618239) (-) (-)	Andhra Pradesh	03/2016 (09/2016)	09/2018 (07/2025)	445.22 0.00	431.25	98.60
697	Construction of Paderu bypass Km 0000 to Km 13000 of 2- lane with paved shoulder on NH-516E (MORTH) (618254) (-) (-)	Andhra Pradesh	03/2023 (01/2025)	07/2026 (12/2026)	244.43 0.00	21.96	13.00
698	Two laning with paved shoulders of Lambasingi to Paderusection of NH 516E (MoRTH) (618255) (-) (-)	Andhra Pradesh	04/2020 (11/2023)	11/2025 (03/2027)	361.24 0.00	180.54	57.99
699	Rehabilitation and Upgradation to 2-lane with paved should ders Sir, configuration of Chaprathipalem to Lambasingi section Km 165500 to Km 205000 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618256) (-) (-)	Andhra Pradesh	08/2020 (10/2022)	10/2024 (09/2026)	311.22 0.00	217.37	93.01
700	Rehabilitation and Upgradation to 2-lane with paved shoulders configuration of Koyyuru to Chaprathipalem section Km 120000 to Km 165500 of NH-516E in the State of Andhra Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode (MoRTH) (618257) (-) (-)	Andhra Pradesh	08/2020 (07/2022)	07/2024 (09/2026)	349.29 0.00	267.62	98.09
701	Construction of i Connecting Road from Z-Morh Tunnel to Zojila Tunnel Road Length 18.475km and ii 14.150 Km long 2-L Bi-directional single tube Zoji-la Tunnel across Zojila Pass on Sonamarg - Kargil section from Km 82 to Km 118 of NH-01 under PMDP (NHIDCL) (618412) (-) (-)	Andhra Pradesh	01/2018 (10/2020)	09/2026 (02/2028)	6,808.69 0.00	3,583.30	68.80
702	Bangalore Chennai Expressway Phase-II Pkg-II from km.96.000 to Km 127.000 Baireddypalle to Bangarupalem section (NHAI) (618475) (-) (-)	Andhra Pradesh	02/2021 (06/2023)	06/2025 (10/2026)	2,548.04 0.00	1,332.88	94.24
703	Bangalore Chennai Expressway Phase-II Pkg-III from km.127.000 to Km 156.000 Bangarupalem to Gudipala section (NHAI) (618476) (-) (-)	Andhra Pradesh	11/2020 (10/2022)	10/2024 (09/2026)	1,407.33 0.00	868.76	99.46
704	Construction of 6 lane elevated corridor including its approaches from Km. 629880 to Km. 634470 Design Chainage of NH-16 in Ranasthalam Town portion in the state of Andhra Pradesh on EPC Mode under NHO. (NHAI) (618524) (-) (-)	Andhra Pradesh	07/2024 (03/2025)	03/2027 (08/2027)	257.98 0.00	61.80	39.10
705	Construction of flyover at Gammon Junction at Km.903.265 on NH16 including vent at Diwancheruvu junction at Km.902.308 Blackspot ID No.AP03299 in Andhra Pradesh on EPC mode under NHO (NHAI) (618525) (-) (-)	Andhra Pradesh	03/2025 (10/2025)	10/2027 (10/2027)	326.61 0.00	60.66	26.20
706	6L of Anandapuram Pendurthi Anakapalli Section from km. 681.000 to km. 731.780 of NH-16 (NHAI) (618579) (-) (-)	Andhra Pradesh	01/2018 (01/2019)	07/2021 (10/2026)	2,527.00 0.00	2,378.74	100.00
707	Nandigama Bypass and Kanchikacherla bypass (NHAI) (618629) (-) (-)	Andhra Pradesh	11/2017 (03/2018)	06/2019 (09/2026)	416.07 0.00	387.77	98.47
708	4L of Kadapa China Orampadu section of NH-716 Package I of Kadapa-Renigunta section (NHAI) (618633) (-) (-)	Andhra Pradesh	12/2022 (03/2026)	03/2028 (03/2028)	1,732.66 0.00	163.41	5.01
709	6L Korlam-Kantakapalle Section of NH-130CD Road from Km 421.100 to Km 445.100 Pkg-3 (NHAI) (618682) (-) (-)	Andhra Pradesh	02/2021 (02/2022)	02/2024 (09/2026)	1,112.70 0.00	850.01	99.50
710	Renigunta - Poyya - Naidupeta km 124.60 to km 183.4 of NH 71 (NHAI) (618700) (-) (-)	Andhra Pradesh	03/2020 (01/2022)	01/2024 (09/2026)	1,863.09 0.00	1,688.88	98.60
711	6L Access Controlled Greenfield Highway from Kodur Ch. 0000 to Vanavolu Ch. 24300 of [NH-544G] Package-1 (NHAI) (618712) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (03/2027)	912.94 0.00	358.13	87.65
712	6L Access Controlled Greenfield Highway from Yerragudipadu Ch. 129000 to Audireddipalle Ch. 160000 of [NH 544G] Package-6 (NHAI) (618713) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (11/2027)	1,200.42 0.00	282.21	47.20

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
713	6L Access Controlled Greenfield Highway from Nallacheruvu palli Ch. 96300 to Yerragudipadu Ch. 129000 of [NH-544G] Package-5 (NHAI) (618714) (-) (-)	Andhra Pradesh	02/2022 (02/2024)	02/2026 (06/2027)	1,253.26 0.00	389.20	67.05
714	6L Access Controlled Greenfield Highway from Odulapalle Ch. 72000 to Nallacheruvu-palli Ch. 96300 of [NH-544G]Package-4 (NHAI) (618715) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (04/2027)	1,058.90 0.00	403.37	76.97
715	6L Access Controlled Greenfield Highway from Vankarakunta Ch. 45700 to Odulapalle Ch. 72000 of [NH-544G]Package-3 (NHAI) (618716) (-) (-)	Andhra Pradesh	12/2022 (03/2024)	03/2026 (03/2027)	992.91 0.00	351.25	77.21
716	6L Access Controlled Greenfield Highway from Vanavolu Ch. 24300 to Vankarakunta Ch. 45700 of [NH-544G] Package-2 (NHAI) (618717) (-) (-)	Andhra Pradesh	01/2023 (03/2024)	03/2026 (02/2027)	750.81 0.00	261.41	87.24
717	6L Access Controlled Greenfield Highway from Kavulakuntla Ch. 196000 to Narayanmpet Ch. 203500Package-09 (NHAI) (618718) (-) (-)	Andhra Pradesh	02/2023 (02/2025)	02/2027 (12/2027)	1,092.18 0.00	242.13	54.56
718	6L Access Controlled Greenfield Highway from Mallapalle Ch. 176000 to Kavulakuntla Ch. 196000 Package-08 (NHAI) (618719) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2027)	909.02 0.00	290.05	65.92
719	6L Access Controlled Greenfield Highway from Audireddipalle Ch. 160000 to Mallapalle Ch. 176000Package-07 (NHAI) (618720) (-) (-)	Andhra Pradesh	02/2023 (03/2024)	03/2026 (04/2027)	987.10 0.00	338.45	73.78
720	6L Access Controlled Greenfield Highway from Chandrasekharapuram Ch. 228000 to Polavaram Ch. 260000of [NH-544G] Package-11 (NHAI) (618721) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (08/2027)	1,292.65 0.00	358.74	64.20
721	4L PS Mydukur - Badvel from Km 585.820 to Km 630.960 of NH-67 (NHAI) (618759) (-) (-)	Andhra Pradesh	05/2022 (09/2023)	09/2025 (12/2026)	1,063.57 0.00	586.02	90.40
722	4L of Pileru to Kalur Section from Km 55.900 to Km 92.800 & Km 94.500 to Km 95.717 of NH-71Package-II (NHAI) (618777) (-) (-)	Andhra Pradesh	03/2022 (10/2023)	11/2025 (09/2026)	1,877.47 0.00	266.59	98.84
723	4L of Madanapalle to Pileru Section from Km 0.000 to Km 55.900 of NH-71Package-I (NHAI) (618778) (-) (-)	Andhra Pradesh	02/2022 (01/2023)	01/2025 (09/2026)	1,877.47 0.00	1,183.12	94.90
724	Development of 4L Road from Samarlakota to Achampeta Junction as part of Kakinada Port Connectivity to NH-16 Rajanagaram Junction in East Godavari District (NHAI) (618803) (-) (-)	Andhra Pradesh	09/2022 (08/2023)	08/2025 (12/2026)	645.63 0.00	694.72	93.00
725	Dedicated Port road to Krishnapatnam Port Package-I from Km. 0.000 to Km. 18.000 (NHAI) (618804) (-) (-)	Andhra Pradesh	03/2018 (12/2018)	12/2020 (03/2027)	348.72 0.00	310.54	80.19
726	6L Connectivity to Port Road from Sabbavaram Sheelanagar-NH516C (NHAI) (618805) (-) (-)	Andhra Pradesh	12/2024 (02/2026)	02/2028 (02/2028)	977.33 0.00	156.52	7.20
727	Improvement of 4L road to 6L road and 4L dedicated Port Roads for the Port connectivity road from Convent junction to Sheelanagar Junction (NHAI) (618806) (-) (-)	Andhra Pradesh	01/2023 (02/2024)	02/2026 (12/2026)	685.99 0.00	508.74	79.00
728	4L Greenfield Road connecting North and South industrial cluster of Khandaleru Creek near Krishnapatnam port at Thamminapatnam to Mollur from Km 0.0 to Km 16.046, Part I & 6L extension of dedicated port road of NH-67 Km 18.0 to Km 19.3, Part II (NHAI) (618807) (-) (-)	Andhra Pradesh	08/2022 (09/2023)	09/2025 (01/2027)	609.43 0.00	593.76	84.03
729	4 Laning of NH-544D from Km 0.000 to km 37.000 of Anantapur- Muchukota section Pkg-1 (NHAI) (618826) (-) (-)	Andhra Pradesh	10/2022 (07/2023)	07/2025 (10/2026)	907.76 0.00	493.10	92.34
730	4 Laning of NH-544D from Km 37.000 to km 69.000 of Muchukota- Bugga section Pkg-2 (NHAI) (618827) (-) (-)	Andhra Pradesh	10/2022 (08/2023)	08/2025 (12/2026)	1,097.57 0.00	466.89	84.92
731	Access Controlled Highway of 4 Lane with Paved Shoulders from TN/AP Border Design Chainage Km 6151 to Puttur Design Chainage Km 81540 of NH-716 & 6 Lane with Paved Shoulders from Mallavaram to Renigunta (NHAI) (618920) (-) (-)	Andhra Pradesh	03/2024 (12/2024)	12/2026 (03/2027)	1,346.82 0.00	204.93	42.48

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
732	4L Access controlled Highway From Vakalpudi Light House to Annavaram on NH-16 section of NH-516F From Km0000 to Km40621 (NHAI) (619046) (-) (-)	Andhra Pradesh	03/2023 (08/2026)	08/2028 (08/2028)	1,439.00 0.00	8.78	0.00
733	Six Laning of Vijayawada Bypass from Chinna Avutapalli to Gollapudi in Vijayawada - Gundugolanu Section from km. 0.00 to km. 30.00 Pkg-III (NHAI) (619076) (-) (-)	Andhra Pradesh	01/2020 (02/2021)	02/2023 (09/2026)	1,581.24 0.00	1,024.59	98.20
734	4 L of China Orampadu-Renigunta section of NH-716 Package-II of Kadapa- Renigunta section (NHAI) (619102) (-) (-)	Andhra Pradesh	12/2022 (03/2026)	03/2028 (03/2028)	1,500.11 0.00	122.05	2.25
735	6L Jakkuva Korlam Section of NH-130CD Road from km 396.800 to km 421.100 Pkg 2 (NHAI) (619111) (-) (-)	Andhra Pradesh	02/2021 (03/2022)	03/2024 (09/2026)	840.51 0.00	573.90	99.83
736	6L Kantakapalle Sabbavaram Section of NH-130CD Road from Km 445.100 to Km 464.662 Pkg-4 (NHAI) (619112) (-) (-)	Andhra Pradesh	02/2021 (10/2022)	10/2024 (03/2027)	1,012.57 0.00	704.27	84.60
737	6L Access Controlled Greenfield Highway from Narayanmpet Ch. 203500 to Chandrasekharapuram Ch. 228000Package-10 (NHAI) (619123) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (07/2027)	813.66 0.00	238.29	66.12
738	6L Access Controlled Greenfield Highway from Polavaram Ch. 260000 to Marripudi Ch. 285500 of [NH-544G]Package-12 (NHAI) (619124) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (05/2027)	747.29 0.00	250.94	70.20
739	6L Access Controlled Greenfield Highway from Somavarappadu Ch.314.600 to Muppavaram Ch.343240 of [NH-544G] Package-14 (NHAI) (619125) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (10/2027)	1,103.90 0.00	279.46	44.56
740	6L Access Controlled Greenfield Highway from Marripudi Ch. 285500 to Somavarappadu Ch. 314600 of [NH-544G] Package-13 (NHAI) (619126) (-) (-)	Andhra Pradesh	02/2023 (02/2024)	02/2026 (04/2027)	976.41 0.00	370.83	73.00
741	6L of Naidupeta Junction - Turpukanupur Section from km 57.046 to km 91.927 (NHAI) (619140) (-) (-)	Andhra Pradesh	08/2022 (10/2023)	10/2025 (09/2027)	1,398.84 0.00	397.32	53.70
742	Construction of four lane access controlled highway from Chillakuru cross road to Turpu KanupurPart 1 of Package - II km 0.000 131.500 of NH - 16 to km 23.770 on New NH-516W including six lane flyover and approaches on NH-16 length km 1.050 and six lane access controlled from Turpu Kanupur to Port South Gate Part 2 of Package - II km 23.770 to km 35.015 on New NH-516W in the state of Andhra Pradesh on HAM Mode under Bharatmala Pariyojana Phase I (NHAI) (619141) (-) (-)	Andhra Pradesh	08/2022 (12/2023)	12/2025 (03/2026)	864.20 0.00	369.28	55.53
743	Balance works in AP Portion and punch list items in TN & AP portion of NH-205 (NHAI) (619160) (-) (-)	Andhra Pradesh	10/2022 (07/2023)	01/2025 (01/2026)	166.52 0.00	98.52	100.00
744	Construction of road from Bomdilla9th Mile- Nafra Lada section of Frontier Highway NH-913 Package 1 9th mile-Nafra 19.554 to 70.00 50.446 (MoRTH) (198592) (-) (-)	Arunachal Pradesh	03/2025 (07/2026)	07/2029 (-)	1,273.44 0.00	151.90	0.00
745	Construction of 2-lane road of Potin to Pangin section of NH-13 from Km 163.59 to Km 206.66 Package-5 on EPC Mode in the State of Arunachal Pradesh under Arunachal Pradesh Package of Roads and Highways of SARDP-NE [Job No SARDP-NE/P- P/Pkg-A/NH-13/Ar.Pr./PWD/2018-19/116] (MoRTH) (617892) (-) (-)	Arunachal Pradesh	03/2019 (11/2020)	11/2023 (10/2026)	450.65 0.00	403.84	96.61
746	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang Package-III from design Km 60.000 to Km 121.500 Design Length 61.500 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Pkg-3 (NHIDCL) (618401) (-) (-)	Arunachal Pradesh	02/2024 (07/2025)	07/2028 (07/2028)	1,418.67 0.00	93.29	2.50
747	Construction of Intermediate Lane with Hard Shoulder of Hunli to Hayuliang from Design Km 0.000 to Km 53.000 Design Length 53.000 km, Greenfield Section of Frontier Highway NH-913 in the State of Arunachal Pradesh on EPC Mode Package-I (NHIDCL) (618402) (-) (-)	Arunachal Pradesh	02/2024 (03/2025)	02/2028 (02/2028)	1,262.43 0.00	257.02	22.12
748	Construction of Intermediate Lane Road with hard shoulder from design Km 0.000 to Km 17.387 Total length 17.387 km of Hunli to Ithun Bridge section on NH-913 Frontier Highway in State of Arunachal Pradesh on EPC mode under NHO-NE (NHIDCL) (618403) (-) (-)	Arunachal Pradesh	02/2024 (01/2025)	01/2027 (01/2027)	275.50 0.00	166.24	60.96

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
749	Construction of Intermediate Lane Road with hard shoulder from design chainage Km 0.000 to Km 53.040 Existing Length68.500 Km & Total Design length 53.04 km of Tato to Monigong section of NH-913 Frontier Highway on Nafra Bomdila to Vijaynagar along China border in state of Arunachal pradesh on EPC mode (NHIDCL) (618404) (-) (-)	Arunachal Pradesh	12/2023 (05/2025)	11/2027 (11/2027)	625.61 0.00	274.89	23.03
750	Construction of Intermediate Lane of Pango to Jorging Road from 0000 to Design Km Design Km 40000 Design Length 40.00 Km, Pkg-I, Greenfield Alignment in the State of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (618405) (-) (-)	Arunachal Pradesh	01/2024 (01/2025)	07/2027 (07/2027)	898.19 0.00	259.63	40.12
751	Construction of Balance work of 2-Lane with PS of Joram Koloriang Road from existing Km122.600 to km138.00 [Design Km108.724 to Km123.714] in Arunachal Pradesh on EPC Mode under SARDP-NE Pkg-7 (NHIDCL) (618433) (-) (-)	Arunachal Pradesh	02/2017 (10/2020)	04/2022 (04/2026)	184.89 0.00	156.42	99.69
752	Roing-Hunli Road Greenfield Alignment Project (NHIDCL) (618434) (-) (-)	Arunachal Pradesh	02/2017 (03/2018)	03/2022 (10/2026)	1,718.59 0.00	1,123.53	82.48
753	Construction of 2-Laning with hard shoulders of Demwe-Brahmakund section of NH-13 from Ch.0.00 km to 18.464 km on EPC under SARDP-NE NHO-NE -Balance Work (NHIDCL) (618445) (-) (-)	Arunachal Pradesh	08/2020 (06/2025)	12/2027 (12/2027)	353.90 0.00	26.82	23.20
754	Improvement and Widening to 2 lane with paved Shoulder of NH-15 old NH-52 from Existing Km 770.600 Design Km 24.819 to Existing km 805.750 Design Km 59.885 Kamlang T-Junction to Chowkham, Existing Length 35.150 Km, Design Length-35.066 Km in the state of Arunachal Pradesh on EPC mode Pkg-2 (NHIDCL) (619014) (-) (-)	Arunachal Pradesh	12/2023 (02/2026)	02/2028 (02/2028)	316.73 0.00	35.10	23.90
755	Improvement and Widening to 2-lane with Paved Shoulder of NH-13 & 15 Old NH-52 from Existing Km 745.60 Design Km 0.000 to Existing km 770.600 Design Km 24.819 Brahmakund T-Junction to Kamlang T-Junction, Existing Length 25.00 Km, Design Length 24.819 Km in the state of Arunachal Pradesh on EPC mode Pkg-1 (NHIDCL) (619248) (-) (-)	Arunachal Pradesh	12/2023 (06/2026)	06/2028 (06/2028)	441.41 0.00	44.87	19.92
756	Construction of road from Bomdilla 9th Mile - Nafra Lada section of Frontier Highway NH-913 Package 4 Dishum-Sachung-Lada 113.00 to 167.75 54.75km (MoRTH) (619256) (-) (-)	Arunachal Pradesh	03/2024 (07/2026)	07/2030 (-)	1,266.86 0.00	107.62	0.00
757	Construction of road from Km 70.000 to Km 113.000 of Bomdila-Nafra-Lada Section of NH-913 Frontier Highway in the State of Arunachal Pradesh L43.000 Km (MoRTH) (619257) (-) (-)	Arunachal Pradesh	02/2024 (08/2026)	08/2030 (-)	1,240.75 0.00	79.00	0.00
758	Construction of road from Taliha to Tato section of Frontier Highway NH-913 Package 3 km 87.13 to 121.541 34.411km (MoRTH) (619266) (-) (-)	Arunachal Pradesh	03/2024 (08/2026)	08/2029 (-)	735.20 0.00	135.42	0.00
759	Construction of road from km 113.25 to km 160.75 of Huri-Taliha section of NH-913 Pkg 3 Frontier Highway to Intermediate Lane on EPC mode in the State of Arunachal Pradesh (MoRTH) (619267) (-) (-)	Arunachal Pradesh	03/2024 (08/2026)	08/2030 (-)	1,228.64 0.00	137.54	0.00
760	Construction of Mangaldoi Bypass NH-15 starting at Ch 26400 and terminating at Ch 41505 under Rangia NH Division L 15.105 Km in the State of Assam. Job No. 15/AS/2021-22/234 (MoRTH) (617895) (-) (-)	Assam	03/2022 (04/2023)	04/2025 (12/2026)	535.03 0.00	215.32	76.78
761	Construction of 4 lane Gauripur Bypass Starting bfrom Km 852.56 of NH-31Dumardoha Pt-II and Terminating at Km 862.17 Baladmara via. Khudimari Pt.- II, Fulkumari, Charaldanga, Sajuakuti,Geramari Pt.-III and finally meeting at km 862.17 of NH-17New/ NH-31Old in the State of Assam under EPC Mode Job no. 31/AS/ 2023-24/265 (MoRTH) (617896) (-) (-)	Assam	03/2024 (04/2025)	10/2026 (03/2027)	421.15 0.00	55.16	34.00
762	Construction of 2 lane Barpeta Bypass from Km 77900Baradi to Km 86150 Deurikuchi Length8.25Km on NH-427 in the state of Assam under EPC ModeJob No.427/AS/2022-23/245 (MoRTH) (618034) (-) (-)	Assam	03/2023 (02/2025)	08/2026 (03/2027)	173.65 0.00	173.65	20.00
763	Construction of new 2 Lane with paved shoulders of NH Standards from km 0.080 to km 11.690 L11.610 km in Majuli and from km 19.715 to km 27.484 L 7.769 km in Jorhat on the newly declared NH 715K and construction of 1.10 km flyover on NH-715 with its approaches and service roads L1.10 km, Total Length 20.479 km in the State of Assam Job No. 715K/AS/2023-24/256 (MoRTH) (618159) (-) (-)	Assam	02/2024 (09/2025)	03/2027 (03/2027)	382.10 0.00	25.60	7.15

All Ongoing Projects							AUGUST 2026
SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
764	Construction of 2 lane Major Bridge including approaches over Brahmaputra between Majuli on North Bank and Jorhat on South Bank from km. 11.690 to km. 19.715 length of bridge 6,812.5m Package - II on NH-715K in the state of Assam Job no. 715/AS/2020-21/213 (MoRTH) (618160) (-) (-)	Assam	03/2025 (12/2025)	12/2027 (12/2027)	1,019.17 0.00	17.38	5.31
765	4-L Bilasipara-Guwahati Package-10 (NHIDCL) (618282) (-) (-)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1,264.90 0.00	633.62	65.64
766	4-L Bilasipara-Guwahati Package-9 (NHIDCL) (618283) (-) (-)	Assam	03/2023 (12/2023)	06/2026 (03/2027)	1,000.27 0.00	506.42	61.78
767	Widening/Improvement to 4-Lane with paved shoulder from Km 99930 to Km 143680 Design Chainage 96000 to 139750 of Paikan to Dhupdhara Sahar of Bilasipura-Guwahati Road on NH-17 in the state of Assam on EPC mode under Bharatmala Pariyojana in Economic Corridors Project Length 43.750km under NHO-NE Package-8 (NHIDCL) (618284) (-) (-)	Assam	03/2023 (12/2023)	12/2026 (12/2026)	1,457.59 0.00	996.13	93.96
768	Construction of New 2-Lane Bridge with its approaches from km 0000 to Km 4385 across River Brahmaputra on NH-17 at Jogighopa in Assam on EPC mode (NHIDCL) (618286) (-) (-)	Assam	09/2021 (11/2021)	11/2024 (03/2027)	746.76 0.00	447.07	84.69
769	Widening/Improvement to 4-Lane with paved Shoulder from Ch. 25.633 Km to Ch. 52.470 Km Design Ch. 21.850 Km to Ch.48.670 Km for Package-2 of Bilasipura-Guwahati road NH-17 Section Near Mowatari, before Chapar Bypass to Tulungia junction with NH-17 in the state of Assam on HAM mode under NHO-NE Package-2 (NHIDCL) (618287) (-) (-)	Assam	11/2023 (12/2024)	06/2027 (06/2027)	1,338.61 0.00	199.15	12.50
770	Widening/Improvement to 4-Lane with Paved Shoulder from Ch.5.580 Km to Ch.25.633 Km Design Ch.0.000 Km to Ch.17.737km Km 901.100 to Km 921.145 of old NH-31 of Bilasipara- Guwahati road NH-17 Section Near Chirakuta to near Mowatari, before Chapar Bypass in the state of Assam on HAM mode Package-1 (NHIDCL) (618288) (-) (-)	Assam	02/2024 (02/2025)	08/2027 (08/2027)	1,081.15 0.00	163.24	35.98
771	Construction and up gradation to 4-Lane of existing two lane with paved shoulder from Hapachara to Tulungia road of NH-117 of existing Km 0.00 to km 14.050 and Design Km 0.000 to km 14.660 under BMP on EPC mode (NHIDCL) (618289) (-) (-)	Assam	03/2020 (06/2020)	12/2022 (03/2026)	224.85 0.00	209.95	97.76
772	Construction of 4-Lane Panchgram Bypass from Design Chainage km 15500 on NH-37 Old NH-53 at Kalinagar Pt.-I Village to Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Package-2 (NHIDCL) (618308) (-) (-)	Assam	03/2023 (08/2024)	02/2027 (03/2027)	676.18 0.00	358.25	60.05
773	Widening/Improvement to 4-Laning and Greenfield alignment with Paved shoulder of Silchar-Badarpur Churaibari section of NH-37 & NH-8 from Design chainage 38.600 End point of proposed Badarpur Bypass to Km. 62.800 Start point of proposed Nilambazar/Cheragi Bypass in the state of Assam on HAM Mode Package-4 (NHIDCL) (618309) (-) (-)	Assam	02/2024 (08/2025)	08/2027 (08/2027)	1,319.55 0.00	185.17	25.46
774	Widening/Improvement to 4-L of Karimgani - sutarkandi section of NH 37 from design Ch 0020 Start of proposed Karimganj Bypass from NH -8 to design Chainage Km 14380 near Sutarkandi Spur Connectivity to Indo/Bangladesh Border on Silchar- Churaibari in the State of Assam on HAM Mode Package-7 (NHIDCL) (618310) (-) (-)	Assam	02/2024 (02/2025)	02/2027 (02/2027)	791.79 0.00	135.92	44.50
775	Widening/Improvement to 4-Lane with Paved shoulder for existing as well as Greenfield alignment of Badarpur Churaibari section of NH-8 from Design chainage 87.700 Chandkhira to Km. 106.500 Churaibari section Assam-Tripura border in the state of Assam on HAM Mode Package-6 (NHIDCL) (618311) (-) (-)	Assam	03/2024 (03/2025)	03/2027 (03/2027)	870.00 0.00	158.08	44.90
776	Widening/Improvement to 4-Lane with Paved Shoulder from existing road and Greenfield alignment form Design Ch. 62.800 start of proposed Nilambazar/Cheragi Bypass to Design Ch. 87.700 near Chandkhira Village of NH-8 on Silchar-Churaibari in the state of Assam on HAM Mode Package-5 (NHIDCL) (618312) (-) (-)	Assam	02/2024 (04/2025)	10/2027 (10/2027)	1,258.13 0.00	187.02	14.60
777	Widening/Improvement of Existing 2 lane to 4-Laning of Karimganj-Silchar section of NH-37 from Design Ch 0.000 near Silchar ISBT to Design Ch 15.970 near Kalinagar Pt I on NH-37 in Assam on HAM Mode Pkg-1 (NHIDCL) (618313) (-) (-)	Assam	03/2024 (09/2025)	09/2027 (09/2027)	1,181.55 0.00	178.80	41.64
778	4-Laning of Dhanehari Lailapur / Vairengte section from Existing Chainage km 12920 to km 43000 of NH 306 Design Chainage km 20000 to km 49360 on Silchar - Vairengte Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode. Project Length 29.360 km under NHO-NE Package-2 (NHIDCL) (618314) (-) (-)	Assam	03/2023 (02/2024)	08/2026 (03/2027)	1,716.21 0.00	1,057.81	82.60

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
779	4-Laning of Silchar - Dhanehari section from Existing Chainage km 263800 of NH 37 to km 12920 of NH 306 Design Chainage km 0000 to km 20000 on Silchar - Vairengte - Sairang road in the State of Assam under Bharatmala Pariyojna on EPC mode Package-1 (NHIDCL) (618315) (-) (-)	Assam	02/2023 (01/2024)	07/2026 (03/2027)	1,256.90 0.00	635.51	60.43
780	Widening/Improvement to 4-Lane with Paved Shoulder from KM 38500 to Km 51246 Design Chainage 38500 to 50959 with proposed Daboka Bypass of Daboka- Parokhaowa of NH 29 on EPC under NHO-NE Package-1 (NHIDCL) (618326) (-) (-)	Assam	01/2023 (11/2023)	11/2025 (06/2026)	516.88 0.00	323.35	99.70
781	Improvement to 4-Lane with Paved Shoulder from existing km 260000 Design Ch.4560 km to existing km Ch.233000 D. Ch.24560 of Silchar near Nutan Dayapur village - Budha Nagar Section Length-20.00 Km of NH-37 under Package Silchar- Jiribam Pkg-1 in the state of Assam on HAM Mode (NHIDCL) (618331) (-) (-)	Assam	01/2024 (01/2025)	01/2028 (01/2028)	957.95 0.00	214.73	48.17
782	Widening/Improvement to 4-Lane with Paved Shoulder from km 626030 Nalani hulla Gaon to km 650450 Chotahapjan on existing Tinsukhia -Makum Bypass of NH-15 OLD NH-37 and Strengthening of existing NH-315 OLD NH-38 from Km 0000 Chotahapjan to Km 16900 Bogapani section 2-Lane PS in Assam on EPCMode under NHO-NE Package-3 (NHIDCL) (618340) (-) (-)	Assam	01/2023 (05/2023)	05/2025 (10/2026)	458.59 0.00	264.54	89.92
783	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 156.489 near P. Leikul to km 176.410 near Borowapu on EPC mode under NHO-NE Assam portion Package-10 (NHIDCL) (618351) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (12/2026)	890.33 0.00	628.77	92.51
784	Widening & Upgradation to 2 lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 136.500 near Hejaichak to km 156.489 near P. Leikul Package-9 on EPC mode under NHO-NE Package-9 (NHIDCL) (618352) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (12/2026)	860.37 0.00	559.71	97.25
785	Widening & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 116.480 near Hangrum to km 136.500 near Hejaichak Package-8 on EPC mode under NHO-NE Package 8 (NHIDCL) (618353) (-) (-)	Assam	03/2023 (08/2023)	08/2025 (12/2026)	904.04 0.00	563.52	96.70
786	Wideinig & Upgradation to 2-lanes with paved shoulders road from Tamenglong to Mahur NH-137 in the State of Assam starting from km 96.870 near Jiri River to km 116.550 near Hangrum Package-7 on EPC mode Package7 (NHIDCL) (618354) (-) (-)	Assam	12/2023 (03/2024)	03/2026 (12/2026)	846.82 0.00	482.38	90.36
787	Widening/Improvement to 4-Lane with Paved Shoulder configuration of existing single lane road from Srirampur near Bhairiguri Village to Kachukhana Harichara Paglagaunj Package-I of Srirampur - Dhubri Section of NH-127B from existing Km 0.000 to Km 28.050 Design Km 0.000 to Km 27.650, Design Length27.650 Km under JICA ODA Loan assistance Phase-V -Balance work (NHIDCL) (618371) (-) (-)	Assam	03/2022 (11/2024)	11/2026 (11/2026)	613.89 0.00	385.77	89.76
788	Construction of 4-Lane Bridge including approaches over River Brahmaputra between Dhubri on North Bank,Assam and Phulbari on south Bank,Meghalaya on NH-127B under JICA ODA Loan assistance Phase-III (NHIDCL) (618373) (-) (-)	Assam	05/2019 (12/2020)	09/2028 (09/2028)	4,997.04 0.00	3,133.25	79.36
789	4-Laning of Jamugurihat to end of Biswanath Chariali By-Pass from Km 182.000 to Km 208.000 of NH-52 on EPC mode in state of Assam under SARDP-NE (NHIDCL) (618436) (-) (-)	Assam	03/2015 (12/2016)	06/2019 (07/2025)	599.00 0.00	433.62	100.00
790	Construction of Balance Work of 4-Laning of NH-37 Section between End of Moran Bypass to Bogibeel junction near Lapetketa Km. 561.700-Km. 580.875 under SARDP- NE, Phase 'A' in the State of Assam on EPC mode Pkg-I Road works & Toll Plaza (NHIDCL) (618437) (-) (-)	Assam	01/2016 (09/2024)	03/2025 (08/2025)	274.34 0.00	116.67	100.00
791	4-Laning of NH-37 Section between Demow to End of Moran Bypass From Km. 534.800 to Km. 561.700 including Emergency Landing Facility ELF under SARDP-NE, Phase 'A' in the State of Assam on EPC mode (NHIDCL) (618438) (-) (-)	Assam	01/2016 (01/2023)	07/2024 (08/2025)	385.57 0.00	681.40	100.00
792	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH- 37 Old from Km 490.800 to Km 534.800, under SARDP- NE on EPC Mode in the state of Assam Pkg- IV Structures & Toll Plaza (NHIDCL) (618440) (-) (-)	Assam	01/2016 (10/2024)	10/2025 (10/2026)	187.09 0.00	16.71	62.67
793	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH- 37 Old from Km 490.800 to Km 501.800 11.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-I Road Works (NHIDCL) (618441) (-) (-)	Assam	01/2016 (10/2024)	09/2025 (10/2026)	467.79 0.00	97.88	88.93

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
794	Construction of Balance Work of the 4-Laning of the Section from Jorhat to Jhanji of NH-37 Old from Km 477.000 to Km 490800 13.800 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (618442) (-) (-)	Assam	01/2024 (02/2024)	08/2024 (06/2026)	358.72 0.00	100.40	100.00
795	Guwahati Ring Road in the State of Assam (NHAI) (618934) (-) (-)	Assam	08/2024 (01/2026)	01/2030 (01/2030)	5,729.47 0.00	364.51	1.30
796	2L with ES of Yagyi - Kalewa section from Milepost 40/0 to Milepost 115/5 in Myanmar (NHAI) (618958) (-) (-)	Assam	12/2017 (05/2018)	06/2023 (12/2027)	1,200.14 0.00	0.00	52.00
797	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 501.800 to Km 514.800 13.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-II Road Works (NHIDCL) (619013) (-) (-)	Assam	10/2014 (10/2024)	01/2026 (10/2026)	508.76 0.00	114.14	81.27
798	Construction of 4-Lane Badarpur Bypass from Design Chainage km 27300 at crossing with NH-6 Old NH-44 Near Siddeswar Pt.-I Village to Design Chainage km 38600 on NH-37 Old NH-44 at Kandigram Chaita Village on Silchar - Churaibari stretch in the State of Assam on EPC Mode under Bharatmala Pariyojana in Economic Corridors Silchar- Churaibari Pkg-3 (NHIDCL) (619057) (-) (-)	Assam	02/2023 (02/2024)	08/2026 (03/2027)	574.26 0.00	331.19	71.09
799	Construction of Balance Work of 4-Laning of the Section from Jhanji to Demow of NH-37 Old from Km 514.800 to Km 534.800 20.000 Km, under SARDP- NE under EPC Mode in the state of Assam Pkg-III Road Works (NHIDCL) (619060) (-) (-)	Assam	10/2014 (10/2024)	09/2025 (10/2026)	344.71 0.00	56.61	74.40
800	Balance work of 4L of NarimbangloJatinga Junction- Harangajoroad section from Km 0.000 to Km 49.230 of NH-27 (NHAI) (619089) (-) (-)	Assam	03/2022 (01/2023)	01/2026 (09/2026)	1,909.98 0.00	1,434.97	98.00
801	Construction of proposed 4Lane Revelgunj bypass NH-19 in the State of Bihar on EPC mode connecting NH 19 to 85 origin (MoRTH) (617897) (-) (-)	Bihar	03/2022 (07/2023)	07/2025 (12/2026)	295.24 0.00	178.52	91.79
802	Widening & Strenthening from km132.895 to km 190.15 NH-80 (MoRTH) (617958) (-) (-)	Bihar	03/2021 (11/2022)	11/2024 (11/2026)	566.10 0.00	376.64	95.15
803	Gaya-Hisua-Rajgir-Nalanda-Biharsharif section km0.00 to 92.935 NH-82 (MoRTH) (617961) (-) (-)	Bihar	01/2014 (11/2016)	11/2019 (12/2026)	1,408.85 0.00	1,784.89	97.00
804	Rehabilitation and Upgrading to 2 lanes/2-lane with paved shoulders configuration and strengthening of of Birpur and Bihpur Section from km 0.0 to Km 106 of NH 106 under phase I of National Highways Interconnectivity Improvement Projects NHIIP ICB No. NHIIP-BR-106-7 [NHIIP-BR-106-7] (MoRTH) (617966) (-) (-)	Bihar	01/2014 (10/2016)	10/2019 (10/2026)	780.77 0.00	832.37	99.74
805	Construction of 4 Lane ROB and its approaches at the level crossing LC No 29 B of Km 29 Ekangarsarai at NH 110 New NH 33 & Railway Km 32.63 at Fatwa FUT Islampur IPR section in the state of Bihar on EPC mode. (MoRTH) (617969) (-) (-)	Bihar	03/2023 (07/2024)	07/2026 (12/2026)	201.08 0.00	57.98	62.00
806	Construction of Bhabhua Bypass from Ch. 10800Design Ch. 10800 to Ch. 19860 Design Ch. 18150 and Chand Bypass from Ch. 38060 Design Ch. 36250 to Ch. 40460 Design Ch. 38650 and widening of existing road to 2 - lane with Paved shoulder from Ch. 40460 Design Ch. 38650 to Ch. 46860 Design Ch. 45050 of NH-219 Total length-16.150 Kmunder EPC mode in the state of Bihar (MoRTH) (618004) (-) (-)	Bihar	02/2022 (06/2026)	12/2027 (12/2027)	179.86 0.00	30.54	3.00
807	Improvement to Two lane with Paved Shoulder from Junction of NH22 near Hajipur to Junction of NH -122 at Bachhwara via Mahnar and Mohiuddin Nagar from Km 0.00 to Km 29.730 of NH 122 B in the State of Bihar. (MoRTH) (618073) (-) (-)	Bihar	02/2024 (08/2024)	02/2026 (02/2027)	226.16 0.00	71.04	65.00
808	Pre construction activity of NH 122B from km 0 to 72.348 and Improvement to two lane with paved shoulders of NH 122B from km 29.730 to km 72.348 in state of Bihar under EPC mode (MoRTH) (618074) (-) (-)	Bihar	02/2022 (05/2023)	08/2026 (10/2026)	624.43 0.00	392.71	97.00
809	Improvement to two lane with paved shoulders of BH WB Border Amdabad Manihari section from design Km 0.000 to Km 23.945 of NH 131 A Total length 23.945 Km under EPC mode in the state of Bihar (MoRTH) (618080) (-) (-)	Bihar	01/2022 (05/2025)	11/2026 (06/2027)	353.27 0.00	512.40	8.00
810	construction of Four-Lane of chausa-Buxar Bypass from Km 45.000 to Km 65.915 Package - 2 in the State of Bihar on EPC Mode. (MoRTH) (618120) (-) (-)	Bihar	09/2022 (01/2026)	01/2028 (01/2028)	1,060.16 0.00	29.84	6.00



All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
811	Improvement to two lane with paved shoulders of NH-319A from km 0 to km 45 in state of Bihar under EPC mode (MoRTH) (618121) (-) (-)	Bihar	02/2022 (06/2023)	12/2024 (11/2026)	427.29 0.00	276.13	93.00
812	Pre-Construction activities from Km 134.000 to Km 190.233 of NH-333A and Construction of 4 no. of Bypasses at Katoria, Lakhpura, Banka & Panjwara total length-14.359 Km to two lane with paved shoulders standard in State of Bihar. (MoRTH) (618126) (-) (-)	Bihar	11/2022 (12/2024)	12/2026 (03/2027)	479.37 0.00	101.50	58.75
813	Estimate for Improvement to two lane with paved shoulder from Ramnagar to Roseda from km 3.500 to 43.000 of NH 527 E on EPC mode in State of Bihar (MoRTH) (618146) (-) (-)	Bihar	01/2022 (10/2024)	04/2026 (06/2027)	495.16 0.00	221.38	40.00
814	construction of a new 4 lane Parallel to existing MG Setu with its approaches from km 0.00 to km 14.500 across river Ganga on NH-19 at Patna in the state of Bihar. (MoRTH) (618228) (-) (-)	Bihar	02/2019 (03/2021)	09/2024 (12/2027)	2,926.42 0.00	1,721.72	75.79
815	Construction of a new 4-lane major bridge across river Kosi at Phulaut including Rehabilitation and upgradation of existing Birpur and Bihpur section of NH-106 from km 106.000 to km 136.000 to 2-lane with paved shoulders in the State of Bihar on EPC mode (MoRTH) (618234) (-) (-)	Bihar	09/2018 (06/2021)	06/2024 (02/2027)	1,478.40 0.00	1,323.35	99.00
816	Construction of New 4-Lane Bridge Parallel to existing Vikramashila Setu from km 8920 to Km 13375 including approach road 35m Naugachhia side & 53 m Bhagalpur side across River Ganga on newly declared NH-131B at Bhagalpur in the State of Bihar (MoRTH) (618246) (-) (-)	Bihar	07/2020 (05/2023)	05/2027 (03/2029)	1,110.23 0.00	522.58	52.60
817	Construction of 6-Lane Elevated / Extra Dose Cable Bridge on River Ganga parallel to & Western side of Digha-Sonepur Rail cum-Road Bridge of NH 139W in the State of Bihar (MoRTH) (618250) (-) (-)	Bihar	01/2024 (05/2024)	11/2027 (12/2028)	3,064.45 0.00	407.62	18.92
818	Improvement and Up gradation to four lane with Paved shoulder configuration from Existing Km 0000 to Km 39500 design km 0500 to Km 40342, Design length km of NH 227A near Mehrauna Ghat UP Bihar Border to Siwan on the state of Bihar on Hybrid Annuity Model HAM basis (MoRTH) (618251) (-) (-)	Bihar	03/2023 (09/2025)	03/2028 (03/2028)	1,661.25 0.00	209.87	10.03
819	Permanent rectification of 3 nos. of black spots in project Highway NH-27 of U.P border - Dewapur - Kotwa section from Km.360.915 to km.440.000 Total Length of 79.085 Km of NH-27 & Permanent rectification of 5 nos. of black spots of project Highway NH-27 of Kotwa - Mehsi - Muzaffarpur Section from km.440.000 to km.520.000 Total length 80.00Km (NHAI) (618571) (-) (-)	Bihar	04/2022 (12/2023)	12/2025 (12/2026)	227.25 0.00	233.89	83.01
820	6L Greenfield Varanasi-Ranchi-Kolkata Highway from Pachmon village to Anarbansalea village From KM. 116000 to KM. 151200 Package-6 (NHAI) (618725) (-) (-)	Bihar	03/2023 (09/2025)	09/2027 (09/2027)	1,915.99 0.00	439.98	24.87
821	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with Chandauli-Chainpur Road near Khainti village to junction with Bhabhua-Adhaura road near Palka village from Km. 27.000 to Km. 54.000 Pkg-2 (NHAI) (618726) (-) (-)	Bihar	03/2023 (10/2025)	10/2027 (10/2027)	1,240.93 0.00	252.45	26.77
822	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with Bhabhua-Adhaura road in Bhairampur village to Konki village From KM. 54.000 to KM. 90.000 Pkg-3 (NHAI) (618727) (-) (-)	Bihar	03/2023 (10/2025)	10/2027 (10/2027)	1,576.94 0.00	328.35	27.91
823	6L Bridge and its approaches across River Ganga as Part of Patna Ring Road NH-131G starting from Km 8.480 near Sherpur to Km 23.000 near Dighwara (NHAI) (618738) (-) (-)	Bihar	09/2022 (09/2023)	09/2027 (03/2029)	6,291.69 0.00	769.02	22.05
824	4L Greenfield Alignment of Amas to Shivrampur from 0.000 Km. to 55.002 Km. of NH 119 D Pkg-I (NHAI) (618739) (-) (-)	Bihar	02/2022 (03/2023)	03/2025 (07/2027)	1,390.92 0.00	642.43	54.80
825	4L Greenfield Alignment of Shivrampur to Ramnagar from Km. 55.002 to Km. 109.300 of NH 119 D Pkg-II (NHAI) (618740) (-) (-)	Bihar	02/2022 (07/2023)	07/2025 (11/2027)	1,494.31 0.00	706.06	50.80
826	4L Greenfield Alignment from Kalyanapur to Tal Dashraha of NH-119D Pkg-III (NHAI) (618741) (-) (-)	Bihar	03/2022 (02/2023)	02/2025 (03/2028)	1,857.58 0.00	957.50	36.25

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
827	Construction of 6-lane Greenfield corridor from Ramnagar to Kacchi Dargah NH-119D from Km 109700 to Km 122300, including widening of the existing NH-31 from Km 196700 to Km 198600, as part of the Amas-Darbhangha. (NHAI) (618742) (-) (-)	Bihar	01/2025 (04/2026)	04/2028 (04/2028)	1,113.46 0.00	13.38	0.80
828	Ara Bypass (NHAI) (618775) (-) (-)	Bihar	03/2025 (10/2025)	04/2027 (04/2027)	226.32 0.00	6.32	25.78
829	Construction of four laning of Bakarpur- Manikpur road section starting from village Chitarsenpur km 0000 and terminating at SH-74 near Manikpur 38814 at NH-139W under Bharatmalapariyona (NHAI) (618790) (-) (-)	Bihar	03/2023 (10/2024)	04/2027 (09/2027)	1,422.37 0.00	671.84	49.00
830	4L PS under NH configuration of Manikpur-Sahebganj of NH-139W (NHAI) (618791) (-) (-)	Bihar	10/2024 (01/2026)	12/2027 (12/2027)	1,538.76 0.00	599.90	27.50
831	Simaria Km. 206.050 to Khagaria Km. 266.282 (NHAI) (618840) (-) (-)	Bihar	12/2015 (10/2016)	04/2019 (12/2026)	664.02 0.00	816.96	97.73
832	4L Elevated Section and at-grade improvements at Begusarai town Simaria - Khagaria section from Km. 221.047 to Km. 225.302 of NH-31 (NHAI) (618841) (-) (-)	Bihar	10/2021 (06/2022)	12/2024 (10/2026)	491.04 0.00	354.71	96.20
833	Bakhtiyarpur-Rajauli Pkg-II from km. 54.405 to km.101.630 (NHAI) (618861) (-) (-)	Bihar	09/2020 (04/2021)	07/2023 (09/2026)	897.45 0.00	914.29	97.85
834	Bakhtiyarpur-Rajauli Pkg-III from km. 101.630 to km.152.520 (NHAI) (618862) (-) (-)	Bihar	09/2020 (12/2021)	06/2024 (09/2026)	2,156.22 0.00	1,823.64	99.14
835	Maheshkunt-Saharsa-Purnea Pkg I km 0.00 to km. 90.00 of NH-107 (NHAI) (618902) (-) (-)	Bihar	02/2017 (12/2019)	12/2021 (12/2026)	662.44 0.00	1,127.24	90.38
836	Maheshkunt -Saharsa-Purnea Pkg II (NHAI) (618903) (-) (-)	Bihar	03/2017 (12/2018)	12/2020 (09/2026)	1,245.33 0.00	1,261.02	94.00
837	Widening with additional 3L abetting Chhapra Bypass Section of NH-19 from Km. 143.200 to Km. 159.255 Pkg-1 (NHAI) (618905) (-) (-)	Bihar	02/2024 (08/2024)	08/2026 (10/2026)	470.50 0.00	318.83	77.28
838	4L Elevated Corridor and at-grade improvements from Design Ch0000 to Design Ch 19870 of Danapur Bihta Section, Design Ch0000 to Design Ch0231 connecting the existing RoB near Danapur station ,1.35 Km ramps and at-grade improvements to 4-lane section on Danapur side and Upgradation of existing Two lane carriageway to Four Lane carriageway from Design Ch19870 to Design Ch23500 of Bihta - Koilwar section (NHAI) (618914) (-) (-)	Bihar	10/2022 (03/2024)	09/2026 (08/2027)	4,432.97 0.00	1,650.59	63.91
839	4L Greenfield starting from NH-30 near Saristabad Patna to Nathupur Project end point of Patna-Gaya-Dobhi Section of NH-83 (NHAI) (618917) (-) (-)	Bihar	07/2023 (03/2024)	08/2025 (09/2026)	488.24 0.00	101.06	90.03
840	4L of Siwan- Masrakh section of Ram Janki Marg from Km 230.385 to Km 281.391 of NH-227A (NHAI) (618926) (-) (-)	Bihar	08/2022 (11/2024)	11/2026 (11/2028)	1,431.36 0.00	521.99	10.97
841	Umagaon-Saharsa Package-IV Koshi Bridge & approach Road - Bheja-Bakaur (NHAI) (618953) (-) (-)	Bihar	02/2019 (02/2020)	08/2023 (03/2027)	1,199.58 0.00	1,331.17	92.40
842	Umagaon - Saharsa Package - I Combined Umagaon-Kaluahi0.000KM to 21.609Km of NH227LSaharghat-Rahika0.000 Km to 26.130KM of NH227JRahika-Rampatti 0.00 KM to 15.00KM of NH527ABideshwarsthan-Bheja0.000KM to 25.915KM of NH527A. (NHAI) (618954) (-) (-)	Bihar	08/2022 (01/2025)	07/2027 (07/2027)	1,473.20 0.00	666.87	23.78
843	2L PS of Majhauri to Charout section from km. 0.00 to km. 63.655 (NHAI) (618955) (-) (-)	Bihar	01/2018 (11/2019)	11/2021 (09/2026)	638.29 0.00	1,104.68	99.80
844	Construction of Major Bridge over Baghmati and Lakhandei River along with Approaches from Design km.16.500 to km.21.500 (NHAI) (618956) (-) (-)	Bihar	02/2024 (10/2024)	04/2027 (03/2028)	498.97 0.00	57.79	26.84
845	4L of Greenfield Alignment from Km. 47.000 to Km. 89.210 of Balbhadarpur to Bela Nawda Section of NH-119D (NHAI) (619127) (-) (-)	Bihar	03/2022 (03/2024)	03/2026 (03/2028)	2,185.75 0.00	764.98	30.41

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
846	Rehabilitation and Upgradation of Chorma - Bairgania Section of National Highway No 227F to 2 lane with paved shoulders from Design Ch.0.000 to Ch. 34.566 (NHAI) (619136) (-) (-)	Bihar	06/2022 (02/2024)	01/2026 (09/2026)	610.78 0.00	340.56	100.00
847	Bakhtiyarpur Km 153.300 to Mokama Km 197.900 (NHAI) (619152) (-) (-)	Bihar	12/2015 (06/2017)	12/2019 (09/2026)	1,898.84 0.00	1,799.39	99.95
848	Umagaon-Saharsa Package-V Bakaur-Parsarma-Bangaon-Bariyahi & Spur to Mahishi (NHAI) (619166) (-) (-)	Bihar	10/2022 (12/2023)	12/2025 (09/2026)	768.35 0.00	509.34	99.50
849	4L of Munger Mirzachauki section from Munger to Kharia village junction from Km 69520 to Km 95580 Pkg-1 (NHAI) (619289) (-) (-)	Bihar	01/2021 (03/2022)	03/2024 (10/2026)	1,659.81 0.00	685.55	85.15
850	Construction of Approach Road to Rail-cum- Road Bridge across river Ganga at Munger Ghat NH-333 B (NHAI) (619301) (-) (-)	Bihar	07/2013 (12/2018)	05/2021 (09/2026)	537.88 0.00	574.02	99.99
851	4L of Munger Mirzachauki section from start of existing Bhagalpur bypass to Rasulpur from Km 125000 to Km 157350 Pkg-3 (NHAI) (619305) (-) (-)	Bihar	01/2021 (04/2022)	04/2024 (12/2026)	1,769.50 0.00	681.07	81.03
852	4L of Munger Mirzachauki section from Km 95580 to Km 125000 Pkg-2 (NHAI) (619306) (-) (-)	Bihar	02/2021 (03/2022)	03/2024 (09/2026)	1,020.84 0.00	643.08	95.90
853	4L of Hajipur-Muzaffarpur Section of the existing NH-77 from Km. 0000 Ramashish Chowk to Km. 46300 and new bypass starting at Km. 46300 and connecting NH-28 of E-W Corridor at Km. 515045 (NHAI) (619317) (-) (-)	Bihar	08/2010 (08/2010)	02/2013 (10/2026)	2,723.39 0.00	2,160.80	99.45
854	Bemetara Bypass NH 30 (MoRTH) (617908) (-) (-)	Chhattisgarh	01/2024 (04/2025)	04/2027 (04/2027)	161.96 0.00	38.39	45.00
855	Construction of 4 Nos Grade separator between km. 281.000 to km. 307.600 km. 286.400 kumhari km. 299.000 Transport Nagar km. 302.000 Power House km. 304.000 Chandra Moura Chowk to km. 305.000 supeia of NH-53 old NH-06 Raipur - Durg 4 Lane on EPC mode in the state of chhattisgarh job NO. NH-53old NH-06 CG-2017-18-56 (MoRTH) (617919) (-) (-)	Chhattisgarh	03/2018 (01/2019)	01/2021 (08/2025)	349.03 0.00	321.49	97.90
856	Up-gradation to Two/Four lane with paved shoulder Configuration of Kondagaon-Narayanpur from design ch. 0.00 - 48.693 Design Length 47.493 Km. 1.20 Km. retained on NH-130D under EPC mode in the State Chhattisgarh. (MoRTH) (617971) (-) (-)	Chhattisgarh	12/2022 (03/2025)	03/2027 (03/2027)	322.40 0.00	142.76	70.00
857	Upgradation to Two lane with Paved Shoulder Configuration of Narayanpur Kasturmeta pkg-II from design ch. 48.693 to 70.453 design length21.760 Km. on NH-130D under EPC mode in the state of Chhattisgarh. (MoRTH) (617972) (-) (-)	Chhattisgarh	12/2022 (12/2024)	06/2026 (-)	200.67 0.00	0.00	0.00
858	Upgradation of Ambikapur-Ramanujganj-Garwa road of NH-343, Package-III, Badki mahri village to Ramanujganj section from existing km 80.600 to km 110.330 Design Ch. 85.370 to Ch. 114.800 of total length 29.430 km to two lane with paved shoulders udner corridor scheme under EPC Mode in the of Chhattisgarh (MoRTH) (618014) (-) (-)	Chhattisgarh	03/2022 (05/2025)	10/2026 (10/2026)	199.05 0.00	76.70	38.56
859	Upgradation of Keonchi - Ratanpur Road of NH 45 Package-I, from design chainage km 237.860 to km 273.200 of length 35.340 km to two lane with paved shoulders under Corridor scheme on EPC mode in the state of Chhattisgarh. (MoRTH) (618015) (-) (-)	Chhattisgarh	03/2022 (07/2024)	01/2026 (12/2026)	225.41 0.00	99.10	60.00
860	Upgradation of Ambikapur Ramanujganj - Garhwa Road NH 343 of Package-I, Rajpuri Khurd Village to Padih Village section from existing km 7.830 to km 57.650 Design Ch. 13.700 to Ch. 62.700 of total length 49.00 km to two lane with paved shoulders under EPC mode in the state of Chhattisgarh (MoRTH) (618016) (-) (-)	Chhattisgarh	03/2022 (05/2025)	05/2027 (05/2027)	397.44 0.00	120.08	28.07
861	Upgradation of Keonchi - Ratanpur Road of NH 45 Package-II, from design chainage km 278.75 to km 321.348 of length 42.598 km to two lane with paved shoulders under Corridor scheme on EPC mode in the state of Chhattisgarh. (MoRTH) (618017) (-) (-)	Chhattisgarh	03/2022 (07/2024)	01/2026 (12/2026)	286.00 0.00	125.64	60.00

All Ongoing Projects							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
862	Upgradation of Bilaspur-Takhatpur-Mungeli-Pandariya-Pondi Road on N.H.-130A Package IIIA Takhatpur By-pass from existing Ch. 26.542 to 32.093 [Design Ch. 18.700 to 25.900] & Mungeli By-pass from existing Ch. 45.786 to 56.275 [Design Ch. 29.600 to 51.600] and Package IIIB Pandariya By-Pass from existing Ch. 82.582 to 87.133 [Design Ch. 77.900 to 81.1000 & Pondi By-pass from existing Ch. 103.166 to 104.756 [Design Ch. 97.000 to 103.395] to two lane with paved shoulder configuration in the (MoRTH) (618018) (-) (-)	Chhattisgarh	03/2022 (01/2024)	07/2025 (12/2026)	351.19 0.00	119.91	11.00
863	Durg-Raipur Bypass Section Package - 1 from km. 0.00 to km. 44.50 near Tendesara to near Khatti Village (NHAI) (618589) (-) (-)	Chhattisgarh	06/2022 (07/2023)	07/2025 (03/2027)	1,828.00 0.00	1,072.30	75.39
864	Durg-Raipur-Arang Package - 2 from km. 44.50 to km. 92.23 near Khatti Village to near Aurang (NHAI) (618590) (-) (-)	Chhattisgarh	06/2022 (06/2023)	05/2025 (03/2027)	1,958.90 0.00	1,009.65	73.96
865	4L of Bilaspur to Urga km 0.00 to 70.2 of NH-130A (NHAI) (618639) (-) (-)	Chhattisgarh	04/2020 (03/2022)	03/2024 (12/2026)	1,855.59 0.00	1,558.35	94.81
866	4L of Urga - Pathalgaon from Km. 70.200 to km. 157.745 of NH-130A (NHAI) (618640) (-) (-)	Chhattisgarh	03/2022 (02/2024)	08/2026 (10/2026)	2,261.30 0.00	1,121.30	81.50
867	4L of Pathalgaon-Kunkuri-CG/JH Border section of NH-43 from Km. 00.000 to Km.104.250 (NHAI) (618646) (-) (-)	Chhattisgarh	08/2024 (04/2026)	04/2029 (04/2029)	3,147.07 0.00	0.03	0.00
868	Development of 6L of Jhanki Sargi Section Road from km 0.000 to km 42.800 of NH-130CD Pkg-CG-1 (NHAI) (618673) (-) (-)	Chhattisgarh	11/2021 (09/2022)	09/2024 (02/2027)	1,368.19 0.00	715.41	99.41
869	Development of 6L Sargi Basanwahi Section from km 42.800 to km 99.500 of NH-130CD Pkg-CG-2 (NHAI) (618674) (-) (-)	Chhattisgarh	12/2021 (01/2023)	01/2025 (10/2026)	1,470.73 0.00	757.66	100.00
870	Development of 6L of Basanwahi Marangpuri Section from km 99.500 to km 124.661 of NH-130-CD (NHAI) (618675) (-) (-)	Chhattisgarh	03/2022 (10/2023)	10/2025 (03/2027)	1,307.16 0.00	518.96	70.73
871	4 laning of Champa - Korba from km 0.00 to km 38.2 (NHAI) (618957) (-) (-)	Chhattisgarh	02/2021 (01/2022)	01/2024 (10/2026)	1,002.33 0.00	944.79	98.75
872	Balance Works of Rehabilitation and Up gradation of NH-43 New NH-30 from Krn 162120 to Krn 173500 Length 11.380 Km. Keshkal Bypass 4-Lane with Paved shoulder in the State Of Chhattisgarh under NHDP-IV through Engineering, Procurement & Construction EPC Basis (MoRTH) (619039) (-) (-)	Chhattisgarh	06/2025 (06/2026)	06/2028 (-)	307.96 0.00	10.71	0.00
873	4/6 Laning of Raipur-Simga Pkg-I from km. 0.00 to km. 48.58 (NHAI) (619103) (-) (-)	Chhattisgarh	10/2015 (04/2016)	04/2018 (09/2026)	1,096.52 0.00	905.64	100.00
874	4 Laning with PS of Pathrapalli-Katghora km 53.3 to km 92.6 Pkg-II of Bilaspur Kathghora (NHAI) (619167) (-) (-)	Chhattisgarh	12/2019 (12/2020)	12/2022 (09/2026)	865.10 0.00	853.93	93.10
875	Balance Work Estimate of Rehabilitation and Up-gradation of NH- 43 from Km. 468.600 to Km. 531.250 Pathalgaon to kunkuri Section to two-lane with paved shoulder in the State of Chhattisgarh on SBD mode under NHO under Annual plan 2025-26 (MoRTH) (619347) (-) (-)	Chhattisgarh	03/2026 (06/2026)	06/2028 (-)	201.16 0.00	4.53	0.00
876	Widening of Existing Road from Intermediate Lane 2-lane to 4-lane Between Km 19.994 to Km 35.180 of NH-848A Rakholi-Khadoli-Velugam Section in U.T. of Dadra and Nagar Haveli and Daman and Diu (MoRTH) (619183) (-) (-)	Dadra & Nagar Haveli and Daman & Diu	10/2022 (02/2024)	06/2026 (09/2026)	198.06 0.00	173.71	92.00
877	Development of 6L UER II [Package - I] NH-1 Near Bakoli till Karala Kanjhawala Road from km. 0.70 to km.15.00 (NHAI) (618509) (-) (-)	Delhi	07/2020 (10/2021)	10/2023 (09/2026)	2,089.94 0.00	1,835.63	99.99
878	Dwarka Expressway from Km -0.600 to Km 5.300 - Pkg-I Shivmurti Chowk-RuB near Dwarka Sector 21 (NHAI) (619202) (-) (-)	Delhi	03/2018 (09/2020)	09/2022 (09/2026)	2,144.67 0.00	3,560.87	98.80

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
879	4-Laning from End of Zuari approaches to Start of Margao Bypass section of NH-66 from Km 536.800 to Km 543.450 (MoRTH) (617941) (-) (-)	Goa	07/2024 (02/2026)	02/2028 (02/2028)	398.25 0.00	1.47	1.12
880	Construction of Six lane Elevated Corridor from Km. 508.000 to Km. 513.150 including approaches on NH-66 (MoRTH) (617942) (-) (-)	Goa	04/2023 (04/2024)	04/2026 (10/2026)	641.46 0.00	484.35	100.00
881	4-laning of Navelim to Cuncolim Section of NH-66 from Km 554.245 to Km 561.480 on HAM Mode (MoRTH) (617943) (-) (-)	Goa	12/2024 (04/2026)	10/2028 (10/2028)	746.75 0.00	1.25	0.00
882	Construction of 4L Flyover from MES College Junction to Bogmalo Junction on NH-566 from Km. 7.106 to Km. 10.460 and 4L VUP at Queeny Nagar Junction from Km. 3.330 to Km. 4.550 (NHAI) (618609) (-) (-)	Goa	01/2024 (08/2024)	07/2026 (05/2027)	463.08 0.00	182.85	59.18
883	Up-gradation of Dhoraji-Jamkandorna-Kalavad Section of NH-927D from Design Chainage km 0/00 to km 58/115 to Two lane with PS configuration in the State of Gujarat on EPC (MoRTH) (617906) (-) (-)	Gujarat	10/2022 (01/2025)	01/2027 (01/2027)	246.60 0.00	0.00	35.00
884	Work of 6 laning/Construction of elevated corridor from km 0/0 to 10/170 Narol Junction to Sarkhej junction including 4 lane Shastri Bridge on Sabarmati river on NH 47 in the State of Gujarat on HAM mode (MoRTH) (617916) (-) (-)	Gujarat	03/2024 (08/2025)	02/2028 (02/2028)	1,295.39 0.00	179.40	40.00
885	Construction of new 4 lane major bridge with approaches on Sabarmati River near Dharoi at Km. 82/00 to 86/00 Design length 3.300 km on NH-58 in the State of Gujarat on Hybrid Annuity Mode HAM (MoRTH) (617926) (-) (-)	Gujarat	03/2024 (08/2025)	08/2027 (08/2027)	398.40 0.00	97.73	58.00
886	Widening to 2LPS between Km 0/0 to 56/0 Khokhara Gujarat Border Vijayanagar Antrasuba Mathasur road of NH 58 in the State of Gujarat (MoRTH) (617927) (-) (-)	Gujarat	03/2024 (09/2025)	09/2027 (09/2027)	699.19 0.00	76.36	36.00
887	Widening 2 lane to 4-lane from KM 92/320 to Km 115/320 Vav Chokdi-Satlasana to to Vrundavan Chokdi, Kheralu on NH-58 in the State of Gujarat. (MoRTH) (617928) (-) (-)	Gujarat	03/2022 (03/2024)	03/2026 (08/2026)	151.13 0.00	151.29	100.00
888	Work of development and construction of elevated corridorfrom km 38/660 to km 42/690 Iscon junction to start point of approach of sanand flyover of NH-147 in the sate of Gujarat (MoRTH) (617976) (-) (-)	Gujarat	03/2023 (06/2024)	06/2026 (09/2026)	530.20 0.00	380.24	92.00
889	Upgradation to two lane with paved Shoulder Configuration from Km. 0/00 to 47/000 of NH 351 Mahuva to Badhada section in the State of Gujarat (MoRTH) (618022) (-) (-)	Gujarat	12/2022 (02/2024)	08/2025 (03/2027)	173.06 0.00	125.54	77.00
890	Upgradation of Mehsana-Visnagar-vadnagar-Kheralu-Idar section from km 0/00 to 81/300 of NH 168G Mehsana to Idar in the State of GujaratTotal Length 81.300 Km on Hybrid Annuity Mode HAM (MoRTH) (618107) (-) (-)	Gujarat	02/2024 (12/2025)	06/2028 (06/2028)	1,155.21 0.00	141.84	23.00
891	Up-gradation and strengthening to 2lanePS from Km 95/500 to km 129/775 of Nh 168G Idar-Bhiloda-Samlaji in the state of Gujarat Length 34.275 km (MoRTH) (618108) (-) (-)	Gujarat	09/2022 (12/2023)	12/2025 (03/2027)	237.28 0.00	180.90	65.00
892	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-26 Ch.696890 to Ch.726390 (NHAI) (618459) (-) (-)	Gujarat	09/2020 (12/2022)	08/2024 (02/2027)	1,555.20 0.00	1,308.08	85.50
893	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-31 Ch.824920 to Ch.844382 [Junction near Pratap nagar Village - Junction near Dodka Village] (NHAI) (618462) (-) (-)	Gujarat	11/2019 (05/2021)	05/2023 (09/2026)	1,644.85 0.00	1,298.04	100.00
894	Vadodara Mumbai Expressway Kim to Ankleshwar Phase IA - Pkg V (NHAI) (618463) (-) (-)	Gujarat	02/2018 (11/2019)	10/2021 (09/2026)	1,324.84 0.00	1,547.27	91.34
895	Vadodara Mumbai Expressway Karvad - Jujuwa from Km. 128.000 to Km. 154.600 Phase-I Package-IX (NHAI) (618467) (-) (-)	Gujarat	07/2023 (04/2024)	10/2025 (07/2027)	2,594.17 0.00	238.42	21.75
896	Balance work of Six Laning of Shamlaji-Motachiloda from Km. 401.200 to Km.494.410 section Design Chainage Km.447.385 to Km 540.595, Length- 93.210 Km of old NH-8 NH-48 in the state of Gujarat on single Percentage Item Rate Contract (NHAI) (618507) (-) (-)	Gujarat	06/2024 (08/2024)	06/2025 (09/2026)	466.80 0.00	581.28	91.83

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
897	Construction of Additional Structures including Approaches in Vadodara Surat Section of NH48 between existing Km. 108.000 to Km. 250.000 (<i>NHAI</i>) (618508) (-) (-)	Gujarat	03/2024 (01/2025)	01/2027 (06/2027)	907.39 0.00	376.84	48.73
898	6L with PS of Samakhiyali to Santalpur section from km. 339.700 to Km. 430.100 of NH-27 (<i>NHAI</i>) (618564) (-) (-)	Gujarat	01/2023 (12/2023)	12/2025 (03/2027)	1,553.76 0.00	29.11	64.52
899	Sanchole - Santalpur from km 99.000 - km 130.073 of NH-754K AJ-RGBS-Package-4 (<i>NHAI</i>) (618615) (-) (-)	Gujarat	02/2020 (03/2021)	03/2023 (09/2026)	778.15 0.00	767.89	99.70
900	4L of Dhrol bypass section of NH-151A Approx. length 5.7 Km & widening upto 4 laning of missing link of Amran section of NH-151A Approx. length 6.55 Km from existing Ch. 42000 to 48500 of ongoing Dhrol-Bhadra-Pipaliya section of NH-151A (<i>NHAI</i>) (618616) (-) (-)	Gujarat	03/2024 (02/2025)	02/2027 (02/2027)	625.58 0.00	166.02	35.47
901	Upgradation to 4L PS from Bhimasar, Junction of NH-41 to Anjar- Bhuj upto Airport Junction from Km 0.000 to Km 65.478 of NH-341 (<i>NHAI</i>) (618787) (-) (-)	Gujarat	03/2022 (01/2023)	06/2025 (03/2027)	1,373.06 0.00	837.99	96.00
902	4L PS Divided Carriageway from Patan Near Rajpur to Gojariya From Km 52.000 to Km 128.940 of NH-68 (<i>NHAI</i>) (618901) (-) (-)	Gujarat	12/2021 (03/2023)	03/2025 (05/2027)	1,181.34 0.00	949.71	87.12
903	4L PS from Ch. 94.030 in Jabugam Village to Ch. 132.320 in Dhamasiya Village of NH-56 Pkg-III (<i>NHAI</i>) (618930) (-) (-)	Gujarat	03/2023 (11/2025)	11/2027 (11/2027)	1,188.46 0.00	180.01	25.82
904	4L PS from Ch. 179.780 in Bitada/Movi Village to Ch. 208.900 in Nasarpore Village of NH-56 Pkg-V (<i>NHAI</i>) (618931) (-) (-)	Gujarat	03/2023 (11/2025)	11/2027 (11/2027)	764.02 0.00	111.34	10.85
905	Construction of 4 lane with PS Idar-Badoli bypass section from design km 81/300 to km 95/500 of NH 168G in the State of Gujarat (<i>MoRTH</i>) (619061) (-) (-)	Gujarat	03/2025 (05/2026)	05/2028 (05/2028)	705.09 0.00	92.49	8.00
906	Widening to 6L of Existing 4L Jetpur - Gondal - Rajkot Section from Km. 117.600 to Km. 185.00 on NH-27 (<i>NHAI</i>) (619087) (-) (-)	Gujarat	03/2022 (09/2023)	09/2025 (01/2027)	2,070.44 0.00	1,144.50	76.83
907	Four Laning of Una to Kodinar from km. 180.478 to km. 221.610 Package-V (<i>NHAI</i>) (619145) (-) (-)	Gujarat	02/2016 (02/2017)	08/2019 (03/2025)	877.71 0.00	1,008.73	100.00
908	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-27 Ch.729.700 to Ch.756.052 (<i>NHAI</i>) (619197) (-) (-)	Gujarat	09/2020 (02/2022)	02/2024 (09/2026)	1,185.69 0.00	1,051.39	98.90
909	Construction of 6 lane Elevated Structure along with its approaches from Km. 142.000 to Km 144.800 Total Length 2.80 km Gondal on NH27 in the state of Gujarat (<i>NHAI</i>) (619273) (-) (-)	Gujarat	02/2026 (06/2026)	06/2028 (06/2028)	262.28 0.00	0.06	0.00
910	Development of 4-lane with paved shoulders from Budhel Junction to Vartej Y-Junction Km 0900 to Km 9400 on EPC mode under NHO in the State of Gujarat (<i>NHAI</i>) (619276) (-) (-)	Gujarat	12/2025 (07/2026)	12/2027 (12/2026)	247.34 0.00	65.09	0.00
911	Upgradation of Existing Two Lane Carriageway to Two Lane Carriageway with Paved Shoulder from Ch. 665686 Existing Km. 665.686 in Khanpur Village in Vansda Taluka to Ch. 710470 Existing Km. 710.483 in Karvad Village in Vapi Taluka Length 44.784 Km Section of NH-56 in the State of Gujarat on EPC Mode (<i>NHAI</i>) (619297) (-) (-)	Gujarat	02/2026 (07/2026)	07/2028 (07/2028)	647.20 0.00	9.24	0.00
912	Delhi-Amritsar-Katra Expressway Phase-I Pkg-I from Jussur Kheri on NH-KMP Expressway to Junction with Rohtak-Panipat road NH-709 near Rukhi Paani village Km 0000 to Km 34000 (<i>NHAI</i>) (618482) (-) (-)	Haryana	12/2020 (12/2021)	12/2023 (07/2026)	1,866.49 0.00	1,609.72	99.91
913	Delhi-Amritsar-Katra Expressway Phase-I Pkg-II from Junction with Rohtak-Panipat road NH-709 near Rukhi Paani village to Junction with Jind-Panipat road NH-352A near Gangana village Km 34000 to Km 60800 (<i>NHAI</i>) (618483) (-) (-)	Haryana	12/2020 (01/2022)	01/2024 (07/2026)	1,533.87 0.00	1,176.23	99.89
914	Construction of Additional Structures, Improvement of Service Road & Maintenance of Six Lane Gurgaon-Jaipur Section of NH-48 old NH-8 between km 42700 to km 107100 in the State of Haryana (<i>NHAI</i>) (618506) (-) (-)	Haryana	05/2024 (05/2025)	05/2027 (05/2027)	401.74 0.00	143.18	61.38

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
915	Gohana - Sonipat PKG-2 (NHAI) (618580) (-) (-)	Haryana	01/2019 (07/2020)	07/2022 (07/2026)	1,275.31 0.00	1,225.85	97.86
916	4L Greenfield Jalbhera Shahbad section from km. 0.000 to km. 22.850 of NH-152G (NHAI) (618788) (-) (-)	Haryana	03/2022 (06/2023)	05/2025 (09/2026)	927.22 0.00	550.77	87.05
917	4L Bhiwani-Hansi road section of NH-148B (NHAI) (618792) (-) (-)	Haryana	11/2022 (12/2023)	12/2025 (11/2026)	1,330.23 0.00	493.13	99.50
918	Jagadhari - Tajewala from Km -0.175 to 32.337 km of NH-344 (NHAI) (618936) (-) (-)	Haryana	03/2022 (02/2023)	02/2025 (03/2027)	1,269.50 0.00	725.04	68.00
919	4L PS of Ambala Ring Road of New NH-44 (NHAI) (619080) (-) (-)	Haryana	02/2023 (10/2023)	10/2025 (09/2026)	1,093.35 0.00	601.46	92.97
920	4L of Jind-Gohana road Package-1 from km. 0.00 to km. 40.601 of NH-352 A under NHO (NHAI) (619092) (-) (-)	Haryana	01/2019 (07/2020)	07/2022 (07/2026)	994.22 0.00	1,064.47	99.97
921	4/6L of Gurgaon - Pataudi - Rewari from km. 0.00 to km.43.87 of NH-352W (NHAI) (619132) (-) (-)	Haryana	05/2020 (11/2021)	11/2023 (09/2026)	1,810.04 0.00	1,282.66	77.76
922	Karnal ring road Lot-4/Pkg-1 (NHAI) (619201) (-) (-)	Haryana	11/2022 (08/2023)	08/2025 (10/2026)	1,741.45 0.00	834.86	96.66
923	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 166.000 to 203.77 net Length 37.770 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618215) (-) (-)	Himachal Pradesh	06/2021 (06/2024)	06/2027 (06/2027)	274.36 0.00	60.73	25.30
924	Improvement/construction of existing CL-5 Road to NH Intermediate lane specification with hard shoulder from Km 133.000 to 166.000 net Length 33.000 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh on EPC mode under project Deepak, BRO (MoRTH) (618216) (-) (-)	Himachal Pradesh	03/2021 (07/2023)	06/2026 (09/2027)	230.55 0.00	75.92	23.24
925	Improvement/construction of existing Class-5 Road to NH Intermediate lane specification with hard shoulder from existing Km 76/340 to 134/940 Design chainage from Km 76/300 to 133/000 net Length 56.700 kms of NH-505 Sumdo-Kaza-Gramphoo road in the state of Himachal Pradesh Package I (MoRTH) (618217) (-) (-)	Himachal Pradesh	03/2021 (05/2023)	05/2026 (08/2027)	314.67 0.00	141.55	62.28
926	Rehabilitation and Upgradation to 2-lane configuration of Kalwahn-Mandi Section km 208.950 to 250.592 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-3 (MoRTH) (618230) (-) (-)	Himachal Pradesh	08/2020 (10/2022)	04/2025 (12/2026)	314.32 0.00	140.98	70.74
927	Rehabilitation and Upgradation to 2-lane configuration of Hamirpur-Karnohal Section km 141.00 to 181.00 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-1 (MoRTH) (618231) (-) (-)	Himachal Pradesh	08/2020 (06/2022)	12/2024 (09/2026)	371.93 0.00	252.54	93.62
928	Rehabilitation and Upgradation to 2-lane configuration of Karnohal- Kalwahn Section km 181.00 to 208.950 of NH-70 in the State of Himachal Pradesh under Green National Highways Corridor Project GNHCP with the loan assistance of World Bank on EPC mode.Package-2 (MoRTH) (618232) (-) (-)	Himachal Pradesh	08/2020 (11/2023)	05/2026 (12/2026)	251.62 0.00	121.55	58.00
929	Construction of missing link from Birhu to Lathiani from Km 35/550 Design chainage Km 0.000 to Km 42/800 Design Chainage Km 8.153on NH-503A including Lathiani Bridge on back water of Govindsagar and its approaches in Himachal Pradesh. (MoRTH) (618253) (-) (-)	Himachal Pradesh	06/2023 (03/2026)	03/2029 (03/2029)	870.95 0.00	100.56	5.80
930	Nerchowk km 190.000 to Pandoh including Pandoh bypass km221.305 (NHAI) (618850) (-) (-)	Himachal Pradesh	03/2016 (01/2018)	07/2020 (09/2026)	1,464.12 0.00	1,559.30	100.00
931	Pandoh bypass 221.305 to Takoli 242.000 of NH-21 in the state of Himachal Pradesh (NHAI) (618851) (-) (-)	Himachal Pradesh	06/2017 (03/2018)	09/2021 (03/2027)	3,419.95 0.00	2,887.37	95.65
932	4L Sundar Nagar Bypass from Km.173.900 to Km.179.600 of NH-21 (NHAI) (618852) (-) (-)	Himachal Pradesh	02/2022 (06/2022)	06/2024 (09/2026)	191.11 0.00	182.64	100.00

All Ongoing Projects						AUGUST 2026	
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
933	Rehabilitation and Upgradation to 4L configuration & Strengthening of Sihuni to Rajol from Km 51.000 to Km 72.000 of NH-154 Package-IIA (NHAI) (618878) (-) (-)	Himachal Pradesh	03/2022 (09/2023)	09/2025 (09/2026)	696.65 0.00	496.72	99.18
934	Rehabilitation and Upgradation to 2L PS configuration & Strengthening of Padhar to Bijni section from Km 180.000 to Km 202.815 of NH-154 Pkg-VA (NHAI) (618879) (-) (-)	Himachal Pradesh	06/2022 (11/2024)	11/2026 (11/2026)	930.86 0.00	667.09	99.86
935	Rehabilitation and Up-gradation to 4L configuration & Strengthening of Thanpuri to Paror section from Km 85.135 to Km 100.840 of NH-154 Pkg-IIC (NHAI) (618880) (-) (-)	Himachal Pradesh	07/2022 (03/2024)	12/2025 (04/2027)	815.68 0.00	497.44	56.61
936	4L PS bijni to mandi section from Km 202.815 to Km 208.000 of NH-20 New NH-154 of Pathankot-Mandi Package-VB (NHAI) (618881) (-) (-)	Himachal Pradesh	02/2023 (03/2025)	09/2027 (09/2027)	1,113.02 0.00	592.16	35.30
937	Rehabilitation and Up-gradation of existing road to 2L PS from End of Hamirpur Bypass near Chilbahal to Bhangbar section from Km. 138.295 to Km.175.270 of NH-88 Pkg-IV (NHAI) (618888) (-) (-)	Himachal Pradesh	03/2022 (04/2023)	04/2025 (12/2026)	1,146.19 0.00	987.51	97.20
938	4L of Bhangbar Near Ranital to Kangra Bypass Section of Old NH-88 New NH-303,503 up to Intersection with NH-154 from Km 175.270 to Km 193.400 Pkg-VB (NHAI) (618889) (-) (-)	Himachal Pradesh	03/2021 (12/2022)	12/2024 (12/2026)	1,322.95 0.00	1,103.47	97.45
939	2L PS of Hamirpur Bypass from Km 121.175 to Km.138.295 of NH-103&3 (NHAI) (618890) (-) (-)	Himachal Pradesh	08/2022 (10/2023)	10/2025 (12/2026)	739.39 0.00	370.02	94.37
940	4L PS from Kalar Bala Village to Nauni Chowk of NH 205 from Km 41.000 to Km 58.450 (NHAI) (618891) (-) (-)	Himachal Pradesh	01/2024 (05/2025)	05/2027 (09/2027)	1,244.43 0.00	145.82	31.46
941	4 Lane with Paved Shoulder from Dareota Village to Kalar Bala NH 205, Design Chainage -Km 33185 to Km 41000, Design Length-7.815 Km Package-IIB (NHAI) (618892) (-) (-)	Himachal Pradesh	06/2025 (06/2026)	06/2028 (06/2028)	992.85 0.00	5.28	0.68
942	4L of Kathlighat to Shakral Village from Km 128.835 to Km 146.300 of NH- 5 Shimla Bypass - Pkg I (NHAI) (618921) (-) (-)	Himachal Pradesh	03/2022 (04/2023)	04/2026 (07/2027)	1,703.48 0.00	1,211.34	64.20
943	4L of Shakral Village to Dhalli Section from Km 146.300 to Km 156.560 Shimla Bypass - Pkg II and Shimla connectivity from Km 0.000 to Km 0.725 of NH-5 (NHAI) (618922) (-) (-)	Himachal Pradesh	04/2022 (03/2024)	03/2027 (12/2027)	1,956.26 0.00	1,537.77	59.88
944	Solan - Kaithlighat Section of NH-22 Now NH-5 from Km. 106.139 to Km.129.05 (NHAI) (619003) (-) (-)	Himachal Pradesh	03/2018 (11/2018)	05/2021 (11/2026)	881.74 0.00	1,348.35	90.11
945	4L of HP/Punjab Border - Mo from km. 11.00 to km. 42.00 of Old NH-20 New NH-154 Package-IA (NHAI) (619153) (-) (-)	Himachal Pradesh	03/2021 (05/2022)	05/2024 (12/2026)	1,002.11 0.00	837.74	68.65
946	Construction of Shopian Bypass on NH-444 taking off from existing chainage Km 36500 and re-joining at km 47588 of existing Chainage New Design Ch. From km 28000 to km 36925 as 2- lane with paved shoulder in the UT of Jammu & Kashmir on EPC mode. (MoRTH) (618038) (-) (-)	Jammu and Kashmir	03/2024 (01/2026)	01/2028 (-)	547.47 0.00	194.18	5.00
947	Widening and strengthening to 2 lane with paved shoulder from existing Ch. Km 56720 to Km 100820 and Design Ch. From Km 62600 to Km 106360 Total Length43.760 Km on road SRINAGAR -BARAMULA URINH-01 in the UT of Jammu & Kashmir under project BEACON, Border Roads Organization BRO on EPC mode. (MoRTH) (618201) (-) (-)	Jammu and Kashmir	09/2023 (11/2024)	11/2026 (06/2027)	702.10 0.00	188.08	52.95
948	Construction of 2 lane with paved shoulders Baramulla Bypass Greenfield bypass from existing Ch. Km 47020 to Km 56720 and Design Ch. From 48500 to 62600 Total length 14.100 km on road Srinagar Baramulla Uri NH-01 in the UT of Jammu & Kashmir under Project.Package-III (MoRTH) (618202) (-) (-)	Jammu and Kashmir	03/2023 (09/2024)	09/2026 (07/2027)	992.43 0.00	502.59	48.80
949	Construction of 4 lane with paved shoulder Pattan bypass Greenfield bypass from existing Ch. Km 24320 to Km 33760 and Design Ch. from Km 24400 to Km 35300, total length 10.900 km on road SrinagarBaramulla Uri NH-01 in the UT of Jammu & Kashmir under Project BEACON, Border Roads Organization BRO on EPC mode. Package-II (MoRTH) (618203) (-) (-)	Jammu and Kashmir	03/2023 (08/2024)	07/2026 (02/2027)	980.21 0.00	538.31	62.50

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
950	Construction of realignment between Pandrass- Pashkyun Total length 27.10 km on road Zozila-Kargil -Leh NH-1 to 2 lane specifications i.e. Drass alignment 9.30 km Kharboo realignment 6.30 km & Kargil alignment 11.50 km under project Vijayak BRO in the UT of Ladakh on EPC Mode (MoRTH) (618204) (-) (-)	Jammu and Kashmir	11/2021 (06/2023)	06/2025 (07/2027)	426.15 0.00	118.68	54.89
951	Construction of 4 lane with paved shoulder from Existing Ch. 14200 to 24320 Design Ch. 14200 to 24400, Ch. 33760 to 42780 Design Ch. 35300 to 44294 & Ch. 43440 to 47020 Design Ch. 44958 to 48500 Delina Flyover including construction of flyover length 1.704 km of total length 22.736 kms in AOR of 760 BRTF on road SRINAGAR BARAMULA URI NH-01 in the UT of Jammu & Kashmir under project BEACON, Border Roads Organization BRO Package-IJob No NH-1-J&K-2022-23-110 (MoRTH) (618205) (-) (-)	Jammu and Kashmir	06/2022 (08/2023)	08/2025 (12/2026)	823.46 0.00	547.50	87.60
952	Widening and Strengthening of Rafiabad-Kupwara-Chowkibal-Tangdhar-Chamkot NH-701 road from design Ch. From 0000 to 51000 to two lanes with paved shoulders under Project Beacon in the UT of Jammu & Kashmir on EPC mode Package-I. (MoRTH) (618206) (-) (-)	Jammu and Kashmir	03/2024 (11/2024)	05/2027 (-)	1,404.94 0.00	530.41	49.55
953	Rehabilitation and upgradation to 2 lane with paved shoulder from existing chainage Km 166.100 to Km 192.98 design chainage Km 146.700 to Km 162.800 including construction of Bhimber Gali Tunnel Total Length of Tunnel 1.100 Km under 31 BRTF on Akhnoor-Poonch Roads on EPC mode NH-144A Package-VII (MoRTH) (618221) (-) (-)	Jammu and Kashmir	09/2021 (07/2024)	07/2026 (07/2027)	734.64 0.00	243.21	60.00
954	Widening and Strengthening up gradation to 2 lane with paved shoulder from existing chainage Km 192.98 to Km 229.820 design chainage Km 162.800 to Km 198.18 under 31 BRTF on Akhnoor-Poonch Road NH-144A in the UT of Jammu and Kashmir under Project Sampark Border Roads Organisation BRO on EPC Mode Package-VIII Job No NH-144A-J&K-2022-2023-111 (MoRTH) (618222) (-) (-)	Jammu and Kashmir	10/2022 (01/2024)	01/2026 (03/2027)	562.45 0.00	158.68	71.27
955	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 64535 to km 85385 Design chainage km 55800 to km 74350 under 13 TF on Akhnoor-Poonch road NH-144A under Project Sampark BRO in the UT of Jammu & Kashmir on EPC mode Package-III Job no NH-144A-J&K-2019-20-79 (MoRTH) (618223) (-) (-)	Jammu and Kashmir	03/2020 (09/2021)	09/2023 (12/2026)	152.93 0.00	137.09	90.06
956	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 49150 to km 64535 Design chainage km 46.450 to km 55.800 including construction of Sungal Tunnel Total length of Tunnel 2.79 km under 13 TF on Akhnoor-Poonch road NH-144A under Project Sampark BRO in the UT of Jammu & Kashmir on EPC mode Package-II Job no NH-144A-J&K-2019-20-78 (MoRTH) (618224) (-) (-)	Jammu and Kashmir	03/2020 (08/2021)	08/2024 (09/2026)	796.97 0.00	575.21	99.00
957	Rehabilitation and up-gradation to 2 lane with paved shoulder from existing chainage km 134950 to km 166100 Design chainage km 116980 to km 146700 under 31 TF on Akhnoor-Poonch road NH-144A in the UT of Jammu & Kashmir under Project Sampark BRO on EPC mode Package-VI Job no NH-144A-J&K-2021-22-106 (MoRTH) (618225) (-) (-)	Jammu and Kashmir	07/2021 (07/2022)	07/2024 (12/2026)	395.25 0.00	283.64	89.20
958	Rehabilitation and upgradation to 2 lane with paved shoulder from existing chainage Km 30.053 to Km 49.150 design chainage Km 30.000 to Km 46.450 including Kandi Tunnel under 31 BRTF on Akhnoor-Poonch Road NH-144A Under Project Sampark in the UT of Jammu & Kashmir EPC modePackage-I Job no NH-144A-J&K-2020-21-83. (MoRTH) (618226) (-) (-)	Jammu and Kashmir	07/2020 (11/2022)	11/2024 (12/2026)	272.49 0.00	200.42	95.27
959	Up-gradation to 2-lane with Paved Shoulder from Km 12.850 to Km20.300 of 7.450Km length on Goha-Khellani section and a link road to Goha village of 2.016 km on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-1 (NHIDCL) (618394) (-) (-)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (10/2026)	228.39 0.00	183.30	94.26
960	Construction & Upgradation to 2-lane with paved shoulder from Design Ch. Km 51700 at Premnagar km 66315 to Km 66535 New Thatri at Start of Km 83rd, Tunnel Km 82665 of 14.835 Km design length on Chenani-Sudhmahadev-Goha Khellani-Kishtwar-Vailoo Donipawa-Ashajipora section of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg - 2 (NHIDCL) (618395) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2023 (06/2027)	512.43 0.00	164.66	53.49
961	Widening and Up-gradation to 2-Lane with Paved Shoulder of configuration and geometric improvement from Km 0.000 to Km 16.990 on Chenani Sudhmahadev section of NH-244 in UT of Jammu and Kashmir to be executed on EPC basis (NHIDCL) (618397) (-) (-)	Jammu and Kashmir	03/2018 (11/2018)	11/2020 (12/2025)	255.90 0.00	240.59	94.06
962	Up-gradation to 2-lane with Paved Shoulder from Km 20.300 to Km 29.030 of 8.730 Km length on Goha-Khellani section on NH-244 in UT of Jammu and Kashmir on EPC Mode Package II (NHIDCL) (618398) (-) (-)	Jammu and Kashmir	07/2020 (10/2020)	04/2022 (06/2026)	210.79 0.00	190.26	96.95



All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
963	Construction of Kishtwar bypass with 2 lane with paved shoulder from Design Km. 80.675 Dulhasti to km 95.550 Bandarkoot of 14.88 km & a link road to Kishtwar town from 0000 to 1.871 of length1.871 Km on Khellani - Kishtwar - Chattroo section in UT of Jammu and Kashmir on EPC Mode Pkg-4 (NHIDCL) (618399) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	08/2023 (12/2027)	859.67 0.00	363.24	50.64
964	Construction & Upgradation to 2-lane with paved shoulder from Design Km 67.805 at the end of Km 83rd Tunnel near Dhrabshalla Ex. Km 83905 to Km 80.675 start of Kishtwar Bypass - Dulhasti Ex. Km 970751 of 12.870 Km length on chenani-Sudhmahadev-Goha Khellani-Kishtwar-vailoo-Donipawa-Ashajipora seition of NH-244 in the UT of J&K on EPC Mode under NHO-Gen Pkg-3 (NHIDCL) (618400) (-) (-)	Jammu and Kashmir	03/2021 (07/2021)	12/2022 (08/2025)	398.51 0.00	120.09	98.55
965	Up-gradation to 4-lane with Paved Shoulder of Jammu-Akhnoor road section of NH-144A from Ganesh Vihar Km 6.000 to Khati Chowk Km 26.350 in UT of Jammu and Kashmir on EPC basis Pkg-3A (NHIDCL) (618406) (-) (-)	Jammu and Kashmir	03/2018 (07/2019)	07/2021 (11/2026)	322.49 0.00	410.94	93.15
966	Jammu-Akhnoor Road Pkg-I (NHIDCL) (618407) (-) (-)	Jammu and Kashmir	03/2018 (01/2023)	01/2025 (10/2026)	245.30 0.00	115.31	75.29
967	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XV [Junction with Hiranagar Road near village Gurha Baildaran to Junction with Jammu Ring Road NH-244A near Jakh village from Km 468100 to Km 503250] (NHAI) (618494) (-) (-)	Jammu and Kashmir	10/2021 (09/2022)	09/2024 (12/2026)	2,714.95 0.00	1,848.00	90.01
968	4/6L Access Control Expressway from Design Chainage Km 515.000 to 528.300 Kunjwani to Sidhra Section of NH-44 and from Design Chainage Km 550.900 to Km 566.520 Domel to Katra Section Phase II-Package XVII (NHAI) (618495) (-) (-)	Jammu and Kashmir	06/2022 (06/2023)	06/2025 (11/2027)	2,894.74 0.00	1,017.24	66.74
969	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XVI Existing Jakh Vijaypur-Kunjwani section of NH-44 including spur Connectivity to Jammu Airport NH-144A [Km 503500 to km 514500] (NHAI) (618496) (-) (-)	Jammu and Kashmir	09/2021 (09/2022)	09/2024 (09/2026)	1,821.72 0.00	1,242.70	94.14
970	Delhi Amritsar Katra Expressway Phase-II Pkg XVIII Development and Upgradation of Four lane Access Control Expressway from Design Chainage KM 530.00 to KM 545.300 Sidhra to Domel Section of NH-44 (NHAI) (618497) (-) (-)	Jammu and Kashmir	12/2022 (11/2023)	11/2025 (06/2027)	1,025.73 0.00	670.32	70.17
971	4L Ring road/bypass around Srinagar city from km 0.000 to km 42.100 Phase-I (NHAI) (618541) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2024 (10/2026)	2,919.96 0.00	1,873.52	89.00
972	4L of existing Wayul Ganderbal Pandach Soura section of old NH-1 as a part of Srinagar Ring Road Phase IIA (NHAI) (618542) (-) (-)	Jammu and Kashmir	12/2024 (05/2026)	05/2028 (05/2028)	827.98 0.00	265.20	0.02
973	4L of twin tube tunnel configuration including approaches from Marog to Digdol from Km.154.210 to Km.158.650 North Bound and from Km.155.940 to Km.160.260 South Bound of Ramban to Banihal Pkg-I of Old NH-1A New NH-44 (NHAI) (618543) (-) (-)	Jammu and Kashmir	07/2021 (08/2022)	08/2025 (12/2027)	1,912.17 0.00	425.31	30.50
974	4L twin tube tunnel including approaches from Digdol to Khuni Nallah North Bound connecting with existing major bridge on NB and South Bound connecting with Tunnel T4 ,Single tube tunnel of Ramban to Banihal Pkg-II of Old NH-1A New NH-44 (NHAI) (618544) (-) (-)	Jammu and Kashmir	07/2021 (02/2022)	06/2024 (09/2026)	1,401.87 0.00	1,071.33	87.10
975	4L of Km.165.092 to Km.171.855 North Bound and from Km.166.895 to Km.173.638 South Bound, excl. certain reaches of North Bound and South Bound of Ramban to Banihal Pkg-III of Old NH-1A New NH-44 (NHAI) (618545) (-) (-)	Jammu and Kashmir	07/2021 (02/2022)	08/2024 (06/2027)	614.48 0.00	312.38	42.80
976	2L NH-1 from km 8.660 to km 33.775 Sumbal to Wayul to 4L dual carriageway NH standard as part of Srinagar Ring Road PhaseII [Design Ch. 41.907 to Ch. 66.609] (NHAI) (618547) (-) (-)	Jammu and Kashmir	11/2022 (12/2023)	06/2026 (03/2027)	961.00 0.00	484.85	55.02
977	Construction of twin tube tunnels on Jammu Kashmir Ring Road NH-244A Between Design Ch. 50600 to 51700 and design Ch. 53535 to 55700 on EPC mode under residual NHDP component of Bharatmala Pariyojna (NHAI) (618549) (-) (-)	Jammu and Kashmir	11/2022 (06/2023)	06/2025 (12/2026)	242.65 0.00	678.54	83.87
978	Corridor Efficiency Improvement including removal of black spots in Lakhanpur - Samba section of NH-44 from Chainage Km. 16.300 to Km. 74.100 (NHAI) (618550) (-) (-)	Jammu and Kashmir	06/2022 (12/2022)	06/2024 (12/2026)	855.74 0.00	204.92	74.63

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
979	Upgradation and Strengthening of Chenani to Nashri Section via Patnitop of NH244 from Km 0.000 to Km 39.100 (NHAI) (618967) (-) (-)	Jammu and Kashmir	03/2024 (08/2024)	08/2026 (03/2027)	295.06 0.00	210.02	64.88
980	Construction/upgradation to 2-lane with paved shoulder from Design Km 95.55 Bandarkoot to Km. 111.06 Chattroo of 15.52 Km length on Khellani-Kishtwar-Chattroo section on NH-244 in UT of Jammu and Kashmir on EPC Mode Pkg-5 (NHIDCL) (619038) (-) (-)	Jammu and Kashmir	03/2021 (08/2021)	02/2023 (03/2026)	497.09 0.00	270.82	99.97
981	Widening and Strengthening of existing paveemnt to two lane with paved shoulders from km 116.00 to km 176.355 of NH-75E in the State of Jharkhand on EPC mode. (MoRTH) (618060) (-) (-)	Jharkhand	01/2022 (01/2023)	07/2024 (10/2026)	315.21 0.00	169.76	90.00
982	Construction of bypass around Lohardaga town of NH-143A in the Sate of Jharkhand under EPC mode. (MoRTH) (618083) (-) (-)	Jharkhand	02/2022 (01/2024)	01/2026 (09/2026)	458.78 0.00	116.23	5.00
983	Widening to 2-lane with paved shoulder from km 0.00 to 44.00 Kuru-Ghaghra section of NH-143A including re-construction of culverts and bridges. (MoRTH) (618084) (-) (-)	Jharkhand	02/2020 (08/2021)	08/2023 (10/2026)	153.01 0.00	108.00	95.00
984	Construction of 2- Lane with paved shoulder from km 56.45 Dharampur More to 93.050 Pakur of NH-333A in the State of Jharkhand on EPC mode (MoRTH) (618127) (-) (-)	Jharkhand	03/2023 (11/2025)	05/2027 (05/2027)	255.73 0.00	32.78	15.00
985	Widening and Reconstruction to 4-lane/4-lane with service road including structures from Pokharia More at Km 47.600 Ex. Km 50.230 to Govindpur at km 62.949 Ex. Km 65.325 of Nh-419 in the State of Jharkhand on EPC mode. (MoRTH) (618242) (-) (-)	Jharkhand	05/2022 (01/2024)	01/2026 (01/2027)	300.46 0.00	175.68	56.31
986	Construction of Six lane elevated flyover including reconstruction/rehabilitation of existing pavement from Km 426230 to Km 430500 Length 4.27 Km at Nirsa in the Barwa Adda Panagarh section of NH-19 from Km.398.240 to Km.521.120 including Panagarh Bypass in the State of Jharkhand on EPC Mode. (NHAI) (618534) (-) (-)	Jharkhand	01/2025 (02/2026)	08/2028 (08/2028)	470.75 0.00	1.43	0.00
987	Construction of Six lane elevated flyover including reconstruction/rehabilitation of existing pavement from Km 406100 to Km 411150 Length 5.05 Km at Gobindpur area in the Barwa Adda Panagarh section of NH-19 from Km.398.240 to Km.521.120 including Panagarh Bypass in the State of Jharkhand on EPC Mode. (NHAI) (618535) (-) (-)	Jharkhand	01/2025 (09/2025)	03/2028 (03/2028)	687.77 0.00	80.51	19.91
988	4 Lane of CG/JH Border-Gumla from km 0.000 to km 32.370 of NH-43 in the State of Jhrkhand (NHAI) (618641) (-) (-)	Jharkhand	08/2024 (02/2026)	02/2028 (02/2028)	1,325.80 0.00	341.47	9.76
989	4L of Palma to Gumla from km. 26.00 to km. 89.170 of NH-23 (NHAI) (618642) (-) (-)	Jharkhand	03/2020 (04/2022)	03/2024 (10/2026)	1,882.93 0.00	1,372.27	99.90
990	4L of Ormanjhi-Gola section from Km 81.450 to Km 53.600 of NH- 320BPKG-II (NHAI) (618644) (-) (-)	Jharkhand	02/2022 (06/2023)	06/2025 (12/2026)	1,214.93 0.00	995.16	86.57
991	4L of Gola-BokaroJaina More section from Km 53.600 to Km 21.110 of NH-320PKG-1 (NHAI) (618645) (-) (-)	Jharkhand	02/2022 (06/2023)	06/2025 (10/2026)	1,007.97 0.00	627.94	78.10
992	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Donoreshan village to junction with NH-20 in Bongabar village from km 288.600 to km 325.500 Pkg -11 (NHAI) (618729) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1,856.12 0.00	284.44	0.00
993	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Deoria village to Donoreshan village from km 253.000 to km 288.600 Pkg -10 (NHAI) (618730) (-) (-)	Jharkhand	03/2023 (05/2026)	05/2028 (05/2028)	1,546.27 0.00	223.12	5.65
994	6 Lane Greenfield Varanasi- Ranchi- Kolkata Highway from Chatra to junction with NH- 100 in Deoria village from km 222.000 to km 253.000 Pkg -9 (NHAI) (618731) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1,418.16 0.00	148.74	0.00
995	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-20 in Bongabar village to junction with NH-30 in Lepo village from km 325.500 to km 358.500 Pkg -12 (NHAI) (618733) (-) (-)	Jharkhand	03/2023 (07/2026)	07/2028 (07/2028)	1,525.52 0.00	253.03	0.10
996	4L Elevated corridor of Kalimandir-Dimna Chowk-Baliguma Jamshedpur Section of NH-33 New NH-18 from km 241940 to km 251961 Length 10.021 km (NHAI) (618736) (-) (-)	Jharkhand	03/2024 (09/2024)	03/2027 (03/2027)	936.26 0.00	346.55	49.50

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
997	Grade separated Interchanges at Km. 113.730 junction with Ranchi Hazaribagh Road & Km. 139.225 junction with Ranchi Jamshedpur road on 4L Ranchi Bypass of NH-33 (NHAI) (618737) (-) (-)	Jharkhand	01/2025 (12/2025)	12/2027 (12/2027)	303.53 0.00	6.01	0.00
998	4L from Km 147.450 Bhogu to Km 196.870 Sankha on NH-75 Sec-III (NHAI) (618830) (-) (-)	Jharkhand	10/2022 (11/2023)	11/2025 (03/2027)	1,517.87 0.00	1,131.66	76.95
999	4L from Km 95.400 Udaipura to Km 147.450 Bhogu on NH-75 Sec-II (NHAI) (618831) (-) (-)	Jharkhand	03/2023 (10/2024)	10/2026 (03/2027)	1,436.80 0.00	419.79	29.20
1000	4L from Km 55.00 Kuru to Km 95.400 Udaipura on NH-75 Sec-I (NHAI) (618832) (-) (-)	Jharkhand	02/2024 (01/2026)	01/2028 (01/2028)	1,274.82 0.00	253.66	11.10
1001	Barhi-Koderma Section of NH31 km 0.00 - km 27.5 (NHAI) (618863) (-) (-)	Jharkhand	02/2017 (11/2019)	08/2024 (09/2026)	662.44 0.00	828.10	98.50
1002	4L of NH-80 from km 215.00 to km 260.00 Mirza Chauki to Farkka Pkg-I (NHAI) (618947) (-) (-)	Jharkhand	03/2018 (12/2021)	07/2023 (10/2026)	1,504.80 0.00	1,038.78	91.83
1003	4L of Basukinath- Deoghar Section of NH-114A (NHAI) (618949) (-) (-)	Jharkhand	09/2022 (12/2023)	12/2025 (09/2026)	1,444.94 0.00	781.51	90.53
1004	Construction of Bypass to NH-114A Connecting NH-333 and NH-133 Deoghar Bypass from design km 0.000 to design Km 49.000 (NHAI) (618950) (-) (-)	Jharkhand	11/2024 (01/2026)	01/2028 (01/2028)	1,565.47 0.00	106.35	12.00
1005	Construction of bypass around Chatra Town on NH-22 old NH-99 in the state of Jharkhand under EPC Mode (MoRTH) (619005) (-) (-)	Jharkhand	03/2023 (01/2026)	01/2028 (01/2028)	235.42 0.00	44.83	14.00
1006	Construction of Elevated corridor from Km. 135.650 to 136.300 on 63, from Km. 249 to Km. 250.050 on old NH-4 and from Km. 192.910 to Km. 193.350 on NH-218 from decongestion of traffic in Ranichennamma circle in Hubli city in the state of Karnataka on EPC basis (MoRTH) (617935) (-) (-)	Karnataka	08/2020 (06/2021)	06/2024 (11/2026)	298.00 0.00	262.05	65.00
1007	Construction of Srinivasapura Bypass from existing Km 453.890 Design Ch. 0000 to existing Km 461.450 Design Ch 10080 on NH-69 in the State of Karnataka Under NH O in EPC mode under Annual Plan 2022-23 NH-69-KNT-2022-23-966 dated 22.11.2022 (MoRTH) (617950) (-) (-)	Karnataka	11/2022 (07/2025)	01/2027 (01/2027)	204.42 0.00	55.06	25.00
1008	Construction of Chintamani Bypass from Design Ch.0000 Existing Ch.428880 to Design Ch.15400 Existing Ch.444010 on NH-69 in the State of Karnataka in EPC Mode under NHO Annual Plan 2022-23. NH-69-KNT-2022-23-989 dated 24.03.2023 (MoRTH) (617951) (-) (-)	Karnataka	03/2023 (01/2026)	07/2027 (07/2027)	314.55 0.00	65.75	15.00
1009	Widening to two lane with paved Shoulders from Km 40.00 to Km 75.00 Existing chainages of Mangalore - Tumkur section of NH-73 in the State of Karnataka on EPC Mode under Annual Plan 2021-22 Job No NH-73-KNT-2021-22-945 (MoRTH) (617955) (-) (-)	Karnataka	03/2022 (03/2023)	03/2025 (12/2026)	718.52 0.00	522.66	86.00
1010	Construction of Major Bridge at Km.180.865 across river Krishna on NH 167 Hagari Jadcherla section (MoRTH) (617989) (-) (-)	Karnataka	03/2019 (05/2019)	11/2021 (04/2027)	157.32 0.00	16,713.20	69.00
1011	Widening of existing 2 lane to 4 lane with paved shoulder from Designed km 25.15 to km 56.70 Except Km 52.70 to 53.50 of NH-169 Nellisara Camp to Thirthahalli of NH-169 on Shimoga-Mangalore section in the state of Karnataka on EPC mode under Annual plan 2022-23 NH-169-KNT-2022-23-978 dated 08.03.2023 (MoRTH) (617997) (-) (-)	Karnataka	03/2023 (02/2026)	02/2028 (02/2028)	538.71 0.00	90.45	6.00
1012	Widening to existing 2 lane with paved Shoulder to 4 Lane with paved shoulder from design Km 153.00 to 168.27 Mala Gate to Karkala of NH -169 on Shimoga - Mangalore section in the state of Karnataka on EPC mode under Annula Plan 2021-22 Job No. NH-169-KNT-2021-22-949 (MoRTH) (617998) (-) (-)	Karnataka	03/2022 (02/2023)	02/2025 (11/2026)	177.94 0.00	135.57	83.00
1013	Widening to 2LPS from Km 67 to Km 115 on Kadur-Hosadurga section NH 173 in the state of Karnataka NH-173-KNT-2022-23-980 dated 13.03.2023 (MoRTH) (617999) (-) (-)	Karnataka	03/2023 (10/2024)	05/2026 (04/2027)	471.62 0.00	230.91	74.79

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1014	Widening to 2LPS from Km 71.00 to 104.00 Existing chainages Sarjapur to Pattadakallu on Bhanapur to Gaddanakeri section NH-367 in the State of Karnataka under NHO on EPC mode under Annual Plan 2022-23 NH-367-KNT-2022-23-972 dated 08.02.2023 (MoRTH) (618027) (-) (-)	Karnataka	02/2023 (03/2024)	03/2026 (12/2026)	445.62 0.00	255.52	90.00
1015	Construction of Bypass at Kuknoor, Yelburga, Gajendragada of Bhanapur Gaddanakeri section of NH-367 in the State of Karnataka under NHO on EPC mode under Annual Plan 2022-23. NH-367-KNT-2022-23-973 dated 08.02.2023 (MoRTH) (618028) (-) (-)	Karnataka	02/2023 (06/2025)	06/2027 (06/2027)	333.96 0.00	147.67	36.00
1016	Widening to 4 lane from Km. 133.00 to 158.04 design Chainage Km. 130.88 to 155.145 Shirur Cross to Gaddankeri of NH-367 in the State of Karnataka on EPC mode. Job No. NH-367-KNT-2021-22-930 (MoRTH) (618029) (-) (-)	Karnataka	01/2022 (01/2023)	01/2025 (03/2027)	350.69 0.00	253.15	83.33
1017	Balance work of Construction of Two/Four lane with paved shoulder from Km 422.000 to 523.600 Chitradurga to Shivamogga of NH-13 in the state of Kanataka on EPC mode. (MoRTH) (618031) (-) (-)	Karnataka	01/2021 (12/2021)	12/2025 (08/2026)	516.96 0.00	386.50	98.00
1018	Widening to Two Lane with Paved Shoulders from KB Cross to Chunchanahalli ie., Design Ch. 485240 Km Existing Km 494.000 to Design Ch. 523393 Km Existing km 533.152 & From Design Ch. 530393 Existing Km 540.175 to Design Ch. 534476 Existing Km 544.200 at Nelligere of NH-150A on EPC mode under Annual Plan 2022-23 NH-150A-KNT-2022-23-977 dated 08.03.2023 (MoRTH) (618086) (-) (-)	Karnataka	03/2023 (07/2025)	01/2027 (01/2027)	617.28 0.00	135.24	48.60
1019	Widening to intermediate/two lane to 2 lane with paved shoulder from Existing chanages Km 112.750 to 142.00 Liingasur to Mudabal cross & from Km. 147.070 to Km. 149.070 Maski city limit of Jewargi Chamrajnagar setion of NH-150A in the state of Karnataka on EPC mode. Job No. NH-150A-KNT-2021-22-951 (MoRTH) (618087) (-) (-)	Karnataka	03/2022 (01/2023)	07/2024 (09/2026)	255.88 0.00	201.76	98.00
1020	Widening to Two Lane with Paved Shoulders from Km 0.00 Design Chainage 0.00 to Km 23.338 Design Chainage 23310 of NH-166E MH/KNT Border- Kanamadi- Bijjargi-Tikota section in the state of Karnataka in EPC Mode under Annual plan 2022-23 NH-166E-KNT-2022-23-974 (MoRTH) (618095) (-) (-)	Karnataka	02/2023 (09/2024)	03/2026 (03/2027)	196.05 0.00	82.41	75.00
1021	Widening to 4 lane from Km 51.60 to 76.20 Hebri to Parkala and from Km 85.20 to 88.90 Karavali junction to Malpe of Thirthahalli-Udupi-Malpe Section of NH-169A in the State of Karnataka on EPC Mode under Annual plan 2021-22 Job No. NH-169A-KNT-2021-22-927 (MoRTH) (618109) (-) (-)	Karnataka	01/2022 (12/2022)	12/2024 (11/2026)	355.72 0.00	269.80	88.33
1022	Widening to 2 Lane with Paved Shoulders from design Km 103.200 Existing Km 103.200 to design Km 116.700 Existing Km 118.470 on AP/KNT Border to Sira Section of NH-544E in the State of Karnataka on EPC mode under Annual plan 2022-23 (MoRTH) (618147) (-) (-)	Karnataka	01/2023 (03/2024)	09/2025 (12/2026)	166.58 0.00	85.43	75.00
1023	Widening to 4LPS of NH-548B from Km 80.000 Near Murgundi to Km 140.200 Near Chikkodi excluding length from Km 118.450 to Km 128.450 in the State of Karnataka under NH O on EPC Mode under Annual Plan 2022-23 - Package 1 NH-548B-KNT-2022-23-979 dated 09.03.2023 (MoRTH) (618148) (-) (-)	Karnataka	03/2023 (04/2026)	04/2028 (04/2028)	785.79 0.00	128.84	6.00
1024	Widening to two lane with paved shoulders from Km 0.00 to 102.310 Design Chainage of NH-548B Murrum-Maharashtra Border in the State of Karnataka (MoRTH) (618149) (-) (-)	Karnataka	02/2023 (01/2025)	01/2027 (01/2027)	957.09 0.00	400.01	63.10
1025	Widening to 4LPS of NH-548B from Km 118.450 Near Shirguppi to Km 128.450 Near Ankali in the State of Karnataka under NH O on EPC Mode Under Annual Plan 2022-23 NH-548B-KNT-2022-23-982 (MoRTH) (618151) (-) (-)	Karnataka	03/2023 (05/2026)	05/2029 (-)	1,084.29 0.00	100.04	0.00
1026	Construction of 2 Lane with paved shoulder from km 55.6 to km 90.7 existing chainages of NH-766C complete Realignment of 13.76 km with 2 major Bridges across Sharavathi Backwaters on EPC mode under Annual Plan 2022-23 in the state of Karnataka NH-766C-KNT-2022-23 dated 14.10.2022 (MoRTH) (618184) (-) (-)	Karnataka	01/2023 (02/2024)	02/2026 (12/2027)	313.56 0.00	185.30	65.00
1027	Widening to 2LPS from Km 0.000 to 37.850 Except Ex. Km 24.45 to 27.20 of NH-766c Byndoor-Ranebennur Section in the state of Karnataka on EPC Mode under Annual Plan 2022-23 NH-766C-KNT-2022-23-969 dated 30.12.2022 (MoRTH) (618185) (-) (-)	Karnataka	12/2022 (08/2025)	08/2027 (08/2027)	394.95 0.00	36.96	12.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1028	Widening to two lane with paved shoulder of NH-73New spur road Ujire - Dharmasthala - Periyashanthi in the State of Karnataka under NHO on HAM Mode Job No. NH-73Spur-KNT-2023-24-996 (MoRTH) (618189) (-) (-)	Karnataka	01/2024 (11/2025)	11/2027 (11/2027)	613.65 0.00	64.40	27.50
1029	4/6L of Bangalore - Pune Section of bypass connecting Dharwad - Hubli from km. 403.80 to km. 433.20 (NHAI) (618517) (-) (-)	Karnataka	12/2021 (03/2023)	09/2025 (05/2027)	1,135.39 0.00	744.44	83.80
1030	Davanagere - Haveri of NH-48 Old NH-4 from km. 260.00 to km. 338.923 (NHAI) (618518) (-) (-)	Karnataka	01/2017 (01/2018)	07/2020 (12/2026)	1,454.67 0.00	1,273.62	98.87
1031	4L of km 0.00 to km 42.00 of Dobbaspeta to Doddaballapura Bypass section of NH-648 old NH-207] [Bangalore Ring Road Pkg 1] (NHAI) (618520) (-) (-)	Karnataka	08/2020 (04/2021)	04/2023 (09/2026)	1,438.74 0.00	1,285.16	99.20
1032	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 26.000 to Km. 97.000 in Gulbarga of NH-150C Pkg-II (NHAI) (618630) (-) (-)	Karnataka	02/2022 (12/2022)	06/2025 (12/2026)	2,355.56 0.00	1,017.39	81.35
1033	4 Lane with PS from Des. Ch 228.500 to Des. Ch. 273.400 of Belgaum-Hungund-Raichur Section of NH 748 A Package-6 (NHAI) (618649) (-) (-)	Karnataka	03/2023 (11/2024)	11/2026 (06/2027)	1,246.15 0.00	412.78	56.93
1034	4 Lane with PS from Des. Ch 89.900 to Des. Ch. 136.100 of Belgaum-Hungund-Raichur Section of NH-748A Package-3 (NHAI) (618650) (-) (-)	Karnataka	01/2024 (04/2025)	04/2027 (03/2028)	1,363.90 0.00	316.73	24.50
1035	4 Lane with PS from Des. Ch 43.800 to Des. Ch. 89.900 of Belgaum-Hungund-Raichur Section of NH-748A Package-2 (NHAI) (618651) (-) (-)	Karnataka	02/2024 (03/2025)	02/2027 (07/2027)	1,427.88 0.00	606.24	58.70
1036	4LPS Access Controlled Highway of Bellary Bypass Balance work from Ch. 254750 to Ch. 266837 and construction of 4LPS from Ch. 277.690 to Ch. 278.690 at D. Hirehal Village Balance work of NH 150A of Bellary Byrapura Section (NHAI) (618697) (-) (-)	Karnataka	02/2024 (08/2024)	07/2026 (11/2027)	626.01 0.00	126.00	38.97
1037	4L of Addahole Near Gundya to Bantwal Cross section Pkg-02 from Design Km 270.270 to Design km 318.55 including flyover at Kalladka Town including approaches from Km. 311.57 to Km. 313.67 of NH-75 Old NH-48 (NHAI) (618702) (-) (-)	Karnataka	12/2020 (11/2021)	11/2023 (04/2027)	1,660.19 0.00	1,452.45	94.21
1038	Bangalore-Nidagatta Pkg. I (NHAI) (618706) (-) (-)	Karnataka	02/2018 (05/2019)	11/2021 (09/2026)	3,496.01 0.00	4,315.20	99.19
1039	Additional works under BM1 to ensure road safety under 6L of Bengaluru Mysuru Access control with close toll from Km.17.300 to Km.136.300 of NH-275 (NHAI) (618707) (-) (-)	Karnataka	11/2024 (01/2026)	01/2028 (05/2028)	738.37 0.00	32.83	12.67
1040	4L of Left-Over Works of Hospet-Bellary -Karnataka/AP border from Km.280.080 Dec.Ch. to Km.375450Des.Ch. of NH-63 New-67 (NHAI) (618709) (-) (-)	Karnataka	03/2023 (05/2023)	05/2025 (04/2028)	1,340.15 0.00	948.93	92.51
1041	Belakeri Port to Kumta - Sirsi road from km 0.00 - km 4.265 of Belekeri Port Road Link Rd. and km 4.965 - km 60.00 of SH-69 (NHAI) (618799) (-) (-)	Karnataka	03/2018 (12/2020)	12/2022 (11/2026)	440.16 0.00	476.34	95.23
1042	4L PS from near Hemmige Village Periyapatna - Hassan Road Jn. to near Hunsur - KR Nagar Jn section from Km. 144.900 to Km. 169.000 of NH-275 Pkg. III (NHAI) (618870) (-) (-)	Karnataka	02/2023 (04/2025)	04/2027 (02/2028)	883.62 0.00	447.20	27.80
1043	4L PS from Near Guddehosur to Start of Kushalnagara Bypass to near Hemmige Village Periyapatna - Hassan Road Jn from Km. 122.200 to Km. 144.900 of NH-275 Pkg. II (NHAI) (618871) (-) (-)	Karnataka	02/2023 (12/2025)	12/2027 (05/2028)	909.86 0.00	328.35	14.53
1044	4L PS from near Hunsur - KR Nagar Junction to near Yalachahalli village KR Nagara - Yelawala Road Junction ffrom Km 169.000 to Km 195.550 of NH-275 Pkg-IV (NHAI) (618872) (-) (-)	Karnataka	02/2023 (04/2025)	04/2027 (04/2028)	1,062.76 0.00	286.32	19.58
1045	4L PS from near Yalachahalli village KR Nagara - Yelawala Road junction to Srirangapatna Bypass Near Paschima Vahini from km 195.550 to Km 214.535 of NH-275 Pkg-V (NHAI) (618873) (-) (-)	Karnataka	01/2023 (04/2025)	04/2027 (04/2028)	1,272.71 0.00	466.92	17.36

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1046	4L of Bettadahalli- Shivamogga section from Km.170.415 to km. 226.750 of NH-206 Tumkur- Shivamogga Pkg-IV (NHAI) (618887) (-) (-)	Karnataka	01/2019 (10/2021)	10/2023 (03/2027)	2,082.98 0.00	1,645.31	84.20
1047	4L of Sannur to Bikarnakatte section from Km 691.350 to Km 736.362 of NH-169 Karkala - Mangalore Package-III (NHAI) (618896) (-) (-)	Karnataka	03/2021 (10/2022)	10/2024 (04/2027)	1,386.41 0.00	1,257.12	76.10
1048	4L Expressway from Km 26.400 to km 53.500 of Malur to Bangarpet section of Bangalore-Chennai Expressway Phase-I Package-II (NHAI) (619065) (-) (-)	Karnataka	12/2020 (09/2021)	09/2023 (09/2026)	1,745.00 0.00	1,103.62	99.80
1049	Tumkur - Nelamangala 6L (NHAI) (619071) (-) (-)	Karnataka	03/2021 (08/2022)	08/2025 (03/2027)	2,032.15 0.00	1,094.39	61.36
1050	Bangalore/TN border to Hoskote (NHAI) (619072) (-) (-)	Karnataka	02/2022 (02/2023)	02/2025 (11/2026)	1,181.68 0.00	1,154.93	94.89
1051	4L of 42.000 to km 80.00 of Dodaballapur Bypass to Hoskote section of NH-648 Old NH-207 [Bangalore Ring Road Pkg 2] (NHAI) (619073) (-) (-)	Karnataka	02/2020 (02/2021)	02/2023 (09/2026)	1,317.74 0.00	1,360.42	99.20
1052	Goa / Karnataka Km.93.700 to Kundapur Km.283.30 (NHAI) (619096) (-) (-)	Karnataka	07/2012 (03/2014)	08/2016 (12/2026)	1,644.92 0.00	1,849.54	97.94
1053	4 Lane with PS from Des. Ch 182.300 to Des. Ch. 228.500 of Belgaum-Hungund-Raichur Section of NH 748 A Package-5 (NHAI) (619106) (-) (-)	Karnataka	03/2023 (11/2024)	11/2026 (08/2027)	1,141.88 0.00	270.91	40.63
1054	4 Lane with PS from Des. Ch 136.100 to Des. Ch. 182.300 of Belgaum-Hungund-Raichur Section of NH-748A Package-4 (NHAI) (619107) (-) (-)	Karnataka	02/2024 (09/2025)	09/2027 (04/2028)	1,311.41 0.00	244.01	15.00
1055	4 Lane with PS from Des. Ch 0.000 to Des. Ch. 43.800 of Belgaum-Hungund-Raichur Section of NH-748A Package-1 (NHAI) (619108) (-) (-)	Karnataka	02/2024 (06/2025)	06/2027 (11/2027)	1,452.43 0.00	509.43	40.21
1056	Hassan km 184.912 to Maranahally km 230.060 of NH - 75 in Karnataka (NHAI) (619117) (-) (-)	Karnataka	12/2015 (03/2017)	03/2019 (09/2026)	1,021.57 0.00	1,073.87	97.80
1057	Nidagatta-Mysore Pkg II (NHAI) (619120) (-) (-)	Karnataka	02/2018 (12/2019)	06/2022 (09/2026)	2,919.80 0.00	3,717.48	99.19
1058	Yekkambi-Haveri (NHAI) (619138) (-) (-)	Karnataka	09/2021 (03/2022)	03/2024 (03/2028)	294.62 0.00	94.93	24.70
1059	BRT Tiger Reserve Boundary Km.287.500 to Bangalore Section Km.458.420 of NH-209 in Karnataka (NHAI) (619150) (-) (-)	Karnataka	04/2016 (08/2017)	08/2019 (09/2026)	2,082.69 0.00	2,243.04	99.70
1060	Belgaum-Khanapur Pkg I Km 0.000-Km 30.800 of NH-4A (NHAI) (619164) (-) (-)	Karnataka	03/2018 (03/2019)	09/2021 (03/2027)	1,214.30 0.00	917.83	75.72
1061	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 97.000 to Km. 162.500 in Yadgir of NH-150C Pkg-III (NHAI) (619211) (-) (-)	Karnataka	03/2022 (04/2023)	10/2025 (03/2027)	2,104.70 0.00	1,003.62	73.90
1062	4L of Channarayapatna Bypass and Hassan Bypass with structures in Devihalli - Hassan section (NHAI) (619214) (-) (-)	Karnataka	04/2020 (01/2021)	01/2023 (02/2027)	688.00 0.00	617.61	82.34
1063	4L Tumkur-Shimoga Pkg-I from Mallasandra to Karadi village of NH-206 from Km. 12.300 to Km. 65.195 (NHAI) (619218) (-) (-)	Karnataka	02/2018 (10/2019)	10/2021 (09/2026)	1,364.14 0.00	1,336.55	100.00
1064	4L of Tumkur-Shimoga Pkg-II from Km 65.195 Karadi to Km 121.900 Banawara of NH-206 (NHAI) (619219) (-) (-)	Karnataka	02/2018 (10/2019)	10/2021 (12/2026)	1,505.85 0.00	1,299.97	99.98
1065	Tumkur-Shimoga Pkg-III from Km 121.900 Banawara to Km 170.415 Bettadahalli of Old NH-206 (NHAI) (619220) (-) (-)	Karnataka	02/2018 (03/2021)	03/2023 (12/2026)	1,444.50 0.00	876.08	98.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1066	Widening to 2 Lanes with paved shoulders from Km.87/000 to 133/720 Nattukal to Thanau Jn. in Palakkad of NH-966 Old NH-213 on EPC mode Basis under NHO Annual Plan 2016-17 in the state of Kerala (NHAI) (618070) (-) (-)	Kerala	02/2017 (08/2017)	08/2019 (06/2026)	294.28 0.00	0.00	98.00
1067	6L of Chengala - Neeleshwaram from km. 56.200 to km. 93.468 (NHAI) (618595) (-) (-)	Kerala	06/2020 (10/2021)	04/2024 (03/2027)	1,746.45 0.00	1,455.92	90.82
1068	6L of Taliparamba to Muzhappilangad from Km 134.650 to Km 170.6 of NH-66 (NHAI) (618596) (-) (-)	Kerala	08/2020 (11/2021)	05/2024 (01/2028)	2,714.60 0.00	2,020.57	83.70
1069	6L of Azhiyur-Vengalam from km. 189.200 to km. 230.400 of NH-66 (NHAI) (618597) (-) (-)	Kerala	10/2020 (10/2021)	07/2024 (03/2028)	3,205.77 0.00	2,428.32	60.07
1070	6L Minor Bridge Paloli Palam at km. 203.160 & Major Bridge Morad at km. 204.895 and allied works (NHAI) (618598) (-) (-)	Kerala	03/2020 (12/2020)	06/2022 (09/2026)	210.00 0.00	190.47	100.00
1071	6L of Ramanatukkara Junction to start of Valanchery bypass section of NH-66 (NHAI) (618599) (-) (-)	Kerala	01/2021 (01/2022)	07/2024 (09/2026)	4,919.46 0.00	3,764.41	100.00
1072	6L of Valanchery bypass to Kappirikkad of NH 66 from km. 298500 to km 335850 (NHAI) (618600) (-) (-)	Kerala	02/2021 (01/2022)	07/2024 (09/2026)	4,023.94 0.00	2,593.06	100.00
1073	6L of Kappirikkad to Thalikulam section from km 335.85 to km 369.015 of NH - 66 old NH-17 (NHAI) (618601) (-) (-)	Kerala	06/2021 (09/2022)	01/2025 (06/2027)	4,225.59 0.00	3,345.37	95.27
1074	6L of Thalikulam to Kodugallur section from km 369.015 to km 397.850 of NH - 66 old NH-17 (NHAI) (618602) (-) (-)	Kerala	06/2021 (09/2022)	02/2025 (06/2027)	4,302.06 0.00	3,320.63	95.05
1075	6L of Kodugallur to Edappally section from km 397.750 to km 423.780 of NH - 66 old NH-17 (NHAI) (618603) (-) (-)	Kerala	11/2021 (10/2022)	04/2025 (05/2027)	3,465.82 0.00	2,178.79	71.11
1076	Aroor-Thuravoor Thekku (NHAI) (618604) (-) (-)	Kerala	08/2022 (02/2023)	01/2026 (12/2026)	2,429.52 0.00	1,802.77	91.63
1077	Thuravoor Thekku-Paravoor (NHAI) (618605) (-) (-)	Kerala	09/2021 (03/2022)	09/2024 (05/2027)	2,878.97 0.00	2,533.61	81.49
1078	Paravoor-Kottankulangara (NHAI) (618606) (-) (-)	Kerala	12/2021 (08/2022)	02/2025 (03/2027)	3,273.61 0.00	2,863.51	71.20
1079	Kottankulangara- Start of Kollam Bypass (NHAI) (618607) (-) (-)	Kerala	06/2021 (04/2022)	10/2024 (03/2027)	2,842.14 0.00	2,373.22	73.89
1080	Widening/Development of Existing NH-85 from Km 0.000 to Km 124.636 section to 2L/LPS section in the state of Kerala on EPC Mode under Bharatmala Pariyojana (NHAI) (618708) (-) (-)	Kerala	09/2022 (06/2023)	06/2025 (03/2027)	1,187.47 0.00	807.31	81.98
1081	Kozhikode Bypass Calicut Bypass Vengalam Jn. to Ramanattukara Jn. (NHAI) (619098) (-) (-)	Kerala	02/2018 (02/2021)	02/2023 (09/2026)	1,424.77 0.00	1,066.67	98.75
1082	6L of Perole Nileshwar town to Taliparamba from Km 94.248 to Km 134.650 of NH-66 (NHAI) (619206) (-) (-)	Kerala	06/2020 (10/2021)	01/2024 (03/2027)	3,041.65 0.00	2,526.57	86.65
1083	Start of Kollam Bypass - Kadambattukonam (NHAI) (619207) (-) (-)	Kerala	06/2021 (10/2022)	03/2025 (06/2027)	2,641.37 0.00	1,990.79	81.80
1084	Kadambattukonam-Kazhakuttom (NHAI) (619208) (-) (-)	Kerala	12/2021 (07/2022)	01/2025 (05/2027)	3,635.64 0.00	2,124.38	44.34
1085	Kargil Zanskar Road (NHIDCL) (618408) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (09/2026)	398.37 0.00	344.61	98.09
1086	Widening & Up-gradation to 2 lane with Paved shoulder of NH-301 Kargil- Zanskar Road from Design km 57.000 Ex. Km. 57.905 to Km 87.000 Ex. Km. 88.2491 of 30.000 Km length Pkg-III (NHIDCL) (618409) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (09/2026)	381.01 0.00	316.16	95.09

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1087	Widening & Up-gradation to 2 lane with paved shoulder of NH-301 Kargil- Zanskar Road from Design Km .30.040 Ex. Km. 30.000 to Design Km 57.000 Ex. Km. 57.905 of 26.960 Km length Pkg-II (NHIDCL) (618410) (-) (-)	Ladakh	03/2021 (07/2021)	01/2023 (10/2026)	404.89 0.00	377.66	89.87
1088	Construction of Rewa Bypass to 4-lane with paved shoulder along with service road from Ratahara Chowk to Chorhata Chowk Road section of NH-30 from km 00.000 to 19.200 in the State of Madhya Pradesh on Hybrid Annuity Mode HAM. (MoRTH) (617909) (-) (-)	Madhya Pradesh	03/2024 (02/2025)	02/2027 (02/2027)	648.05 0.00	119.26	67.00
1089	Rehabilitation and upgradation Umaria to Shahdol section of NH-78 from Existing Km. 68/4 to Km. 142/2 to 2LPS including construction of Birshinghpur and Shahdol Bypass on EPC mode under NHDP-IVA (MoRTH) (617911) (-) (-)	Madhya Pradesh	03/2015 (08/2015)	07/2017 (09/2026)	511.83 0.00	504.85	94.50
1090	Upgradation and reconstruction of Shahpura-Dindori Section of NH 45 from Km 103.700 Design to Km 164.580 Design including 3 bypasses Total length 60.88km to Two lane with paved shoulder configuration along with One time improvement in 03 nos of bypassed built-up areas in a total length of 12.341 km in the State of Madhya Pradesh on EPC mode (MoRTH) (617914) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	12/2025 (06/2027)	241.23 0.00	129.86	41.25
1091	Upgradation & widening of Jharkheda- Berasia - Dholkhedi from design km 0000 to km 87900 Design length 87.90km of NH-346 including 3 nos. bypasses of 13.10 Km in the State of Madhya Pradesh under EPC mode. (MoRTH) (618019) (-) (-)	Madhya Pradesh	03/2022 (05/2023)	05/2025 (09/2026)	365.21 0.00	304.07	91.00
1092	Rehabilitation & Upgradation of KurwaiMungaoliChanderi Road section of NH-346, from Design Chainge 0.000 to 81.300 Km Total length 83.1 km to Two lane with paved shoulder configuration along with One time improvement in 07 nos of bypassed built-up areas in a total length of 22.615 km in the state of Madhya Pradesh on EPC mode. (MoRTH) (618020) (-) (-)	Madhya Pradesh	03/2022 (02/2023)	02/2025 (12/2026)	386.49 0.00	242.83	67.57
1093	Up-gradation of Pichhore- Dinara section of NH-346 from Km 292.750 to 334.550 to two lane with paved shoulders in the state of Madhya Pradesh on EPC mode (MoRTH) (618021) (-) (-)	Madhya Pradesh	02/2024 (12/2025)	06/2027 (06/2027)	425.97 0.00	90.26	38.02
1094	Rehabilitation & Upgradation of existing intermediate lane to two Lane with paved shoulder from km. 0.600 Gulganj bypass on NH-34 to km. 43.00 Barna River length 42.400 km. on Gulganj-Amanganj-Pawai-Katni NH43 Extn. in the state of Madhya Pradesh on EPCmode. (MoRTH) (618035) (-) (-)	Madhya Pradesh	03/2023 (11/2024)	05/2026 (12/2026)	275.40 0.00	131.31	60.14
1095	Upgradation and reconstruction of existing intermediate lane to two Lane with paved shoulder configuration from km. 43.00 Barna River to km. 77.00 ken river length 34.00 km. on Gulganj-Amanganj-Pawai-Katni NH43 Extn. along with One time improvement in 01 no. of bypassed built-up area in a total length of 1.585 km in the state of Madhya Pradesh on EPCmode. (MoRTH) (618036) (-) (-)	Madhya Pradesh	03/2023 (11/2024)	11/2026 (03/2027)	315.55 0.00	119.05	43.00
1096	Upgradation and reconstruction of Dindori - Mandla Section of NH 543 from Km 77100 Design to Km 170580 Design Total length 93.48km to Two lane with paved shoulder configuration along with One time improvement in 04 nos of bypassed built-up areas in a total length of 7.23 km in the state of Madhya Pradesh on EPC mode (MoRTH) (618043) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	07/2026 (09/2026)	492.12 0.00	309.82	88.00
1097	Upgradation of Shahdol- Sagartola Section of NH 543 from km 0000 to km 69400 to 2 lane with paved shoulders under Hybrid Annuity Mode HAM in the State of Madhya Pradesh (MoRTH) (618044) (-) (-)	Madhya Pradesh	02/2024 (03/2026)	03/2028 (03/2028)	851.40 0.00	49.32	12.06
1098	Construction of Kaithi-Padaria Kala bypass, Patna-Tamoli bypass, Jaso bypass and Nagod bypass total length 15.44 Km to 2-lane with paved shoulders flexible pavement on NH-943 in the State of Madhya Pradesh on EPC Mode. (MoRTH) (618068) (-) (-)	Madhya Pradesh	03/2022 (10/2023)	10/2025 (12/2026)	158.36 0.00	63.03	62.80
1099	Upgradation of Nasrullagani-Rehti-Budhni Sction to 2-lane with paved shoulder from Km 0150 to Km 50500 of NH-146B in the state of Madhya Pradesh on EPC mode. (MoRTH) (618085) (-) (-)	Madhya Pradesh	12/2021 (04/2023)	10/2024 (10/2026)	305.12 0.00	237.68	92.33
1100	Construction of Kasrawad bypass, Selani bypass, Khargone bypass & Bistan bypass Total length. 31.950 km Section of NH-347 C to Two lane with paved shoulder configuration in the State of Madhya Pradesh on EPC mode. (MoRTH) (618129) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	467.93 0.00	269.61	99.15
1101	Construction of Morena bypass, Ambah bypass & Porsa bypass Totat length 27.16 km Section of NH-552 Ext. to TWo lane with paved shoulder configuration in the state of Madhya Pradesh on EPC mode (MoRTH) (618156) (-) (-)	Madhya Pradesh	02/2023 (10/2024)	10/2026 (10/2026)	492.66 0.00	314.26	75.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1102	Construction of Ater realignment & Bhind bypass Total length. 21.50 km Section of NH-552Extn. to Two lane with paved shoulder configuration in the State of Madhya Pradesh on EPC mode. (MoRTH) (618157) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	06/2026 (12/2026)	348.06 0.00	103.82	69.95
1103	Upgradation of Goras to Shyampur Road section of NH-552 Ext., from Design Chainage 48.400 to 111.800 Km Total length 63.40 km to two lane with paved shoulder configuration along with One time improvement of 8.91 km in the state of Madhya Pradesh on EPC mode (MoRTH) (618158) (-) (-)	Madhya Pradesh	03/2023 (12/2024)	12/2026 (12/2026)	416.96 0.00	56.68	16.84
1104	Construction of Two lane with paved shoulder configuration of Shujalpur Bypass section of NH-752C from km 33100 Design to km. 42570 Design total design length 10.470 km in the State of Madhya Pradesh on EPC mode. (MoRTH) (618170) (-) (-)	Madhya Pradesh	03/2023 (03/2024)	09/2025 (12/2026)	214.07 0.00	69.76	46.76
1105	Work of Upgradation of Jirapur-Pachore Road including Pachore, Jirapur, Chhapiheda & Khujner Bypasses from 0000 to 58790 Design Length 58.79 Km section of NH-752C to 2LPS in the State of Madhya Pradesh under EPC mode (MoRTH) (618171) (-) (-)	Madhya Pradesh	03/2022 (01/2024)	01/2026 (12/2026)	352.69 0.00	167.59	57.26
1106	Bypass on Western side of Gwalior City (NHAI) (618619) (-) (-)	Madhya Pradesh	03/2025 (01/2026)	01/2028 (01/2028)	998.95 0.00	227.59	0.00
1107	Additional works 2VUPS, MR-10 junction flyover and underpass in Six lane Indore-Dewas section of NH-52 in the state of Madhya Pradesh on EPC Mode (NHAI) (618620) (-) (-)	Madhya Pradesh	08/2022 (01/2023)	07/2024 (03/2027)	207.77 0.00	155.24	90.18
1108	Indore - Edlabad Pkg-II [Tejainagar to Balwara] (NHAI) (618621) (-) (-)	Madhya Pradesh	03/2022 (01/2023)	01/2025 (12/2026)	1,162.80 0.00	824.50	87.80
1109	4L of Indore - Boregaon Pkg-III [Balwara to Dhangaon] from km. 42.260 to km. 82.660 of NH347BG & 753L (NHAI) (618622) (-) (-)	Madhya Pradesh	01/2021 (04/2022)	04/2024 (10/2026)	1,001.69 0.00	835.16	92.50
1110	4L Boregaon Buzurg to Shahpur Pkg I of Boregaon Buzurg to Muktainagar of NH 753L (NHAI) (618623) (-) (-)	Madhya Pradesh	11/2022 (02/2024)	01/2026 (10/2026)	1,504.37 0.00	556.92	92.50
1111	4L Greenfield Rudhi to Deshgaon Pkg V of Betul-Khandwa/Deshgaon (NHAI) (618654) (-) (-)	Madhya Pradesh	11/2022 (10/2023)	10/2025 (03/2027)	521.21 0.00	216.60	63.79
1112	2L PS of Roshni to Ashapur Section of NH-347B from Design KM Ch. 89.900 to 114.000 KM Package III of Betul Khandwa (NHAI) (618655) (-) (-)	Madhya Pradesh	03/2024 (08/2024)	08/2026 (09/2026)	200.99 0.00	132.61	100.00
1113	4L from km 0.000 to 42.040 Bhopal Ratnaigiri Tiraha to Vidisha Morikodi (NHAI) (618661) (-) (-)	Madhya Pradesh	10/2024 (11/2025)	11/2027 (11/2027)	1,032.30 0.00	194.11	20.23
1114	4L Vidisha Gyarpur section of NH-146 from Design Chainage km 59475 existing chainage km 81240 to Design Chainage km 88361 existing chainage km 110.315 (NHAI) (618662) (-) (-)	Madhya Pradesh	10/2024 (03/2026)	03/2028 (03/2028)	980.20 0.00	113.19	12.25
1115	i 4L Vidisha to Hinotiya from km 0.000 to Km 27.000 Vidisha Mehulwa-Talbehat Pkg-I Section of NH- 346 and ii 4L Vidisha to Morikori from Km 39.000 to 59.476 section of NH-146 (NHAI) (618663) (-) (-)	Madhya Pradesh	09/2022 (12/2023)	12/2025 (12/2026)	1,003.87 0.00	434.21	90.04
1116	Berkhedi to Godpehra on NH-44 Sagar link road (NHAI) (618664) (-) (-)	Madhya Pradesh	02/2022 (11/2022)	11/2024 (12/2026)	524.84 0.00	391.54	93.05
1117	4- Laning of Mohari to Satai Ghat section NH-934 from Km 50300 to Km 89875 Total length 39.575 km Package-2 in the State of Madhya Pradesh on EPC Mode (NHAI) (618666) (-) (-)	Madhya Pradesh	08/2022 (08/2024)	08/2026 (09/2026)	710.92 0.00	533.05	99.91
1118	4L of near Satai Ghat to Chowka section of NH-34 from D. Ch. 89.875 to D. Ch. 145.000 Package-3 (NHAI) (618667) (-) (-)	Madhya Pradesh	10/2024 (10/2025)	10/2027 (10/2027)	1,005.59 0.00	224.70	38.26
1119	4-lanning of Rahatgarh to Berkhedi section of NH-146 from Design Ch 124470 to Ch. 134.549 (NHAI) (618671) (-) (-)	Madhya Pradesh	03/2025 (12/2025)	12/2027 (12/2027)	618.33 0.00	53.19	14.60

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1120	4-lanning of Gyaraspur to Rahatgarh section of NH-146 from Design Ch. 88361 to Ch 124470 in the state of MP on HAM mode (NHAI) (618672) (-) (-)	Madhya Pradesh	10/2024 (11/2025)	11/2027 (11/2027)	903.44 0.00	191.87	35.25
1121	Outer Ring Road of Jabalpur Town from Manegaon to NH-45 Pkg-2 (NHAI) (618684) (-) (-)	Madhya Pradesh	11/2022 (03/2024)	03/2026 (03/2027)	917.26 0.00	529.01	78.75
1122	Outer Ring Road of Jabalpur Town from NH45 to Kushner Pkg-3 (NHAI) (618685) (-) (-)	Madhya Pradesh	09/2022 (03/2024)	03/2026 (12/2026)	911.24 0.00	552.62	79.80
1123	Outer Ring Road of Jabalpur Town from Kushner to Amjhar Road including Airport Connectivity Pkg-IV (NHAI) (618686) (-) (-)	Madhya Pradesh	08/2022 (03/2024)	03/2026 (03/2027)	612.94 0.00	369.68	79.63
1124	Outer Ring Road of Jabalpur Town from Barela to Manegaon Pkg-1 (NHAI) (618687) (-) (-)	Madhya Pradesh	09/2022 (03/2023)	03/2025 (03/2027)	652.33 0.00	501.21	89.72
1125	Outer Ring Road of Jabalpur Town from Amjhar Road including Airport Connectivity to barela Pkg-V (NHAI) (618688) (-) (-)	Madhya Pradesh	10/2024 (10/2025)	10/2027 (10/2027)	794.70 0.00	105.49	32.38
1126	Indore - Harda Pkg-I [Indore to Raghav Garh from km. 0.25 to km. 26.903] (NHAI) (618694) (-) (-)	Madhya Pradesh	01/2022 (11/2022)	10/2024 (09/2026)	1,011.29 0.00	710.89	96.09
1127	4L of Chandesara to Khedakhajuriya from Km. 0.000 to - 750 & Km 0.000 to km 41.400 of NH-148NG Pkg-I (NHAI) (618735) (-) (-)	Madhya Pradesh	12/2021 (09/2022)	05/2024 (03/2027)	909.84 0.00	587.82	99.00
1128	2L PS of Hinotiya-Mehulwa section of NH-346 from Km. 27.000 to Km 75.700 Vidisha Mehulwa-Talbehat Pkg-II Section of NH- 346 (NHAI) (618751) (-) (-)	Madhya Pradesh	10/2022 (09/2023)	09/2025 (03/2027)	581.65 0.00	274.61	69.04
1129	Itarsi Km. 63.000 to Betul Km. 137.000 of NH-69 in Madhya Pradesh (NHAI) (618762) (-) (-)	Madhya Pradesh	08/2017 (02/2018)	02/2020 (12/2026)	950.27 0.00	666.78	100.00
1130	Balance works of 4 lane divided carriageway of Missing Link section of NH-39 Rewa Bypass from junction with NH 30 near Bela to Junction with MPRDC ring road near Silpara on SH 9 design length 13.100 km on EPC Mode under Bharatmala Pariyojana in the State of Madhya Pradesh (NHAI) (618784) (-) (-)	Madhya Pradesh	08/2023 (04/2024)	04/2026 (01/2027)	355.36 0.00	264.26	84.44
1131	Construction of 6 lane Indore western bypass from km 0000 to Km 34000 Pkg -I in the State of Madhya Pradesh on Hybrid Annuity Mode under NHO (NHAI) (618932) (-) (-)	Madhya Pradesh	02/2024 (01/2026)	12/2027 (12/2027)	1,534.70 0.00	721.68	27.60
1132	Construction of 6 lane Indore western bypass from km 34000 to Km 64000 Pkg-II in the state of Madhya Pradesh on Hybrid Annuity Mode under NHO (NHAI) (618933) (-) (-)	Madhya Pradesh	03/2024 (02/2026)	02/2028 (02/2028)	1,430.56 0.00	881.78	17.50
1133	4L of Budhni to Shahganj Bypass End Package-III of NH-146B from Km. 73.750 to Km. 102.000 (NHAI) (618962) (-) (-)	Madhya Pradesh	03/2024 (08/2025)	08/2027 (08/2027)	1,102.97 0.00	196.81	28.95
1134	Construction work of 4-laning of Shahganj bypass end to Badi Package-IV of NH-146B from design km 102.000 to design km 142.357 Design length 40.357 km (NHAI) (618963) (-) (-)	Madhya Pradesh	02/2024 (03/2025)	03/2027 (03/2027)	784.14 0.00	347.21	53.60
1135	4 Laning of Sandalpur to Nasrullaganj Pkg-1 section of NH-146B Length 43.2 Km. (NHAI) (618964) (-) (-)	Madhya Pradesh	03/2025 (01/2026)	01/2028 (01/2028)	1,425.98 0.00	198.59	11.57
1136	Six laning with both sides Service Road of Ayodhya Bypass from Design Km 0000 near Ashram Tiraha on NH-46 to Km 16439 end at Ratnagiri Tiraha on Nh-146 (NHAI) (618966) (-) (-)	Madhya Pradesh	02/2024 (08/2025)	08/2027 (08/2027)	1,123.17 0.00	177.29	21.61
1137	Upgradation of Sarvardewla to Pal MP/MH Border Road section of NH-347 C from Design Chainge km 81.600 to 137.400 Total length 55.80 km to two lane with paved shoulder configuration along with One time improvement of 1 .95 km in the State of Madhya Pradesh on EPC mode. (MoRTH) (619007) (-) (-)	Madhya Pradesh	03/2023 (01/2026)	01/2028 (01/2028)	461.23 0.00	22.20	3.10
1138	Dhangaon - Borgaon section km 81.000 to km 139.000 [Indore - Edlabad Pkg IV] (NHAI) (619100) (-) (-)	Madhya Pradesh	01/2020 (08/2021)	08/2023 (10/2026)	866.00 0.00	746.60	99.80

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1139	Indore - Harda Pkg-II [Raghavgarh to Nanasa from km. 29.30 to km. 92.30] (NHAI) (619114) (-) (-)	Madhya Pradesh	01/2023 (03/2024)	03/2026 (06/2027)	1,081.51 0.00	370.33	40.25
1140	Balance work for rehabilitation and upgradation of Sidhi -Singrauli Road from Km 82/400 to Km 187/99 Design Length 105.59 Km of NH-39 Old NH-75E to four lane with paved shoulder in the State of Madhya Pradesh on Item Rate Mode. (NHAI) (619304) (-) (-)	Madhya Pradesh	01/2026 (05/2026)	05/2028 (05/2028)	568.32 0.00	4.09	0.00
1141	Construction of 6 lane flyover from Khapari ROB to Mihan Interchange design chainage km 8760 to 11450 L- 2.69 km and upgradation of existing 4L PS road to 6LPS with service road by flexible pavement design chainage km 11450 to 14500 L- 3.05 [total project length 5.74 km] in section of Nagpur - Hyderabad NH-44 Old NH-7 in Nagpur district in the state of Maharashtra on HAM mode. (MoRTH) (617912) (-) (-)	Maharashtra	03/2024 (10/2025)	10/2027 (10/2027)	619.55 0.00	22.85	12.21
1142	Construction of New Four Lane Bypass to Parbhani City Parwa to Asola Km 463/265 to Km 481/180 Design Ch. 19220 to Ch. 34434 Length-15.214 Km section of NH-61 on EPC mode in the State of Maharashtra. (MoRTH) (617932) (-) (-)	Maharashtra	03/2022 (07/2023)	10/2024 (10/2026)	496.64 0.00	216.62	73.00
1143	Nasratpur to Barasgaon section of NH-61 2L / 4L PS from Km.514/00 to 558/200 (MoRTH) (617934) (-) (-)	Maharashtra	07/2017 (09/2017)	09/2019 (08/2026)	406.54 0.00	528.24	95.84
1144	Udgir Raavi Degloor Aadampur phata to Sagroli fata (MoRTH) (617937) (-) (-)	Maharashtra	11/2024 (04/2026)	04/2028 (-)	809.77 0.00	42.26	20.00
1145	Rehabilitation And Upgradation to four lane with paved shoulder configuration from km 24350 to km 61875 Jawale - Borgaon Kale of NH-63 in the State of Maharashtra on EPC mode under Annual Plan 2024-25 Total length - 37.525 Km. (MoRTH) (617938) (-) (-)	Maharashtra	12/2024 (09/2025)	03/2027 (03/2027)	574.18 0.00	28.75	20.00
1146	Balance work of NH-66 from design Km 84/00 to Km 87/100 Indapur Bypass and Km 91/600 to Km 99/100 Mangaon Bypass to four lane with paved shoulder in State of Maharashtra under NHO on EPC Mode. (MoRTH) (617945) (-) (-)	Maharashtra	03/2025 (10/2025)	04/2027 (04/2027)	354.21 0.00	156.44	70.34
1147	Kashedi to Parshuram Ghat section of NH-66 from Km 161/600 - Km 205/400 - 4L PS (MoRTH) (617946) (-) (-)	Maharashtra	03/2016 (02/2018)	02/2020 (12/2025)	1,142.62 0.00	1,241.63	97.50
1148	Arawali Kante section of NH-17New NH-66 4L PS from Km.241/300 to 281/300 (MoRTH) (617947) (-) (-)	Maharashtra	03/2016 (11/2017)	11/2019 (03/2026)	1,006.99 0.00	773.14	80.06
1149	Kante - Wakad section of NH-66 4L PS from Km.281/300 to 332/200 (MoRTH) (617948) (-) (-)	Maharashtra	03/2016 (11/2017)	11/2019 (11/2025)	1,117.75 0.00	1,315.34	90.14
1150	Kopargaon to Savali Vihir section (MoRTH) (617965) (-) (-)	Maharashtra	06/2022 (01/2023)	07/2024 (09/2026)	195.38 0.00	105.16	93.50
1151	Rehabilitation, upgradation & widening of existing highway to 2L/4LPS Rigid Pavement of NH 160 section- Phaltan to Mhaishal near Karnataka Border including Tasgaon Bypass, from existing chainage Km 301/430 to Km 458/415 in the State of Maharashtra- Package-II & Package III combined- starting from existing chainage Km 341/300 to Km 394/130 and design chainage Km 340/250 at Dahiwadi Village to Km 392/950 ending at Vita Village in the State of Maharashtra on EPC Mode. (MoRTH) (617978) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	631.76 0.00	303.71	88.30
1152	Rehabilitation, upgradation & widening of existing highway to 2L/4LPS Rigid Pavement of NH 160 section- Phaltan to Mhaisal near Karnataka Border including Tasgaon Bypass, from existing chainage Km 301/430 to Km 458/415 in the State of Maharashtra. Package-I starting from existing chainage Km 301/430 at Phaltan Village Junction of Phaltan Baramati Road Design Chainage -301/430km & ending at existing chainage Km 341/300 Dahiwadi Village Bus Stop Design chainage Km 340466km in the S (MoRTH) (617979) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	533.76 0.00	217.44	77.07
1153	Rehabilitation/ Upgradation of existing Highway to four lane standards in Kurkheda town from km.413257 to km 410775, Two lane in Shankarpur Gurnuli km 42400 to km 43100 section and Reconstruction of Major Bridge at Ch. 448558 Bhuti Nallah and Ch. 411695 Sati River bridge, Minor Bridge at Ch. 411477 and Ch. 405800 Lendhari Bridge of NH 543 Bhamhapuri-wadsa-kurkheda-korchi-Deori-Amgaon road on EPC mode in the State of Maharashtra (MoRTH) (618042) (-) (-)	Maharashtra	03/2022 (11/2023)	05/2025 (12/2026)	163.86 0.00	62.18	50.25
1154	Widening, Reconstruction & Up-gradation to 2 lane with Paved Shoulder/Four Lane configuration for the work of Ahmednagar to Sabalkhed & Ashti to Chinchpur Section of NH-561 from Design km 2915 to km 37728 & Design km 55100 to km 70000 in the State of Maharashtra on EPC mode. Length 49.713 km (MoRTH) (618047) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	657.16 0.00	383.14	93.93

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1155	Up-gradation to 2/4 lane with paved shoulder configuration of NH-652 from Tuljapur Naldurg-Akkalkot road Chainage from Km. 00.000 to km 30.982 in the State of Maharashtra on EPC mode. (MoRTH) (618049) (-) (-)	Maharashtra	03/2024 (01/2025)	07/2026 (09/2026)	183.41 0.00	85.70	98.00
1156	Construction of four-lane Concrete Road from Police Headquarter Gondia City to Rawanwadi Village Birsai Airport Junction from design km 0.000 to km 15.781 existing km 39/720 of NH-753 to existing Km 8/400 of NH 543 on sections from Kohmara-Goregaon- Police HeadquarterKaranja - Collector Office Square - Balaghat T Point- Rawanwadi- Rajegaon of NH-753 and NH-543 in Gondia District in the state of Maharashtra. Total Length of the project 15.781 Km. (MoRTH) (618059) (-) (-)	Maharashtra	02/2023 (02/2024)	08/2025 (10/2026)	328.11 0.00	111.48	34.15
1157	Strengthening, Widening & Up-gradation of newly declared NH-761 from NH-61Junction-BelheAlkutiDevibhoyareNighojShirur, from Design chainage Km 0.000 to Km 37.970 from Single/Intermediate/2L to 2LPS in the State of Maharashtra on EPC Mode Length 37.970 Km (MoRTH) (618061) (-) (-)	Maharashtra	03/2024 (03/2025)	09/2026 (09/2026)	386.16 0.00	114.55	62.50
1158	Rehabilitation/Upgradation of existing Highway to 2LPS/4 lane of Dhawali to Rajoli from Design Km.149476 to 163476 existing Km.150000 to 164000, Pandhasala to Mohadongri from design Km.170476 to 181476 existing Km.171000 to 182000, Ambeshivni Fata to Bodli from design Km.183476 to 185476 existing Km.184000 to 186000 and Made Tukum to Gadchiroli from design Km.188476 to 189476 existing Km.188000 to 18900 having length 28 km of NH-930 of Dhawali to Gadchroli road in the (MoRTH) (618065) (-) (-)	Maharashtra	03/2022 (03/2024)	09/2025 (03/2027)	316.44 0.00	84.06	37.20
1159	Nandurshingote to Kolhar (MoRTH) (618088) (-) (-)	Maharashtra	09/2024 (06/2025)	12/2026 (12/2026)	325.79 0.00	263.09	45.00
1160	Rehabilitation & Up-gradation of Mudkhed to Nanded section from Km. 372000 to Km 388400 of NH 161A i.e. Nanded-Bhokar-Himayatnagar-Kinwat-Mahur-Arani Road Design chainage from Km 372000 Mudkhed to Km 387650 Nanded of NH 161A Length 15.65 Km to 2/4Lane with paved shoulders configuration in the State of Maharashtra on EPC mode. (MoRTH) (618089) (-) (-)	Maharashtra	03/2022 (04/2023)	04/2025 (10/2026)	206.54 0.00	7.77	65.14
1161	Pen to Khopoli 2LPS (MoRTH) (618094) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (12/2025)	369.39 0.00	212.04	86.30
1162	Rehabilitation and Up-gradation to 2 lane road with paved shoulders configuration for the balance work of 13 km length on Helwak-Patan-Karad section Km. 85000 to 133 417 of NH-166E in the state of Maharashtra on EPC mode. (MoRTH) (618096) (-) (-)	Maharashtra	02/2024 (10/2024)	04/2026 (02/2027)	181.45 0.00	84.97	87.00
1163	Guhagar - Rampur - 2L-PS - km 0/00 Guhagar to 26/230 Rampur and 40/00 Mirjoli to 53/600 Sati on NH-166E (MoRTH) (618097) (-) (-)	Maharashtra	01/2017 (06/2017)	06/2019 (08/2025)	407.20 0.00	274.73	91.89
1164	Upgradation of existing 2 lane flexible pavement to 2 lane paved shoulders rigid pavement from design chainage Km 66.00 to Design Km 82.440 Start of Kolhapur Municipal corporation near Phulewadi to kale, design length 16.440 Km section on Talere Gaganbawada-Kolhapur road NH 166G in the state of Maharashtra on EPC mode (MoRTH) (618098) (-) (-)	Maharashtra	03/2021 (11/2022)	05/2024 (08/2026)	167.97 0.00	102.29	93.75
1165	Strengthening and Widening of road Sakoli- Wadsa-Armori-Gadchiroli-Ashti- Allapalli - Sironcha National highway NH 353C in Km 262/00 to 321/00 including 16 minor Bridges and 2 Major Bridge Total length 59 Km section from repalpalli to sironcha in Gadchiroli Dist in the State of Maharashtra. (MoRTH) (618133) (-) (-)	Maharashtra	03/2021 (06/2022)	05/2024 (03/2027)	280.57 0.00	210.92	67.39
1166	Rehabilitation /Upgradation from Lagam to Alapalli section Desing Km. 199/400 to km 227/400 Length 28.0 Km to 2 lane with Paved Shoulders/ 4 lane configuration section of NH-353 C Sakoli-Wadsa-Armori-Gadchiroli-Ashti-Alapalli Sironcha in Gadchiroli District on EPC mode in the state of Maharashtra. (MoRTH) (618134) (-) (-)	Maharashtra	02/2023 (09/2024)	09/2026 (09/2026)	459.39 0.00	220.61	85.05
1167	Rehabilitation and Up-gradation of Jarud - Sirsala section of NH-361F km 59500 to km11500 to Two lane with paved shoulder/ Four Lane in the state of Maharashtra on EPC mode Length 55.5 Km. (MoRTH) (618137) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	540.35 0.00	217.20	72.10
1168	Widening, Reconstruction & Up-gradation to 2 lane with Paved Shoulder/Four Lane configuration for the work of Sautada to Shirapur Section of NH-561 from Design km 86300 to km 125589 in the state of Maharashtra on EPC mode. Design length 39.289 km (MoRTH) (618138) (-) (-)	Maharashtra	03/2024 (05/2025)	11/2026 (11/2026)	349.57 0.00	77.84	62.96

All Ongoing Projects							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1169	Rehabilitation and Up-gradation of Gangakhed Loha section of NH-361F from Km 169/00 to 210/00 to two lane with paved shoulder/ four lane configuration in the state of Maharashtra on EPC mode Length - 41.00 Km. (MoRTH) (618139) (-) (-)	Maharashtra	03/2024 (04/2025)	09/2026 (09/2026)	355.12 0.00	0.00	43.46
1170	Rehabilitation and Up-gradation of i. Deogaon phata to Digras phata Ch. 0/000 to 15/000 & Selu to Borgavhan Ch 20/900 to 35/800 [Length 29.9km] ii. Injegaon Dhamoni to Pohner Phata Ch.58/200 to Ch. 83/700 [Length25.5 km] and iii. Pohner phata to Pathri Design Ch. 42/700 to 58/200 [Length 15.5 km] sections of NH-548B to Two lane with paved shoulder configuration in the state of Maharashtra on EPC mode Total project length 70.9 Km. (MoRTH) (618150) (-) (-)	Maharashtra	03/2024 (05/2025)	05/2027 (05/2027)	761.83 0.00	96.78	22.00
1171	Mhaswad to Tembhurni section of NH-548C - 2L PS (MoRTH) (618152) (-) (-)	Maharashtra	01/2017 (08/2017)	07/2019 (08/2026)	488.60 0.00	298.45	96.19
1172	Satara to Mhaswad (MoRTH) (618153) (-) (-)	Maharashtra	01/2017 (08/2017)	08/2019 (08/2026)	653.46 0.00	384.64	98.08
1173	Rehabilitation & upgradation of Jamkhed to Sautada Section of NH548 D from km 195.375 to km 208.774, Length 13.399 Km to 2L PS /4L configuration with rigid pavement in the state of Maharashtra on EPC mode. (MoRTH) (618154) (-) (-)	Maharashtra	03/2022 (01/2023)	07/2024 (06/2026)	157.62 0.00	0.00	68.93
1174	Development/Widening of Talegaon Chakan Shikrapur Nhavara Section of NH-548D from existing chainage km. 54/000 to 82/300 and Design chainage Km. 54/000 to 82/120 Shikrapur to Nhavara Section to 2LPS/4L Configuration on EPC Mode in the State of Maharashtra. (MoRTH) (618155) (-) (-)	Maharashtra	03/2024 (01/2025)	07/2026 (03/2027)	396.17 0.00	237.74	72.52
1175	Paithan - Shirur section 2LPS Km 0.0 to 55.00 (MoRTH) (618172) (-) (-)	Maharashtra	03/2017 (06/2017)	06/2019 (10/2026)	341.80 0.00	253.74	82.00
1176	Shirur-Kharda section from 55937 km to 114486 km to 2LPS/4L (MoRTH) (618173) (-) (-)	Maharashtra	02/2017 (06/2017)	06/2019 (08/2026)	381.77 0.00	262.20	83.93
1177	Rehabilitation and Upgradation to two lane with paved shoulder configuration of NH-752G from Sakri to Pimpalner Section Design Ch km 0000 to Ch km 21411 in the state of Maharashtra on EPC Mode. Length 21.411 km. (MoRTH) (618174) (-) (-)	Maharashtra	03/2024 (04/2025)	10/2026 (10/2026)	226.58 0.00	142.62	100.00
1178	Rehabilitation and upgradation from ch km 50/200 to 56/800 and km 62/600 to 100/403 of Kolde to Visarwadi Near Junction with NH-6 section of NH 752G total length 44.40 to two-lane with paved shoulder / four lanes in the State of Maharashtra on EPC mode. (MoRTH) (618176) (-) (-)	Maharashtra	03/2025 (01/2026)	01/2028 (-)	349.08 0.00	66.84	35.45
1179	Pal Phata Phulambri - Khultabad 2LPS (MoRTH) (618177) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (09/2026)	227.19 0.00	155.88	95.29
1180	Widening and strengthening of Gangakhed to Kingaon section of NH-752K in Km 38/750 to 72/304 Flexible Pavement Length33.554 km to 2-lane configuration on EPC mode in the State of Maharashtra. (MoRTH) (618178) (-) (-)	Maharashtra	02/2024 (12/2024)	06/2026 (10/2026)	162.67 0.00	5.76	91.00
1181	Pune raigarh District Border To Mangaon Ch 69000 to 103775 NH-753F (MoRTH) (618180) (-) (-)	Maharashtra	03/2018 (06/2018)	12/2019 (07/2026)	223.46 0.00	124.00	89.08
1182	Balance work of Rehabilitation and Up-gradation to 2-lane road with paved shoulders configuration for NH- 965DD from Pacharal-Mandangad-Mhapral-Rajewadi Upto Junction of NH-66 Ch-22700 to 75100 Km and Ambadave connector Birth place of Dr. Babasaheb Ambedkar Ch-0000 to 7325 Km length Km 59.725 in the state of Maharashtra on EPC mode. Balance Work (MoRTH) (618198) (-) (-)	Maharashtra	03/2018 (01/2022)	01/2024 (10/2026)	388.93 0.00	249.66	93.07
1183	Rehabilitation, Upgradation & Widening of existing Highway to Rigid Pavement 2 Lane with Paved Shoulder of NH 965DD from Lonand Shirval-Bhor Mandangad-Pchral Section ShindewadiPhata to Varandah Ghat Dist Border from Km 33/550 to 92/550 in the state of Maharashtra on EPC mode. (MoRTH) (618199) (-) (-)	Maharashtra	02/2023 (07/2024)	07/2026 (02/2027)	723.13 0.00	217.90	53.50
1184	Vadodara Mumbai Expressway Phase II - Pkg XIII [Km. 26.582 to Km. 50.700] Shirsad - Masvan (NHAI) (618469) (-) (-)	Maharashtra	06/2020 (02/2022)	02/2024 (08/2026)	3,536.90 0.00	1,986.56	98.20
1185	Vadodara Mumbai Expressway Phase II - Pkg XIV [Km. 3.000 to Km. 20.200 of Spur] Shirsad - Akloli (NHAI) (618470) (-) (-)	Maharashtra	05/2021 (11/2022)	05/2024 (09/2026)	2,058.79 0.00	645.91	98.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1186	Vadodara Mumbai Expressway Phase II - Pkg XV [Km. 20.200 to Km. 43.000 of Spur] Akloli - Amne (NHAI) (618471) (-) (-)	Maharashtra	05/2021 (11/2022)	05/2024 (08/2026)	2,610.88 0.00	651.95	94.60
1187	Vadodara Mumbai Expressway Phase II - Pkg XVI [Km. 43.000 to Km. 69.800 of Spur] Amne - Bhoj (NHAI) (618472) (-) (-)	Maharashtra	06/2021 (11/2022)	10/2024 (08/2026)	4,051.80 0.00	952.69	95.50
1188	Vadodara Mumbai Expressway Phase II - Pkg XVII [Km. 69.800 to Km. 79.783 of Spur] Bhoj - Morbe (NHAI) (618473) (-) (-)	Maharashtra	09/2021 (01/2023)	07/2025 (08/2026)	2,208.68 0.00	931.24	90.73
1189	Upgradation & rehabilitation of Service Roads on both sides in urban areas of Pune City on PuneSatara section of NH48 (NHAI) (618511) (-) (-)	Maharashtra	01/2025 (06/2025)	06/2027 (06/2027)	604.59 0.00	69.84	24.08
1190	Tunnel at Khambataki Ghat Section and its approaches from existing Km. 771.730 to existing Km. 782.000 (NHAI) (618512) (-) (-)	Maharashtra	11/2017 (02/2019)	02/2022 (10/2026)	907.03 0.00	687.05	89.20
1191	6L of Kagal-Satara section from Km 592.500 to Km 658.000 of NH-48 Pkg-I (NHAI) (618513) (-) (-)	Maharashtra	12/2021 (01/2023)	01/2025 (02/2027)	2,111.95 0.00	634.62	51.14
1192	6L of Kagal-Satara section from Km 658.000 to Km 725.000 of NH-48 Pkg-II (NHAI) (618514) (-) (-)	Maharashtra	12/2021 (12/2022)	12/2024 (12/2026)	2,330.71 0.00	206.69	90.12
1193	4L of Indora Chowk to Pachpaoli and Agrasen Chowk - Ashoka Chowk (NHAI) (618557) (-) (-)	Maharashtra	03/2023 (07/2023)	06/2026 (09/2026)	1,038.84 0.00	699.60	84.00
1194	6L of Gonde Km. 439.038 to Pimpri Sado Km. 459.905 section of NH-848 Old NH-3 (NHAI) (618585) (-) (-)	Maharashtra	02/2024 (10/2024)	04/2027 (11/2027)	856.93 0.00	160.20	40.50
1195	Improvement and strengthening of existing 2 lane stretch to 2-Lane with PS 1.5m on both sides on Ghoti-Sinnar section of NH-160A using Thin White Topping 200mm thick in the State Of Maharashtra on EPC Mode (NHAI) (618586) (-) (-)	Maharashtra	03/2025 (06/2025)	06/2026 (10/2026)	254.78 0.00	119.17	77.00
1196	4L Mitigation Measure structures on CH/MH Border to Wainganga Bridge Section of NH-6 New NH-53 (NHAI) (618588) (-) (-)	Maharashtra	02/2021 (11/2021)	11/2023 (10/2026)	540.24 0.00	464.37	99.79
1197	Balance work of 4L Panvel to Indapur section of NH-66 Old NH- 17 from km 0.000 Panvel to km 42.300 Kasu (NHAI) (618594) (-) (-)	Maharashtra	12/2022 (03/2023)	10/2024 (09/2026)	329.82 0.00	188.13	98.66
1198	Four laning from Dive Ghat Km. 220.900 to Hadapsar Km. 234.150 of Mohol Alandi section Pkg VI of NH-965 (NHAI) (618626) (-) (-)	Maharashtra	12/2023 (10/2024)	10/2026 (04/2027)	819.52 0.00	141.56	70.01
1199	Construction of 7 Nos of Standalone safety structures/works at different locations on various NHs (NHAI) (618627) (-) (-)	Maharashtra	01/2025 (07/2025)	01/2027 (01/2027)	168.52 0.00	38.33	33.35
1200	Strengthening of Existing Alignment of Pandharpur Town Part Bypassed Section of NH 965 from KM 36.230 to KM 44.230 from Chh. Shivaji Maharaj Chowk to Wakhari (NHAI) (618628) (-) (-)	Maharashtra	08/2022 (11/2023)	10/2025 (03/2027)	150.21 0.00	80.94	69.25
1201	Loha-Waranga Section of NH-361 from km 187.800 to km 244.369 (NHAI) (618653) (-) (-)	Maharashtra	03/2018 (03/2019)	03/2021 (12/2026)	1,236.08 0.00	1,557.02	96.22
1202	Bodhre - Dhule (NHAI) (618693) (-) (-)	Maharashtra	02/2021 (01/2022)	07/2024 (10/2026)	1,344.78 0.00	838.04	97.69
1203	Upgradation of 2L/4L with Paved Shoulder of Shirwal-Lonand Section from KM 159900 To KM 188025 of NH-965DD Section I and 2L With Paved Shoulder of Lonand-Satara Section from KM 51500 To KM 96246 Of NH-965D Section II in Satara District in the State of Maharashtra on EPC Mode under NHO- (NHAI) (618754) (-) (-)	Maharashtra	03/2025 (06/2025)	06/2027 (06/2027)	538.11 0.00	189.06	43.57
1204	Up-gradation to Four Lane with Paved Shoulder configuration of the highway starting from existing km 88.400 Savali Vahir to km 163.400 start of Ahmednagar bypass Design Length 75.000 km section of NH-160 in the State of Maharashtra under Bharatmala Pariyojana on EPC Mode (NHAI) (618766) (-) (-)	Maharashtra	10/2024 (04/2025)	04/2027 (04/2027)	862.00 0.00	327.05	48.55

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1205	4L of Ratnagiri - Kolhapur section from km 67.140 to km 112.340 of NH-166 Pkg II (NHAII) (618836) (-) (-)	Maharashtra	02/2022 (05/2023)	05/2025 (01/2027)	1,985.38 0.00	1,239.81	81.57
1206	4L of Ratnagiri - Kolhapur section from km 112.340 to km 145.300 of NH-166 PkgIII (NHAII) (618837) (-) (-)	Maharashtra	02/2022 (05/2023)	05/2025 (01/2027)	1,939.23 0.00	1,092.06	68.95
1207	4L of Nagpur-Katol Section from Km. 13.00 to Km. 62.900 of NH-353J (NHAII) (618937) (-) (-)	Maharashtra	02/2021 (10/2021)	10/2023 (03/2027)	1,166.96 0.00	1,181.44	81.54
1208	Construction of Standalone Flyover cum ROB from Design Ch.66.600 to Design Ch.68.800 in Gadchandur Town on NH-353B (NHAII) (618939) (-) (-)	Maharashtra	02/2025 (07/2025)	07/2027 (07/2027)	191.31 0.00	40.01	40.08
1209	Rehabilitation and Up gradation of Charthana Jintur Section of NH 752 I Km 25100 to 47100 to 2 Lane with Paved Shoulder configuration Flexible Pavement in the state of Maharashtra on EPC mode. Reg- Resubmission of Annual Plan Estimate. (MoRTH) (619008) (-) (-)	Maharashtra	03/2025 (01/2026)	07/2027 (07/2027)	157.69 0.00	61.90	85.00
1210	Construction of six lane Flyover at Katraj junction at Km, 3/880 of NH 548-DD Vadgaon - Katraj - Kondhwa - Mantarwadi Chowk - Loni Kalbhor - Theur Phata - Lonikand Road in Pune Dist of the State of Maharashtra. On Engineering Procurement and construction EPC Basis mode L.1.326 Km, (MoRTH) (619042) (-) (-)	Maharashtra	02/2021 (03/2022)	02/2026 (02/2023)	163.51 0.00	108.55	89.20
1211	Capacity Augmentation in the stretch of DhulePimpalgaon section of NH60 Km. 261.720 to Km. 380.000 by Construction of Slip/Service Road on either side at various locations total length 30.30 Km LHSRHS and Flyover 2 x 30m at Sawadgaon Phata Km. 310.415 (NHAII) (619043) (-) (-)	Maharashtra	12/2025 (04/2026)	10/2026 (10/2027)	341.63 0.00	10.90	5.10
1212	Satara Km 725.000 to Pune Km 865.350 of NH - 4 New NH - 48 in Maharashtra (NHAII) (619069) (-) (-)	Maharashtra	09/2009 (10/2010)	05/2022 (12/2026)	361.72 0.00	387.34	99.05
1213	Balance works of 4L Panvel Indapur section of NH66 old NH17 from km 42.300 kasu to km 84.600 Indapur (NHAII) (619095) (-) (-)	Maharashtra	06/2022 (11/2022)	05/2024 (09/2026)	546.44 0.00	420.99	96.73
1214	4L of Ratnagiri - Kolhapur section of NH-166 from km 0.000 to km 19.769 and km 31.000 to km 67.140 Pkg I (NHAII) (619149) (-) (-)	Maharashtra	02/2022 (11/2022)	11/2024 (11/2026)	1,774.03 0.00	1,444.74	97.40
1215	4L of Baramati to Indapur Pkg-II from km. 41.400 to km. 84.550 of NH-965G Saint Tukaram Marg (NHAII) (619163) (-) (-)	Maharashtra	01/2021 (09/2021)	09/2023 (12/2026)	1,471.32 0.00	1,071.02	86.20
1216	Vadodara Mumbai Expressway Phase II - Pkg XII [Km. 50.700 to Km. 77.000] Masvan - Ganjad (NHAII) (619198) (-) (-)	Maharashtra	08/2020 (03/2022)	03/2024 (08/2026)	1,711.38 0.00	979.42	99.87
1217	Vadape to Thane from km 539.202 to km 563.000 section of NH-3 new NH-848 (NHAII) (619203) (-) (-)	Maharashtra	03/2018 (01/2019)	07/2021 (10/2026)	1,252.92 0.00	491.86	87.00
1218	Capacity Augmentation in the stretch of Pimpri Sado Vadape section of NH848 Km. 460900 to Km. 537000 by Construction of Slip/Service Road on either side at various locations total length 25.140 Km LHSRHS, Flyover 2 x 25m at Borivali Junction Km. 528550 & LVUP 1 x 15m at Sherekarpada Km. 528800 (NHAII) (619204) (-) (-)	Maharashtra	12/2025 (04/2026)	10/2027 (10/2027)	372.03 0.00	1.50	1.00
1219	Dharampuri-Lonand from km. 117.00 to 166.40 Pkg-IV on Mohol-Alandi Section (NHAII) (619210) (-) (-)	Maharashtra	01/2021 (09/2021)	09/2023 (09/2026)	1,411.71 0.00	1,474.29	97.40
1220	Rehabilitation and upgradation of Wardha Salod Hirapur - Pulgaon Section of NH 347A from km 134/283 to Km 159/075 [Design Chainage Km 0000 to Km 24792] to two Lanes with paved shoulder configuration in the state of Maharashtra on EPC mode. (MoRTH) (619263) (-) (-)	Maharashtra	03/2025 (07/2026)	12/2027 (-)	252.95 0.00	0.05	0.00
1221	Construction of 6 Lane Elevated corridor from KM 612582 to KM 617540 including construction of Service Roads in Kolhapur City on NH -48 in the State of Maharashtra on EPC mode under NHO (NHAII) (619298) (-) (-)	Maharashtra	02/2026 (06/2026)	06/2029 (06/2029)	1,039.00 0.00	0.06	0.00
1222	Construction of a 6-Lane Elevated Corridor from Km 593766 to Km 596620 Including Construction of Service Roads in Kagal City on NH-48 in the State of Maharashtra on EPC Mode. (NHAII) (619299) (-) (-)	Maharashtra	03/2026 (06/2026)	06/2028 (06/2028)	357.99 0.00	0.08	0.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1223	Construction of Four Lane Nagpur-Katol section of NH-353J including Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I Mitigation Structures from Design Ch. 37000 to Ch. 45990 Tiger Corridor-I in the State of Maharashtra on EPC Mode (NHAI) (619300) (-) (-)	Maharashtra	01/2026 (06/2026)	12/2027 (12/2027)	300.68 0.00	0.00	0.00
1224	Widening/Improvement of existing 2-Lane road to 4-Lane Divided Highway from Sekmai to Nilakuthi section of Imphal-Kohima Road Design Chainage from Km 297700 to Km 308729 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5B (NHIDCL) (618298) (-) (-)	Manipur	03/2021 (07/2021)	01/2023 (09/2026)	211.70 0.00	272.30	95.48
1225	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Daili to Kuraopokpi section of Imphal-Kohima road NH-02 Design Chainage from Km 274610 to Km 287000 in the state of Manipur on EPC mode Pkg-4B (NHIDCL) (618299) (-) (-)	Manipur	09/2020 (12/2024)	06/2026 (01/2027)	268.98 0.00	210.28	58.70
1226	Improvement/Up-gradation of existing 2-Lane Road to 4-Lane Divided Highway from Taphukuki to Daili section of Imphal-Kohima road NH-02 Design Chainage from Km 262175 to Km 274610 in the state of Manipur on EPC mode Pkg-4A (NHIDCL) (618300) (-) (-)	Manipur	09/2020 (10/2020)	04/2022 (12/2026)	379.39 0.00	314.73	91.39
1227	Widening/Improvement of existing 2-lane to 4-Lane Divided Highway from Kuraopokpi to Sekmai section of Imphal-Kohima Road Design Ch. km 287.00 to 297.700 of NH-39 New NH-02 in state of Manipur on EPC mode Pkg-5A (NHIDCL) (618301) (-) (-)	Manipur	09/2020 (02/2025)	08/2026 (12/2026)	228.97 0.00	143.26	48.36
1228	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 16.900 to Km 30.970 of NH-202 in the state of Manipur on EPC mode Package-2 (NHIDCL) (618302) (-) (-)	Manipur	03/2020 (07/2020)	06/2022 (10/2026)	256.04 0.00	195.00	98.12
1229	Widening/Improvement to 2-lane with earthen shoulder of Yaingangpokpi - Finch corner road section of NH-202 from Km 0.000 to Km 16.900 of NH-202 in the state of Manipur on EPC mode Package-1 (NHIDCL) (618303) (-) (-)	Manipur	03/2020 (07/2020)	06/2022 (10/2026)	222.77 0.00	140.90	88.96
1230	Widening/Improvement to 2 Lane with earthen shoulder of Jessami to Laynen bridge Nagaland border section of NH-29 of Imphal -Ukhrul - Jessami Economic Corridor from km 0.000 to km 11.009 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-7 (NHIDCL) (618304) (-) (-)	Manipur	03/2023 (12/2024)	06/2026 (02/2027)	164.89 0.00	132.28	31.23
1231	Widening/Improvement to 2 lane with earthen shoulder of Marrem Khullen to Jessami section of NH-202 of Imphal - Ukhrul - Jessami Economic Corridor from Design Chainage km 95.700 to km 140.180 in the State of Manipur on EPC mode under Bharatmala Pariyojana under NHO-NE Package-6 (NHIDCL) (618305) (-) (-)	Manipur	03/2023 (12/2024)	12/2026 (08/2027)	554.66 0.00	230.00	27.34
1232	Widening/Improvement to 2 lane with earthen shoulder of Choithar to Marrem Khullen section of NH-202 of Imphal Ukhrul Jessami Economic Corridor from Design Chainage km 53.110 to km 95.700 in the State of Manipur on EPC mode under Bharatmala Pariyojana, under NHO-NE Package-5 (NHIDCL) (618306) (-) (-)	Manipur	03/2023 (05/2025)	03/2027 (08/2027)	564.05 0.00	173.58	14.50
1233	Widening to 2 lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 169570 Near Nungkao vllage under Tamenglong District to km 205974 near Jiribam Bridge under Jiribam district under NHO-NE PKG-7 (NHIDCL) (618333) (-) (-)	Manipur	01/2023 (12/2023)	12/2025 (12/2026)	760.16 0.00	428.17	92.52
1234	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from km 131.280 to km 169.570 on EPC mode in Manipur under NHO-TSP PKG-6 (NHIDCL) (618334) (-) (-)	Manipur	12/2021 (02/2023)	02/2025 (12/2026)	504.76 0.00	328.00	95.20
1235	Widening to 2 Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Ch. from Km 101280 Near Khongsang Village to Km 131280 near Puilon Kambiron Village on EPC Mode in Manipur PKG-5 (NHIDCL) (618335) (-) (-)	Manipur	12/2021 (11/2022)	05/2024 (12/2026)	410.68 0.00	386.28	91.02
1236	Widening to 2 -Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 66.110 km to 101.280 Km Existing Chainage km 67.496 to km 103.557 on EPC Mode in Manipur PKG-4 (NHIDCL) (618336) (-) (-)	Manipur	09/2021 (06/2022)	12/2023 (12/2026)	579.63 0.00	408.21	86.53
1237	Widening to 2-Lane with Paved shoulder of Imphal to Jiribam section of NH-37 from Design Chainage 15.940 km to 33.120 Km Existing Chainage Km 15.946 to Km 33.395 Total length17.180 Km in the State of Manipur on EPC mode PKG-2 - Balance Works & Rectification works (NHIDCL) (618338) (-) (-)	Manipur	03/2021 (03/2025)	03/2026 (10/2026)	195.14 0.00	162.73	93.22

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1238	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from Design Chainage 69.875 Km to 121.769 Km in the State of Manipur on EPC mode Package-3 (NHIDCL) (618344) (-) (-)	Manipur	03/2021 (08/2021)	08/2023 (12/2026)	673.27 0.00	563.39	85.84
1239	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section from Km 48.587 to Km 69.875 in the State of Manipur on EPC mode under NHO Package-2B (NHIDCL) (618345) (-) (-)	Manipur	06/2020 (08/2020)	08/2022 (10/2026)	365.53 0.00	198.73	88.20
1240	Widening to 2-lane with Hard shoulder of Churachandpur to Tuivai Section of NH-102B from km 32.835 to km 48.587 in the State of Manipur on EPC mode under NHO Package-2A (NHIDCL) (618346) (-) (-)	Manipur	04/2020 (07/2020)	06/2022 (09/2026)	232.99 0.00	155.44	100.00
1241	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from km 130.000 to km 141.029 Package-4B in the State of Manipur on EPC Mode (NHIDCL) (618348) (-) (-)	Manipur	06/2020 (11/2025)	11/2026 (11/2026)	177.76 0.00	100.95	14.63
1242	Balance work of Widening to 2 Two lane with hard shoulder of Churachandpur to Tuivai section of NH-102B from Design Chainage km 118850 to km 130000 Package-4A in the State of Manipur on EPC Mode (NHIDCL) (618349) (-) (-)	Manipur	04/2020 (08/2025)	08/2026 (11/2026)	204.12 0.00	115.96	26.53
1243	Construction of of 2 -Lane with paved shoulders road from Tamenglong-Tousem-Lisang-Mahur Road NH-137 starting near Dialong Village from km 10.000 at Dialong to km 31.430 near Old Tamenglong , near Barak River on EPC Mode Package-2 (NHIDCL) (618355) (-) (-)	Manipur	07/2021 (09/2021)	03/2023 (03/2026)	483.87 0.00	375.87	95.28
1244	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur in the state of Manipur from km 31.430 at Old Tamenglong to km 43.480 ending near Phelong on EPC Mode Package-3 (NHIDCL) (618356) (-) (-)	Manipur	03/2021 (06/2021)	12/2022 (04/2026)	234.08 0.00	201.13	98.50
1245	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 in Manipur starting from km 54.180 near Azuram to km 80.630 near Mandeu on EPC Mode Package 5 (NHIDCL) (618357) (-) (-)	Manipur	09/2021 (11/2021)	05/2023 (01/2026)	477.86 0.00	330.13	84.87
1246	Construction of 2 -Lane with paved shoulders road from Tamenglong to Mahur NH-137 starting from km 80.630 near Mandeu to km 96.870 near Jiri River on EPC Mode Package-6 (NHIDCL) (618358) (-) (-)	Manipur	09/2021 (11/2021)	05/2023 (12/2025)	311.18 0.00	231.08	87.42
1247	Construction of 2-laning with Hard shoulder of Ukhrul Tolloi - Tadubi section of NH-102A from Design Chainage km 9450 to km 50850 in the State of Manipur on EPC mode under NHO-NE Package-2 (NHIDCL) (618387) (-) (-)	Manipur	03/2023 (03/2024)	03/2026 (12/2026)	578.98 0.00	283.36	80.75
1248	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 50.850 km to 81.870 km in the State of Manipur on EPC mode under NHO-TSP Package -3 (NHIDCL) (618388) (-) (-)	Manipur	09/2021 (07/2023)	01/2025 (12/2026)	315.56 0.00	257.41	94.50
1249	Construction of 2-laning with Hard shoulder road of Ukhrul - Tolloi - Tadubi section of NH-102A from Design Chainage 81.870 km to 105.825 km in the State of Manipur on EPC mode under NHO-TSP Package -4 (NHIDCL) (618389) (-) (-)	Manipur	09/2021 (08/2022)	02/2024 (10/2026)	310.76 0.00	287.73	97.00
1250	Improvement of existing road to 2 laning with Hard Shoulders of Maram-Peren section Package-1B, length- 17.660 km from Design Chainage 22.340 km to 40.000 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618415) (-) (-)	Manipur	02/2021 (06/2021)	12/2022 (03/2026)	188.36 0.00	0.00	100.00
1251	Improvement of existing road to 2 laning with Hard Shoulders of Maram -Peren section Package-1A, length- 22.340Km from Design Chainage 0.000 km to 22.340 km on NH-129A in the State of Manipur on EPC mode (NHIDCL) (618416) (-) (-)	Manipur	02/2021 (06/2021)	12/2022 (03/2027)	226.32 0.00	190.19	75.08
1252	Rehabilitation and Up-gradation of Nongstoin Wahkaji section of Project Road Km 0000 to Km 43060 to Intermediate Lane with earthen shoulder under SARDP-NE Phase-A in the State of Meghalaya on EPC mode. Job No- SARDP-NE ong-Don-Maw/MG/2020-21/294 (MoRTH) (617885) (-) (-)	Meghalaya	08/2020 (02/2022)	08/2023 (09/2026)	302.88 0.00	232.62	99.62
1253	Improvement and Widening two lannig with paved Shoulder of NH 127B from km 31.500 Goeragre to km 63.224 Package-II in state of Meghalaya (MoRTH) (618076) (-) (-)	Meghalaya	12/2023 (05/2025)	05/2027 (-)	504.00 0.00	75.72	4.50

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1254	Improvement and Widening of National Highway No. 127B Darugiri - Songsak - Williamnagar Junction Section to two lane with paved shoulder from design Km 0000 to Km 36635 Design length 36.635 Km existing Km 112000 to Km 151060 of NH-1278 under Bharatmala Pariyojana Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618294) (-) (-)	Meghalaya	03/2023 (09/2025)	09/2027 (09/2027)	801.07 0.00	186.68	27.76
1255	Improvement/Widening of New NH-217 Dainadubi-Darugiri section to Two lane with paved shoulder in Meghalaya from design Km 0000 to Km 40840 existing Km 8600 to Km 53000 of Old NH-62 under BMP Lot-1 Pkg-1B Meghalaya portion (NHIDCL) (618295) (-) (-)	Meghalaya	03/2023 (03/2025)	03/2027 (03/2027)	705.83 0.00	0.00	49.82
1256	Improvement/Widening to 2-L with Paved Shoulder/ 4-Laning of NH-40 section from Km 151330 to Km 163400 design Km 63.530 to Km 71.520 including Dawki Bridge of length 368 m between Shillong-Dawki under JICA ODA Loan assistance Phase-II Pkg-5 -Balance work (NHIDCL) (618374) (-) (-)	Meghalaya	07/2020 (05/2024)	11/2026 (11/2026)	284.21 0.00	170.81	43.86
1257	Improvement/Widening to 2-Lane with Paved Shoulder from design Km 45.760 to Km 63.530 between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance work Pkg-4 (NHIDCL) (618375) (-) (-)	Meghalaya	07/2020 (04/2024)	04/2026 (10/2026)	445.51 0.00	42.39	53.85
1258	Improvement/Widening to 2-Lane with Paved Shoulder between Shillong-Dawki road up to Bangladesh Border from design Km 10.670 to Km 37.550 under JICA ODA Loan assistance Phase-II -Balance Work-Pkg-2 (NHIDCL) (618376) (-) (-)	Meghalaya	07/2020 (02/2024)	08/2026 (12/2026)	525.67 0.00	0.00	53.22
1259	Improvement/Widening to 2-L with Paved Shoulder/4-L from Km 81740 to Km 93490 design Km 0000 to Km 10670 of NH-40 New NH-106 & 206 section & 4-L from design Km 0.00 to Km 0.930 of NH-44 section between Shillong-Dawki under JICA ODA Loan assistance Phase-II -Balance Work Pkg-1 (NHIDCL) (618377) (-) (-)	Meghalaya	07/2020 (10/2023)	10/2025 (06/2026)	351.12 0.00	243.50	100.00
1260	Rehabilitation and up gradation of Nongstoin-Rambrai-Kyrshai road up to Meghalaya-Assam border from Km 0.335 to km 34.039 to 2-Lane under NHO - NE in the State of Meghalaya Package-1 (NHIDCL) (618418) (-) (-)	Meghalaya	09/2021 (05/2022)	05/2024 (03/2027)	359.86 0.00	310.09	83.15
1261	Construction of 2-Lane with paved shoulders of Shillong Western Bypass starting from NH-06 near Ladumsaw existing Km 60.900 of old NH40 to NH106 old NH 44E Package-III, from km 24700 to km 38256 under SARDP-NE PHASE A in the state of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618419) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (06/2027)	562.48 0.00	340.17	52.29
1262	Construction of 2 lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw existing km 60.900 of old NH-40 to NH-106 old NH-44E, Package-II km 12800 to km 24700 under SARDP-NE Phase A in the State of Meghalaya on EPC Mode (NHIDCL) (618420) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (06/2027)	686.03 0.00	360.59	50.95
1263	Construction of 2-Lane with paved shoulder of Shillong Western Bypass starting from NH-06 near Ladumsaw Existing km 60.900 of old NH-40 to NH106 old NH-44E, km 0000 to km 12800 Package-I under SARDP-NE PHASE A in the State of Meghalaya on EPC Mode Greenfield alignment (NHIDCL) (618421) (-) (-)	Meghalaya	03/2023 (09/2024)	09/2026 (03/2027)	620.30 0.00	332.96	75.41
1264	4-Laning of Vairengte - Chhimluang section Package-3 of NH-306 from Existing Chainage km 43000 to Km 59700 Design Chainage km 46000 to km 60850 on Silchar - Vairengte- Sairang road in the State of Mizoram under Bharatmala Pariyojna under NHO-NE. Package-1&2 in Assam state (NHIDCL) (618316) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	491.39 0.00	245.24	17.86
1265	4-Laning of chhimluang-Kolasib from section pkg-4 of NH-306 & NH-6 existing chainage km 59700 to km 86000 design chainage km 61000 to km 77500 on Silchar-vairengte-sairang road in the state of Mizoram under Bharatmala Pariyojna on EPC mode Vairengte - Sairang Pkg-4 (NHIDCL) (618317) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	561.91 0.00	224.19	17.12
1266	4-Laning of Kolasib - Sethawn section Package-5 of NH-6 from Existing Chainage km 86000 to km 107850 Design Chainage km 77500 to km 95500 on silchar - voirengte - sairang road under Bharatmala Pariyojna on EPC mode under NHO-NE Vairengte - Sairang Pkg-5 (NHIDCL) (618318) (-) (-)	Mizoram	11/2021 (07/2025)	07/2027 (06/2027)	720.40 0.00	260.12	11.86
1267	4-Laning of Sethawn - N. Kawnpui section Package-6 of NH-6 from Existing Chainage km 107850 to km 126315 Design Chainage km 95500 to km 111850 on Silchar-Vairengte- Sairang road, Vairengte - Sairang Pkg-6 (NHIDCL) (618319) (-) (-)	Mizoram	12/2021 (07/2025)	01/2027 (12/2026)	595.65 0.00	189.40	6.72

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1268	Construction of 4-Laning of N. Kawnpui N. Mualvum Mualkhang via Khamrang Village section Package-7 of NH-6 from Existing Chainage km 127200 to km 142000 Design Chainage km 111850 to km 123400 on Silchar - Vairengte - Sairang road in the State of Mizoram on EPC mode (NHIDCL) (618320) (-) (-)	Mizoram	02/2024 (10/2025)	10/2028 (-)	866.32 0.00	198.28	18.90
1269	Construction of 4-Laning of West Serawlg-Sairang section of NH-6 from Existing Chainage km 142000 to km 158900 Design Chainage km 123400 to km 136260 on Silchar - Vairengte - Sairang road in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-8 (NHIDCL) (618321) (-) (-)	Mizoram	02/2024 (11/2025)	11/2028 (-)	875.79 0.00	288.71	13.95
1270	Construction of Twin Tube Uni-directional Aizawl Bypass Tunnel of 2.5 km and its approaches of 2.1 km from km 10.600 to km 15.200 on Sarrang - Phaibawk section of NH-6 in the State of Mizoram on EPC Mode under NHO-NE Package-2 (NHIDCL) (618323) (-) (-)	Mizoram	01/2024 (12/2025)	12/2028 (-)	1,313.28 0.00	0.11	0.00
1271	Construction of 2-lane Aizawl Bypass from km 15.200 to km 34.500 Package-3 on Sairang - Phaibawk section of NH-6 in the State of Mizoram under Bharatmala Pariyojna on EPC Mode under NHO-NE (NHIDCL) (618324) (-) (-)	Mizoram	02/2023 (10/2025)	11/2028 (-)	720.72 0.00	102.91	15.10
1272	Construction of 2-laning with hard shoulder of Lunglei to Chhumkhum from Design Chainage Km 0.000 to Km 37.420 of NH-302 [Lunglei-Tlabung] Package-A (NHIDCL) (618362) (-) (-)	Mizoram	03/2021 (06/2021)	12/2022 (11/2026)	698.45 0.00	554.29	64.78
1273	Construction of 2-laning with hard shoulder configuration of Chhumkhum to Tlabung from Design Chainage Km 37.420 to Km 74.950 of NH-302 in Mizoram under Bharatmala Pariyojana on EPC mode [Pkg-B] (NHIDCL) (618363) (-) (-)	Mizoram	06/2021 (07/2021)	01/2023 (12/2026)	740.58 0.00	494.49	61.34
1274	Widening and Up-gradation to 2- Lane with Paved Shoulder Configuration and geometric improvement from Km. 208. 000 to Km 250.000 Package-5 on Aizawl Tuipang Section of NH-54 in the State of Mizoram Package-5 (NHIDCL) (618379) (-) (-)	Mizoram	09/2019 (10/2019)	04/2023 (08/2026)	752.89 0.00	125.64	95.35
1275	Widening and up-gradation to 2-lane with paved shoulder configuration and geometric improvements from km 339.00 to km 380.00 Siaha on Aizawl-Tuipang section under JICA ODA Loan assistance Phase-I Package-8 (NHIDCL) (618383) (-) (-)	Mizoram	09/2019 (03/2020)	09/2023 (06/2026)	637.06 0.00	551.56	99.82
1276	2-laning of Zorinpui - Longmasu section of NH-502A from km 0.000 to km 28.244 in the State of Mizoram on EPC mode under NHO-NE, stretch of IMBR (NHIDCL) (618452) (-) (-)	Mizoram	02/2023 (12/2024)	12/2026 (12/2027)	781.85 0.00	48.39	4.71
1277	Up-gradation to 2 lane with paved shoutders of Pawlrang - Rulchawm section- of NH-102B of Aizawl - Imphal Economic Corridor from Existing Chainage km 72.030 to km 104.129 including 2.459 km re-alignment section from Tuivai River to Rulchawm connecting km 48.150 of NH-6 [Design Chainage km 68.170 to km 98.579] in the State of Mizoram under Bharatmala Pariyojna on EPC mode under NHO-NE Package-3 Keifang- Tuivai Pkg-3 (NHIDCL) (619010) (-) (-)	Mizoram	12/2021 (11/2023)	05/2025 (07/2026)	500.88 0.00	443.52	99.52
1278	Balance work of widening to two laning/re-alignment and geometric improvement from Km. 11000 to Km. 114618 with rectification of damaged stretches and provision of protection works in vulnerable location of NH-44 in the State of Mizoram. (MoRTH) (619321) (-) (-)	Mizoram	10/2025 (05/2026)	05/2028 (-)	170.96 0.00	0.00	2.00
1279	Bangalore Chennai Expressway Phase-II Pkg-I from km.71.000 to Km 96.000 Bethamangala in the state of Karnataka to Byreddypalli (NHAI) (619199) (-) (-)	Multi-States (Andhra Pradesh, Karnataka)	12/2020 (10/2022)	10/2024 (09/2026)	1,410.01 0.00	747.22	99.20
1280	6L Aluru - Jakkuva Section of NH-130CD Road from km 365.033 to km 396.800 Pkg. 1 (NHAI) (618681) (-) (-)	Multi-States (Andhra Pradesh, Odisha)	02/2021 (03/2022)	03/2024 (10/2026)	1,216.12 0.00	731.37	99.63
1281	Bangalore Chennai Expressway Phase-III Package I Gudipala to Walajahpet from Km 156.000 to Km 180.000 (NHAI) (618477) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	10/2020 (05/2022)	05/2024 (10/2026)	1,481.87 0.00	751.77	99.02
1282	6L of Veera Kaveri Raja Puram to Pondavakkam from km 61.380 to km 96.040 of NH 716B Pkg-III (NHAI) (618634) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	03/2021 (01/2023)	01/2025 (09/2026)	1,439.77 0.00	809.30	98.89
1283	Walajahpet/Ranipet to TN/AP Border Section of from Km.106.800 to Km.133.36 NH-4 (NHAI) (618769) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	12/2024 (09/2025)	09/2027 (09/2027)	1,338.14 0.00	243.33	15.58

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1284	6L of Kumarajapet to Veera Kaveri Raja Puram from km 43.800 to km 61.380 of NH-716B Pkg-II (NHAI) (618772) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	02/2021 (10/2023)	10/2025 (09/2026)	702.52 0.00	405.96	99.80
1285	6 laning of Balance Work of Chennai - Tada from km. 21.40 to km. 54.40 (NHAI) (619077) (-) (-)	Multi-States (Andhra Pradesh, Tamil Nadu)	12/2017 (03/2018)	03/2020 (09/2026)	464.62 0.00	389.97	100.00
1286	Khammam-Devarapalle Pkg III [4L Access Controlled Greenfield from Chintagudem village to Recherla village Design Chainage 63117 to 105236] (NHAI) (618747) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	01/2021 (09/2022)	09/2024 (09/2026)	829.50 0.00	669.77	98.82
1287	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from Remidicherla village at Design Ch. 280.200 Km to Jakkampudi village on NH-16 at Design Ch. 309.909 Km Package-III (NHAI) (618818) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2023 (10/2025)	05/2027 (12/2027)	1,183.23 0.00	229.02	5.80
1288	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from Brahmanapallik village at Design Ch. 250.400 Km to Remidicherla village at Design Ch. 280.200 KmPackage-II (NHAI) (619143) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	03/2023 (03/2025)	03/2027 (06/2027)	826.01 0.00	176.60	25.78
1289	6L Access Controlled Greenfield Highway of Julekal village to Dinnedevarapadu village from Km 242.200 to Km 280.400 Pkg-2 (NHAI) (619212) (-) (-)	Multi-States (Andhra Pradesh, Telangana)	01/2022 (01/2023)	01/2025 (04/2027)	1,227.57 0.00	539.20	70.60
1290	Widening/Improvement to 4-Lane with Paved Shoulder from km 55000 Nagabang Gamsuk to km 82514 Oyan in the State of Assam and Arunachal Pradesh on EPC mode under Bharatmala Pariyojna of Length 27.514 Km Package-3 (NHIDCL) (618359) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	03/2023 (09/2024)	03/2027 (03/2027)	665.47 0.00	380.97	96.70
1291	6L of Aurangabad to Bihar-Jharkhand border Chordaha section from km. 180.000 to km. 209.827 of NH-2 PKG-01 (NHAI) (618531) (-) (-)	Multi-States (Bihar, Jharkhand)	02/2021 (12/2024)	12/2026 (12/2026)	1,054.46 0.00	242.25	37.93
1292	6L Greenfield Varanasi-Ranchi-Kolkata Highway from Anarbansalea village to Sagrampur village From KM. 151200 to KM. 184700Package-7 (NHAI) (618724) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2023 (07/2025)	06/2027 (03/2028)	1,719.20 0.00	388.27	28.16
1293	6L Greenfield Varanasi- Ranchi- Kolkata Highway from Sonepurbigha village to junction with NH- 22 Chatra Bypass near Chatra from km 184.700 to km 222.000Pkg - 8 (NHAI) (618732) (-) (-)	Multi-States (Bihar, Jharkhand)	03/2023 (05/2026)	05/2028 (05/2028)	1,728.17 0.00	204.73	4.50
1294	Hariharganj to Parwa Mode section from km 23.284 to km 57.049 of NH-98 (NHAI) (618951) (-) (-)	Multi-States (Bihar, Jharkhand)	09/2020 (03/2022)	02/2024 (09/2026)	1,125.78 0.00	830.08	91.30
1295	4L of Sahibganj - Manihari Ganga Bridge including Manihari Bypass (NHAI) (618952) (-) (-)	Multi-States (Bihar, Jharkhand)	10/2016 (11/2020)	10/2024 (10/2027)	2,301.89 0.00	2,026.97	87.02
1296	Six Laning of Bihar - Jharkhand Border Chordaha - Gorhar section of NH-2 from km 249.525 to km 320.810 (NHAI) (619078) (-) (-)	Multi-States (Bihar, Jharkhand)	12/2017 (06/2019)	11/2021 (12/2026)	1,772.70 0.00	1,292.61	78.00
1297	4L of Munger Mirzachauki section from Km 157350 to Km 193931 Pkg-4 (NHAI) (619307) (-) (-)	Multi-States (Bihar, Jharkhand)	02/2021 (08/2022)	08/2024 (10/2026)	1,376.56 0.00	896.75	92.74
1298	Six Laning of Varanasi to Aurangabad from km. 786.00 to km. 978.40 of Old NH-2 (NHAI) (618530) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	02/2009 (09/2011)	03/2014 (09/2026)	3,241.56 0.00	2,864.10	99.92
1299	6L Greenfield Varanasi-Ranchi-Kolkata Highway from junction with NH-19 & Varanasi Ring Road near Rewasa village to junction with Chandauli-Chainpur road near Khainti village from Km. 0.000 to Km. 27.000 - Pkg-1 (NHAI) (618728) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2023 (11/2024)	11/2026 (05/2027)	1,433.39 0.00	598.10	47.63
1300	Construction of additional 3-Lane Bridge over River Ganga for connection between Buxar and Bharauli on NH-922 in the State of Uttar Pradesh and Bihar on Hybrid Annuity Mode (NHAI) (618882) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	03/2024 (08/2025)	02/2028 (02/2028)	531.61 0.00	47.40	22.26
1301	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package III [from Pindari km 78.150 to Rawalganj Bypass Km 117.120] on EPC Mode in the state of Uttar Pradesh. (NHAI) (619154) (-) (-)	Multi-States (Bihar, Uttar Pradesh)	10/2022 (08/2023)	08/2025 (11/2026)	1,493.50 0.00	1,064.59	86.11

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1302	4L of Kishanganj - Bahadurganj section from Km. 0.000 to Km. 23.649 & interchange at Start Point Length - 1.200 Km of NH-27 (NHAI) (618584) (-) (-)	Multi-States (Bihar, West Bengal)	01/2025 (12/2025)	12/2027 (12/2027)	962.84 0.00	221.43	20.14
1303	Vadodara Mumbai Expressway Talsari to Karvad Phase IB - Pkg X [Km 103.400 to Km 128.000] (NHAI) (619064) (-) (-)	Multi-States (Dadra & Nagar Haveli and Daman & Diu, Gujarat, Maharashtra)	10/2020 (03/2022)	03/2024 (12/2027)	1,909.74 0.00	1,098.49	36.23
1304	Balance work of 2L PS from Km 30.800 to Km 70.800 and 2L with Rigid Carriageway from Km 70.800 to km 84.120 of Khanapur- KA/GOA Border section of NH-4A (NHAI) (618942) (-) (-)	Multi-States (Goa, Karnataka)	01/2022 (11/2022)	05/2024 (03/2027)	226.76 0.00	110.31	85.80
1305	Bal. Works of Fagne Km. 510.000 to Maharashtra/Gujarat Border Km. 650.794 (NHAI) (618637) (-) (-)	Multi-States (Gujarat, Maharashtra)	12/2019 (09/2020)	09/2022 (12/2026)	1,654.07 0.00	1,448.08	99.70
1306	Delhi-Amritsar-Katra Expressway Phase-I Pkg-V from Junction with Ambala-Kaithal-Hissar road NH-152 near Kharak Pandwa village to Junction with Patiala-Samana-Patran road SH-10 near Ghagga village Km 120250 to Km 157920 (NHAI) (618486) (-) (-)	Multi-States (Haryana, Punjab)	01/2021 (05/2022)	05/2024 (09/2026)	1,741.86 0.00	1,508.23	98.70
1307	4L Ismailabad to Ambala Section of NH-152 Lot-4/Package-1 (NHAI) (619093) (-) (-)	Multi-States (Haryana, Punjab)	02/2023 (12/2023)	12/2025 (02/2027)	609.32 0.00	311.06	76.30
1308	6L of Ambala-Chandigarh greenfield section from Km. 0.000 to Km. 25.000 with 4L spur to Lalru from Km. 0.000 to Km. 5.828 & spur to PR-7 road from Km. 0.000 to Km. 11.157 (NHAI) (619134) (-) (-)	Multi-States (Haryana, Punjab)	03/2022 (10/2023)	10/2025 (09/2026)	1,641.66 0.00	1,296.35	90.01
1309	6L access Controlled Greenfield Highway from Adhoya Musalmana to Sadopur section of Shamli -Ambala Package-III Design Ch. Form km 84.400 to km 121.786 (NHAI) (619216) (-) (-)	Multi-States (Haryana, Punjab)	05/2022 (05/2023)	05/2025 (12/2026)	1,491.72 0.00	825.10	81.33
1310	Additional Structures on 6LGurgaon-Jaipur Section of NH-48 between KM 42.700 to KM 273.00 (NHAI) (618505) (-) (-)	Multi-States (Haryana, Rajasthan)	08/2022 (12/2022)	06/2024 (11/2026)	409.64 0.00	204.85	88.90
1311	4 laning of Aligarh-Palwal Section from Km. 46.390 Design Chainage to Km. 69.110 Terminating at junction EPE Package-II from Kurana- Eastern Peripheral Expressway of NH-334D (NHAI) (618691) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	03/2024 (08/2025)	08/2027 (08/2027)	939.17 0.00	276.52	17.16
1312	6L access Controlled Greenfield Highway from Ranipur Barsi to Adhoya Musalmana section of Shamli -Ambala Package-II Design Ch. Form km 45.500 to km 84.400 (NHAI) (618723) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	06/2022 (05/2023)	05/2025 (02/2027)	1,554.21 0.00	862.64	82.75
1313	Construction of Greenfield Connectivity to Jewar International Airport from DND-Faridabad-Ballabhgarh Bypass KMP Link - Spur to Delhi Mumbai Expressway (NHAI) (619068) (-) (-)	Multi-States (Haryana, Uttar Pradesh)	07/2022 (06/2023)	06/2025 (04/2027)	2,920.69 0.00	1,804.32	76.30
1314	2L/4L of Hoshiarpur to Una section including Hoshiarpur Bypass of NH 503A (NHAI) (618907) (-) (-)	Multi-States (Himachal Pradesh, Punjab)	03/2023 (05/2025)	05/2027 (05/2027)	571.34 0.00	265.20	26.43
1315	Delhi-Amritsar-Katra Expressway Phase-II Pkg-XIV from Junction with Pathankot-Gurdaspur road NH-54 near Balsua to Junction with Hiranagar Road near village Gurha Baildaran km 423500 to km 468100 (NHAI) (619066) (-) (-)	Multi-States (Jammu and Kashmir, Punjab)	10/2021 (09/2022)	09/2024 (10/2026)	3,044.02 0.00	1,782.31	87.30
1316	Barwa Adda Km. 398.240 to Panagarh Km. 521.120 (NHAI) (618533) (-) (-)	Multi-States (Jharkhand, West Bengal)	08/2010 (04/2014)	09/2016 (09/2026)	1,560.39 0.00	1,696.36	100.00
1317	6L Greenfield Varanasi- Ranchi- Kolkata Highway from junction with NH-320 in Lepo village to Kamlapur villageJH/WB border from km 358.500 to km 387.200 Pkg -13 (NHAI) (618734) (-) (-)	Multi-States (Jharkhand, West Bengal)	03/2023 (09/2025)	09/2027 (09/2027)	1,154.49 0.00	331.43	24.76
1318	2L PS of JH / WB Border km. 70.524 - Purulia km.84.400 & Purulia km. 94.30 - Chandil Junction with NH-33 km. 153.705 of Old NH-32 (NHAI) (618909) (-) (-)	Multi-States (Jharkhand, West Bengal)	03/2018 (12/2019)	08/2022 (10/2026)	1,652.40 0.00	1,652.44	97.75
1319	4L of NH-80 section of Mirza Chauki to Farakka section from existing km 190.00 to design km 200.75 junction at km 3.100 of NH 133 B and from existing km 260.00 to existing km 283.00 design km 274.133 in the state of Jharkhand package - II (NHAI) (618948) (-) (-)	Multi-States (Jharkhand, West Bengal)	02/2025 (02/2026)	01/2028 (01/2028)	782.18 0.00	225.87	7.98
1320	Six Laning of KT/KL Border Thalapaddy -Chengala from Km. 17.200 to Km. 57.20 (NHAI) (619205) (-) (-)	Multi-States (Karnataka, Kerala)	05/2020 (11/2021)	05/2024 (09/2026)	1,981.07 0.00	1,795.92	100.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1321	6L from Sankeshwar Bypass to MH-KNT Border from Km. 555.017 to Km. 592.853 of NH-48 Pkg-II (NHAI) (618516) (-) (-)	Multi-States (Karnataka, Maharashtra)	01/2022 (10/2022)	04/2025 (05/2027)	1,388.70 0.00	1,203.78	85.30
1322	Akkalkot MH/KN border New Greenfield corridor from Km 512.000 to Km 548.400 of NH-150C part of Akkalkot KN/TS Border section Package XIV (NHAI) (618636) (-) (-)	Multi-States (Karnataka, Maharashtra)	03/2023 (10/2024)	10/2026 (06/2027)	1,370.75 0.00	336.55	57.54
1323	Bangalore Ring Road STRR-NH-948A- Package-I of Phase-III from Belagondapalli TN to TN/KNT border from km 144.480 to 179.969 (NHAI) (618519) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	03/2022 (05/2023)	05/2025 (12/2026)	1,260.74 0.00	777.13	92.95
1324	Hosur to Dhamrapuri Pkg-1 [Neraluru - Thorapalli Agraharam] (NHAI) (618581) (-) (-)	Multi-States (Karnataka, Tamil Nadu)	10/2021 (10/2022)	10/2024 (01/2027)	1,828.66 0.00	1,467.50	78.70
1325	6L of MH/KN Border Nimbal Village to KN/TS Border Singnodi Village from Km. 162.5 to Km. 203.100 in Raichur of NH-150C Pkg-IV (NHAI) (618631) (-) (-)	Multi-States (Karnataka, Telangana)	03/2022 (11/2022)	05/2025 (09/2026)	1,499.73 0.00	840.34	99.51
1326	6L Access Controlled Greenfield Highway of Nandinne village to Julekal village from Km 202.900 to Km 242.200 Pkg-1 (NHAI) (618632) (-) (-)	Multi-States (Karnataka, Telangana)	02/2022 (01/2023)	01/2025 (09/2026)	972.06 0.00	459.47	93.79
1327	Thalassery Mahe Bypass Km 170.600 to Km 189.200 of NH-17New NH-66 in Kerala (NHAI) (619097) (-) (-)	Multi-States (Kerala, Puducherry)	09/2017 (12/2017)	05/2020 (09/2026)	1,181.12 0.00	1,534.73	100.00
1328	4L Shahpur to Muktainagar from Km. 186.000 to km 216.278 of NH 753L Pkg II of Boregaon Buzurg to Muktainagar (NHAI) (619101) (-) (-)	Multi-States (Madhya Pradesh, Maharashtra)	12/2022 (03/2024)	03/2026 (10/2026)	784.35 0.00	368.01	64.00
1329	Construction of 26 VUPs, Major Bridge, Service Road etc. on Lalitpur-Sagar-Lakhnadon section of NH-44 NS (NHAI) (618556) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	02/2023 (03/2024)	03/2026 (08/2026)	665.91 0.00	574.39	97.40
1330	4L of Chowka to Kaimaha near MP/UP Border section NH-34 from D. Ch. 145.000 to D. Ch. 197.266 excluding existing Chhatarpur bypass from D. Ch. 160.307 to D. Ch. 168.630 Package-4 (NHAI) (618668) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	10/2024 (09/2025)	09/2027 (09/2027)	996.50 0.00	328.65	49.18
1331	4L of Bamni - Rajura - Warur - Devada upto M.S. Border of NH - 930D from km 19.000 to km 51.985 (NHAI) (618941) (-) (-)	Multi-States (Maharashtra, Telangana)	03/2022 (03/2024)	03/2026 (12/2026)	968.05 0.00	852.15	78.16
1332	Viluppuram Km.0.000 to Puducherry Km.29.000 (NHAI) (618844) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (10/2026)	1,358.31 0.00	527.54	98.32
1333	Puducherry Km.29.000 to Poondiyankuppam Km.67.000 (NHAI) (618845) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (11/2021)	11/2023 (10/2026)	1,588.40 0.00	460.48	98.75
1334	Sattanathapuram to Nagapattinam from Km 123.800 to Km 179.555 (NHAI) (618847) (-) (-)	Multi-States (Puducherry, Tamil Nadu)	03/2018 (10/2020)	10/2022 (12/2026)	2,899.77 0.00	1,595.47	85.60
1335	6L with access control provision Saharanpur bypass to Ganeshpur section from 13.89 Km to 41.820 Km of Delhi- Dehradun Economic Corridor package-2 (NHAI) (618711) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2022 (11/2022)	11/2024 (09/2026)	796.65 0.00	510.29	99.29
1336	4-laning of Pilibhit - Sitarganj from Km. 32.500 to Km. 70.800 Pkg-2 of NH-30 (NHAI) (618783) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	01/2023 (03/2024)	03/2026 (10/2027)	1,471.19 0.00	480.64	44.41
1337	Road Safety Improvement of Critical Junctions on MuzaffarnagarHaridwar Section of NH-334 from Km 143000 to Km 196000 (NHAI) (618886) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	04/2025 (10/2025)	10/2027 (10/2027)	238.66 0.00	47.37	22.64
1338	Improvement & Up-gradation of NH-734 Section of Moradabad-Thakurdwara Kashipur including Moradabad & Kashipur Bypass Package-III Kashipur Bypass Length 14.490 Km., Starts from Ch. 38770 and ends at Ch. 53260 existing Ch. 05560 (NHAI) (618928) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	02/2023 (03/2024)	09/2025 (03/2027)	936.12 0.00	400.47	53.84
1339	4/6L of Spur to Haridwar Greenfield from Km. 0.000 to Km. 50.70 (NHAI) (618969) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	11/2021 (02/2023)	02/2025 (09/2026)	2,155.95 0.00	1,543.42	92.98
1340	4L of Haridwar-Nagina section from km. 0.00 to km. 71.614 of NH-74 (NHAI) (619217) (-) (-)	Multi-States (Uttar Pradesh, Uttarakhand)	12/2015 (01/2018)	07/2020 (10/2026)	1,659.12 0.00	1,548.54	99.85

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1341	Widening of existing Single lane / Intermediate lane road to 2 lane from Km 101 to Km 125 of NH 61 (MoRTH) (617886) (-) (-)	Nagaland	06/2020 (06/2024)	06/2026 (04/2027)	252.20 0.00	65.40	44.46
1342	Construction of 2-lane with Paved shoulder of Kohima- Bypass Road Connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29, NH-39New NH-02 from Design Km 32.00 to Design Km 43.454Design Length-11.454 Km in the State of Nagaland under SARDP-NE on EPC Mode Package-IV (NHIDCL) (618290) (-) (-)	Nagaland	07/2020 (10/2020)	04/2022 (12/2026)	202.36 0.00	102.45	46.77
1343	Construction of 2-lane with Paved shoulder of Kohima-Bypass Road connecting NH-39 New NH-02, NH150New NH-02, NH7-61 New NH-29 and NH-39 New NH-02 from Design km 21.000 to km 32.268 [Design length11.268 km] in the state of Nagaland Under SARDP-NE on EPC Mode Package- 3 (NHIDCL) (618291) (-) (-)	Nagaland	07/2020 (06/2023)	06/2025 (12/2026)	159.85 0.00	128.51	39.62
1344	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting New NH-02 and New NH-29 from Design Km 10.500 to design Km 21.000 [Design Length-10.500 km] including TUNNEL of 500m at Ch. 11.000 in the state of Nagaland Under SARDP-NE on EPC Mode Package-2 (NHIDCL) (618292) (-) (-)	Nagaland	07/2020 (10/2020)	10/2022 (10/2027)	277.44 0.00	201.99	71.29
1345	Construction of 2-Lane with paved shoulder of Kohima-Bypass Road connecting NH-39New NH-02, NH-150New NH-02, NH-61New NH-29 and NH-39New NH-02 from design Km 0.00 to Km 10.500 in the State of Nagaland under SARDP-NE on EPC Mode Package-1 -Balance work (NHIDCL) (618293) (-) (-)	Nagaland	07/2020 (11/2023)	11/2026 (11/2026)	232.29 0.00	120.94	27.39
1346	Balance work of Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 old NH-150 from existing km 98.380 near Chizami vill. to km120.367 Nagaland/Manipur Border [Design km 95.700 to design km 117.200] [Design Length 21.500 km] in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode Package-V under NHO (NHIDCL) (618296) (-) (-)	Nagaland	03/2020 (11/2023)	11/2025 (09/2026)	330.80 0.00	268.18	98.39
1347	Construction of 2-lane with hard shoulder of Kohima - Jessami road on NH-29 Old NH-150 from existing Km 30.474 Near Kidwema road Chakahabama to existing Km 53.220 Near Kikruma Village Design Km 29.60 to Km 51.50 Design length-21.90 Km in the state of Nagaland Under Bharatmala Pariyojna on EPC Mode under NHO Package-II -Balance work (NHIDCL) (618297) (-) (-)	Nagaland	03/2020 (01/2024)	01/2026 (12/2026)	355.79 0.00	0.00	43.13
1348	4-Laning of Balance work of Dimapur-Kohima Road from design km 152.490 to km 166.700 Existing km 156.000 to km 172.900 Excluding Dimapur & Kohima Bypass under SARDP-NE Package-III (NHIDCL) (618328) (-) (-)	Nagaland	03/2016 (09/2023)	09/2025 (09/2026)	562.98 0.00	551.33	84.32
1349	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-I Design Chainage 0000 Km to 34795 Km, in the State of Nagaland on EPC mode under NH O-NE (NHIDCL) (618364) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	430.24 0.00	0.00	87.00
1350	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-III Design Chainage 69875 Km to 106816 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618365) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	497.18 0.00	0.00	85.67
1351	Widening to 2 Lane with Hard shoulder of Akegwo-Avangkhu section of NH-202K for Package-II Design Chainage 34795 Km to 69875 Km in the State of Nagaland on EPC mode under NHO-NE (NHIDCL) (618366) (-) (-)	Nagaland	12/2022 (08/2023)	02/2026 (02/2026)	442.54 0.00	0.00	58.50
1352	Construction of 2 laning with Hard shoulder of Peren-Dimapur section on NH 129A from Design Km 146.208 to Km 163.592 Length- 17.384 km in the state of Nagaland on EPC mode under NHO-TSP Package-III (NHIDCL) (618413) (-) (-)	Nagaland	02/2021 (06/2023)	06/2025 (09/2026)	177.77 0.00	111.89	95.62
1353	Construction of Balance work for 2-lane with hard shoulder of Peren- Dimapur section on NH-129A from Design Km 126.775 to Km 146.208 Length 19.433 Km in the state of Nagaland on EPC mode under NHO-TSP Package-II (NHIDCL) (618414) (-) (-)	Nagaland	01/2021 (09/2023)	09/2025 (09/2025)	258.52 0.00	136.09	96.53
1354	Construction of 2-lane with hard shoulders of Merangkong-Tamlu-Mon road Wakching Twon portion on EPC basis from existing Chainage Km 59000 to Km 73640 [Design Km. 59000 to Km, 72450] Design length - 13.450 Km under SARDP-NE package-V Balance work (NHIDCL) (618422) (-) (-)	Nagaland	03/2021 (09/2023)	09/2025 (07/2026)	161.73 0.00	101.28	99.75

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1355	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon MTM Road from existing Km 20.456 to Km 41.065 Design Km. 20 to Km. 40.0 Design Length- 20.000 Km in the State of Nagaland under SARDP-NE Phase-A Pkg-2 Balance work (NHIDCL) (618423) (-) (-)	Nagaland	03/2018 (08/2023)	08/2025 (03/2026)	215.79 0.00	173.12	100.00
1356	Construction of 2-Lane with hard shoulders of Merangkong-Tamlu-Mon Road on EPC Basis from existing road Km. 76.640 to Km 98.065 Design chainage Km. 63.800 to Km. 86.835 Design Length-23.035 Km in the state of Nagaland under SARDP-NE PKG-IV Balance work (NHIDCL) (619059) (-) (-)	Nagaland	03/2018 (09/2023)	09/2025 (12/2026)	323.98 0.00	147.38	79.03
1357	New construction of Major Bridge with Approaches from Km 0.000 to 1.200 Madhopur -Badabanta section of NH-20 under NHO in Annual Plan 2022-23 in the State of Odisha (MoRTH) (617898) (-) (-)	Odisha	03/2023 (04/2025)	10/2027 (10/2027)	199.50 0.00	5.03	0.00
1358	Widening and Strengthening to 4LPS/2LPS from km 0.000 to 35.800 Kuakhia - Mangalpur section of NH 20 in the state of Odisha on Annual Plan 2021-22 (MoRTH) (617899) (-) (-)	Odisha	03/2022 (02/2024)	02/2026 (11/2026)	636.10 0.00	446.67	56.11
1359	construction or By-pass road on NH-26 for Nabrangpur Town (MoRTH) (617902) (-) (-)	Odisha	03/2023 (12/2024)	12/2026 (12/2026)	168.95 0.00	77.75	38.00
1360	Construction of Bypass road to Balangir town from km 72/400 Desing km 0/0 to km 79/800 Design km 11/670 of NH-26 in the State of Odisha. (MoRTH) (617904) (-) (-)	Odisha	02/2022 (04/2023)	10/2025 (03/2027)	238.78 0.00	121.31	55.00
1361	Construction of 4 lane ROB with approaches in lieu of LC No. RV-172 at km 176.00 of NH-201 present NH-26 at Kesinga including land acquisition in the state of Odisha on EPC mode under Annual Plan 2021-22 (MoRTH) (617905) (-) (-)	Odisha	12/2021 (05/2023)	05/2025 (05/2027)	324.09 0.00	161.75	78.00
1362	Widening and Strengthening of existing S/L, I/L, & D/L to 2 Lane with PS from Km 256/455 to 256/503, 256/820 to 256/960, 265/760 to 266/010, 266/010 to 266/800, 270/975 to 271/055, 276/460 to 276/560, 276/560 to 276/700, 276/700 to 277/480, 285/780 to 288/290, 288/290 to 291/050 and construction of 3 Nos. of Bypass from Km 266/800 to 267/300, 270/025 to 270/975, & 284/700 to 285/780 on NH-53 under NHO in Annual Plan 2022-23 for the State of Odisha. (MoRTH) (617918) (-) (-)	Odisha	03/2023 (06/2026)	12/2027 (-)	174.21 0.00	62.29	0.00
1363	Widening and Strengthening to 2LPS including LA from km 318.970 to 353.450 Balikuda-Mulkani Section of NH-55 under NHO in Annual Plan 2022-23 in the State of Odisha. Job No. NH-55-OD-2022-23-656 (MoRTH) (617920) (-) (-)	Odisha	01/2022 (06/2025)	06/2027 (06/2027)	511.54 0.00	50.15	3.00
1364	Widening and strengthening to 2LPS including LA of Kandarpur-Balikuda from km 277/500 to 318/970 of NH-55 in the State of Odisha under Annual Plan 2021-22. (MoRTH) (617921) (-) (-)	Odisha	03/2022 (06/2023)	06/2025 (06/2027)	499.79 0.00	352.67	66.00
1365	Construction of Jharsuguda Bypass including Land acqusition on NH-49 from km 258.636 to km 283.300 design chainage 258.636 to km 289.876 under NHO in Annual Plan 2022-23 for the state of Odisha Job No.NH-49-OD-2022-23-655 (MoRTH) (617922) (-) (-)	Odisha	09/2021 (01/2025)	07/2027 (07/2027)	587.10 0.00	164.89	25.00
1366	Construction of Daspalla Bypass from km 195.250 To 200.635 of NH-57 including land acquisition in the state of Odisha on EPC mode under Annual Plan 2022-23. (MoRTH) (617923) (-) (-)	Odisha	02/2023 (05/2025)	05/2027 (05/2027)	155.97 0.00	54.64	25.00
1367	Construction of Bypass to Khordha town from Km 294/000 to 300/300 on NH-57 including LA in the State of Odisha on EPC mode. (MoRTH) (617925) (-) (-)	Odisha	02/2022 (05/2023)	11/2024 (10/2026)	157.49 0.00	118.68	92.00
1368	Construction of Bypass on NH-59 from Km 336/350 to 349/910 13.56 km near Berhampur town including 4-lane RoB in the state of Odisha. (MoRTH) (617930) (-) (-)	Odisha	03/2021 (03/2022)	12/2025 (12/2026)	196.94 0.00	92.70	70.00
1369	Construction of four lane ROB and its approaches in lieu of existing Level Crossing No. RV-71 at km 435 on NH-217 New NH-353 at Khariar including land acquisition under NHO in Annual Plan 2021-22 for the state of Odisha for F.Y. 2021-22 to F.Y 2033-34 (MoRTH) (618003) (-) (-)	Odisha	11/2021 (06/2023)	12/2024 (09/2026)	154.49 0.00	106.00	90.00
1370	Widening & strengthening to 2LPS from km 0,000 to 40.000 Dhaugaon- Podamari section of NH 326 in the State of Odisha under Annual Plan 2021.22. (MoRTH) (618012) (-) (-)	Odisha	03/2022 (02/2024)	02/2026 (12/2026)	186.52 0.00	84.85	60.00

All Ongoing Projects							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1371	Construction of Dharmagarh Bypass on NH-130C including land acquisition in the state of Odisha on EPC Mode under Annual plan 2022-23. (MoRTH) (618079) (-) (-)	Odisha	03/2023 (04/2025)	10/2026 (06/2027)	172.66 0.00	62.32	15.00
1372	Widening to 2 lane with paved shoulded of Jareikela Jharkhand/Odisha Border - Dhabaleswar section from 0/0 to 36/0 of NH-320D in the State of Odisha under Annual Plan 2021-22. (MoRTH) (618122) (-) (-)	Odisha	03/2022 (10/2024)	10/2026 (10/2026)	172.09 0.00	53.11	34.00
1373	Bhadrak KM 136.500 to Baleshwar KM 199.141 (NHAI) (618523) (-) (-)	Odisha	11/2014 (03/2019)	09/2021 (11/2026)	844.67 0.00	785.30	91.32
1374	Construction of 6-lane flyover at Ainthapali junction and a 2-lane ROB LHS on NH-53 Earlier NH-6 in Sambalpur, on EPC mode in Odisha under NHO (NHAI) (618591) (-) (-)	Odisha	03/2024 (06/2024)	12/2026 (12/2026)	374.17 0.00	112.53	54.20
1375	Balance work of 8 nos. of Elephant Underpasses EUPs, 1 no. of Vehicular Underpass VUP, 1 nos. of Light Vehicular Underpass LVUP, 1 nos. of Pedestrian Underpass PUP, 1 nos. of Foot Over Bridge FOB and A2 side approach of Jharpokharia Flyover at Km.215.270 in Baharagora-Singhara section of NH-49 (NHAI) (618592) (-) (-)	Odisha	09/2023 (11/2024)	05/2026 (10/2027)	320.64 0.00	55.30	25.04
1376	Balance work of Rehabilitation and Upgradation to four laning of Baharagora Singhara section of NH-49 from Km.229.727 to Km.238.990 Length 9.263 Km. including construction of five nos. of Elephant Underpasses EUP and fourteen nos. of Animal Underpasses AUP inside the buffer zone of Similipal Tiger Reserve Area in Bangriposi Ghat section in the State of Odisha on EPC Mode (NHAI) (618593) (-) (-)	Odisha	03/2025 (05/2025)	11/2027 (11/2027)	263.32 0.00	14.33	9.95
1377	6L Greenfield Kaliagura Baunsagar Section of NH-130-CD Road from km 249000 to km 293000 Package OD-5 (NHAI) (618677) (-) (-)	Odisha	09/2021 (05/2022)	05/2024 (11/2026)	1,539.75 0.00	1,026.83	97.80
1378	6L Greenfield Baunsagar - Baraja Section of NH-130-CD Road from km 293000 to km 338500 Package OD-6 (NHAI) (618678) (-) (-)	Odisha	08/2021 (06/2022)	05/2024 (09/2026)	1,265.59 0.00	1,001.47	99.60
1379	6L Flyover including RE Wall approaches with Flexible Pavement in the Elephant Corridor of Angul Sambalpur Section of NH-42 New NH-55 Km.202.533 (NHAI) (618704) (-) (-)	Odisha	09/2023 (06/2024)	06/2026 (09/2026)	150.86 0.00	106.14	100.00
1380	4L Godibandha to Ballhar Chhak, Ballhar Chhak to Banarpal & Banarpal to Start of Angul bypass at Km.314.130 to Km.321.035 of NH53, at Km.75.200 to Km.84.000 of NH149 & at Km.84.000 to Km.86.100 of NH55 (NHAI) (618705) (-) (-)	Odisha	12/2024 (02/2026)	02/2028 (02/2028)	973.12 0.00	299.01	5.40
1381	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.39.000 to Km.60.00 Package-3 (NHAI) (618820) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (03/2027)	861.84 0.00	395.98	92.02
1382	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km 18.00 to Km 39.00 in the State of Odisha on HAM mode Package-2 (NHAI) (618821) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (11/2026)	920.47 0.00	435.46	98.22
1383	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.0.00 to Km.18.00Package-1 (NHAI) (618822) (-) (-)	Odisha	03/2023 (12/2023)	12/2025 (01/2027)	929.91 0.00	403.23	96.75
1384	3L Major Bridge over River Brahmani at Km. 401.250 Duburi - Chandikhole Section of NH-200 New NH -53 (NHAI) (618908) (-) (-)	Odisha	04/2022 (08/2022)	01/2025 (09/2027)	153.61 0.00	73.76	38.00
1385	6L of Badakumari - Karki Section from Km 179.000 to km 226.500 of NH-130-CD Package OD-3 (NHAI) (619109) (-) (-)	Odisha	03/2021 (04/2022)	04/2024 (09/2026)	1,101.76 0.00	713.51	99.70
1386	Four Laning of Angul to Sambalpur from Km.112.000 to Km.265.000 (NHAI) (619118) (-) (-)	Odisha	09/2016 (03/2017)	08/2019 (09/2026)	2,510.04 0.00	2,465.02	99.98
1387	Cuttack-Angul Section of NH-42 New NH-55 from km 0.400 to km 60.200 Pkg-I in the State of Odisha (NHAI) (619119) (-) (-)	Odisha	10/2017 (01/2018)	07/2020 (12/2026)	999.32 0.00	1,132.56	99.00
1388	4 Laning of Duburi Chandikhole from km 388.376 to km 428.074 Pkg-III (NHAI) (619158) (-) (-)	Odisha	01/2018 (02/2020)	08/2022 (12/2026)	789.00 0.00	725.21	86.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1389	Rehabilitation and Up gradation from 4 to 8 laning of Chandikhole Paradip Section of NH-53 Old NH 5A from Km.60.000 to Km.76.646 Package-4 (NHAI) (619181) (-) (-)	Odisha	03/2023 (11/2024)	10/2026 (12/2027)	882.45 0.00	201.34	36.02
1390	6L of Hatibena - Badakumari Section from Km 146.50 to km 179.00 of NH-130-CD Package OD-2 (NHAI) (619213) (-) (-)	Odisha	02/2021 (03/2022)	03/2024 (09/2026)	791.17 0.00	734.23	99.99
1391	Cuttack-Angul Section of NH-42 New NH-55 from Km.60.200 to Km. 112.000 Pkg-II in the State of Odisha (NHAI) (619215) (-) (-)	Odisha	10/2017 (03/2018)	09/2020 (12/2026)	991.41 0.00	1,084.35	99.66
1392	Development to 4-lane with paved shoulder for the road section Talwandi Sabo-Raman road to refinery Road junction with Bathinda Dabwali Road of NH-254 from existing Km 131.600 to Km 155.650 Design Km 131600 to km 155600 in the State of Punjab. Job No NH-254-PB-2022-23-565 (MoRTH) (618010) (-) (-)	Punjab	03/2023 (05/2025)	11/2026 (11/2026)	546.67 0.00	382.82	72.00
1393	Up-gradation to two lane with paved shoulder configuration of NH-354 Section Arifkes-Ferozepur-Muktsar-Malaut from Km 201.500 to Km 212.500 & Km 229.690 to Km 269.960 and strengthening of existing pavement from Km 212.500 to Km 229.690 excluding Km 218.500 to 223.690 of NH-354 on EPC Mode in the State of Punjab. Job No. NH-354-PB-2020-21-532 (MoRTH) (618024) (-) (-)	Punjab	03/2021 (10/2023)	04/2025 (09/2026)	263.19 0.00	193.83	89.00
1394	Delhi-Amritsar-Katra Expressway Phase-I Pkg-IX from Junction with Ludhiana-Moga road NH-5 near Mullanpur Dakha to Junction with Jalandhar - Moga road NH-703 near Kang Sahibu village Km 260860 to km 303900 (NHAI) (618489) (-) (-)	Punjab	12/2020 (07/2022)	07/2024 (03/2027)	1,851.47 0.00	1,944.05	73.35
1395	Delhi-Amritsar-Katra Expressway Phase-I Pkg-XII from Junction with Amritsar-Mehta-SriHargobindpur-Tanda road NH-503A near SriHargobindpur to Junction with Pathankot-Gurdaspur road NH-54 near Gurdaspur Km 362420 to km 397700 (NHAI) (618492) (-) (-)	Punjab	03/2021 (02/2025)	02/2027 (06/2027)	1,734.18 0.00	781.01	27.60
1396	Delhi-Amritsar-Katra Expressway Phase-I Spur-I from Jn. with Kapurthala - Sultanpur Lodhi Road NH-703A near Isharwal village to Jn. with Kapurthala - Tarn Taran road NH-703AA near Goinwal Sahib [Km 24000 to Km 41000 of Amritsar connectivity] (NHAI) (618493) (-) (-)	Punjab	12/2021 (04/2023)	04/2026 (03/2028)	2,165.23 0.00	635.80	34.79
1397	Greenfield connectivity from Govindsar village on Delhi Amritsar Katra Expressway to Talwara village on NH-44 Pathankot by-pass (NHAI) (618551) (-) (-)	Punjab	11/2024 (07/2025)	07/2027 (07/2027)	666.81 0.00	231.08	29.01
1398	Development of 6L Greenfield Jalandhar Bypass starting from Kahlwan NH-03 ending at Kang Sahbu NH-703 via Sarmastpur NH-44 - Madara NH-03 - Khajurla NH-44 (NHAI) (618552) (-) (-)	Punjab	03/2021 (01/2023)	01/2025 (06/2027)	1,754.84 0.00	1,252.18	56.70
1399	6L of Jodhpur Romana Bathinda - Mandi Dabwali Punjab Haryana Border section of NH-54 from km. 0.000 to km. 27.400 of NH-54 (NHAI) (618610) (-) (-)	Punjab	05/2020 (08/2023)	08/2025 (09/2026)	789.26 0.00	719.19	99.00
1400	6L Amritsar-Bathinda Greenfield section from village Tiba on NE-5A to Jn. with Moga Jalandhar road NH-703 near Dharamkot from km 0.000 to km 39.000 of NH-754A Pkg-1 (NHAI) (618617) (-) (-)	Punjab	03/2021 (11/2022)	11/2024 (12/2027)	1,229.38 0.00	1,077.84	72.41
1401	6L Amritsar-Bathinda Greenfield section from Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka to Jn. with Mandi Dabwali Bathinda Road on NH-54 near Sangat Kalan from km 93.000 to km 154.866 of NH-754A Pkg-3 (NHAI) (618618) (-) (-)	Punjab	03/2021 (06/2024)	06/2026 (07/2027)	2,029.17 0.00	1,443.14	74.00
1402	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Amritsar-Bathanda Greenfield Road NH-754A near Rampura Phul to Jn. with Moga-Barnala Road NH-703 near village Tallewal from Km 0.0 to Km 30.3 of NH-754AD Pkg-1 (NHAI) (618647) (-) (-)	Punjab	06/2021 (09/2023)	09/2025 (10/2026)	906.51 0.00	687.98	81.50
1403	Development of 6-lane Greenfield Southern Ludhiana Bypass from intersection with NH-44 near Village Rajgarh to intersection with Delhi Katra Expressway NE-5 near Village Ballawal, km 0000 to km 25240 (NHAI) (618648) (-) (-)	Punjab	11/2024 (03/2026)	03/2028 (03/2028)	1,424.55 0.00	178.12	5.79
1404	Moga - Bagha Purana - Bajakhana from km. 0.00 to km. 43.32 (NHAI) (618764) (-) (-)	Punjab	05/2020 (12/2022)	12/2024 (12/2026)	1,032.59 0.00	804.37	76.00
1405	4L of Greenfield section from Sirhind to Mohali (NHAI) (618776) (-) (-)	Punjab	03/2022 (05/2023)	05/2025 (09/2026)	1,237.65 0.00	1,391.88	98.66

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1406	4/6L Greenfield LudhianaRupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km 66.0 to Km 91.0 i/c spur to Kharar from Km 0.0 to Km 19.5 with Ludhiana bypass of NH-205K Pkg-3 (NHAI) (618785) (-) (-)	Punjab	07/2021 (02/2023)	02/2025 (12/2026)	1,501.02 0.00	1,173.74	80.71
1407	4L of Phagwara - Hoshiarpur (NHAI) (618786) (-) (-)	Punjab	11/2022 (03/2025)	03/2027 (07/2027)	1,196.38 0.00	556.53	20.03
1408	4L of Fazilka to Abohar section of NH-07 including construction of Greenfield Abohar & Fazilka Bypasses (NHAI) (618793) (-) (-)	Punjab	03/2023 (04/2024)	04/2026 (08/2027)	1,409.88 0.00	914.43	67.00
1409	Amritsarairport Junction - Ramdas from km. 100.835 to km. 139.813 Pkg - IV (NHAI) (618794) (-) (-)	Punjab	12/2020 (03/2022)	09/2023 (10/2026)	524.88 0.00	403.35	96.00
1410	Amritsar Bypass Pkg III from km. 71.496 to km. 105.158 (NHAI) (618795) (-) (-)	Punjab	02/2021 (08/2022)	08/2024 (12/2026)	1,474.77 0.00	1,223.82	82.88
1411	4L of Beas-Mehta-Batala-Dera Baba Nanak from intersection with Jalandhar-Amritsar Highway NH-3 near Beas till start of Batala Bypass near Village Acchhal from Km. 0.000 to Km. 31.300 Pkg-1 (NHAI) (618809) (-) (-)	Punjab	08/2021 (06/2023)	06/2025 (05/2027)	809.51 0.00	701.25	68.20
1412	4L of existing Beas Baba Bakala - Dera Baba Nanak Section from start of Batala Bypass till intersection with Ajnala Gurdaspur Highway NH 354 near Dera Baba Nanak from Km. 31.300 to Km. 69.100 with Additional batala Bypass Pkg-II (NHAI) (618810) (-) (-)	Punjab	10/2021 (06/2023)	06/2025 (03/2027)	1,003.38 0.00	818.68	80.90
1413	4L of Amritsar-Ghoman - Tanda - Una Section from Km 8.270 to Km 54.000 of NH-503A Package-I (NHAI) (618906) (-) (-)	Punjab	12/2020 (06/2022)	06/2024 (03/2027)	857.91 0.00	773.01	68.90
1414	6L Amritsar-Bathinda Greenfield section from Jn. with Moga Jalandhar road NH-703 near Dharamkot to Jn. with Bhagta Bhai Ka-Bhadaur Road near Dyalpura Bhai Ka from km 39.000 to km 93.000 of NH-754A Pkg-2 (NHAI) (619099) (-) (-)	Punjab	03/2021 (06/2024)	06/2026 (06/2027)	1,801.37 0.00	1,268.59	66.64
1415	6L Access Controlled Ludhiana-Bathinda Greenfield highway from Jn. with Moga-Barnala Road NH-703 near village Tallewal to Jn. with Delhi-Katra Expressway NE-5 near Ludhiana village Ballawal from Km 30.300 to Km 75.543 of NH-754AD Pkg-2 (NHAI) (619105) (-) (-)	Punjab	07/2021 (09/2025)	09/2027 (09/2027)	1,555.13 0.00	723.45	25.55
1416	Delhi-Amritsar-Katra Expressway Phase-I Spur-III from Junction with Amritsar-Jalandhar road NH-3 near Bishambarpura to Junction with Amritsar-Anjala road NH-354 near Amritsar Airport [Km 71000 to Km 99000 of Amritsar connectivity] (NHAI) (619200) (-) (-)	Punjab	03/2021 (11/2022)	10/2024 (12/2027)	1,641.75 0.00	1,374.83	34.37
1417	4/6L Greenfield Ludhiana Rupnagar highway from Jn. with NE-5 village near to ManewalLudhiana to Jn. with NH-205 near Bheora Village Rupnagar from Km. 0.00 to Km. 37.7 including spur to Kharar with Ludhiana bypass of NH-205K Pkg-1 (NHAI) (619318) (-) (-)	Punjab	05/2021 (12/2022)	12/2024 (12/2027)	1,368.91 0.00	533.48	15.31
1418	Widening of Pachpadra-Bagundi Section to 4 Lane from Km 73/60 to 95/70 of NH-25 on EPC mode in the state of Rajasthan. (MORTH) (617901) (-) (-)	Rajasthan	01/2022 (12/2022)	12/2024 (07/2026)	194.88 0.00	55.29	98.58
1419	Construction of 2 lane with paved shoulder for the work of Development of remaining sections of NH-325 Balotra to sanderao via Jalore to 2 lane with paved shoulder configuration by Construction of Byasses for town portions1 Asotra- Brahmdham bypass 2Siwana Bypass 3 Mokalsar Bypass 4 Major realignment at Kathadi 5 Major realignment at Bishangarh 6 Jalore Bypass 7 Ahore Town portion 8 Dujana Bypass in the state of Rajasthan on EPC Mode (MoRTH) (618011) (-) (-)	Rajasthan	12/2021 (05/2022)	05/2024 (10/2026)	411.44 0.00	297.73	93.22
1420	Upgradation to Two-lane with paved shoulder of Hanumangarh to Kenchiyan section from Km 0.000existing chainage-Km 23.200 to Km 49.605existing chainage-Km 74.645 of NH-54 in the State of Rajasthan on EPC mode. (MoRTH) (618069) (-) (-)	Rajasthan	03/2022 (10/2024)	10/2026 (10/2026)	334.64 0.00	185.26	72.00
1421	Up-gradation to 2 lane with paved shoulder from Neechli Oden Nathdwara at Design Km 88.800 existing km 55.95 to Bhatewar at Design Km 142.028 existing km 0.00 of NH-162E in the State of Rajasthan on EPC mode. (MoRTH) (618092) (-) (-)	Rajasthan	02/2023 (10/2024)	10/2026 (10/2026)	606.61 0.00	256.14	65.19

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1422	Upgradation to 2-Lane with Paved Shoulder from Design Km 36300 to Design Chainage 47918 and from Design Ch 69900 to Design Ch 83940 of NH-248A Natni Ka Bara in the State of Rajasthan on EPC Mode. (MoRTH) (618117) (-) (-)	Rajasthan	02/2024 (11/2024)	05/2026 (03/2027)	154.89 0.00	28.47	23.00
1423	Construction of 2 lane with Paved Shoulder for Northern Bypass Phase-II of Kota city in the State of Rajasthan. (MoRTH) (618200) (-) (-)	Rajasthan	03/2022 (10/2023)	04/2025 (11/2026)	317.74 0.00	154.91	52.57
1424	Balance work of Rehabilitation and Up-gradation to 4-Lane configuration of Ras-Beawar Section Km 00.000 to km 30.050 of NH-158 in the State of Rajasthan under Green National Highway Corridor Project GNHCP. (MoRTH) (618235) (-) (-)	Rajasthan	01/2025 (06/2025)	12/2026 (12/2026)	278.10 0.00	104.40	58.10
1425	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-10 Ch. 292.950 to Ch. 319.400 [End of Interchange on NH-166 near village Mui to Hardeoganj village near Indergarh] (NHAI) (618457) (-) (-)	Rajasthan	11/2019 (05/2021)	05/2023 (04/2027)	1,272.97 0.00	1,164.39	95.25
1426	Delhi-Vadodara Greenfield Alignment NH-148N Pkg-15 Ch. 419.000 to Ch.427.300 [Junction with NH-12 near village Ummadpura to Major bridge over Takli river near Nayagaon Jageer village] (NHAI) (618458) (-) (-)	Rajasthan	07/2020 (07/2021)	01/2024 (09/2026)	1,854.68 0.00	1,534.71	98.28
1427	Sangariya near Chautala-Rasisar near Bikaner section of NH-754K Phase-I AJ/SR-Package-7 (NHAI) (618611) (-) (-)	Rajasthan	02/2019 (06/2021)	06/2023 (09/2026)	520.63 0.00	450.73	100.00
1428	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-6 (NHAI) (618612) (-) (-)	Rajasthan	10/2019 (08/2021)	08/2023 (09/2026)	846.59 0.00	707.32	100.00
1429	Deogarh near Dhandhaniya-Rajasthan/Gujarat Border Phase-I AJ/DRGB-Package-7 (NHAI) (618613) (-) (-)	Rajasthan	10/2019 (07/2021)	07/2023 (09/2026)	662.08 0.00	561.80	99.20
1430	6L access controlled Highway from Km 40080 to Km 86513 Mator to Barodameo Section (NHAI) (618757) (-) (-)	Rajasthan	09/2022 (03/2024)	03/2026 (06/2027)	2,010.20 0.00	723.71	37.27
1431	6L accesscontrolled highway from km 0000 to km 40080 Paniyala to Mator Section of Paniyala-Barodameo ICR (NHAI) (618758) (-) (-)	Rajasthan	09/2022 (09/2024)	09/2026 (09/2026)	1,764.86 0.00	585.41	42.75
1432	Tanot -Ramgarh-Bhadasar-Jaisalmer NH-68 and BhadasarMokal-Sarkaritala up to Pakistan Border NH-968 Pkg-BM/5 (NHAI) (618796) (-) (-)	Rajasthan	02/2018 (04/2019)	04/2021 (09/2026)	828.58 0.00	756.00	100.00
1433	Widening Strengthening of 2-Lane with Paved Shoulder from MyajlarJaisalmer from Design Chainage 0000 to 98350 Section of NH-11 & SundraMyajlarAmbasingh ki Dhani Road from Design Chainage 46000 to 81601, part of MunabaoTanot Road Section of NH-70 along with Strengthening/Widening of Existing Connection of NH-70 & NH-11 of length 0.914 km in the State of Rajasthan under NHO on Hybrid Annuity Mode (NHAI) (618797) (-) (-)	Rajasthan	03/2025 (12/2025)	12/2027 (12/2027)	1,237.71 0.00	94.08	21.22
1434	4L of Karwar Km. 281.980 of NH-62 Nagaur road to Dangiyavas of Jodhpur Ring Road Pkg-II (NHAI) (618838) (-) (-)	Rajasthan	11/2021 (08/2022)	08/2024 (09/2026)	736.75 0.00	464.14	100.00
1435	Construction of Four lane Elevated Structure at Raniwada Circle in Sanchore City on NH-68 (NHAI) (618853) (-) (-)	Rajasthan	01/2024 (07/2024)	07/2026 (11/2026)	353.30 0.00	199.77	89.37
1436	Construction of two lane with paved shoulder of Ghatol Bypass from km 133.250 to km 140.950 of NH-56 old NH No. 113 on EPC mode in the State of Rajasthan. (MoRTH) (619251) (-) (-)	Rajasthan	03/2025 (03/2026)	09/2027 (-)	170.49 0.00	40.77	24.00
1437	Upgradation of 6 laned Jaipur- Kishangarh section of NH-48 from km 274100 to 363885 involving construction of flyovers and Service road in Rajasthan On Engineering, Procurement & Construction EPC Mode (NHAI) (619270) (-) (-)	Rajasthan	03/2026 (08/2026)	01/2029 (08/2028)	910.91 0.00	0.00	0.00
1438	Construction of Elevated Corridor at Kherwara Town on Udaipur Ratanpur Shamlaji Section of NH-48 in Udaipur District in the State of Rajasthan on EPC mode (NHAI) (619271) (-) (-)	Rajasthan	03/2026 (07/2026)	01/2029 (01/2029)	363.89 0.00	0.38	0.00

All Ongoing Projects							AUGUST 2026
Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1439	Construction of two lane with paved shoulder Gangtok Bypass Road from Ranipool to Burtuk Ch 0.00 Km to 23.316 L23.316 Km in the State of Sikkim (MoRTH) (618071) (-) (-)	Sikkim	10/2021 (05/2022)	05/2024 (12/2026)	385.15 0.00	254.56	92.00
1440	Construction/Up gradation of Existing road to 2 Lane with Paved Shoulder including Geometric Improvement from Ranipool to Pakyong Balance work from Km 2.000 to 16.167 of NH-717-A on EPC basis under SARDP-NE Phase A in the State of Sikkim (NHIDCL) (618426) (-) (-)	Sikkim	03/2018 (01/2023)	07/2024 (12/2026)	264.84 0.00	127.34	87.03
1441	Realignment of NH-717A from Design Ch.0.00 Km 77.800 of NH-10 to Design Ch.2.00 Km 3.100 of NH-717A with two lane paved shoulder including Major Bridge of 680 m in the State of Sikkim on EPC Mode-COS work (NHIDCL) (618428) (-) (-)	Sikkim	01/2021 (04/2021)	04/2023 (05/2026)	264.84 0.00	70.71	100.00
1442	Construction & Upgradation of existing road to 2-lane with paved shoulder from New Rolep Bridge at km 37.600 to Chochenpheri at km 52.00 in the section of Rongli to Chochenpheri of NH 717B Pkg-II C (NHIDCL) (618446) (-) (-)	Sikkim	10/2020 (05/2021)	05/2024 (09/2026)	493.42 0.00	395.19	79.13
1443	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Helipad near Menla at Km 82000 to Menla at Km 94030 of Rhenock-Menla Spur NH-717B Package-IIIB on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618447) (-) (-)	Sikkim	01/2021 (02/2021)	02/2024 (05/2027)	410.60 0.00	241.77	82.64
1444	Construction of 2-Laning with Paved Shoulder of New Greenfield Alignment From Chochenpheri at Km 52000 to Helipad near Menla at Km 82000 of Rhenock-Menla Spur NH-717B Package-IIIA on EPC Basis under SARDP-NE Phase 'A' in the State of Sikkim. (NHIDCL) (618448) (-) (-)	Sikkim	10/2020 (12/2020)	12/2023 (05/2027)	816.79 0.00	474.96	64.31
1445	Construction & Upgradation of existing road to 2-lane with paved shoulder from km27.200 End of Rongli bypass to km37.600New Rolep Bridge of Rhenok-Menla spur NH-717B on EPC Mode under SARDP-NE Phase-A in Sikkim Pkg-II B (NHIDCL) (618449) (-) (-)	Sikkim	07/2020 (10/2020)	04/2023 (09/2026)	230.45 0.00	249.71	86.19
1446	Rehabilitation & Upgradation of existing road to 2-lane with paved shoulder including geometric improvement of section from start of Rabangla km33.600 to km58.840 under SARDP-NE Phase A Pkg- IV (NHIDCL) (618450) (-) (-)	Sikkim	07/2020 (10/2020)	05/2022 (12/2026)	292.80 0.00	256.52	65.15
1447	Construction of Bypass to Madurai Achambathu Viratipathu in between km 6/850 10/382 of NH 49 Extn New NH 85 including Land Acquisition on Engineering, Procurement & Construction EPC basis Contract under NH O Annual Plan 2021-22 in the state of Tamil Nadu job No.NH-49 Extn New NH 85 - TN-2021-22-997 (MoRTH) (617962) (-) (-)	Tamil Nadu	03/2022 (09/2024)	08/2026 (10/2026)	238.97 0.00	217.37	94.00
1448	Bangalore Chennai Expressway Phase-III Package II Walajahpet to Arakkonam from Km 180.000 to Km 204.500 (NHAI) (618478) (-) (-)	Tamil Nadu	01/2021 (07/2022)	07/2024 (10/2026)	1,106.65 0.00	616.01	93.04
1449	Bangalore Chennai Expressway Phase-III Package III Arakkonam to Kancheepuram from Km 204.500 to Km 230.000 (NHAI) (618479) (-) (-)	Tamil Nadu	12/2020 (08/2022)	07/2024 (12/2027)	1,525.10 0.00	360.95	53.56
1450	Construction of Trumpet Interchange Connecting Bangalore Chennai Expressway km.261705 to km. 262800 with Maduravoyal to Walajapet Section of NH 48 near Sriperumbudur Toll Plaza at km. 35700 (NHAI) (618480) (-) (-)	Tamil Nadu	05/2023 (02/2024)	08/2025 (10/2026)	162.55 0.00	59.96	38.52
1451	4L Bangalore-Chennai Expressway from Km. 230.000 to Km. 261.705 of Kancheepuram to Sriperumbudur Section Phase-III/Package-IV (NHAI) (618481) (-) (-)	Tamil Nadu	02/2021 (07/2022)	07/2024 (10/2026)	3,605.73 0.00	1,009.84	89.97
1452	Karaipettai to Walajapet from Km 71.015 to 107.091 (NHAI) (618521) (-) (-)	Tamil Nadu	08/2018 (02/2019)	02/2021 (09/2026)	766.51 0.00	613.76	93.55
1453	Balance Works for six laning of Sriperumbudur to karaipettai section of NH-4 New NH-48 from 37000 Existing Km 37000 to Km 71015 Existing Km 71000 in Tamilnadu on EPC mode underNHDP Phase-V (NHAI) (618522) (-) (-)	Tamil Nadu	06/2024 (01/2025)	10/2026 (03/2027)	411.16 0.00	161.60	38.26
1454	Improving the Alignment of Thoppur Ghat Section from Km 158.500 to Km 165.100 in Dharmapuri - Salem Section of NH-44 (NHAI) (618561) (-) (-)	Tamil Nadu	03/2024 (03/2025)	03/2028 (03/2028)	904.99 0.00	230.58	47.84
1455	4L of Madurai Ring Road Phase 1 [Vadipatti-Thamrapatti] from km 0.00 - km 29.960 (NHAI) (618563) (-) (-)	Tamil Nadu	12/2018 (03/2020)	03/2022 (09/2026)	900.05 0.00	905.53	99.42

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1456	4L of left-over works including additional structures from Kerala/Tamil Nadu border to Kanyakumari Section from Km 43.0 to Km 96.174 of NH66 (<i>NHAI</i>) (618608) (-) (-)	Tamil Nadu	11/2022 (08/2023)	08/2025 (12/2026)	1,564.23 0.00	1,004.18	81.85
1457	6L of Pondavakkam to Kannigaipair from km 96.040 to km 116.100 of NH 716B Pkg- IV (<i>NHAI</i>) (618635) (-) (-)	Tamil Nadu	02/2021 (01/2023)	01/2025 (12/2027)	1,359.81 0.00	409.63	44.53
1458	4L of Thirumangalam to Vadugapatti section from km 0.000 to km 36.000 of NH-744 (<i>NHAI</i>) (618744) (-) (-)	Tamil Nadu	03/2022 (02/2023)	02/2025 (10/2026)	1,076.97 0.00	685.87	95.95
1459	Melur - Pilayarpatti - Karaikudi from km 99.920 of NH 38 to km 12.9 of NH 383 Ext. (<i>NHAI</i>) (618756) (-) (-)	Tamil Nadu	12/2018 (03/2020)	03/2022 (09/2026)	1,103.86 0.00	948.46	98.12
1460	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package II from Km 4.604 to Km 9.700 (<i>NHAI</i>) (618800) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1,616.97 0.00	271.12	18.13
1461	Construction of New Double Tier 4-lane Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from Km -0342 to Km 20223 Package 1 from Km - 0342 to Km 4604 (<i>NHAI</i>) (618801) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1,388.59 0.00	297.34	22.80
1462	Poondiyankuppam Km.67.000 to Sattanathapuram Km.123.800 (<i>NHAI</i>) (618846) (-) (-)	Tamil Nadu	03/2018 (01/2022)	01/2024 (10/2026)	2,565.63 0.00	1,210.20	99.80
1463	4L of Madathukulam - Pollachi from km. 74.38 to km. 116.95 of old NH-209 New NH-83 (<i>NHAI</i>) (618894) (-) (-)	Tamil Nadu	01/2019 (12/2020)	12/2022 (09/2026)	1,772.13 0.00	1,063.22	97.65
1464	Kamalapuram to Oddanchatram from km. 0.00 to km. 35.822 (<i>NHAI</i>) (618895) (-) (-)	Tamil Nadu	01/2019 (01/2021)	01/2023 (09/2026)	1,319.42 0.00	649.84	93.60
1465	Balance Works for Four laning of Vikravandi to Sethiyathope section from Km 0.0 to Km 65.96 of NH-45C in Tamil Nadu under NHDP Phase-IV on EPC mode (<i>NHAI</i>) (618898) (-) (-)	Tamil Nadu	01/2025 (06/2025)	06/2027 (06/2027)	1,163.17 0.00	320.41	37.62
1466	Kallagam km.38.700 to Meensurutti Km.98.433 of NH-227 in Tamil Nadu (<i>NHAI</i>) (618899) (-) (-)	Tamil Nadu	02/2018 (04/2019)	04/2021 (09/2026)	1,499.12 0.00	1,112.05	100.00
1467	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package IV from Km 14.185 to Km 20.593 (<i>NHAI</i>) (619045) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1,205.40 0.00	96.86	8.58
1468	6-laning of Krishnagiri Km.0.000 to Walajahpet Km.148.300 section on NH-46 under NHDP-V (<i>NHAI</i>) (619074) (-) (-)	Tamil Nadu	12/2009 (06/2011)	12/2013 (09/2026)	1,673.17 0.00	708.34	99.99
1469	Chengapalli km 102.035 to Neelambur Km144.680 and Madukkarai Km 170.880 to Walayar K183.010 Package No. NS-2/BOT/TN-08 (<i>NHAI</i>) (619086) (-) (-)	Tamil Nadu	10/2009 (09/2010)	03/2013 (10/2026)	1,247.43 0.00	7.46	100.00
1470	Thorapalli - Agraharam - Jittandahalli Section from km 23.350 to km 60.100 [Hosur to Dhamrapuri Pkg-2] (<i>NHAI</i>) (619094) (-) (-)	Tamil Nadu	02/2019 (12/2021)	12/2023 (12/2026)	1,243.57 0.00	823.86	77.57
1471	Mahabalipuram - Pondicherry Pkg-I [Mamallapuram to Mugaiyur] (<i>NHAI</i>) (619129) (-) (-)	Tamil Nadu	02/2019 (05/2022)	05/2024 (01/2027)	1,360.54 0.00	921.42	58.65
1472	Mahabalipuram - Pondicherry Pkg-II [Mugaiyur to Marakkanam] (<i>NHAI</i>) (619130) (-) (-)	Tamil Nadu	02/2019 (12/2023)	12/2025 (03/2027)	1,116.13 0.00	818.96	53.41
1473	Four Laning of Chettikulam to Natham section of NH-785 (<i>NHAI</i>) (619131) (-) (-)	Tamil Nadu	03/2018 (11/2018)	11/2020 (08/2026)	837.61 0.00	641.94	99.75
1474	Construction of New Double Tier 4L Elevated Corridor from Chennai Port to Maduravoyal in Chennai District from km -0.342 to Km 20.593 and Package III from Km 9.700 to Km 14.185 (<i>NHAI</i>) (619139) (-) (-)	Tamil Nadu	03/2023 (11/2023)	05/2026 (03/2029)	1,299.36 0.00	209.50	17.24

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1475	4 Laning of Paramakudi to Ramanathapuram Section of NH-87 Old NH-49 (NHAI) (619156) (-) (-)	Tamil Nadu	07/2025 (05/2026)	05/2028 (05/2028)	1,853.16 0.00	218.27	0.00
1476	Access Controlled Highway of 4 Lane with Paved Shoulders from Tiruvallur Design Chainage Km 1756 to TN/AP Broder Design Chainage Km 6151 of NH-716 Chennai-Tirupati Package-1 (NHAI) (619161) (-) (-)	Tamil Nadu	03/2024 (12/2024)	12/2026 (03/2027)	1,376.10 0.00	182.19	46.31
1477	Balance works of four lane from km 43.950 Thiruvallur Bypass to km 61.470 Veppampattu Bypass passing through Thannerkulam, Thozur and Sevapet Bypass 17.520 kms of Tirupathi- Tiruttani- Chennai section of NH 205 (NHAI) (619222) (-) (-)	Tamil Nadu	03/2022 (09/2022)	09/2024 (09/2026)	467.99 0.00	596.15	97.92
1478	6-laning of km 9.900 to km 19/948 Aramgarh to Shamshabad Section of Hyderabad-Bangalore section of NH-44 Under NHO EPC basis in the state of Telangana (MoRTH) (617913) (-) (-)	Telangana	01/2018 (05/2018)	05/2020 (06/2026)	283.15 0.00	270.88	92.62
1479	Widening to two/four lane with paved shoulder from Km.180.600 to Km.223.000 of NH-63 on Nizamabad-Jagadapur road on EPC mode under NHO in the state of Telangana. (MoRTH) (617936) (-) (-)	Telangana	10/2016 (03/2017)	03/2019 (-)	253.99 0.00	0.00	100.00
1480	6-Laning of Pune-Hyderabad Section of NH-65 from Km 493/0 to Km 524/0 from Sangareddy X Roads to Madinaguda in the State of Telangana (MoRTH) (617939) (-) (-)	Telangana	03/2023 (07/2024)	07/2026 (06/2027)	1,297.75 0.00	453.75	47.80
1481	Rehabilitation and Upgradation of LB-Nagar to Malkapur section to 6-Lane main carriageway with service roads, drains cum footpath, including VUPs and widening of Minor bridge & road safety provisions from Km. 15/00 to Km 40/00 of NH-65 Old NH-9 under NH O for the year 2020-21 in the state of Telangana on EPC Mode. (MoRTH) (617940) (-) (-)	Telangana	03/2021 (07/2022)	07/2024 (12/2026)	545.11 0.00	398.53	83.47
1482	Construction of six lane elevated corridor from km 7.950 Uppal to km 14.200 of NH-163 to De-Congest the urban limits of Hyderabad-Bhoopalapatnam section on EPC mode in the state of Telangana (MoRTH) (617980) (-) (-)	Telangana	03/2018 (07/2018)	07/2020 (12/2027)	626.76 0.00	290.80	55.25
1483	Widening & Strengthening of Existing 2LPS to 4 lane PS from Km 150000 to Km 159000 and Km 165400 to Km 186000 of NH-163 old NH-202 under NH O for the year 2020-21 on EPC Mode in the state of Telangana. (MoRTH) (617983) (-) (-)	Telangana	03/2021 (07/2022)	07/2024 (12/2026)	317.19 0.00	252.45	91.00
1484	Rehabilitation and upgradation of NH-167 from design km 113.900 to 154.479 Mallepally Haliya section to two lane with paved shoulders on EPC mode in the stte of Telangana (MoRTH) (617994) (-) (-)	Telangana	02/2018 (06/2018)	11/2019 (12/2025)	294.13 0.00	249.23	88.22
1485	Construction of 4-lane flyover at Amberpet-X road, Hyderabad on NH-202 in the State of Telangana (MoRTH) (618001) (-) (-)	Telangana	05/2018 (06/2021)	06/2023 (06/2026)	216.53 0.00	214.53	92.10
1486	Rehabitiitation and upgradation from km 121/000 to 154/000 Nakrekal to Mallampally section of NH-365 to 2 lane with paved shoulders in the state of Telangana in the EPC mode (MoRTH) (618025) (-) (-)	Telangana	03/2018 (06/2018)	12/2019 (09/2026)	192.67 0.00	171.88	96.00
1487	Widening to two lane with paved shoulders from Km 0/000 to Km 45/946 of Nizampet-Narayankhed-bidar section of NH-161B in the state of Telangana under Annual Plan 2021-22 on EPC mode under NHO (MoRTH) (618091) (-) (-)	Telangana	03/2022 (02/2024)	02/2026 (03/2027)	512.98 0.00	173.34	47.57
1488	Widening to two lane with paved shoulders from Km 0/000 to Km 79/300 of Kalwakurthy - Kollapur section of NH-167K in the state of Telangana under annual plan 2021-22 on EPC mode under NHO. (MoRTH) (618104) (-) (-)	Telangana	03/2022 (07/2023)	07/2025 (08/2026)	886.69 0.00	620.25	90.05
1489	Widening and strengthening to 4 lane / 2-lane with paved shoulders of Mahabubnagar - Chincholi section from km 60/255 to Km 102/834 of NH-167N in the State of Telangana on EPC mode. (MoRTH) (618105) (-) (-)	Telangana	03/2022 (10/2023)	10/2025 (11/2026)	631.49 0.00	219.29	50.14
1490	Widening and Strengthening to 2/4 lane with paved shoulders of Mahabubnagar Chincholi section from Km 0/0 to Km 60/255 of NH-167N in the state of Telangana under Annual plan 2021-22 on EPC modepackage-I under NHO Job No.167N-TS-2021-22-75 (MoRTH) (618106) (-) (-)	Telangana	01/2022 (05/2026)	11/2027 (03/2026)	703.68 0.00	499.88	90.69

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1491	Widening to 2 lane with paved shoulders from 0.00 to 32.970 ofAdilabadto Bela section of NH 353B in the State of Telangana (MoRTH) (618130) (-) (-)	Telangana	10/2022 (05/2024)	05/2026 (12/2026)	490.92 0.00	159.09	80.08
1492	Widening to two/four lane with paved shoulders from Km.34.250 to Km.71.830 of NH-365A on Kodad-Khammam-Kurvi road. (MoRTH) (618140) (-) (-)	Telangana	10/2022 (02/2025)	01/2027 (01/2027)	445.76 0.00	67.29	14.85
1493	Widening and Improvement of existing carriage way to 2 lane with paved shoulders from Km. 86/160 to 131/730 of Jangaon-Duddeda section of NH-365B in the State of Telangana on EPC Mode (MoRTH) (618141) (-) (-)	Telangana	01/2022 (12/2022)	12/2024 (12/2026)	423.48 0.00	262.93	77.85
1494	Widening to Two lane with paved shoulders from 106/830 to 158/496 of Yellareddy-Rudrur Section of NH-765D in the state of Telangana on EPC mode under NHO under Annual plan 2022-23 (MoRTH) (618182) (-) (-)	Telangana	10/2022 (07/2024)	07/2026 (08/2027)	499.88 0.00	248.31	69.20
1495	Widening to 2 lane with paved shoulders from Km 62/920 to km 106/830 of Medak - Yellareddy section in the State of Telangana under Annual Plan 2022-23 on EPC mode under NHO (MoRTH) (618183) (-) (-)	Telangana	10/2022 (08/2024)	08/2026 (08/2026)	399.01 0.00	170.44	70.60
1496	Rehabilitation and Up-gradation of Valigonda to Thorrrur Section to Two Lane with Paved Shoulders from Km 39.180 to Km 108.300 of NH-930P in the State of Telangana on Engineering, Procurement and Construction EPC Basis (MoRTH) (618186) (-) (-)	Telangana	01/2022 (12/2022)	09/2025 (09/2026)	549.28 0.00	389.39	94.97
1497	Widening to two lane with paved shoulders of 'Bodhan Basar Bhainsa ' section from Km 38/900 to 95/300 of NH-161BB in the state of Telangana under Annual Plan 2021-22 on EPC Mode under NH O. (MoRTH) (618190) (-) (-)	Telangana	03/2022 (03/2023)	03/2025 (09/2026)	644.45 0.00	459.72	98.60
1498	Widening to 2 lane with Paved Shoulders of Siddipet-Elkathurthy section from Km 69/978 to km 133/619 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618196) (-) (-)	Telangana	01/2022 (12/2022)	09/2024 (12/2026)	578.85 0.00	0.00	85.00
1499	Widening to 2 lane with Paved Shoulders of Medak - Siddipet section from Km 0/0 to km 69/978 of NH-765DG in the State of Telangana under Annual plan 2021-22 on EPC mode (MoRTH) (618197) (-) (-)	Telangana	01/2022 (01/2023)	01/2025 (12/2026)	882.18 0.00	428.70	74.06
1500	Khammam-Devarapalle Pkg I [4L Access Controlled Greenfield from Thallampadu village to Somavaram village Design Chainage 0000 to 33604] (NHAI) (618746) (-) (-)	Telangana	01/2021 (10/2022)	10/2024 (10/2026)	797.36 0.00	684.72	97.26
1501	4L of Karimnagar-Warangal section from km 49.500 to km 117.820 of NH-563 (NHAI) (618765) (-) (-)	Telangana	03/2022 (07/2023)	07/2025 (09/2026)	2,146.86 0.00	1,274.82	92.40
1502	4L Access Controlled Greenfield Highway Section Mancherial Warangal from Pangidipalle village at Design Ch. 72.350 Km to Oorugonda village at Design Ch. 112.240 KmPackage-III (NHAI) (618811) (-) (-)	Telangana	03/2023 (10/2025)	10/2027 (01/2028)	1,183.71 0.00	209.85	5.63
1503	4L Access Controlled Greenfield Section Mancherial Warangal from Puttapaka village at Design Ch. 35.300 Km to Pangidipalle village at Design Ch. 72.350 KmPackage-II (NHAI) (618812) (-) (-)	Telangana	01/2023 (06/2025)	06/2027 (12/2027)	1,129.33 0.00	211.69	9.04
1504	4L Access Controlled Greenfield Section Mancherial Warangal from Narva village at Design Ch. 3.834 Km to Puttapaka village at Design Ch. 35.300 Km Package-I (NHAI) (618813) (-) (-)	Telangana	03/2023 (12/2024)	12/2026 (10/2027)	1,127.90 0.00	162.07	11.28
1505	4L Access Controlled Greenfield Highway section on NH163G Warangal-Khammam from Oorugonda village in Hanamkonda District at Design Ch. 112.240 Km to Venkatpur village in Warangal District at Design Ch. 150.240 KmPackage-I (NHAI) (618814) (-) (-)	Telangana	03/2023 (06/2025)	06/2027 (05/2028)	1,142.60 0.00	162.11	0.00
1506	4L Access Controlled Greenfield Highway section on NH-163G Warangal-Khammam from Venkatpur village in Warangal District at Design Ch. 150.240 Km to Thallasenkesa village in Mahabubabad District at Design Ch. 189.650 kmPackage-II (NHAI) (618815) (-) (-)	Telangana	03/2023 (04/2024)	04/2026 (03/2027)	1,092.88 0.00	430.46	77.65
1507	4L Access Controlled Greenfield Highway section on NH-163G Warangal-Khammam from Thallasenkesa village at Design Ch. 189.650 km to V.Vekatayapalem village in Khammam District at Design Ch. 220.480 KmPackage-III (NHAI) (618816) (-) (-)	Telangana	03/2023 (07/2025)	07/2027 (02/2028)	1,105.25 0.00	204.68	10.11

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1508	4L Access Controlled Greenfield Highway section on NH-163G Khammam Vijayawada from V. Venkatayapalem village at Design Ch. 220.480 Km to Brahmanapallik village at Design Ch. 250.400 Km Package-I. (NHAI) (618817) (-) (-)	Telangana	03/2023 (03/2025)	03/2027 (06/2027)	973.45 0.00	271.81	45.89
1509	Hyderabad - Maneguda (NHAI) (618944) (-) (-)	Telangana	10/2021 (11/2024)	11/2026 (05/2027)	958.86 0.00	433.39	24.20
1510	4L of Kodad Design Km 0.00/Existing Km 185.00 of NH-65 to Khammam Design Km 31.800/Existing Km 29.400 of NH-365A (NHAI) (618945) (-) (-)	Telangana	01/2021 (01/2022)	05/2024 (09/2026)	1,149.17 0.00	937.96	99.98
1511	Upgradation to Two Lane with Paved Shoulders from Km 0.000 to Km 41.920 Green Field Alignment of Gowrelly to Valigonda Section of NH-930P in the State of Telangana on EPC Mode under Annual Plan 2022-23 (MoRTH) (619009) (-) (-)	Telangana	11/2022 (05/2026)	04/2028 (03/2028)	690.33 0.00	102.92	4.87
1512	Khammam-Devarapalle Pkg II [4L Access Controlled Greenfield from Somavaram village to Chintagudem village Design Chainage 33604 to 63117] (NHAI) (619128) (-) (-)	Telangana	01/2021 (09/2022)	09/2024 (08/2026)	615.78 0.00	524.11	98.02
1513	Rehabilitation and upgradation of NH-221 from km 121/0 to 165/0 Rudrampur to Bhadrachalam section to two lane with paved shoulder under NHDPIV in the state of Telangana through EPC mode (MoRTH) (619193) (-) (-)	Telangana	01/2015 (02/2015)	02/2017 (09/2026)	295.47 0.00	209.88	82.76
1514	Construction of 4 lane Bypass to Nalgonda Town Irorn Km 000 Existing Ch. 181590 to Km 14.00 Existing Ch. 28/685 ol Nakrekal to Nagarjunsagar Section of NH -565 in the State of Telangara on EPC under Annual Plan 2024 -25 (MoRTH) (619253) (-) (-)	Telangana	10/2024 (10/2025)	10/2027 (10/2027)	516.17 0.00	262.22	62.07
1515	Rehabilitation & Upgradation of Thorrru to Nehru Nagar section to Two Lane with Paved shoulders from Km 109/420 to Km 178/500 of NH 930P in the state of Telangana on EPC mode under Annual Plan 2022-2023 (MoRTH) (619265) (-) (-)	Telangana	01/2025 (07/2026)	07/2028 (07/2028)	675.45 0.00	24.95	2.50
1516	Rehabilitation and up-gradation of road from km 16.077 to km 43.935 total length 27.858 km of Lalchara-Kanchanpur section via Shivbari on NH-44A to 2 lane with paved shoulder in the state of Tripura on EPC Mode Pkg-2 under BharatMala Pariyojana Manu-Simlung -2 (NHIDCL) (618307) (-) (-)	Tripura	02/2022 (01/2023)	01/2025 (01/2026)	456.88 0.00	205.69	54.56
1517	Improvement & widening of existing NH-08 to 4-lane with Paved Shoulder from Champak Nagar to Khayerpur section design Km 242500 to Km 261610 in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618350) (-) (-)	Tripura	12/2023 (09/2024)	09/2026 (03/2027)	920.66 0.00	404.82	48.30
1518	Improvement and Widening to 2-lane with paved shoulder of road from design Km 72.000 Pati Chhari to design Km 107.654 Harina Total length 35.654 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-4 (NHIDCL) (618367) (-) (-)	Tripura	01/2024 (12/2024)	12/2026 (12/2027)	726.90 0.00	100.84	9.50
1519	Improvement and Widening to 2-lane with paved shoulder of road from design Km 36.000 Rangamati to design Km 72.000 Pati Chhari Total length 36.000 Km on Teliamura to Harina section of NH 208 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-3 (NHIDCL) (618368) (-) (-)	Tripura	01/2024 (09/2024)	09/2026 (05/2027)	670.90 0.00	183.24	14.90
1520	Improvement and Widening to 2-lane with paved shoulder of road from existing Km 438.170 Khowai Chowmuhani to existing Km 439.410 South Pulinpur of NH-08 and from design Km 0.000 South Pulinpur to design Km 36.00 near Rangamati of NH 208 on Khowai Teliamura- Harina section Total length 37.24 in the state of Tripura on EPC mode under JICA ODA Loan Phase VI Package-2 (NHIDCL) (618369) (-) (-)	Tripura	01/2024 (09/2024)	09/2026 (03/2027)	657.21 0.00	306.14	61.40
1521	Improvement and Widening to 2-lane with paved shoulder of road from Km 101.300 to km 127.319 Total Length 26.019 Km i.e. the Khowai Teliamura-Amarpur-Harina-Sabroom section of NH 208 in the state of Tripura on EPC under JICA ODA Loan Phase VI Package-1 (NHIDCL) (618370) (-) (-)	Tripura	01/2024 (07/2024)	07/2026 (04/2027)	431.78 0.00	265.36	63.15
1522	Rehabilitation and up-gradation of road from design km 25.250 to km 36.460 Total lenth 11.210 km of Kailashahar-Kurti Bridge section on NH-208A to 2-lane with paved shoulder on EPC basis under NHO Package-III- Balance Work (NHIDCL) (618385) (-) (-)	Tripura	02/2020 (09/2024)	03/2026 (03/2026)	174.43 0.00	67.10	53.14

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1523	Melaghar-Srimantapur section on NH-08 Spur from Km 23 to Km 34.500 11.5 Km and overlay from Km 20.30 to Km 22.00 1.7 Km Total Length 13.2 Km (NHIDCL) (618411) (-) (-)	Tripura	01/2023 (05/2023)	11/2024 (10/2026)	195.95 0.00	95.54	72.48
1524	Construction of 4-Lane with paved shoulder Agartala bypass Western side, length 25.402 km connecting NH-8 near Amtali to NH-108B near Lembuchhera in the state of Tripura on EPC basis under NHO-NE (NHIDCL) (618417) (-) (-)	Tripura	03/2023 (03/2024)	03/2027 (03/2027)	2,026.05 0.00	462.34	9.20
1525	Rehabilitation and upgradation to four lane road from km 70.500 to km 78.600 of NH-92 under EPC mode in the State of Uttar Pradesh (MoRTH) (617963) (-) (-)	Uttar Pradesh	01/2022 (01/2025)	01/2027 (01/2027)	296.02 0.00	128.07	40.00
1526	Widening to Four Lane rigid pavement configuration from Km 90.00 to Km 100.800 on NH-96 Km 42.0 to Km 53.300 as per new NH-330,design length of 11.300 km under EPC mode in the state of Uttar Pradesh. (MoRTH) (617964) (-) (-)	Uttar Pradesh	12/2022 (11/2024)	11/2026 (11/2026)	309.63 0.00	63.04	32.21
1527	Balance work of Construction of Ring Road for Raebareli City on eastern side of NH-24B Phase-1 on EPC mode. (MoRTH) (618009) (-) (-)	Uttar Pradesh	12/2019 (10/2020)	04/2022 (12/2026)	319.96 0.00	293.18	95.00
1528	Construction of Balrampur bypass with 2L flexible pavement configuration from km.223.000 of NH-330 to km.328.300 of NH-730 under EPC mode (MoRTH) (618054) (-) (-)	Uttar Pradesh	12/2022 (08/2024)	02/2026 (12/2026)	515.69 0.00	365.38	56.00
1529	Construction of Pratapgarh Bypass Extension connecting NH-31 to NH-330 on EPC mode in the State of Uttar Pradesh. (MoRTH) (618055) (-) (-)	Uttar Pradesh	10/2022 (01/2024)	06/2025 (09/2026)	225.17 0.00	134.10	78.00
1530	Improvement and Up-gradation to two Lane with Paved Shoulder Configuration from existing km. 420.00 Shohratgarh to km. 454.00 Uska Bazar of NH-730 in the state of Uttar Pradesh EPC basis (MoRTH) (618056) (-) (-)	Uttar Pradesh	01/2022 (03/2024)	09/2025 (12/2026)	509.65 0.00	268.33	62.00
1531	Construction of Shohratgarh Bypass on NH-730 under EPC mode in the State of Uttar Pradesh (MoRTH) (618057) (-) (-)	Uttar Pradesh	10/2022 (11/2023)	05/2025 (12/2026)	189.31 0.00	85.77	54.00
1532	Widening & Strenghteningof section from Bharthana chowk to Kodarkoot km.0.00 to km.40.00 of NH-91-A on EPC mode (MoRTH) (618063) (-) (-)	Uttar Pradesh	03/2020 (03/2023)	09/2024 (12/2026)	262.37 0.00	115.38	94.00
1533	Construction of Amethi bypass Part-II at km.30.050 of NH-931 under EPC mode in the state of Uttar Pradesh (MoRTH) (618066) (-) (-)	Uttar Pradesh	12/2022 (02/2025)	02/2027 (02/2027)	283.86 0.00	105.94	52.00
1534	Rehabilitation & Up-gradation from design Km. 0.000 to Km. 69.280 of NH-931 Pratapgarh - Amethi - Gauriganj -Musafirkhana to two lane with paved shoulder on Engineering, Procurement & Construction EpC mode in the State of Uttar Pradesh (MoRTH) (618067) (-) (-)	Uttar Pradesh	05/2023 (11/2025)	11/2027 (11/2027)	1,086.30 0.00	141.20	10.90
1535	Construction of two lane with paved shoulder from existing Km.0.000 to Km.55.610 design km. 0.000 to km. 54.048 of NH-124D (MoRTH) (618075) (-) (-)	Uttar Pradesh	12/2021 (02/2024)	02/2026 (03/2027)	840.93 0.00	210.11	77.00
1536	Construction of Mariahu Bypass with four lane paved shoulder configuration Km. 53.540 to Km.59.200 of NH-135A on EPC mode in the state of Uttar Pradesh (MoRTH) (618081) (-) (-)	Uttar Pradesh	03/2023 (02/2024)	02/2026 (12/2026)	438.24 0.00	255.05	55.00
1537	Widening & Upgradation to four lane configuration from Km.34.900 Bhadohi to km.73.134 Jaunpur of NH-135A on EPC mode (MoRTH) (618082) (-) (-)	Uttar Pradesh	03/2021 (11/2022)	05/2024 (10/2026)	395.62 0.00	358.27	95.00
1538	Improvement and upgradation to two lane with paved shoulder configuration from existing km 90.00 to 130.00 Design length 39.15 of NH-227A near Sikriganj to Barhalganj in the State of UP on EPC Mode. (MoRTH) (618111) (-) (-)	Uttar Pradesh	08/2021 (12/2023)	06/2025 (09/2026)	403.36 0.00	204.35	96.00
1539	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg Package I, from km 228.920 Jagarnathpur to Km 235.960/0.000 MakhaudaDham to Km 29.000 Sarpur in the State of Uttar Pradesh on EPC basis (MoRTH) (618112) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	11/2026 (05/2027)	912.50 0.00	421.43	8.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1540	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg Package III, from Km.47.800 Gosaiganj to Km.73.300 Bikapur in the State of Uttar Pradesh on EPC basis. (MoRTH) (618113) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	11/2026 (05/2027)	587.97 0.00	285.20	52.45
1541	Improvement and up-gradation of NH-227B 84 Kosi Parikrama Marg PackageV, from Design Km.140.960 Patranga to Km.160.200 Bahuvan Madar Majha on EPC mode in the State of Uttar Pradesh (MoRTH) (618114) (-) (-)	Uttar Pradesh	03/2023 (02/2026)	08/2028 (08/2028)	1,192.33 0.00	105.72	8.00
1542	Improvement and Up-gradation from Km. 73.300 Bikapur to Km.140.960 Patranga of NH-227B 84 Kosi Parikrama Marg to 2LPS along with Parikrama Path (MoRTH) (618116) (-) (-)	Uttar Pradesh	11/2022 (01/2026)	01/2028 (01/2028)	1,679.75 0.00	707.07	40.50
1543	Rehabilitation and upgradation from km 51.600 to km 75.700 of NH-321G Nuhkhas to Etah section to two lane with paved shoulder configuration under EPC mode in the State of Uttar Pradesh (MoRTH) (618124) (-) (-)	Uttar Pradesh	01/2022 (02/2024)	08/2025 (11/2026)	343.54 0.00	88.97	73.00
1544	Improvement and up-gradation to 2LPS of NH-227B 84-Kosi Parikrama Marg PackageVI, Design Km 160200 Bahuvan Madar Majha to Km 224040 Jagarnathpur under HAM (MoRTH) (618162) (-) (-)	Uttar Pradesh	05/2023 (01/2026)	01/2028 (01/2028)	2,008.70 0.00	506.45	22.00
1545	Rehabilitation and Up-gradation from km. 0000 to km.40390 of NH-730S MaharajganjNichloulThuthibari to two lane with paved shoulders in the State of U.P. on Engineering, Procurement & Construction EPC Basis. (MoRTH) (618163) (-) (-)	Uttar Pradesh	03/2023 (06/2024)	12/2025 (12/2026)	809.25 0.00	352.88	61.00
1546	Construction of four lane highway with paved shoulder from Km.74.700 to Km.112.950 of NH-731A i/c Yamuna Bridge on HAM in the state of Uttar Pradesh. (MoRTH) (618164) (-) (-)	Uttar Pradesh	03/2022 (06/2024)	06/2026 (09/2026)	1,141.67 0.00	627.83	100.00
1547	Construction of 4-lane green field highway from Km. 35.000 to Km. 49.155 of NH-731A with paved shoulders on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618166) (-) (-)	Uttar Pradesh	01/2022 (10/2023)	10/2025 (09/2026)	697.66 0.00	340.43	100.00
1548	Widening to four lane with paved shoulder from Design Km.49.200 to Km.89.285 of NH-731B on EPC mode in the state of Uttar Pradesh (MoRTH) (618168) (-) (-)	Uttar Pradesh	03/2022 (01/2024)	01/2026 (01/2027)	917.91 0.00	685.18	56.00
1549	Construction of Two Lane with paved shoulder highway from Design Ch.0.000 to Ch.49.200 of NH-731B on EPC Mode (MoRTH) (618169) (-) (-)	Uttar Pradesh	03/2022 (11/2023)	11/2025 (09/2026)	640.18 0.00	580.93	99.00
1550	Rehabilitation and upgradation of Salon - Jais - Jagdishpur Road section of NH-931A, from design Chainage km 0.000 to km 5.740 to four lane divided carriageway and from design Chainage km 5.740 to km 53.500 to two lane with paved Total length km 53.500 along with One time improvement in 04 no's of realigned/bypassed built-up areas in a total length of 9.732 km in the state of Uttar Pradesh on EPC mode (MoRTH) (618187) (-) (-)	Uttar Pradesh	05/2023 (10/2025)	10/2027 (10/2027)	947.15 0.00	179.04	11.56
1551	Construction of 6-lane bridge on Ganga on NH-96 and its approaches in Phaphamau Allahabad on EPC mode (MoRTH) (618233) (-) (-)	Uttar Pradesh	07/2018 (02/2021)	02/2024 (09/2026)	1,948.25 0.00	1,295.12	92.00
1552	Construction of Basti Ring Road Phase-I with 4L configuration for Basti City in the state of Uttar Pradesh on HAM mode (MoRTH) (618243) (-) (-)	Uttar Pradesh	12/2022 (06/2025)	06/2027 (06/2027)	1,138.72 0.00	404.59	39.00
1553	Construction of Raebareli Ring Road Phase-2 with four Lane configuration for Raebareli City in the state of Uttar Pradesh on Hybrid Annuity Model HAM basis (MoRTH) (618244) (-) (-)	Uttar Pradesh	03/2022 (05/2025)	05/2027 (05/2027)	1,273.72 0.00	524.96	56.00
1554	Construction of 4 lane Mirzapur bypass including bridge over river Ganga from km 0.000 to km 15.000 of NH 135A in the State of Uttar Pradesh on HAM Mode. (MoRTH) (618247) (-) (-)	Uttar Pradesh	03/2024 (01/2026)	01/2029 (01/2029)	1,708.62 0.00	341.16	8.00
1555	Widening to 4 lane from km. 139.00 to km 179.20 of NH-135A Pkg-III Jaunpur Akbarpur section and Akbarpur bypass on Hybrid Annuity Mode in the state of Uttar Pradesh. (MoRTH) (618248) (-) (-)	Uttar Pradesh	05/2023 (01/2026)	01/2028 (01/2028)	1,653.15 0.00	340.43	24.00
1556	Widening to 4 lane from km. 108.50 to km 139.00 of NH-135A Pkg-II Jaunpur Akbarpur section on Hybrid Annuity Mode in the state of Uttar Pradesh (MoRTH) (618249) (-) (-)	Uttar Pradesh	03/2023 (03/2025)	03/2027 (03/2027)	1,511.57 0.00	398.15	45.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1557	Improvement and Up-gradation to two Lane with Paved Shoulder/Four Lane configuration from existing Km 130.000 to Km 191.000 design km 131.500 to Km 188.735, Design length 57.235 Km of NH-227A near Barhalganj to Mehrauna Ghat in the state of Uttar Pradesh on Hybrid Annuity Model HAM basis (MoRTH) (618252) (-) (-)	Uttar Pradesh	01/2022 (11/2024)	05/2027 (05/2027)	974.19 0.00	765.31	59.00
1558	Construction of Salempur bypass to 4LPS from km 64.000 of NH-727A Km 171.00 of Sonauli Balia Marg, old SH-01, near Mahadahan Chauraha to km 61.500 of NH-727B Km 178.500 of Sonauli Balia Marg, old SH-01, near near Ahirauli Village under Hybrid Annuity Mode HAM in the State of Uttar Pradesh (MoRTH) (618260) (-) (-)	Uttar Pradesh	03/2022 (11/2025)	11/2027 (11/2027)	1,348.06 0.00	318.71	38.00
1559	Construction of Deoria Bypass from existing Km. 27.140 to existing Km. 46.780 Design Km. 49.109 on NH727A Design length 21.969 Km. to four lane with paved shoulder configuration under Hybrid Annuity Mode HAM in the State of Uttar Pradesh (MoRTH) (618262) (-) (-)	Uttar Pradesh	03/2023 (08/2025)	07/2027 (07/2027)	1,734.70 0.00	482.81	10.00
1560	Rehabilitation and Up-gradation to 2LPS from Km. 0.000 to Km. 7.800 and Km. 35.400 to Km. 52.345 Design length 24.745 Km., except Bihar portion of NH-727B Tamkuhiraj to Bihar Border and Bihar Border to Majhauri on EPC mode in the State of Uttar Pradesh (MoRTH) (618263) (-) (-)	Uttar Pradesh	03/2023 (01/2025)	07/2026 (10/2026)	701.02 0.00	436.04	81.18
1561	Widening and Strengthening to two Lane with Paved Shoulder/Four Lane with paved shoulder configuration from km. 61.500 of NH-727B near Nawalpur km 178.500 of Sonauli Balia Marg, Old SH-01 i.e. end point of Salempur Bypass to km. 106.495 of NH-727B near Sikanderpur under EPC mode (MoRTH) (618264) (-) (-)	Uttar Pradesh	05/2023 (12/2025)	05/2028 (05/2028)	2,061.86 0.00	599.82	43.00
1562	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Miranpur Katra to radhaita section of NH-730CKm.114.000 to Km 137.250package-III in state of Uttar Pradesh undergreen national Highway Corridor ProjectGNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618265) (-) (-)	Uttar Pradesh	04/2020 (07/2022)	07/2024 (12/2026)	172.50 0.00	144.33	92.00
1563	Rehabilitation and upgradation to 2-lane with paved sholuders configuration of Bewar-Allahaganj- section of NH-730C Km.0.000 to Km 52.770 package-I in state of Uttar Pradesh undergreen national Highway Corridor Project GNHCP with the loan assistance of world Bank on EPC mode. (MoRTH) (618266) (-) (-)	Uttar Pradesh	04/2020 (11/2022)	11/2024 (10/2026)	325.24 0.00	306.61	99.00
1564	Widening/Upgradation to four lane configuration of Shahjahanpur-Bisalpur section from km 0.00 to km 47.026 of NH-731K on Hybrid Annuity Mode in the state of Uttar Pradesh. (MoRTH) (618267) (-) (-)	Uttar Pradesh	03/2023 (05/2026)	05/2028 (05/2028)	1,590.20 0.00	194.98	1.00
1565	6L Elevated Kanpur - Lucknow Exeressway Pkg-1 from Km. 10980 to Km. 28500 (NHAI) (618499) (-) (-)	Uttar Pradesh	12/2021 (02/2023)	07/2025 (09/2026)	1,972.94 0.00	775.81	100.00
1566	Construction of 4L Connector from Delhi Meerut Expressway Km 50.000 of Pkg IV to Km 8.520 of NH-235 Pkg-5 (NHAI) (618500) (-) (-)	Uttar Pradesh	09/2021 (03/2022)	03/2024 (09/2026)	1,081.39 0.00	463.14	78.00
1567	Varanasi Ring Road Pkg-II connecting Sandaha Village km 11.70 / NH-29 with Revasa Village km 818.80 / NH-2 (NHAI) (618529) (-) (-)	Uttar Pradesh	12/2017 (02/2019)	02/2022 (10/2026)	1,991.71 0.00	1,758.76	96.86
1568	Construction of Ring Road around Kanpur from Ch.68.650 to Ch.93.209 Jarkala to Pakari Package-IV in State of Uttar Pradesh. (NHAI) (618536) (-) (-)	Uttar Pradesh	02/2023 (12/2024)	06/2027 (06/2027)	1,603.53 0.00	287.37	39.20
1569	Construction of Ring Road around Kanpur from Km.000 to Km. 23.325 Chachendi Sachendi I to Maharajpur Package-I (NHAI) (618537) (-) (-)	Uttar Pradesh	01/2023 (12/2023)	06/2026 (02/2027)	1,753.75 0.00	479.58	62.15
1570	Construction of Ring Road around kanpur from Ch.51.200 to Ch. 68.650 Badarka to Harbanch-Uchti Pkg-III (NHAI) (618538) (-) (-)	Uttar Pradesh	09/2023 (01/2025)	07/2027 (07/2027)	1,792.68 0.00	297.75	34.80
1571	Construction of Ring Road Kanpur from Ch. 32.090 to Ch.51.200 Transganaga to Sathara Package-II B (NHAI) (618539) (-) (-)	Uttar Pradesh	08/2024 (03/2025)	09/2027 (09/2027)	1,089.41 0.00	68.11	20.40
1572	Construction of Ring Road around Kanpur from Ch.23.325 to Ch.32.090 Chaudhariya to Transganga Package-IIA (NHAI) (618540) (-) (-)	Uttar Pradesh	08/2024 (11/2025)	10/2027 (04/2028)	1,089.41 0.00	260.33	49.85

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1573	Construction of left out portion of Agra Inner Ring Road connecting village Deori to NH-44 village Bad from Km. 0.000 to Km. 7.772 (NHAI) (618554) (-) (-)	Uttar Pradesh	07/2022 (03/2023)	09/2024 (11/2026)	879.26 0.00	629.11	94.00
1574	4L Green Field Northern East side Gorakhpur Bypass 26.616 Kms starting from NH-29E Chainage 83.308 and end at NH-28 Chainage 285.100 (NHAI) (618566) (-) (-)	Uttar Pradesh	02/2023 (01/2024)	01/2026 (03/2027)	1,973.98 0.00	1,046.53	73.78
1575	4/6L of Northern Ayodhya Bypass starting Km. 112.540 and ending Km. 139.928 north of existing NH-27 part-1 and part-2 south of NH-27 from km 0.000 to km 5.000. (NHAI) (618567) (-) (-)	Uttar Pradesh	08/2024 (07/2025)	01/2028 (01/2028)	2,289.34 0.00	286.37	33.53
1576	4/6L Southern Ayodhya Bypass from Km 5.000 to Km 37.172 starting near Km. 112.540 and ending at Km. 153.281 of NH-27 (NHAI) (618568) (-) (-)	Uttar Pradesh	08/2024 (03/2025)	09/2027 (09/2027)	2,541.13 0.00	326.56	39.50
1577	4 -Laning of MP/UP Border to Kabarai section of NH-34&35 from km 197.000 to km 242.991 Length 45.991 Km Sagar-Kabrai Package-5 under Bharat Mala Pariyojana EC in MP & UP on HAM (NHAI) (618669) (-) (-)	Uttar Pradesh	10/2022 (02/2025)	02/2027 (02/2027)	1,632.93 0.00	574.14	61.77
1578	4 lanning of Aligarh Palwal section from km 0.00 to km 46.39 package -1 from khereshwar junction-kurana of NH33D , including khair & jattari bypass in the state of UP on HAM mode (NHAI) (618690) (-) (-)	Uttar Pradesh	03/2024 (03/2025)	03/2027 (03/2027)	1,663.38 0.00	592.48	21.25
1579	DL/UP Border - EPE Crossing Pkg-02 (NHAI) (618710) (-) (-)	Uttar Pradesh	09/2020 (05/2021)	11/2023 (09/2026)	2,002.79 0.00	1,740.61	100.00
1580	6L access Controlled Greenfield Highway from Gogwan Jalalpur Shamli to Ranipur Barsi Saharanpur of Shamli -Ambala section Package-I Design Ch. Form km 00.600 to km 45.500 (NHAI) (618722) (-) (-)	Uttar Pradesh	06/2022 (05/2023)	05/2025 (03/2027)	1,843.59 0.00	771.67	68.20
1581	4L Spur of Meerut-Garh-Mukteshwar section connecting NH-119 and NH-58 bypassing Meerut Town of NH 709 A (NHAI) (618761) (-) (-)	Uttar Pradesh	10/2021 (02/2023)	02/2025 (09/2026)	991.89 0.00	884.85	96.98
1582	Four laning of Agra-Aligarh Section from Km. 0.000 Junction of NH-34 Aligarh Km 144.60 to Km. 28.000 near Asroi village in Hathras of NH-509 Package-I (NHAI) (618768) (-) (-)	Uttar Pradesh	06/2024 (03/2026)	03/2028 (11/2028)	1,309.08 0.00	313.15	3.96
1583	4L of Bareilly-Pilibhit-Sitarganj from Km. 0.000 to Km. 32.500 of NH-30 Pkg-1 (NHAI) (618782) (-) (-)	Uttar Pradesh	02/2023 (03/2024)	03/2026 (03/2027)	1,394.14 0.00	626.04	64.12
1584	4L of Sonauli - Gorakhpur (NHAI) (618798) (-) (-)	Uttar Pradesh	12/2021 (03/2023)	03/2025 (12/2026)	2,555.50 0.00	1,330.97	89.00
1585	2L PS Greenfield bypass laiganj ajhara, mohanganj and Raniganj on Raebareli - Jaunpur Section Design km 0.00 to Km 531.77 of NH-31 (NHAI) (618842) (-) (-)	Uttar Pradesh	12/2024 (06/2026)	06/2028 (12/2026)	1,280.68 0.00	205.64	0.00
1586	Construction of two lane with paved shoulders bypass to Mungrabadshapur town starting from near Kodahu at Km 47/225 of NH-319D and ending near Nauwadandi at Km 219/720 of NH-31 under NHO in the state of Uttar Pradesh on EPC mode (NHAI) (618843) (-) (-)	Uttar Pradesh	02/2025 (09/2025)	03/2027 (03/2027)	197.60 0.00	59.06	22.79
1587	Construction of Underpass beneath airport runway on NH-31 old NH-56 for proposed expansion of runway of Babatpur Airport Varanasi (NHAI) (618848) (-) (-)	Uttar Pradesh	02/2025 (09/2025)	09/2027 (09/2027)	649.44 0.00	0.09	29.86
1588	Improvement and Up-Gradation of Existing Road to 4L PS from Km 123.650 to 175.080, from Start of Shahabad Bypass to End of Hardoi bypass of NH 731 Pkg-2B (NHAI) (618856) (-) (-)	Uttar Pradesh	09/2022 (11/2023)	11/2025 (03/2027)	1,101.79 0.00	540.05	71.33
1589	Improvement and Up-Gradation of Existing Road to 4L PS from Km 88.750 to 123.650, from Start of Shahjahanpur Bypass to start of Shahabad bypass of NH 731Pkg.-2A (NHAI) (618858) (-) (-)	Uttar Pradesh	09/2022 (01/2024)	01/2026 (03/2027)	955.34 0.00	371.22	70.56
1590	Improvement and Up-Gradation of Existing Road to 4L PS from Km 229.070 to 260.800, End of Hardoi District to Lucknow Ring road of NH 731 Pkg-4 (NHAI) (618859) (-) (-)	Uttar Pradesh	09/2021 (10/2022)	10/2024 (09/2026)	575.66 0.00	390.55	99.33

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1591	Four Lane Highway from Chandan Nagar Existing Km. 59.025 of NH 530B/Design Km. 179.5000 to Bareilly BypassStartExisting Km. 59.025 of NH 530B/Design Km. 218.000 Section of NH 530B, in the State of Uttar Pradesh on HAM Mode under NH0 (NHAI) (618866) (-) (-)	Uttar Pradesh	12/2024 (11/2025)	11/2027 (11/2027)	2,077.00 0.00	491.00	34.50
1592	4L Kasganj-Badaun Section from Km. 123.100 to Km. 179.500 Pkg-III of NH530B (NHAI) (618867) (-) (-)	Uttar Pradesh	03/2023 (05/2025)	05/2027 (12/2027)	2,009.11 0.00	593.25	40.00
1593	4L from Devinagar Bypass End Existing Km. 208.000 of NH 530B/Design Km. 66.000 to Kasganj Bypass End Existing Km.150.100 of NH 530B/ Design Km. 123.100 of NH 530B (NHAI) (618868) (-) (-)	Uttar Pradesh	03/2023 (06/2024)	06/2026 (12/2026)	2,289.52 0.00	1,042.31	77.00
1594	Construction of 4/6 lane Highway of Southern Bareilly Bypass, starting at Ch. 237000 of NH 530 near Jhumka chauraha, Dhantiya village and ending at Ch. 267000 of NH 30 near Invertis University including Trumpet Interchange (NHAI) (618869) (-) (-)	Uttar Pradesh	12/2024 (12/2025)	06/2028 (06/2028)	1,122.02 0.00	622.57	16.40
1595	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package II [from Shahapur km 42.500 to Pindari km 78.150] on EPC Mode in the state of Uttar Pradesh. (NHAI) (618884) (-) (-)	Uttar Pradesh	10/2022 (10/2023)	10/2025 (09/2026)	1,493.65 0.00	790.31	98.40
1596	Construction of Four Lane Highway from Ghazipur- Ballia-UP/Bihar State Border Greenfield section of NH-31 Package IV [from Buxur Spur of length km 17.270 on EPC Mode in the state of Uttar Pradesh. (NHAI) (618885) (-) (-)	Uttar Pradesh	10/2022 (06/2023)	06/2025 (11/2026)	617.88 0.00	286.85	90.57
1597	4L Greenfield Western Side spur of Rampur-Rudrapur Section from Km 0.000 to Km 13.700 connecting NH-24 to NH-87 bypassing rampur town (NHAI) (618911) (-) (-)	Uttar Pradesh	12/2021 (05/2023)	11/2024 (02/2027)	646.27 0.00	369.70	63.79
1598	4L Behsuma at Km 39.250 Ex. Km 39240 To Bijnor at Km 78.810 Ex. Km 86590 Design Length 39.560 Km of NH-119 Pkg-II (NHAI) (618923) (-) (-)	Uttar Pradesh	03/2023 (05/2024)	05/2026 (12/2026)	2,158.20 0.00	1,236.27	70.12
1599	2L PS of Najibabad Kotdwar section from 112.575 to Km. 138.635 of NH 119 (NHAI) (618924) (-) (-)	Uttar Pradesh	10/2021 (03/2024)	09/2025 (10/2026)	188.87 0.00	60.90	55.90
1600	Bijnor-Kotawali (NHAI) (618925) (-) (-)	Uttar Pradesh	02/2021 (11/2021)	05/2023 (09/2026)	300.58 0.00	302.11	99.02
1601	4L of Moradabad-Thakurdwara-Kashipur Section from Km. 0.000 to Km. 38.77 of NH-734 Pkg-II (NHAI) (618927) (-) (-)	Uttar Pradesh	10/2022 (03/2024)	03/2026 (06/2027)	2,006.82 0.00	1,001.96	54.55
1602	4L of Moradabad western side spur connecting NH-734 & NH-24 from Km. 0.000 to Km. 33.200 Pkg-I (NHAI) (618929) (-) (-)	Uttar Pradesh	11/2022 (09/2023)	09/2025 (12/2026)	1,841.92 0.00	1,133.10	83.06
1603	4 Lane Inner Ring Road around Allahabad City Pkg-2 Prayagraj Southern Bypass 43.200 - 50.860 (NHAI) (618960) (-) (-)	Uttar Pradesh	08/2023 (12/2023)	06/2026 (06/2027)	1,377.51 0.00	485.92	46.74
1604	4 Lane Inner Ring Road around Allahabad City Pkg-1 Prayagraj Southern Bypass 34.400 43.200 (NHAI) (618961) (-) (-)	Uttar Pradesh	02/2025 (12/2025)	12/2027 (12/2027)	775.94 0.00	87.58	24.55
1605	6L access control Greenfield highway of Vill-Khyawari to Vill-Latifpur at Saharanpur Bypass from Km. 82.000 to Km. 119.790 Pkg-4 (NHAI) (618968) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (09/2026)	1,428.19 0.00	1,396.07	99.24
1606	6L access control Greenfield highway of Vill-Lohadda to Vill-Karaunda Mahajan from Km. 27.000 to Km. 56.500 Pkg-2 (NHAI) (618970) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (08/2026)	1,335.45 0.00	1,253.61	98.06
1607	6L access controlled Greenfield highway of Junction of EPE Vill.-Mavikalan to Vill.-Lohadda from Km. 0.000 to Km. 27.000 Pkg-1 (NHAI) (619168) (-) (-)	Uttar Pradesh	03/2021 (09/2022)	09/2024 (09/2026)	1,602.48 0.00	1,424.73	99.29
1608	Construction of Four Lane Gola Flyover at Km 99.850 of NH 730 Major Junction with State Highways -93 of Engineering, Procurement and Construction EPC mode in the State of Uttar Pradesh. (MoRTH) (619194) (-) (-)	Uttar Pradesh	03/2025 (05/2026)	10/2027 (10/2027)	168.05 0.00	6.35	16.00

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1609	6L access-controlled highway from Ganeshpur tonear Mohand of Ganeshpur Dehradun section from Km.0 to Km.8.3 of NH-72A Package-1 (NHAI) (619308) (-) (-)	Uttar Pradesh	11/2020 (10/2021)	10/2023 (09/2026)	836.24 0.00	813.14	98.92
1610	Landslide treatment work on NH 58 from Kodyala Km. 266.130 to Devprayag Km. 296.925 10 location under EPC mode in the State of Uttarakhand on EPC Mode (MoRTH) (617888) (-) (-)	Uttarakhand	01/2023 (02/2024)	02/2025 (09/2026)	192.54 0.00	97.78	99.00
1611	Treatment of landslide zone from location no. 01 to 28 km 62.860 to 152.750 on NH-12509 in the State of Uttarakhand under EPC mode in NHO Annual Plan 2022-23 (MoRTH) (617889) (-) (-)	Uttarakhand	11/2022 (06/2023)	06/2024 (09/2026)	192.22 0.00	139.29	98.50
1612	Construction of Champawat Bypass with two lane with paved shoulder configuration starting from existing chainage 121.700 to existing chainage 129.450 Design Length 9.847 of NH-125 in District-Champawat in the state of Utrrakhand on EPC mode. (MoRTH) (617890) (-) (-)	Uttarakhand	02/2025 (01/2026)	12/2027 (-)	220.89 0.00	8.57	8.50
1613	Construction of 2 lane with paved shoulder of Kund Bypass from Design Km 35.130 to Km 47.700 existing Km 33.130 to Km 41.260 of NH-109 in the State of Uttarakhand (MoRTH) (617929) (-) (-)	Uttarakhand	02/2018 (05/2018)	05/2020 (12/2026)	247.41 0.00	151.81	84.70
1614	Construction of Rudraprayag tunnel of length 900.30 MTR including approaches and one major bridge on river Alaknanda connecting NH-107/old-109 to NH-07old-58 on EPC mode in the state of Uttarakhand. (MoRTH) (617967) (-) (-)	Uttarakhand	02/2021 (01/2023)	07/2025 (09/2026)	251.88 0.00	158.45	99.00
1615	Construction & Widening Including Augustmuni Bypass Ch-16.545 to Ch - 19.890 to 2L/PS from Km 16.545-Km 33.130 & 45.980 -57.975 Augustmuni to Kund & Guptkashi to Sitapur on NH 109 in UK (MoRTH) (617968) (-) (-)	Uttarakhand	03/2017 (02/2018)	02/2020 (03/2024)	418.89 0.00	358.36	95.00
1616	Rehabilitation and upgradation of 2 lane with paved shoulder from existing km. 195.175 to km. 220.000 Design Chainage km71.300 to Km. 95.947 Excluding existing chainage Km 200.300 to Km 202.400 Design chainage Km 76.400 to Km 78.400 on Dharasu to Yamunotri Road of NH- 134 Old NH-94 (MoRTH) (617974) (-) (-)	Uttarakhand	05/2025 (10/2025)	04/2028 (-)	344.73 0.00	42.81	53.74
1617	Widening to 2 Lane from Existing Chainage Km 74.700 Km 100.660 Design Chainage Km 53.365 to Km 78.785 on NH- 507 in the State of Uttarakhand. (MoRTH) (618039) (-) (-)	Uttarakhand	01/2024 (10/2025)	04/2028 (-)	346.82 0.00	0.00	31.75
1618	Rehabilitation and Upgradation to Two lanes with Paved Shoulders configuration and Strengthening from Km 175.00 to Km 196.00 Gumkhal to Satpuli of NH-119 New NH-534 in the State of Uttarakhand under NHO Annual Plan 2021-22 under EPC mode (MoRTH) (618040) (-) (-)	Uttarakhand	03/2022 (01/2025)	01/2027 (-)	452.81 0.00	172.27	42.00
1619	Rehabilitation and upgrading to two lanes with paved shoulders and Strengthening of Kotdwar-Pauri-Srinagar road section from Km 232.00 to 274.470 on NH-119 New 534 Paidul to Srinagar in the State of Uttarakhand on EPC Mode under NHO Annual Plan 2021-22. (MoRTH) (618041) (-) (-)	Uttarakhand	02/2022 (12/2025)	12/2027 (-)	299.31 0.00	13.05	3.00
1620	Rehabilitation and up-gradation to 2-lane configuration of Bageshwar to Kangarchina road from km 129.600 to Km 161.600 Existing Chainage 136.00 to Km 169.00 of NH-309Ain the State of Uttarakhand Package-IV under NHO Annual Plan 2021-22 (MoRTH) (618119) (-) (-)	Uttarakhand	03/2022 (08/2024)	02/2027 (-)	472.23 0.00	189.12	67.00
1621	Widening to 2-lane with Hard Shoulder configuration of Mana Ch. 0.00 to Mana Pass Ch. 50.987 road on NH-07 under Bharatmala Pariyojna in the state of Uttarakhand under Annual Plan 2022-23 length 50.987 (MoRTH) (618207) (-) (-)	Uttarakhand	10/2022 (10/2023)	10/2027 (10/2028)	573.96 0.00	78.26	21.03
1622	Construction & up gradation of existing road to 2-Lane with paved shoulder from existing chainage km 468000 to km 489350 Design Chainage km 465150 to km 471500 of NH-07 Old NH-58 including Joshimath bypass on EPC mode in the state of Uttarakhand Length 6.35 km (MoRTH) (618209) (-) (-)	Uttarakhand	03/2022 (09/2022)	09/2025 (08/2027)	258.85 0.00	84.90	37.23
1623	Rehabilitation and upgradation of Askot-Lipulekh on EPC Basis for Phase-I Existing Km 72.00 to 107.620 Design Chainage Km 21330 to Km 56935 under Project Hirak of BRO in the state of Uttarakhand under Bharatmala Pariyojna Phase-I on EPC Mode Length-35.605 Km CA No EPC/MORT&H/HRK/01/2021-22 (MoRTH) (618210) (-) (-)	Uttarakhand	09/2020 (12/2021)	12/2023 (10/2026)	603.92 0.00	403.85	81.17

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1624	Improvement/construction of 2-lane with paved shoulder of Askote Llipulekh road from Tawaghat village to Budhi village design km. 56935 to km 95748 and from end of Tunnel portal to Kali Mandir design km 113828 to km. 133078 [total design length 58.063 km] under project Hirak of BRO in the state of Uttarakhand under Bharatmala Pariyojna on EPC Mode (MoRTH) (618211) (-) (-)	Uttarakhand	05/2022 (11/2024)	11/2026 (07/2027)	649.60 0.00	97.44	39.93
1625	STABILIZATION OF LAND SLIDE AND SLOPE PROTECTION AT KM 11.00 TO KM 11.08, 29,730 KM TO 30,060 KM, 30,400 KM TO 31,060 KM, 34,750 KM TO 35,300 KM, 38,950 KM TO 39,030 KM & 39,460 KM TO 39,540 KM TWO LOC CLUBBED, KM 40,400 TO KM 40,650, KM 43,500 KM 43,680, 52,460 RISHIKESH - DHARASU ROAD NH-94 ON EPC MODE IN THE STATE OF UTTARAKHAND. NOSE OF LAND SLIDE - 12 NOS (MoRTH) (618212) (-) (-)	Uttarakhand	01/2024 (10/2025)	04/2027 (-)	197.26 0.00	20.70	22.00
1626	Rehabilitation and Upgradation of road Rishikesh Dharasu Old NH-94 with 2-lane with paved shoulder from km 76.000 to km 110.000 Design Chainage from km 74.733 to km 107.347 32.614 km including construction of Kamand re-alignment from existing Chainage Km 105.200 to Km 108.600 design chainage Km 103.436 to Km 105.949 - total length 2513 mtrs and land slide treatment work between design chainage Km 73.800 to Km 74.00 200m on EPC mode under improvement to NH connectivity to Chardham in (MoRTH) (618213) (-) (-)	Uttarakhand	03/2018 (01/2019)	01/2021 (10/2026)	273.76 0.00	227.84	96.46
1627	Rehabilitation and upgradation to 2 lane / 2 lane with paved shoulder configuration for design chainage km 107.347 to km 129.208 & km 133.878 to km 138.570 existing chainage km 110.000 to km 133.020 & km 137.330 to km 142.028 and land slide treatment at existing km 138.500 Design chainage km 134.970 of NH -94 on EPC mode under improvement to NH connectivity to Chardham in the state of Uttarakhand. (MoRTH) (618214) (-) (-)	Uttarakhand	03/2018 (01/2019)	07/2021 (06/2024)	346.50 0.00	296.56	100.00
1628	Rehabilitation & upgradation of existing road to 2-lane with hard shoulder from Joshimath km 0.00 to Saraihotra km 29.725 road on NH-107B under Bharatmala Pariyojna on EPC mode in the state of Uttarakhand (MoRTH) (618218) (-) (-)	Uttarakhand	10/2022 (05/2023)	05/2025 (03/2027)	338.38 0.00	159.26	80.00
1629	Upgradation to 2-lane with Hard shoulder configuration of Suraihotra Ch. 29.725 km to Malari Ch. 60.550 km road on NH- 107B under in the state of Uttarakhand. (MoRTH) (618219) (-) (-)	Uttarakhand	10/2022 (05/2024)	05/2026 (12/2026)	292.76 0.00	142.36	76.67
1630	Construction, Operation & Maintenance of 2-L Bi-directional Silkyara Bend- Barkot Tunnel with escape passage including approaches Tunnel-4.531 & Approach road- 0.328 on Dharasu-Yamunotri section b/w Chainage 25.400km and 51.00km falling along NH-134 Old NH-94 on EPC mode (NHIDCL) (618390) (-) (-)	Uttarakhand	03/2018 (07/2018)	07/2022 (03/2027)	1,383.78 0.00	860.71	76.96
1631	Construction for Mitigation Measures of 5 Nos. Landslides, 05 No. Sinking Zones and 01 No. Bridge from Ch. 450.00 to Ch. 468.00 18 Km. Length on NH-07 Package-III (NHIDCL) (618391) (-) (-)	Uttarakhand	12/2023 (06/2024)	12/2025 (02/2027)	250.33 0.00	112.33	89.84
1632	Construction for Mitigation Measures of 5 Nos. Landslides, 5 Nos. Sinking Zones in between Ch. 433.00 to 450.00 BANERPANI VILLAGE on NH-07 on EPC mode in the state of Uttarakhand Package-2 (NHIDCL) (618392) (-) (-)	Uttarakhand	12/2023 (12/2024)	06/2026 (01/2027)	259.64 0.00	0.00	71.94
1633	4L of Haridwar Nagina section Design Ch. LME from km 13.829 to km 17.110 & km 26.077 to km 27.508 and Design Ch. RME from km 13.839 to km 17.120 & km 26.078 to km 27.509 of EUP mitigation measures on NH74 (NHAI) (618875) (-) (-)	Uttarakhand	11/2021 (08/2022)	02/2024 (12/2026)	183.92 0.00	119.67	70.42
1634	Construction of 4-lane connectivity to Banbasa ICP at India Nepal border from NH-09 old NH-125 Sitarganj-Tanakpur at Km 40.00 near Jagbuda bridge under Bharatmala Priyojana of NH-109D on EPC mode in the State of Uttarakhand (NHAI) (619142) (-) (-)	Uttarakhand	06/2022 (03/2023)	09/2024 (04/2027)	216.97 0.00	218.93	75.24
1635	Upgradation and 4L of Haridwar Bypass from Km 0.000 Km 188.100 of NH-58 to Km. 15.100 Km 5.100 of NH 74 PKg-1 (NHAI) (619155) (-) (-)	Uttarakhand	11/2021 (10/2022)	10/2024 (11/2026)	1,602.89 0.00	770.29	80.36
1636	Realignment of Rudrapur-Kathgodam Section of NH-87 New NH-109 From Design Chainage 000 Existing Chainage Km.54050 To Design Chainage 7875 Existing Chainage Km.61550 Due To Proposed Expansion Of Pantnagar Airport in the state of Uttarakhand. (NHAI) (619221) (-) (-)	Uttarakhand	08/2025 (06/2026)	09/2027 (09/2027)	252.97 0.00	0.19	0.00
1637	4L Medinipur to Ballupur from Km. 458.65 to Km. 487.65 of NH-07Pkg-2 (NHAI) (619292) (-) (-)	Uttarakhand	03/2022 (02/2023)	02/2025 (09/2026)	1,092.90 0.00	745.31	93.90

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1638	Construction of 4 Lane Access Controlled Bypass for Dehradun on NH307 from Design Chainage km 0050 Jhajra on NH-07 to Design Chainage km 12220 Asharori on EPC Mode in the State of Uttarakhand under NHO (NHAI) (619293) (-) (-)	Uttarakhand	12/2023 (04/2025)	04/2027 (04/2027)	715.97 0.00	204.77	62.79
1639	Road Safety Improvement of existing four lane section of Dehradun-Lal Tappar-Nepali Farm Section of NH-7 and Nepali Farm-Motichur NH-34 on EPC Mode in Uttarakhand under NHO. (NHAI) (619294) (-) (-)	Uttarakhand	05/2025 (02/2026)	08/2028 (08/2028)	720.67 0.00	19.14	5.13
1640	Four/Six laning of Bhaniyawala-Jollygrant-Rishikesh spur section of NH-07 from Km. 0.000 to Km 19.780 (NHAI) (619295) (-) (-)	Uttarakhand	02/2023 (12/2025)	11/2027 (11/2027)	742.43 0.00	13.35	0.00
1641	Construction of additional major Bridge with 4- lane configuration of length 1.48 km on NH-60 NH-14 over River Kangshabati from Km. 117.770 to Km 119.250 and additional major Bridge with 4- lane configuration of length 0.900 km on NH-60 NH-14 over River Shilabati from Km. 173.220 to Km 174.120 in the district of Paschim Medinipur of West Bengal under Annual Plan for FY 2023-24 on EPC mode. Job No 014-W8-2023-24/527 (MoRTH) (617893) (-) (-)	West Bengal	11/2023 (11/2025)	05/2028 (05/2028)	304.83 0.00	0.90	3.68
1642	Construction or 4 lane Raniganj Bypass of length 5.261 km on NH-60 new NH-14 from km 273.00 of NH to km 478.18 of NH-2 New NH 16 in paschim Bardhaman, West Bengal in EPC Mode- reg. Job No. 014-WB-2022-23/514 (MoRTH) (617894) (-) (-)	West Bengal	03/2023 (03/2024)	03/2026 (05/2027)	410.83 0.00	270.63	70.05
1643	Construction of ROB and its approaches in lieu of LC No. 10/B/T at Km 307.050 of NH-60. (MoRTH) (617931) (-) (-)	West Bengal	03/2016 (08/2023)	08/2025 (10/2027)	155.87 0.00	20.60	17.08
1644	Construction of new road at the missing link portion of NH-81 along approved alignment between Harishchandrapur and Eastern approach of Kalindri Bridge from Km 46.550 to Km 59.697 in the district of Malda. Job No-081-WB-2015-16/400 (MoRTH) (617960) (-) (-)	West Bengal	08/2016 (11/2016)	11/2018 (10/2026)	271.17 0.00	226.54	85.62
1645	Development to 4/6-lanning of NH-31 New NH-10 with both side service roads from km 569.258 to km 581.030 end of AH-02 project on NH- 31 near Shivmandir to Sevoke Army Cantonment in districts of Darjeeling and Jalpaiguri in the state of West Bengal on EPC Mode Job No. 010/WB/2021-22/490 (MoRTH) (618227) (-) (-)	West Bengal	03/2022 (03/2023)	09/2025 (03/2027)	995.04 0.00	676.60	76.17
1646	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of Kafer- Lava More section from km 40.00 to km 61.100 of NH717-A on EPC under SARDP-NE A in state of West Bengal Pkg-VA (NHIDCL) (618427) (-) (-)	West Bengal	06/2020 (10/2020)	04/2023 (12/2026)	311.02 0.00	268.20	95.98
1647	Construction & upgradation of existing road to 2-lane with paved shoulder including geometric improvement of sect. from Pedong bypass to Reshi Border km 79.700 to km 96.254 of NH-717A under SARDP-NE-A on EPC as part of Alternate connectivity to Gangtok Lava More-Reshi Border Pkg-VB (NHIDCL) (618429) (-) (-)	West Bengal	06/2020 (10/2020)	04/2022 (08/2026)	345.38 0.00	418.73	97.22
1648	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 0.00 to Km 13.00 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVA (NHIDCL) (618430) (-) (-)	West Bengal	03/2018 (10/2019)	04/2022 (08/2026)	402.94 0.00	261.90	99.23
1649	Construction of alternative highway to Gangtok in Sikkim via Bagrakot -Chuikhim-Nimbong -Kafer-Bakhim-Algarah-Rhenock in the State of West Bengal and from Rhenok-Rorathang-Pakyong along with spur from Aritar-Rolep-Menla in the State of Sikkim from Km 13.00 to Km 25.60 of Bagrakot -Kafer section of NH 717A on EPC Mode under Phase-A of SARDP-NE in the State of West Bengal PKG- IVB (NHIDCL) (618431) (-) (-)	West Bengal	03/2018 (10/2020)	04/2023 (12/2026)	295.97 0.00	255.94	97.73
1650	Binnaguri Bypass-Descoped portion of Ghoshpukur-Dhupguri Section of NH-31Dpkg-1 (NHAI) (618572) (-) (-)	West Bengal	03/2025 (11/2025)	11/2027 (11/2027)	309.99 0.00	4.92	3.67
1651	Balance Works of 4L of NH-31D from Km. 113.200 to Km. 154.854 Package-II A Ghoshpukur-Salsalabari Section (NHAI) (618574) (-) (-)	West Bengal	11/2023 (12/2024)	06/2027 (06/2027)	1,818.46 0.00	461.24	61.10
1652	6L Elevated Kona Expressway from Km. 0.145 to Km. 7.337 of NH-117 (NHAI) (618808) (-) (-)	West Bengal	03/2023 (06/2024)	12/2026 (12/2027)	1,212.56 0.00	451.59	39.99

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1653	4 laning of Barasat - Barajaguli Section of NH-12 from Km. 31.000 to Km. 48.679 in the district of North 24 - Parganas (NHAI) (618823) (-) (-)	West Bengal	02/2024 (08/2024)	02/2026 (10/2027)	352.01 0.00	98.02	43.52
1654	Development to 4-laning of the de-scoped stretches from Km 115.342 to Km 191.700 of NH-34 in Nadia District 3.962 & Murshidabad District 5.538 pertaining to Krishnagar to Berhampore section of NH-34 New NH-12 , in the state of West Bengal under NHO. (NHAI) (618824) (-) (-)	West Bengal	03/2024 (07/2024)	01/2026 (06/2027)	201.10 0.00	64.72	54.79
1655	Bridge over Ganga River at d/s of Farraka Barrage including Approaches connecting Farakka-Raiganj (NHAI) (618825) (-) (-)	West Bengal	08/2018 (12/2018)	12/2021 (09/2026)	622.04 0.00	637.37	96.71
1656	Construction of Dubrajpur Bypass with 4-lane configuration of length 5.676 km on NH-60 new NH-14 from design chainage 0.00 existing km 316.135 on NH-60 to design chainage 5.676 existing km 320.980 on NH-60 in the district of Birbhum, West Bengal under Annual Plan 2022-23 in EPC Mode- reg. Job. No. 014-WB-2022-23/518 (MoRTH) (619004) (-) (-)	West Bengal	03/2023 (12/2025)	12/2027 (12/2027)	560.79 0.00	155.66	11.50
1657	Slope protection and landslide mitigation at 4 vulnerable locations km 1.950 to Km 2.100, km 11.100 to 11.450, km 22.435 to km 22.485 and km 22.610 to km 22.680 within Sevoke-Rangpo section of NH-10 old NH-31A in Darjeeling & Kalimpong district in the State of West Bengal on EPC mode (NHIDCL) (619187) (-) (-)	West Bengal	02/2024 (06/2025)	06/2027 (06/2027)	152.27 0.00	22.06	36.11
	Total (982)				937,452.25 0.00	510,396.35	
	Ministry of Ports, Shipping and Waterways						
	Shipping						
1658	Development of Container Terminal at Tuna-Tekra, Deendayal Port on BOT Basis Under PPP Mode (Deendayal Port Trust) (609424) (-) (-)	Gujarat	10/2022 (03/2024)	03/2027 (09/2027)	4,243.64 0.00	2,878.70	60.00
1659	Replacement and revamping of pipeline projects in oil jetty area, Kandla (Deendayal Port Trust [DPT]) (701570) (-) (-)	Gujarat	09/2021 (09/2021)	09/2023 (03/2025)	171.00 0.00	149.50	92.00
1660	Mechanization of Berth No.14 for handling Containers and other cargo on DBFOT basis - Phase II (New Mangalore Port Authority) (617804) (-) (-)	Karnataka	12/2023 (06/2024)	03/2027 (-)	153.23 0.00	97.45	95.00
1661	Deepening and Optimization of Inner Harbour facilities including development of Western Dock on BOT basis to handle Cape size vessels (Paradip Port Trust [PPT]) (701574) (-) (-)	Odisha	05/2022 (01/2023)	12/2027 (10/2028)	3,004.63 0.00	2,279.12	78.00
	Total (4)				7,572.50 0.00	5,404.77	
	Tourism, Hospitality & Wellness						
1662	National Maritime Heritage Complex [NMHC] Phase-I (Indian Port Rail & Ropeway Corporation Ltd. [IPRCL]) (707215) (-) (-)	Gujarat	02/2019 (01/2022)	12/2026 (10/2026)	573.00 0.00	674.35	80.06
	Total (1)				573.00 0.00	674.35	
	Department of Telecommunications						
	Telecommunication						
1663	SETTING UP OF PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE [NICF] AT GHITORNI (National Communication Academy - Finance [Erstwhile NICF]) (709859) (-) (-)	Delhi	10/2014 (04/2018)	02/2020 (01/2027)	248.20 0.00	237.43	98.00
1664	Provision of 4G based Mobile Services in Uncovered Villages and National Highways of Meghalaya (Department of Telecommunications) (701598) (-) (-)	Meghalaya	09/2019 (09/2020)	03/2022 (06/2026)	971.96 0.00	167.23	100.00
1665	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase 1 Upgradation (Department of Telecommunications [DoT]) (617413) (-) (-)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	04/2022 (05/2024)	05/2025 (12/2026)	1,884.60 0.00	376.80	99.53

All Ongoing Projects

AUGUST 2026

SI.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1666	Mobile connectivity in Left Wing Extremism [LWE] affected areas-Phase2 (Department of Telecommunications [DoT]) (701599) (-) (-)	Multi-States (Andhra Pradesh, Bihar, Chhattisgarh, Jharkhand, Madhya Pradesh, Maharashtra, Odisha, Telangana, Uttar Pradesh, West Bengal)	05/2018 (09/2021)	03/2023 (11/2026)	1,577.57 0.00	493.48	90.27
1667	Provision of 4G based mobile services in 7,287 uncovered villages of 44 Aspirational District across 5 states of Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra & Odisha (Department of Telecommunications [DoT]) (701602) (-) (-)	Multi-States (Andhra Pradesh, Chhattisgarh, Jharkhand, Maharashtra, Odisha)	11/2021 (05/2022)	11/2023 (01/2027)	3,685.00 0.00	1,108.93	82.72
1668	Provision of 4G Mobile Services in Uncovered Villages of Arunachal Pradesh and 2 Districts of Assam (Department of Telecommunications) (701597) (-) (-)	Multi-States (Arunachal Pradesh, Assam)	12/2020 (10/2021)	04/2023 (09/2026)	1,255.49 0.00	237.98	99.84
1669	502 Aspirational District Scheme in Four states - Bihar, Madhya Pradesh, Rajasthan and Uttar Pradesh (Department of Telecommunications [DoT]) (704495) (-) (-)	Multi-States (Bihar, Madhya Pradesh, Rajasthan, Uttar Pradesh)	12/2019 (03/2021)	03/2022 (06/2026)	421.65 0.00	152.96	99.59
1670	Amended BharatNet Program - KTK, GOA, PY (Department of Telecommunications) (108841) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	3,742.00 0.00	435.31	10.34
1671	Amended BharatNet Program - HR (Department of Telecommunications) (124199) (-) (-)	PAN India	08/2023 (03/2026)	03/2029 (-)	837.00 0.00	83.68	0.00
1672	Amended BharatNet Program - PB (Department of Telecommunications) (171218) (-) (-)	PAN India	08/2023 (02/2025)	02/2028 (-)	1,245.00 0.00	0.00	31.29
1673	Amended BharatNet Program - MP, DD and DNH (Department of Telecommunications) (175860) (-) (-)	PAN India	06/2023 (05/2025)	05/2028 (-)	4,943.00 0.00	562.13	9.29
1674	Amended BharatNet Program - WB & ANI (Department of Telecommunications) (210914) (-) (-)	PAN India	08/2023 (02/2025)	02/2028 (-)	1,674.00 0.00	223.41	16.65
1675	Amended BharatNet Program - AS (Department of Telecommunications) (240484) (-) (-)	PAN India	08/2023 (03/2026)	03/2029 (-)	832.00 0.00	83.16	0.00
1676	Amended BharatNet Program - OD (Department of Telecommunications) (317725) (-) (-)	PAN India	08/2023 (07/2026)	07/2029 (-)	1,713.00 0.00	0.00	0.00
1677	Saturation 4G mobile coverage of Uncovered Villages through USOF (Department of Telecommunications [DoT]) (400013) (-) (-)	PAN India	07/2022 (07/2022)	06/2024 (03/2027)	26,316.00 0.00	8,722.82	89.40
1678	Amended BharatNet Program - J&K, LAD (Department of Telecommunications) (437130) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	1,621.00 0.00	170.05	10.15
1679	Amended BharatNet Program - MGH, MZM, TRP (Department of Telecommunications) (462136) (-) (-)	PAN India	08/2023 (04/2025)	04/2029 (-)	768.00 0.00	0.00	0.00
1680	Amended BharatNet Program - HP (Department of Telecommunications) (476006) (-) (-)	PAN India	08/2023 (02/2025)	02/2028 (-)	1,292.00 0.00	148.93	25.62
1681	BharatNet Phase-II (Department of Telecommunications) (547243) (-) (-)	PAN India	07/2017 (11/2017)	05/2023 (-)	22,174.56 0.00	20,691.72	93.33
1682	Amended BharatNet Program - KL (Department of Telecommunications) (660056) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	765.00 0.00	94.95	1.64
1683	Amended BharatNet Program - UKD (Department of Telecommunications) (665021) (-) (-)	PAN India	08/2023 (05/2025)	05/2028 (-)	1,821.00 0.00	209.87	22.14
1684	4G Services by BSNL (Department of Telecommunications [DoT]) (701593) (-) (-)	PAN India	11/2020 (11/2020)	03/2024 (03/2026)	28,466.00 0.00	9,173.00	98.63
1685	BharatNet (Department of Telecommunications [DoT]) (706775) (-) (-)	PAN India	07/2017 (10/2011)	08/2023 (03/2019)	12,709.00 0.00	10,320.00	99.98

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1686	MPLS-IP BASED ACCESS AND AGGREGATION NETWORK [MAAN] IN BSNL ALONG WITH TEST AND MEASURING EQUIPMENT (BSNL) (709856) (-) (-)	PAN India	05/2023 (05/2023)	08/2024 (08/2026)	645.13 0.00	410.40	100.00
1687	Planning, Engineering, Supply, Installation, Testing, Commissioning, Integration & Annual Maintenance of 4G mobile network at 1 Lakh sites on PAN India basis including Mumbai & Delhi LSA on turnkey basis under Phase IX.2 Project. (BSNL) (709857) (-) (-)	PAN India	05/2023 (06/2023)	06/2025 (09/2026)	24,544.55 0.00	9,173.85	98.63
1688	Amended BharatNet Program - BR (Department of Telecommunications) (914467) (-) (-)	PAN India	08/2023 (03/2025)	03/2028 (-)	1,550.00 0.00	222.77	19.18
1689	Amended BharatNet Program - RJ (Department of Telecommunications) (938832) (-) (-)	PAN India	08/2023 (03/2026)	03/2029 (-)	2,839.00 0.00	283.93	0.00
1690	Amended BharatNet Program - SKM (Department of Telecommunications) (946208) (-) (-)	PAN India	08/2023 (06/2026)	06/2029 (-)	160.00 0.00	0.00	0.00
1691	Amended BharatNet Program - ARP, NGL, MNP (Department of Telecommunications) (976009) (-) (-)	PAN India	08/2023 (06/2025)	06/2028 (-)	1,168.00 0.00	123.28	0.71
1692	Amended BharatNet Program - UP (East) (Department of Telecommunications) (222253) (-) (-)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	5,008.00 0.00	502.00	8.18
1693	Amended BharatNet Program - UP (West) (Department of Telecommunications) (708687) (-) (-)	Uttar Pradesh	08/2023 (02/2025)	02/2028 (-)	1,917.00 0.00	0.00	8.79
	Total (31)				158,794.71 0.00	64,410.07	
	Department of Water Resources, River Development & GR						
	Waste & Water						
1694	Interception and Diversion and STP works in Bhagalpur under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616600) (-) (-)	Bihar	10/2017 (03/2022)	02/2025 (12/2026)	413.29 0.00	126.67	97.00
1695	Sewage Treatment Plant 100MLD and Sewerage Network 288 km in Digha-Patna under Hybrid annuity based PPP mode-Namami Gange Programme (National Mission for Clean Ganga) (616611) (-) (-)	Bihar	08/2017 (07/2019)	12/2025 (09/2026)	824.00 0.00	403.34	59.00
1696	Sewage Treatment Plant 50MLD and Sewerage Network 150 km in Kankarbagh Patna under Hybrid annuity based PPP mode Namami Gange Programme (NMCG1) (616612) (-) (-)	Bihar	08/2017 (07/2019)	12/2025 (-)	578.89 0.00	348.61	55.00
1697	Sewer Network, SPS and STP at Begusarai (National Mission for Clean Ganga) (616615) (-) (-)	Bihar	03/2010 (03/2018)	04/2025 (12/2026)	230.06 0.00	261.82	97.00
1698	Sewer Networks, SPS and STP at Hajipur (National Mission for Clean Ganga) (616616) (-) (-)	Bihar	03/2010 (03/2018)	06/2025 (12/2026)	305.19 0.00	346.46	95.00
1699	Interception & Diversion with Rehabilitation of sewerage scheme at Agra under Hybrid annuity based PPP model-Namami Gange Programme (National Mission for Clean Ganga) (616594) (-) (-)	Uttar Pradesh	05/2020 (04/2023)	04/2025 (12/2026)	842.25 0.00	208.64	86.00
1700	Pollution Abatement Works for River Kali Meerut under Meerut Municipality Interception & Diversion with STP (National Mission for Clean Ganga) (616605) (-) (-)	Uttar Pradesh	05/2020 (11/2024)	12/2024 (03/2027)	690.71 0.00	34.79	63.00
1701	Pollution Abatement works for River Ganga at Hooghly Chinsurah- Municipal Town Interception & Diversion with STP (National Mission for Clean Ganga) (616604) (-) (-)	West Bengal	05/2018 (12/2021)	03/2025 (09/2026)	154.73 0.00	103.28	94.00
	Total (8)				4,039.12 0.00	1,833.61	
	Water Resources						
1702	Sardar Gouthu Latchanna Thotapalli Barrage Project (Water Resources-AP) (400100) (-) (-)	Andhra Pradesh	04/2005 (01/2006)	12/2019 (12/2027)	353.05 0.00	879.15	95.88
1703	Gundlakamma project (Water Resources-AP) (400101) (-) (-)	Andhra Pradesh	04/2005 (04/2005)	12/2019 (03/2027)	397.41 0.00	624.78	98.30
1704	Polavaram Irrigation Project (Water Resources-AP) (701415) (-) (-)	Andhra Pradesh	01/2009 (11/2009)	04/2022 (06/2027)	10,151.04 0.00	28,159.22	86.20

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Original/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1705	Borolia Irrigation Project (Department of Water Resources, River Development & GR) (701370) (-) (-)	Assam	04/1996 (12/1996)	12/2022 (03/2026)	256.16 0.00	44.70	55.44
1706	Kelo Irrigation Project (Water Resources-CT) (400111) (-) (-)	Chhattisgarh	04/2008 (04/2008)	12/2019 (06/2026)	459.97 0.00	620.15	73.00
1707	Kudali Irrigation Project (Department of Water Resources, River Development & GR) (701399) (-) (-)	Chhattisgarh	04/2009 (12/2009)	12/2025 (03/2026)	382.29 0.00	249.06	86.31
1708	Sardar Sarovar Project (Narmada and Water Resources, Water Supply and Kalpsar Department-GJ) (701372) (-) (-)	Gujarat	04/1996 (04/1996)	12/2019 (03/2028)	20,718.17 0.00	31,986.52	93.70
1709	Subernarekha Multipurpose Project, Jharkhand (Department of Water Resources-JH) (701376) (-) (-)	Jharkhand	04/2011 (01/2012)	12/2019 (03/2026)	3,807.77 0.00	6,089.12	70.00
1710	Upper Tunga Irrigation Project (Water Resources-KA) (701377) (-) (-)	Karnataka	04/2014 (04/2014)	12/2019 (11/2026)	770.16 0.00	1,517.10	99.90
1711	Bargi Diversion Project Phase - IV [km. 154 to km 197] (Water Resources-MP) (400115) (-) (-)	Madhya Pradesh	04/2008 (01/2009)	12/2019 (03/2026)	751.03 0.00	814.02	75.00
1712	Bargi Diversion Project Phase - III [km. 104 to km 154] (Water Resources-MP) (400116) (-) (-)	Madhya Pradesh	04/2007 (04/2007)	12/2019 (12/2026)	1,229.15 0.00	2,271.97	82.09
1713	Bodwad Parisar Sinchan Yojna (Department of Water Resources-MH) (617422) (-) (-)	Maharashtra	05/2002 (01/2017)	07/2027 (-)	1,923.81 0.00	338.91	49.60
1714	Waghur Project (Department of water resources-MH - II) (701383) (-) (-)	Maharashtra	04/1996 (04/1996)	12/2019 (03/2026)	1,058.99 0.00	1,642.68	89.57
1715	Gosikhurd Project (Department of water resources-MH - II) (701386) (-) (-)	Maharashtra	04/2008 (04/2008)	12/2019 (06/2028)	7,196.47 0.00	14,439.47	72.65
1716	Aruna Medium Irrigation Project (Department of water resources-MH - II) (701391) (-) (-)	Maharashtra	04/2009 (01/2010)	12/2019 (06/2026)	210.45 0.00	1,734.71	100.00
1717	Lower Pedhi Project (Department of water resources-MH - II) (701396) (-) (-)	Maharashtra	04/2008 (04/2008)	12/2019 (03/2026)	255.97 0.00	3,066.05	65.00
1718	Nardave Medium Irrigation Project (Department of water resources-MH - II) (701398) (-) (-)	Maharashtra	04/2009 (04/2009)	12/2019 (06/2028)	211.46 0.00	879.80	75.00
1719	Thoubal Multipurpose Project (Water Resources Department-MN) (701400) (-) (-)	Manipur	04/1997 (04/1997)	12/2019 (12/2026)	1,449.44 0.00	1,848.17	99.00
1720	North Koel Reservoir Project (Department of Water Resources, River Development & GR) (701412) (-) (-)	Multi-States (Bihar, Jharkhand)	08/2017 (01/2021)	03/2021 (06/2027)	1,622.27 0.00	345.94	47.00
1721	Ken-Betwa Linking Development Project (Department of Water Resources, River Development,) (701530) (-) (-)	Multi-States (Madhya Pradesh, Uttar Pradesh)	NA (03/2022)	03/2029 (-)	21,030.00 0.00	8,530.86	0.00
1722	Integrated Anandpur Barrage Project (Water Resources-OR) (603945) (-) (-)	Odisha	04/1997 (01/1998)	12/2019 (06/2028)	567.03 0.00	2,836.51	62.85
1723	Subernarekha Project, Odisha (Department of Water Resources, River Development & GR) (701402) (-) (-)	Odisha	12/1995 (01/1998)	12/2019 (03/2026)	3,055.88 0.00	8,330.62	95.50
1724	Kanupur Irrigation Project (Irrigation and CAD-TG) (701404) (-) (-)	Odisha	04/2003 (01/2004)	12/2019 (06/2027)	989.43 0.00	2,804.16	79.50
1725	Relining of Rajasthan feeder and Sirhind Feeder canal (Department of Water Resources-PB) (701410) (-) (-)	Punjab	02/2016 (04/2018)	06/2021 (06/2026)	1,441.26 0.00	2,380.88	100.00
1726	Shahpur Kandi Dam Project (Department of Water Resources-PB) (701411) (-) (-)	Punjab	02/2010 (04/2018)	06/2022 (06/2026)	2,285.81 0.00	2,201.94	88.00
1727	Sri Ram Sagar Project Stage - II (Irrigation and CAD-TG) (400102) (-) (-)	Telangana	04/1996 (04/2005)	12/2019 (12/2025)	736.13 0.00	971.47	97.00

All Ongoing Projects

AUGUST 2026

Sl.No	Project Name (Agency) (Project Code) (Legacy OCMS Code) (PMGID)	State	Date of Approval (Start Date) MM/YYYY	Orignal/Target DoC (Revised DoC) MM/YYYY	Original Cost Revised Cost in Rs. Crore	Cumulative Expenditure in Rs. Crore	Physical Progress (%)
1728	Indiramma Flood Flow Canal Project (Irrigation and CAD-TG) (400103) (-) (-)	Telangana	04/1996 (01/2006)	12/2019 (12/2026)	1,331.30 0.00	4,491.08	92.00
1729	J. Chokka Rao Devadula Lift Irrigation Scheme (Irrigation and CAD-TG) (701405) (-) (-)	Telangana	04/2006 (04/2006)	12/2019 (12/2025)	8,200.71 0.00	4,841.09	87.70
1730	Madhya Ganga canal Phase-II (Irrigation & Water Resources-UP) (701408) (-) (-)	Uttar Pradesh	04/2008 (04/2008)	12/2019 (12/2025)	1,060.67 0.00	4,575.74	82.39
1731	Jamrani Dam Multipurpose Project (Irrigation-UK) (613787) (-) (-)	Uttarakhand	10/2023 (11/2023)	06/2029 (-)	2,584.10 0.00	1,379.51	29.44
	Total (30)				96,487.38 0.00	140,895.38	

Note:

1. Projects with Revised Cost Less than Rs. 150 cr may or may not be correct, the data is under reconciliation.

2. PAIMANA is currently in the process of API integration with the Indian Railways Projects Sanctions & Management (IRPSM) system, Ministry of Railways to fetch the latest data of ongoing central infrastructure projects. For data Sanctity, Projects are on-boarded onto the PAIMANA portal after being mapped and vetted by the Ministry of Railways.

3. The Flash Report covers selected categories and infrastructure subsectors from the DEA’s Harmonized Master List (HML), based on data reported by the concerned Line Ministries/Departments. It does not cover the entire HML and should be interpreted in the context of its coverage and data reported.



**Government of India
Ministry of Statistics and
Programme Implementation
Khurshid Lal Bhawan, Janpath Road, New Delhi-110001
Website: <https://paimana-proj.mospi.gov.in/>**
